

# Daily Report - MADISON ST BRT (211)

Date: 10/7/2021

## Diary

Hansen, Justin (HANSEN,JUS)



| Note                | Note Index |
|---------------------|------------|
| Pre Madison meeting |            |

## Diary

Hill, Theodore J. (HILL,TJ)



|                                                                                                                                                                      |  |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|
| Today we had a kick off meeting at the delridge office for the Madison project.<br>After the meeting I went to the port to check on the steel form cleaning process. |  |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|

## Diary

Mahan, Mark (MAHAN,MAR)



| Note | Note Index |
|------|------------|
|------|------------|

Meeting plans and work on job.

 **Diary**

Waldrop, Austin L. (WALDROP,AUS)



| Note | Note Index |
|------|------------|
|------|------------|

Meeting at delridge office

Date: 10/14/2021

 **Diary**

Pruss, Jafra (PRUSS,JAF)



| Note | Note Index |
|------|------------|
|------|------------|

placed No parks  
Went over 4 week schedule ordered UPOs

Date: 10/18/2021

 **Diary**

Pruss, Jafra (PRUSS,JAF)



| Note                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     | Note Index |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| <p>0600 at port loaded cones</p> <p>0630 Put in closure #35</p> <p>0658 Put in closure #4</p> <p>Placed bags over conflicting permanent signs where no parks were located and also over parking meter</p> <p>Called in cars in No Park zones</p> <p>Worked with Kemp West to trim trees from sidewalk</p> <p>Prime in closure on Spring street working on Corners</p> <p>Survey crew working in closure</p> <p>Removed closures on Madison at 1300 and moved UPOs up to 13th to work with Kemp West to keep working on tree trim</p> <p>Preset closure #14 for Joint clamp work</p> <p>1200 daily meeting went over what TCP's we will need for the rest of week was told #223 and #219 will be 24 hours starting Thursday ordered UPO's to cover these shifts</p> <p>Made sure all signs taken down after each closure was finished</p> <p>1504 While taking down signs Tawnya Keen tripped and fell over a sign and put her arm out to break her fall felt like she broke her arm I reached out to Bruce and was told to call Austin Byron who told me to take her to the hospital. Took her to Virginia Mason ER where they gave her Pain meds and took an X-ray which showed a spiral fracture of her left radial head. Took her home. Paperwork</p> |            |

 **Diary**

Solt, Bruce (SOLT,BRU)



Cool - (45 - 60); Partly Sunny / Cloudy

| Note                                                                                             | Note Index |
|--------------------------------------------------------------------------------------------------|------------|
| <p>Civil 1 working in yard helping out with tree boxes and preparing to mobilize to project.</p> |            |

Civil 3 completed welding brackets on containers, installing registration holders on trailers and receiving materials at port yard. Mark W directed crew on configuration of bins at end of day to accommodate PRIMES storage of materials.

Civil 4 not working today. Justin in today to prepare for start tomorrow.

Civil 6 on-site installing catch basin socks and tree boxes in all areas crews plan to begin working.

Kemp West on-site today and completed pruning trees from. 1st on Madison and Spring to approx 18th.

Tonya Keen tripped and fell at the end of the day. Jafra Pruss took her to ER for X Rays. Doctors determined spiral fracture of bone below the elbow. Went on area way inspection at 3rd and Madison and 3rd and Spring St today.

---

*No notes found*



*No notes found*



Date: 10/19/2021

## Diary

Mahan, Mark (MAHAN,MAR)



### Note

### Note Index

Received shoppe structures cleaned out equipment and trucks at port.

## Diary

Pruss, Jafra (PRUSS,JAF)



### Note

### Note Index

Put in closure #14 opened at end of day  
 Put in closure #272 opened at end of day  
 Put in Closure # 214 opened at end of day  
 Pre set for next days work  
 Drove site standing up cones every hour  
 Ordered t-par eg replacements  
 Painted cone marks on Madison 1st to 2nd  
 Pre set for closure #215  
 Play of the day meeting  
 UPO time cards  
 Replaced missing signs  
 MAde adjustment to Closure on Madison  
 End of the night after opening Madison minus small staging section noticed  
 cars thought there were 3 lanes since parking lanes do not have visible  
 parking lines so I placed cone tapers at parking areas to cut down on any  
 Jansen Inc.

confusion

---


*No notes found*



*No notes found*



*No notes found*

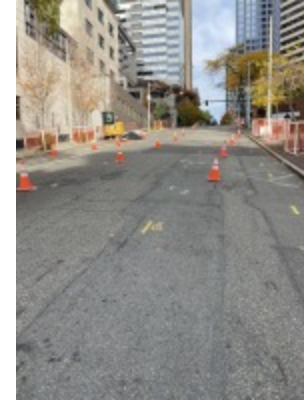

No notes found



No notes found



 **Diary**

Solt, Bruce (SOLT,BRU)

 Cool - (45 - 60); Partly Sunny / Cloudy

| Note                                                                                                                                                                                                                                                                                                                                               | Note Index |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| Civil 1, 3 and 5 working at port yard today finalizing lay down, loading traffic control features, accepting deliveries and beginning to assemble trench boxes. Austin Pellham on-site today to attend areaway walkthrough at 1st and Spring St. spent some time with Austin Pellham this afternoon previewing and planning his work on Spring St. |            |
| Civil 4 completed roadway demo and common excavation over waterline scheduled for pipe clamps to be installed at joints. After removing hard surfaces PROVAC factored off entire run of pipe and no joints were found.                                                                                                                             |            |

Representative from SPU water, ?, came and verified with crew and Tawny with HNTB that no clamps will be required at this location. Crew sheeted excavation with pins and cold patchEd edges for the night.

No notes found



Date: 10/20/2021

 Diary

Hansen, Justin (HANSEN,JUS)



| Note | Note Index |
|------|------------|
|------|------------|

Backfill joint clamp trench at 1st and Madison and temp pave  
Remove and salvage granite curb  
Jansen Inc.

pothole possible utility conflicts in storm trench from cb1. To connection  
Found conflict with duct bank in trench  
Layout for saw cutting

---

*No notes found*



*No notes found*



*No notes found*



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



 **Diary**

Mahan, Mark (MAHAN,MAR)



| Note                                                | Note Index |
|-----------------------------------------------------|------------|
| Order shoring for Denny storm run                   |            |
| Unload 1 truck load of 8 inch ductile iron pipe     |            |
| Unload 1 truck load of 12 inch ductile iron pipe    |            |
| Unload semi truck of roadway forms and speed screed |            |
| Build 2 8x8 aluminum trench boxes.                  |            |

 **Diary**

Pellham, Austin L (PELLHAM, A)



Drizzle; Partly Sunny / Cloudy; Cool - (45 - 60); Ground Wet - Workable

| Note                                                                                                                                                 | Note Index |
|------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| Painted lines for saw cut. Saw cut centerline and sidewalk between 1st and 2nd on Spring. Began breaking from 1st toward 2nd on the south two lanes. |            |

No notes found



No notes found



No notes found



No notes found




No notes found



No notes found



No notes found

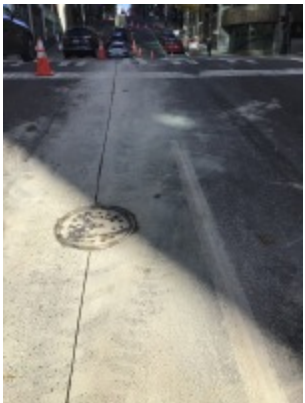

No notes found



No notes found



No notes found



No notes found



 **Diary**

Pruss, Jafra (PRUSS,JAF)



| Note                                                             | Note Index |
|------------------------------------------------------------------|------------|
| Put in closure # 215 Left closure in place                       |            |
| Put in closure #14 Opened minus small staging area               |            |
| Put in closure #272                                              |            |
| Made adjustments per Metro Request                               |            |
| Removed closure and all signs                                    |            |
| Missing 4 Road Work Ahead signs from over night replaced         |            |
| UPOs at 1st/spring 1st/Madison 2nd spring 2nd Madison 3rd/Spring |            |
| 3 UPOs for #272                                                  |            |
| Made sure Breaks Were given                                      |            |

Play of the day meeting

Made changes to the UPO schedules Rewrote and sent over to Seattle Blue.

Ordered additional signs needed for upcoming closures and picked up from National Barricade

Made sure signs had sandbags on them

Spoke to UPOs about being at the intersection and helping to clear out traffic was not received well spoke with Kathy from Seattle Blue regarding issue still was not resolved

Took down all signs not needed making sure to leave up Road Work Ahead signs

Assigned TCS and Flaggers tasks and start times for tomorrow

7 pm Checked out UPOs on Spring street and Checked in new officers

giving direction on what is expected

Midnight back out for lunch breaks for officers

## Diary

Solt, Bruce (SOLT,BRU)



Cool - (45 - 60); Overcast

### Note

### Note Index

Civil 1 on-site today to coordinate with crew working for site feature and sign removal. Nothing at this time in zone 1. Finished the day at port assisting civil 6 with deliveries and assembling boxes and curb ramps.

Civil 3 completed saw cutting on sidewalk and roadway for southern half of block between 1st and 3rd on Spring. Mobilized 310 excavator with all attachments and 308 excavator with all attachments to Spring St today. Crew began breaking roadway out late morning.

Civil 4 completed bedding, backfilling and temp patch paving joint clamp excavation at 1st and Madison this morning. Crew potholed inlet location to verify clearance over unlocated ductile line and confirmed it will fit. Crew removed hard surface over conduits and duct bank to pothole utilities. Upon Jansen Inc.

uncovering existing 8" line it was found to be resting directly on 3" signal conduits that are on top of an electrical duct bank. HNTB notified and inspector Tawny R sent photos and email to them. Line will not be able to be installed to design invert. Crew back filled holes and patch paved for the night.

Civil 6 at port yard today assembling trench boxes and curb ramps. Crew also accepting deliveries of pipe and materials, two loads of ductile iron arrived today and one semi load of steel rail forms and power screed for concrete. Crew preloaded tilt deck with pipe for civil 4 delivery in the morning. Crew also loaded pipe lasers and gear for work next week on storm line.

Met with KCM area supervisor at eastbound bus stop just east of 15th this morning. Worked thru stop and ada issues with him, UPO's and HNTB Tawny to get bus curbside in order to continue work.

Met with HNTB, urban Forestry and Kemp West this morning for discussions concerning tree protection pits and tree pruning procedures. Urban forestry really pushing against the spec for more durable material like chain link for tree boxes. Adam pointed out that some of the boxes will need to increase in size for trees in landscaped areas over 6" in diameter.

Kemp West on-site and completed 2 ea tree removal and stump grinding at both locations. Crews will return tomorrow to prune trees from 18 to 22nd.


Salinas on-site for full depth and sidewalk cutting on Spring St for civil 3.

---

No notes found



No notes found

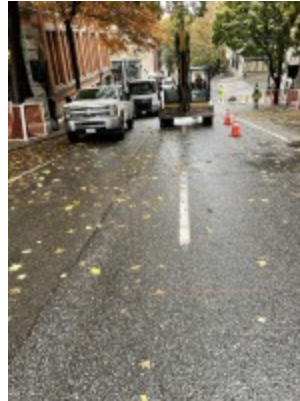

No notes found



Date: 10/21/2021

## Diary

Mahan, Mark (MAHAN,MAR)



### Note

### Note Index

Field memo 001

Start potholing with Pro vac vactor truck PV 460, Jansen 310 backhoe and breaker, birch equipment rental John Deere 85 excavator and breaker and work truck 136 at 20th and Madison for field memo#001 at 9:00 am told to stop potholing and put on standby at 11:30 by Tawni Russell with Exeltech because archaeologists needs to look at railroad ties found under roadway in pothole area for field change 0001 by Tawni Russell with exeltech inspection. Jansen Inc.

Archaeologists came out and inspected 4 demoed locations and filed a report. At 13:30 We were told we can move demoed material to a stock pile so we can clean up site and cover holes with road sheets and pin and cold patch for the night to open lane eastbound.

Received Jansen 310 John Deere backhoe and attachments  
 10 Jansen road sheets  
 Birch rental John Deere 85 excavator and breaker

Delivered 4 sticks of 8 inch ductile pipe to 1st and Madison and pick up 310 John Deere backhoe and take it to 22nd and Madison.

---

Roadway demoed for exploring if storm run will need dewatering.



Demo roadway for field memo 001 and found woody debris, stopped work by Exeltech for archaeologists to assess historic value.





Mild - (60 - 75); Partly Sunny / Cloudy; Drizzle; Normal Ground

## Note


## Note Index

Saw cut Madison and Spring confirmed all saw cut lines with Tawni Russell with Exeltech. Saw cut all lines for road demo on north side of Madison. Saw cut line at the top of Spring on 2nd ave. Didn't saw cut sidewalk on the corner of 2nd and Madison because there needed to be further discussion of whether or not to save or remove street names that were poured into the sidewalk landings. (See attached picture of sidewalk)

Breaking for road demo on Spring.

Set up asphalt berm on the top of spring to attempt to prevent water from heading down the hill towards 1st.

*No notes found*

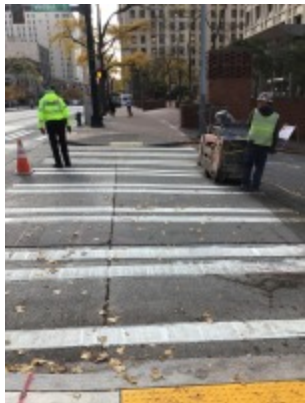

*No notes found*



*No notes found*



No notes found



No notes found



No notes found



## Diary

Rogalski III, Floyd J. (ROGALSK,FLO)



Note

Note Index

Striping and reflective button install Madison st 1st to 3rd

## Diary

Solt, Bruce (SOLT,BRU)



Mild - (60 - 75); Overcast

**Note****Note Index**

Civil 3 on-site today and completed breaking southern half of roadway from 1st to 3rd on Spring St this afternoon. Salinas on-site and completed sawcutting from 1st to 3rd on Madison to include sidewalk cuts and one additional cut on Spring at intersection of 2nd Ave. All demo limits review and approved by Tawny with HNTB prior to cutting.

Civil 4 did not work.

Civil 6 began the day and mobilized 4 sticks of 8" ductile pipe to 1st and Madison St for inlet installation and loaded the backhoe to take up to 20th and Madison. Brian returned with 10 road sheets for scheduled work next week. Crew broke out 4 of the five locations for the work described in FM 001, ground water investigation. All activities shutdown by archeology after first railroad tie was discovered. Consequently only one hole was completed at MH 17 and four of the five locations the roadway were broken and prepared for the vector truck today.

---

No notes found



Date: 10/22/2021

 **Diary**

Mahan, Mark (MAHAN,MAR)



| Note                                                                                                                                                                                                                                                                                                                                                                          | Note Index |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| Field memo 001                                                                                                                                                                                                                                                                                                                                                                |            |
| Started with meeting with Mark White and Bruce Solt about potholing for field memo 001, discussed sequence of storm run and where we will land material and truck routing and how the operation will play out.<br>Pro vac truck 125 showed up at 7:30 and we vacuumed out potholes at station<br>At 11:30 am Dan Monroe with HNTB said no more vac trucking until Jansen Inc. |            |

Archaeologists report is final.

Jake with OSG came on site and introduced himself to the crew.

Cameron and Grant had a meeting with SDOT inspector about dewatering the site for the storm pipe installation.

Mark White was here to watch the potholing and look at water levels for field memo 001.

Went to 1st and Madison and helped civil group 3 with install of inlet 1 and clean up.

---

Pro-vac truck 125 at 22nd and Madison to 20th and Madison to pothole for field memo 001



Potholing for field memo 001.



Railroad ties found in all 5 areas to pothole so far



Railroad ties found in all areas to pothole.



## Diary

Pellham, Austin L (PELLHAM, A)



Mild - (60 - 75); Partly Sunny / Cloudy; Overcast; Normal Ground

### Note

### Note Index

Started at Port to load up fittings, tools, and earthquake joints to install Inlet 1 and 1B. Began breaking for inlet 1 at 8 am and had concrete removed by 830. Had a difficult time removing ex inlet and maintaining the existing Ada ramp to be reopened after shift ends. Cut and removed existing pipe back 8ft back and attached new line to the existing with a 8x8 strong back DI fernco. Dug and set inlet 1 and tied in new line. Mudded pipe inside and out, floor, and picking eyes of the inlet. Backfilled with type 2 and cold patch with materials onsite from earlier in the week. Ran out of backfill material so we steel sheeted over the inlet and finished patching back the Ada ramp for the

weekend. Swept up work area and covered the spoils pile from digging that I had dumped on spring street to be hauled out on Mondays demo. Didn't make it to inlet 1B by 3 before first ave had to be reopened.

---

*No notes found*



*No notes found*



*No notes found*



No notes found



No notes found



No notes found



No notes found



Existing inlet to be removed ran under the Ada ramp. Had a difficult time removing it without breaking out the Ada wing.



# Diary

Pruss, Jafra (PRUSS,JAF)



| Note                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Note Index |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| <p>Jafra Pruss 0530-</p> <p>Sean Woodbridge 0600-1330</p> <p>Tawnya Keen 0700-1300</p> <p>Derron Wiggins 0600-1330</p> <p>Foluke Jackson 0700-1530</p> <p>UPO's at</p> <p>1st and Madison 24 hours</p> <p>2nd and Madison 24 hours</p> <p>1st and Spring 24 hours</p> <p>2nd and Spring 24 hours</p> <p>3rd and Spring 24 hours</p> <p>Float for 1st to 3rd 0900-1500</p> <p>19th/Madison 0700-1330</p> <p>20th/Madison 0700-1330</p> <p>21st/Madison 0700-1330</p> <p>Prime/float 0700-1500</p> <p>0530 Drove site checked cones/signs and stood up any knocked over</p> <p>0600 put in TCP #223</p> <p>0700 closed crosswalk on Madison at 1st</p> <p>Checked in new UPO's and made sure they knew what they were doing</p> <p>Informed Tawnya about right lane closure on 1st</p> <p>Put in Right lane closure at 17th on Madison EB an WB</p> <p>Made adjustments to closure to minimize the impact to buses</p> <p>Spoke with MEtro supervisor about the changes and he was ok with the way it was in</p> <p>Spoke with Eugene about in line bus stops in #223 closure made adjust to Jansen Inc.</p> |            |

taper at 18th on Madison EB to remove the in line stop per our conversation  
 Play of the day meeting  
 Canceled UPO's for next week on tcp #223  
 Drove site stood up cones  
 1300 took down tcp #223 for day  
 1330 removed right lane closure from Madison/17th  
 1500 opened right lane on 1st NB took down any signs not needed  
 Drove site again checked cones/signs stood up any knocked over  
 1530 Drove site checked Cones and signs stood up anything knocked over

1900 Checked out UPO's and Checked in new ones gave instruction on  
 what was expected  
 1200 drove site checked signs stood up anything knocked over checked on  
 UPO's

## Diary

Rogalski III, Floyd J. (ROGALSK,FLO)



### Note

### Note Index

Removed 4benches and 3 bike racks from NW side of Denny and Madison.  
 Unloaded and began assembling temporary ADA-ramps

## Diary

Solt, Bruce (SOLT,BRU)



Mild - (60 - 75); Drizzle

**Note****Note Index**

Civil 3 completed removal of existing inlet and pipe at NE corner of 1st and Madison to facilitate the installation of the new inlet #1. Received verbal confirmation to cut existing 8" ductile pipe east of conduit and duct bank and begin new installation there to inlet #1. Tawny said official email is forthcoming. Crew back filled trench and cold patched in front of ADA for the weekend. Jafra opened up crosswalk. First ave closure was taken down at 1500 per the spec.

Civil 6 continued with pot holing for ground water as directed in FM 001. Crew was able to break out last area and provac continued with vectoring. All activities were shut dow at 1100 by HNTB after notification that the archeology report needed to be completed. Also received word that the storm work will not take place pending further review of groundwater conditions encountered already in two of the potholes. Crew covered all holes, cleaned up the roadway and closure was reopened to traffic around noon.

---

No notes found



Date: 10/23/2021

 **Diary**

Pruss, Jafra (PRUSS,JAF)



| Note                                                                                                                                                      | Note Index |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| Drove site picked up signs from tcp#223<br>Stood up knocked over devices<br>0700 0900 1100 1300 1600 1900 2400<br>Checked in officers at 0700 and at 1900 |            |

Date: 10/24/2021

## Diary

Pruss, Jafra (PRUSS,JAF)



| Note                                                                                                                                                                                                                                                                                                    | Note Index |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| <p>Checked in upo 0700 drove site stood up knocked over devices</p> <p>Laid down No Parks due to high winds</p> <p>Doubled up cones due to high winds</p> <p>Added arrow sign a first and spring to make closure less confusing</p> <p>Drove site stood up knocked over devices 0700 1030 1500 1900</p> |            |

Date: 10/25/2021

## Diary

Mahan, Mark (MAHAN,MAR)



8:57 AM, Possible Drizzle, 53.56°F, 64% Humidity, 14.91 MPH Winds

| Note                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | Note Index |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| <p>Start at 6:00 am at Home Depot picking up materials needed for inlet install.</p> <p>Transport cold patch and pea gravel to 1st and Madison from 22nd and Madison.</p> <p>At 9:am closure was put in on 1st and Madison street and we started vibration monitoring and demoing roadway to install inlet 1B. At 9:08 am called Tawni Russell inspector with Exeltech to ask if we want to raise to new ductile iron pipe invert in existing Catch Basin as per the plans and break into the brick cone. Inspector said to demo existing inlet and tie into existing ductile iron pipe and not to disturb brick cone. Demoed roadway with 305.5 Caterpillar Excavator and breaker it took 2 1/2 hours to demo a 20 x 4 trench</p> |            |

and demo existing inlet with that small machine. Pothole by hand 2 electrical conduits rite next to existing inlet to remove inlet. Installed inlet 1B and 10.5 feet of 8 inch ductile iron pipe and 1 earthquake joint. Use 2 ferncos.

Cleaned up excavation and backfill and cold patched roadway and opened 1st street closure by 3:00pm. Clean up site and helped civil crew 3 cover their grade with plastic and sandbags to keep rain water off excavation.

---

Excavating to install inlet 1B and 8 inch ductile iron pipe.



Cold patching new inlet 1B and open closure.




Layout and start demoing for inlet 1B



Demoing existing inlet to install inlet 1B



Vibration monitoring on 1st street watermain.

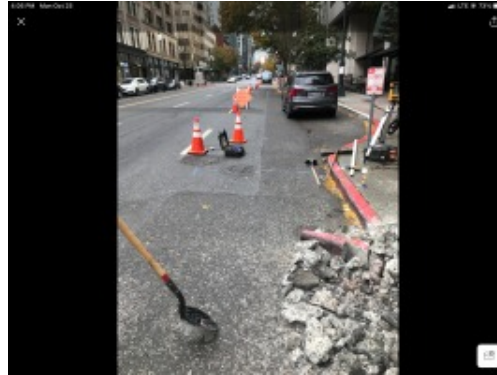


Demo roadway, curb and sidewalk to install inlet 1B.



1-4 inch steel and 1-2 inch pvc conduits rite next to existing inlet.



Backfilling and cleaned work area around inlet 1B.

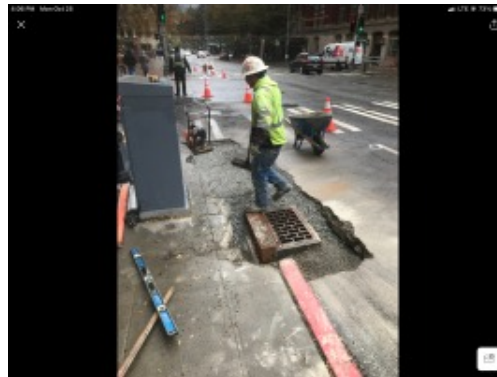

 Diary

Pellham, Austin L (PELLHAM, A)

 Very Windy; Overcast; Drizzle; Rain

| Note                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | Note Index |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| <p>Had a tough day today. Demo went very slow due to having machines that seemed undersized for the job at hand after realizing the breaker on the 310 didn't break deep enough to hit the last layer of concrete. Concrete removal varied in depth on each side of the excavation. Got the west side of the alley common ex and began over exing in one area after being instructed by Tawni Russell of exeltech and Jacob Schmidt of OSG. Stopped over exing after being instructed by Bruce to stop due to having no bid item for over ex. Covered all grade after trucks were signed out and grade was flattened out.</p> |            |

No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



 **Diary**

Pruss, Jafra (PRUSS,JAF)



| Note                                                                                          | Note Index |
|-----------------------------------------------------------------------------------------------|------------|
| put in modified tcp 199 closing both right lanes on Madison from 14th to 19th                 |            |
| 0900 put in TCP 92.a 1500 opened right lane removed any traffic control in way                |            |
| Metro supervisor moved cones from 2nd and Madison bus stop was already scheduled to be closed |            |
| Spoke with Jon R. About temp bus stop ramps not meeting ADA                                   |            |
| Jansen Inc.                                                                                   |            |

requirements had Floyd bring out new ramp and put in place

Informed Bruce that sidewalk and drop off on Spring street needed  
Delineation t-par was gotten and put in place

Also informed him that porta potty on 1st and Spring still needed to moved  
out of the right lane checked at end of night still in place told Austin he will  
move it in the morning

Crosswalk closure put in by Sean on 1st and Madison per Bruce informed  
him that it was not on TCP and that we needed to follow it

Gave breaks for UPOs

Put in lane shift on Spring from 2nd to 3rd for Prime Electric

Loaded signs for TCP 4 for Prime Electric

Placed sandbags on all signs and No Parks

End of day drove site to check all closures noticed crosswalk closure on 15th  
asked about it was informed that Austin put in place per Bruce informed that  
only traffic could install closures and that this was not per plan and not in  
correct either. Went to port picked up signs installed crosswalk closure with  
Detour.

Checked all signs and stood up knocked over devices

## Diary

Rogalski III, Floyd J. (ROGALSK,FLO)



Note

Note Index

Assembled temporary ped ramps at port  
Installed one at 17th and Madison

---

## Diary

Solt, Bruce (SOLT,BRU)



Cool - (45 - 60); Drizzle; Overcast

| Note                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | Note Index |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| <p>Civil 3 began roadway demo export today. All but one load of hard surfaces exported today. Common excavation was completed from 1st to west side of alleyway. Encountered an area 6' x 25' that will require overexcavation as well as a strip along the curb. Received verbal and email confirmation to proceed. As of this time we do not know any further details such as the use of fabric and type of materials to place. Email sent from Cameron with no response. Two signs were removed along curb and a Paystation will need to be coordinated for removal. Anticipate Cat 315 to be delivered tomorrow.</p> <p>Civil 5 arrived on-site today to begin their work in zone 3 starting with Inlet 25. Crew was able to remove all hard surfaces over trench line breaking with the Hitachi 85. Crew will not have their full closure in place until Wednesday now with PRIME working on temp signals on both sides of the road at 16th. All materials except for bricks brought out to the site.</p> <p>Civil 6 began breaking trench line this morning for inlet 1 on 1st street. Received direction from HNTB to connect to the existing 8" ductile short of the cb to avoid disturbing the brick structure. Crew was able to complete the installation, bedding, backfill and temp patch pave before 3 pm to open the road.</p> |            |

No notes found



No notes found



No notes found



 **Diary**

Waldrop, Austin L. (WALDROP,AUS)



| Note                                                      | Note Index |
|-----------------------------------------------------------|------------|
| Load up inlet type 250 B and 8" di pipe at the port       |            |
| Get equipment mobilized in to closure at 15th and Madison |            |
| Deere 135 with attachments                                |            |
| Deere 85 with attachments birch equipment                 |            |
| Cat 938 loader from 1st ave                               |            |
| Break trench line and demo.                               |            |

Demo existing inlet on corner of 15th

Excavate for inlet 25 at 15th

Deere 135 excavator had small hydraulic leak coming from underneath.  
Pertek came out and fixed it.

Load up grout and plastic at port for tomorrow's work

---

*No notes found*



*No notes found*



Date: 10/26/2021

 **Diary**

Mahan, Mark (MAHAN,MAR)



Rainy overcast

**Note****Note Index**

Loaded up at port fabric and Caterpillar 315 breaker for Civil group 3 on spring street.

Started breaking roadway demo at 08:00am on 1st and Madison street with Caterpillar 308 excavator.

PC0009.01 Force Account-Crew went to 3rd and Madison at 11:00am to break concrete under sidewalk that was removed for Prime electric to pothole pole foundation. Was called back at 12:00pm that concrete continued so Bruce Solt had a crew of 2 guy take backhoe up and they broke out concrete until 4:00pm and then they were told to stop. Sent Tawni Russell a text about concrete in pothole at 1:30pm that we were working on it and will be tracking it with force account. Then at 3:00pm I talked to her on Spring street and she said that she called her boss Shawn and the we should have stopped and sent a RFI to move forward.

At 11:00am Birch equipment brought PC138 Komatsu excavator with digging bucket. Than at 12:15pm a third party brought the wrong breaker and the clean out bucket for the machine. I sent the breaker back to Birch equipment.

Took 315 Caterpillar excavator from Civil group 3 on spring street to get breaking on 1st and Madison street. Operators misunderstood layout and broke on the wrong side of saw cut for about 16 feet. Broke out most of roadway and curbs for trucking tomorrow. Will remove 4 pieces of granite curb to be reclaimed for city.

Stayed with Civil group 3 to help them excavate under CDF in trench line and excavate for ITS vault tomorrow.

Demo roadway with excavator



Demoed wrong side of saw cut



Demoed wrong side of sawcut 1st and Madison street



3rd and Madison street potholing



Demo concrete obstruction in Prime electric pothole



PC0009.01 obstruction in pot hole at Southwest corner of 3rd and Madison street



3rd and Madison potholing



New operator moved rental excavator and chipped curb we are to save.



Demo roadway at alley looking west on Madison to 1st street.



## Diary

Pellham, Austin L (PELLHAM, A)



Cool - (45 - 60); Overcast; Drizzle; Very Windy

### Note

### Note Index

Started the day with loading pumps and generator at the port to pump water from excavation, removed plastic. Began roadway demo at the top of spring street. Moved down to the alley and removed roadway and curb around SCL vault to open up as much as possible for ITS ditch. Had some force account for over ex at the bottom of the hill. Tawni to review EWO tomorrow morning. Removed and salvaged granite curb at the bottom of the hill. Began digging ITS ditch at alley up towards 2nd. Hit a lot of CDF but moved the ditch behind curb to a line the worked till we hit a un-located ductbank. Called Tawni and she sent down Wayne to begin tracking force account to hand

tunnel the duct bank to run ITS under. Then dug back each side with the 305 to run lines under. Continued digging up the hill to the type 5 box at the 2nd and spring intersection. Had to work late in order to be ready for Prime Wednesday morning.

---

*No notes found*




*No notes found*



*No notes found*



No notes found

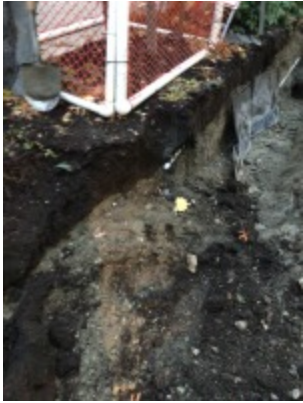

No notes found




No notes found



No notes found



No notes found

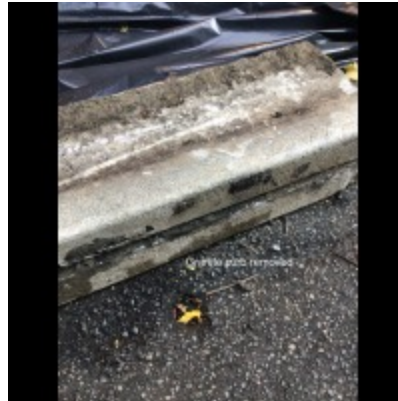

 Diary

Pruss, Jafra (PRUSS,JAF)



No notes found



 Diary

Rogalski III, Floyd J. (ROGALSK,FLO)



| Note | Note Index |
|------|------------|
|------|------------|

Unloaded trucks at the port

Jansen Inc.

Assembled 3 temporary curb ramps, at the port.

## Diary

Solt, Bruce (SOLT,BRU)



Cool - (45 - 60); Partly Sunny / Cloudy; Rain

### Note

### Note Index

Civil 3 completed common ex and majority of the over excavation as directed by HNTB. Crew removed all of granite curb features slated for salvage in the plans. A small portion of over excavation remains closer to the corner of 1st near curb line. Crew began excavating for ITS at alley way between 1st and 2nd on south side of Spring. Encountered a ductbank running up road. Crew was able to dig ditch behind curb with 2 ft of bury to the east. Encountered an unlocated ductbank in conflict with trenching. DSC sent out by our team and was quickly answered to excavate deeper and go under. Time to be tracked on FA. Installation and inspection scheduled for tomorrow morning.

Civil 5 completed roadway breaking on curb lane from 15th -16th on north side of Madison today. Crew skipped over driveway into 7/11 and stopped short of crosswalk at 16 th. While excavating for 8" removal and reinstall action of storm pipe an unlocated 3" conduit was encountered and damaged. Office notified and DSC sent, awaiting response. Crew fully exposed conduit and was still able to complete the installation of the ductile run,bed and backfill as well. Portion of storm run sheeted for the night awaiting repairs by PRIME in the morning.

Civil 6 completed roadway breaking from 1st to 2nd on the north side of Madison. Instructed crew to break all roadway out in front of alleyway as directed to me. Salinas scheduled for sawcutting in the morning for this portion. While Mark was up taking care of pot holing for PRIME some of the roadway outside of demo limits was broken by new crew. Panels were already cut and marked, crew missed where line jogged in necking down to one lane. Potholing demo for PRIME continues with completion of 3rd and Jansen Inc.

Spring pothole and commencement of potholing at SW corner of 3rd and Madison. Crew had to return twice for more breaking as additional concrete obstructions were found. Finally pulled crew of when they encountered thick concrete with rebar reinforcement. Extra time to be tracked under DSC submitted to SDOT.

---

*No notes found*



*No notes found*



*No notes found*



No notes found



No notes found



No notes found



No notes found



 Diary

Waldrop, Austin L. (WALDROP,AUS)

**Note****Note Index**

Set inlet #25 type 250 B at 15th

Remove old inlet and ductile iron pipe

Trench for new pipe to be installed

While trenching we struck and broke an unmarked 4" conduit that had no wires only mule tape in it. I talked with Bruce and he got with Jeremy from prime to get it fixed. Jeremy did not have parts to fix until tomorrow. We dug up and exposed conduit so that it can be repaired. I made sure with Jeremy that it was ok if we still installed are 8" DI pipe and sent him pictures of what it would look like, he said yes he can still fix conduit with pipe installed.

Wayne from HNTB said to just tie are pipe into existing DI earthquake joint in existing manhole. Email should have been received.

Jack broke roadway for tomorrow's work

Install 36' 8" DI pipe from new inlet to existing manhole.

Bed pipe with pea gravel and finish backfill with type 17.

Steel sheet over section we could not backfill due to broken conduit.

Talked with Sean Woodbridge about keeping crosswalk closed for over night and will finish tomorrow with cold mix and re open crosswalk.

No notes found



No notes found



No notes found



No notes found




No notes found



No notes found



No notes found

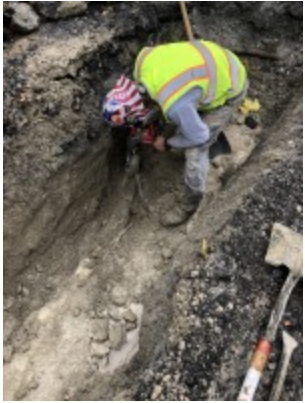

No notes found



No notes found



No notes found



Date: 10/27/2021

## Diary

Hill, Theodore J. (HILL,TJ)



### Note

### Note Index

Today we Jeff Landre and I walked the job and started to game plan for starting up concrete next week. We picked up forms at 3rd and Denny and went to the port to unload materials and access what other items and products we may need.

## Diary

Landre, Jeffrey (LANDRE,JEFF)



### Note

### Note Index

Check out job site.

## Diary

Mahan, Mark (MAHAN,MAR)



### Note

### Note Index

Pothole 2 utility pole on Madison street mid street north and south between

Jansen Inc.

HeavyJob | <https://heavyjob.hcssapps.com/> | 855-231-7878

5th and 6th street for Prime electric.

1st and Madison- finished demoing roadway concrete. Loaded out 270 square yards of concrete demo and 1-20 yard load of common excavation. While excavating roadway concrete averages 15 inches thick. While common excavation averages 3 inch so far.

East west surveyed saw cut on joint line was off from 6 inches from actual joint from 1 street to 2nd street where 2 in grind and over lay is scheduled to be done. Notified Exeltech inspector Tawni Russell and Jansen Madison managers that this will need to be addressed.

---

Demo concrete roadway at 1st and Madison  
mixed load of bricks concrete and asphalt.



Pinned steel sheets to roadway



Loading out roadway demo under trolley lines into  
OMA side dumps



Broke out sidewalk for pothole mid block on Madison between 5th and 6th streets north and south.



Potholing Prime electric



Loaded out mixed load of asphalt, concrete, bricks, wood, gravel and dirt from intersection of 1st and Madison street old road under band-ade



Started to common excavate



Loaded out 1 load of common ex.



Loading out roadway demo at alley.



Covered subgrade for weather coming on Thursday.



## Diary

Pellham, Austin L (PELLHAM, A)



Cool - (45 - 60); Overcast; Drizzle; Normal Ground

### Note

### Note Index

Finished digging ITS ditch and had pipe installed by prime. Inspected at 1230. Backfilled. Began digging common ex between alley and 2nd ave. Ran into numerous ductbanks in the way of digging sub grade. Began tracking force account to scrape down CDF to grade but it was too ineffective to continue. Awaiting guidance to move forward on digging sub grade. Set up erosion control and stabilized the site for incoming rain storm.

No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



## Diary

Solt, Bruce (SOLT,BRU)



Cool - (45 - 60); Overcast

| Note                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             | Note Index |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| <p>Civil 3 complete backfilling of ITS trench after installation by PRIME and positive inspection by Ray with SDOT signals. SCL network crew on-site this morning previewing inside vault just east of alleyway on Spring. Crew chief let us know that conflicting ductbank for ITS run was 16" below top of vault lid. We will not be able to achieve our minimum bury depth to cross alleyway and they will not let us trench under their ductbank. Jon with HNTB present an would talk with SDOT about changing to a rigid conduit to cross alley as there exist many other utilities to get to the other side. Crew also encountered high strength CDF poured to within two inches of finis grade the</p> <p>Jansen Inc.</p> |            |

length of or common excavation that the 315 could not scrape down. Awaiting reply on how to proceed. Type 2 imported for sub grade. With delays crew was not able to get as much as anticipated done.

Civil 5 completed roadway demo between 15th and 16th skipping over driveway into 7/11 and stopping short of crosswalk at 16th. PRIME was finally able to get conduit repaired and crew back filled and temp patched trench line. Crosswalk opened and crosswalk at 16th closed by shifts end. Crew will be able to demo to desired point on Friday. Common excavation was completed from 7/11 to the east end of demo. All sub grade was suitable.

Civil 6 was able to get most of the roadway demo out today as well as a good portion of the common excavation. All sub grade looked good so far, no over excavation required. Upon removing concrete panel closer to 1st and along saw cutting, it was discovered to have another joint line 6" to the south that will need to be removed.

All crews shut down for weather anticipated to roll in tonight depositing a lot of rain. Work zones covered and secured at end of shift.

---

No notes found



No notes found



No notes found



No notes found



No notes found



 Diary

Waldrop, Austin L. (WALDROP,AUS)

**Note****Note Index**

Remove pavement in curb lane starting at 16th heading west skipping driveway to 7/11

Change the bit on breaker to 135 excavator

Saw-cut centerline. Talked with Bruce and we decided to saw-cut past the panels that stay due to limited width of roadway. Extra 60' of saw-cut

Prime fixed broken unmarked conduit at 15th.  
Finished backfill on storm and cold patch so traffic control could open crosswalk at 15th.

Pothole utilities by shovel

Common excavate starting at 16th to 7/11 driveway

Jacob Schmidt checked sub-grade with probe. Said sub-grade was good, no over excavation needed.

Import type 2, spread and compact

Cover grade with plastic.

Clean site and prep for weather conditions

No notes found



No notes found



No notes found



Date: 10/28/2021

 **Diary**

Pellham, Austin L (PELLHAM, A)

 Rained Out

| Note                             | Note Index |
|----------------------------------|------------|
| Rained out all crew stayed home. |            |

 **Diary**

Solt, Bruce (SOLT,BRU)



Mild - (60 - 75); Partly Sunny / Cloudy; Rain

## Note

## Note Index

All crews home today for foul weather. Day spent planning and scheduling.  
Site looks good.

---

Date: 10/29/2021

## Diary

Brickman,Joshua (BRICKMA,JOS)

---



Cool - (45 - 60); Sunny; Partly Sunny / Cloudy; Normal Ground

## Note

## Note Index

Foreman meeting at 0600. At 0730 fire up 85 and switch over to breaker.  
Break out pot hole location for prime on west side of 7/11 then at 0845 broke out pothole for pole just east of 7/11. Then at 0900 moved plate for pro vac at 20th to start first pothole. Cleaned up concrete rubble. At 1100 moved plate for second pothole by 20th. Broke out to end of rail road ties to verify no rail on top of ties. At 1400 moved backhoe back down to 2nd then gave tanner ride back up to his truck. 1530 met with Bruce to go over demo and plans for bus foundation on 1st. 1630 went to port to load up fin form and t bar. Left port at 1800.

---

FA -



## Diary

Hill, Theodore J. (HILL,TJ)



| Note                                                      | Note Index |
|-----------------------------------------------------------|------------|
| Today we worked on the the office walls mounting plywood. |            |

## Diary

Mahan, Mark (MAHAN,MAR)



Raining in AM cleared off around 10:30AM

| Note                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | Note Index       |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|
| First Oma truck didn't show until 8:45am on 1st and Madison Jansen truck showed up last in line and last load of the day                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      | EQPVAN -<br>FA - |
| Excavated 223 feet of ITS trench from 1st street to 2nd street with all obstructions listed below                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             | VIS-INSP -       |
| <p>Force account PC0014.01 ITS Obstructions Madison 1st to 2nd North, encountered 4 unlocated gas lines, 1 unlocated 3 inch electrical conduit at station 201+60, an abandoned electrical vault and electrical ductbank with 8 3 inch steel conduit encased in concrete at station 201+50, 6 inch cast iron sewer pipe unhooked from 6 in clay side sewer pipe, abandoned 10 in side sewer pipe, 3 inch steam pipe at station 201+60, 4 inch gas main at station 201+55, CDF encased water main at station 202+35, abandoned cable car yoke filled with CDF at station 202+40</p> <p>Demo roadway and loaded out 153 square yard of demo.</p> |                  |

Cutting subgrade to excavate ITS trench.




Move cold patch berm to top of second and Madison to divert rain water around work zone.




Unlocated gas line and sewer pipe out of sewer manhole not connected clay sewer pipe.




6 inch sewer pipe not connected to clay sewer pipe

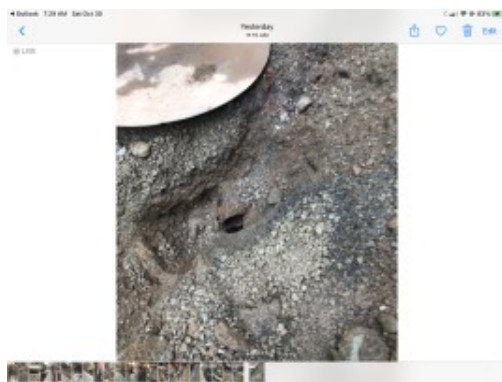


Unlocated 3 inch electrical conduit at station 201+60 PC0014.01

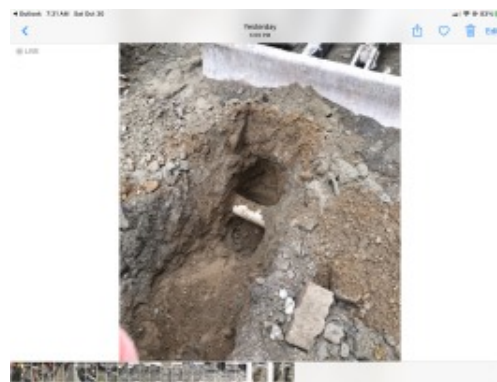


CDF block at station 202+40 EC05 plans sheet said there was a abandoned cable car yoke in this area.

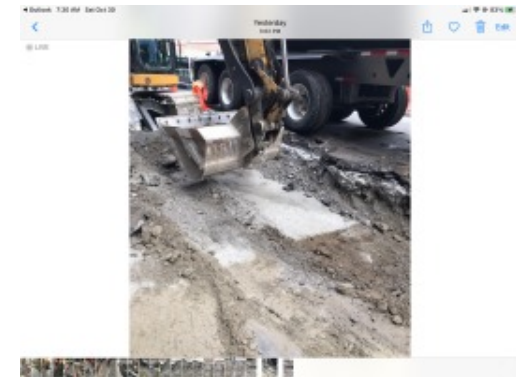


PC0014.01 CDF encased water main and valve at station 202+35

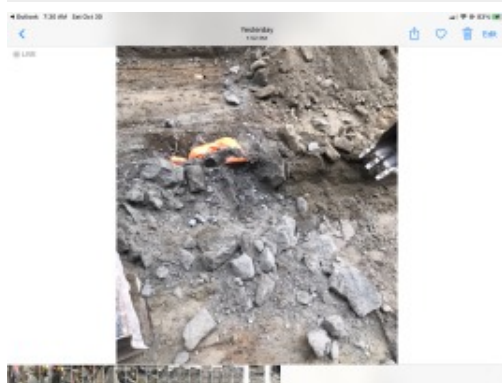

PC0014.01 Pro Vac hydro excavating obstructions in ITS trench

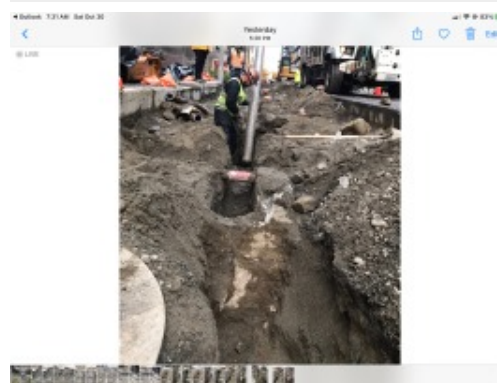

Excavate ITS trench from 1st to 2nd on Madison North.

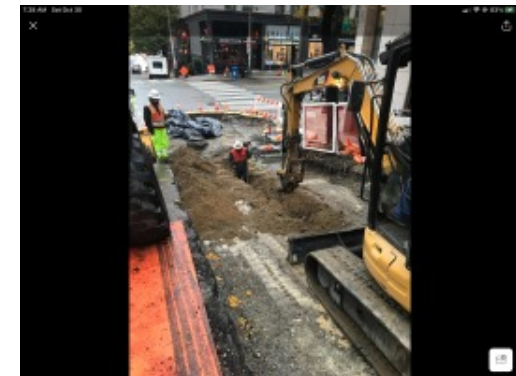

Old and new pole foundations in new curb line



ITS trench Madison street



Granite curb foundation North side of Madison at station 200+62 to 200+82 and 201+00 to 201+60 that need to be remove for new curb.




Load out roadway demo and cleaning around water valve.



ITS trench heading east on Madison from 1st street.



308 Caterpillar excavator cutting sub grade common excavation

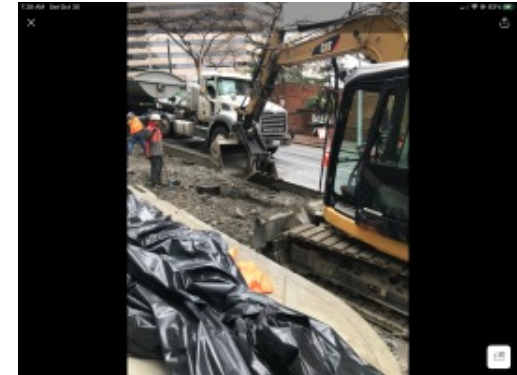


Loading out roadway demo



Curb to be saved at station 240+00 north is falling out from under sidewalk while demoing roadway and excavating subgrade




Water line and valve in cased in CDF, PC0014.01 vac truck hydro excavate ITS trench.

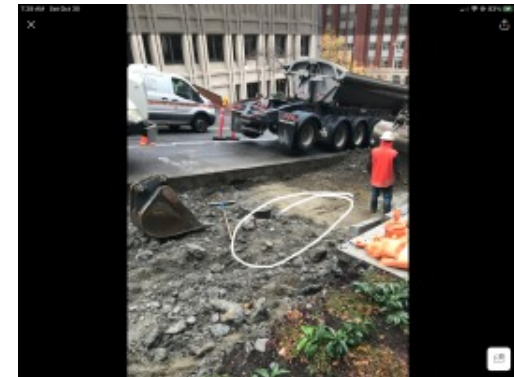


Yellow 3 unlocated gas lines, blue 12 inch cast iron water main, purple abandoned electrical vault and 8-3 inch abandoned steel conduits incased in




Unlocated gas line in front of 6 inch sewer pipe not connected to clay sewer pipe.

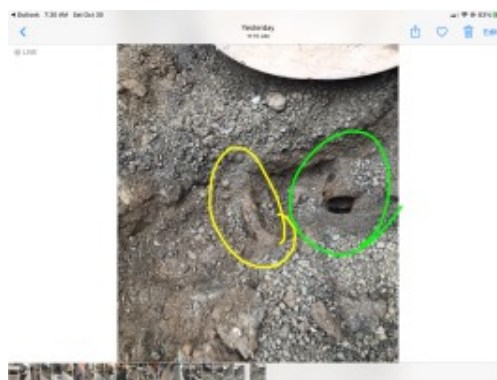


Concrete obstruction next to sewer manhole found that it is an abandoned electrical vault. PC0014.01

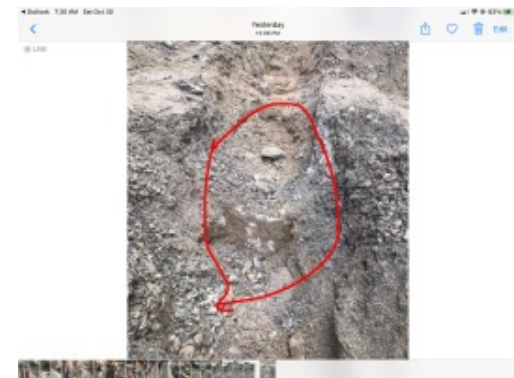


PC0014.01 red abandoned electrical conduit and duct bank, green unlocated abandoned sewer, yellow 4 inch gas main, white steam line at station

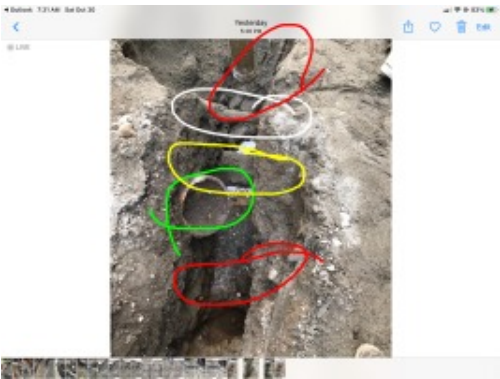

PC0014.01 yellow unlocated gas pipe, blue after main, green 6 inch unconnected sewer pipe from sewer manhole.

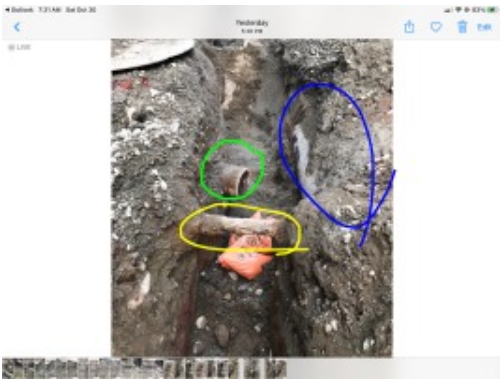

PC0014.01 red abandoned electrical ductbank removed conduit, white stem pipe.

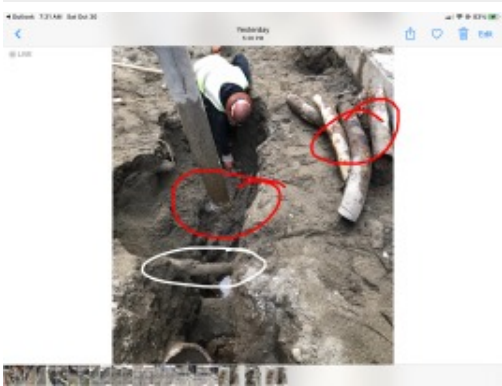

# Diary

Pellham, Austin L (PELLHAM, A)

 Cool - (45 - 60); Rain; Overcast; Ground Wet - Workable

| Note                                                                                                                                                                                                                                                                   | Note Index |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|
| <p>Began day with over ex on spring near 1st along curb line 20x1.5x1. Shawn and Daniel began scraping down CDF to sub grade, tracked as FA. Began Demo on the second lane between 1st and 2nd. Type 2 on all sub graded surfaces/prepared for trucking on Monday.</p> |            |

No notes found



No notes found



 Diary

Rogalski III, Floyd J. (ROGALSK,FLO)



| Note                                                                                                                                        | Note Index |
|---------------------------------------------------------------------------------------------------------------------------------------------|------------|
| 6am meeting<br>Removed 4 signs and 3 posts from the south side of Spring between 1st and 2nd.<br>Assembled temporary curb ramps at the port |            |

 Diary

Solt, Bruce (SOLT,BRU)



Cool - (45 - 60); Rain; Overcast; Partly Sunny / Cloudy

## Note

## Note Index

Civil 2 completed all potholing for FM 001. Waterline potholing was called off mid morning. Crew also broke out two locations for PRIME to pothole for foundations. First at 15th and second at 16th. Moved equipment around to set up for Monday. Took Josh to work zone on 1st between Madison and Spring St to show him his activities for Tuesday. Civil 2 will not be working Monday as Josh has court to attend.

Civil 3 completed all EWO with the over poured hsftb in road sub grade today. Over excavation completed near curb line on anEWO sheet as well. Type 2r imported and placed on inside lane to accommodate trucks for Monday hauling of roadway demo. Civil 3 was able to get two loads of demo hauled out, some common excavation and all salvaged granite curb.

Civil 6 completed haul out of roadway demo this afternoon. Common excavation completed up to near the end of the curb lane. ITS trenching completed for the length from back of curb to back of curb 1st to 2nd on Madison. One obstruction remains at the alleyway that will get removed on Monday morning. The short trench will also be done Monday that crosses Madison at west side of intersection of 2nd Ave. Numerous unlocated or abandoned utilities and large amounts of CDF were encountered, primarily from the alleyway to the east up Madison. All obstructions backed up with emails to manager group and HNTB present and acknowledges the conflicts. Mark tracked all the extra effort on an EWO sheet. PROVAC on-site to facilitate getting thru some of the areas. Crew was able to get through all of this with no collateral damage.

No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



No notes found



Date: 10/30/2021

## Diary

Pruss, Jafra (PRUSS,JAF)



| Note                                                                                              | Note Index |
|---------------------------------------------------------------------------------------------------|------------|
| 0730 picked up knocked over signs and cones                                                       |            |
| 0815 SCL on site                                                                                  |            |
| 0820 first manhole 1st and spring 2nd crew on spring and 3r in closure                            |            |
| 0830 Second manhole 1st and Madison                                                               |            |
| 0845 Rainer asphalt on Madison and second in lane shift restricted part of crosswalk in left lane |            |
| 0845 3rd manhole spring                                                                           |            |
| 0900 4th manhole 3rd and Madison                                                                  |            |
| Jansen Inc.                                                                                       |            |

0910 Rainier asphalt gone opened lane they closed  
0930 5th manhole on Madison north side north side between 3rd and 4th  
1000 6th manhole south side on Madison between 3rd and 4th  
1015 2nd SCL crew moved to spring between 1st and 2nd  
140 SCL back at 3rd and spring  
1500 SCL done

0600/1300/1700/2200 Drove site checked site

---
