SDOT
Seattle Department of Transportation

Submittal Transmittal & Response

Shaded areas are for SDOT use only

Submittal Number: 859 Date: 9/18/2025

Contract Name: Rapid Ride J Line Bus Rapid Transit **PW #:** 2023-002

Contractor: Jansen Inc. **Fed Aid #:** WA-2024-012-00, WA-2024-013-00, WA-2023-070-00

The Contractor submits the following noted attachments to Engineer for review and response:

Sub Item#	Bid Item # (or Spec Sec #, if no bid #)	Description	SDOT Response
1	9	CPM Update 11 - 08.2025	
2			
3			
4			
5			
6			
7			
8			
9			
10			
11			
12			

Submitted by: ☐ Resubmittal ☐ Supplemental Submittal

Austin Byron — Printed Name
Title
510-340-0187 — Phone #

The Engineer has reviewed the above noted documents and responded as noted above, under "SDOT Response".

Key:
- **NE** = NO EXCEPTIONS TAKEN
- **MC** = MAKE CORRECTIONS NOTED: No resubmittal required, but corrections noted are required
- **SI** = SUBMIT SPECIFIED ITEM: Resubmittal required – rejected, see comments below
- **RR** = REVISE AND RESUBMIT: Resubmittal required – rejected, see comments below
- **RJ** = REJECTED – see comments below

Note: Review is only for conformance with the general design concept of the Project and does not extend to consideration of structural integrity, safety, detailed compliance with Contract requirements and any other obligation of the Contractor. Any action shown is subject to the requirements of the construction Contract. Contractor is responsible for confirming and correlating all dimensions; fabricating and construction techniques; coordinating its work with that of all other trades; and the satisfactory performance of its entire work in strict accordance with the construction Contract. The review is undertaken solely to satisfy Engineer's obligations and does not relieve Contractor from its obligation fully to perform all Contract requirements, nor shall such review give rise to any right of action or suit in favor of Contractor or third persons, against the Owner. Comments or actions may not be complete, once non-compliance is documented, the review may be discontinued and the submittal rejected.

Engineer's Comments and Sign-off:

# (key to above)	Comments
1	

Engineer Signature	Printed Name & Title	Date

☐ See Attached Engineer's Comments ☐ See Mark-Up of Submittal Documents ☐ See Other Attachments

RapidRide J-Line Bus Rapid Transit

UPDATE: #11 August 2025

PROJECT NAME: RapidRide J-Line Bus Rapid Transit

SCHEDULE CUTOFF DATE: 9/08/2025

NTP: 10/07/2024

SUBSTANTIAL COMPLETION: 4/01/2027

PHYSICAL COMPLETION: 5/03/2027

PROJECT COMPLETION: 5/06/2027

ORIGINAL CONTRACT COMPLETION DATE: 03/24/2027

CONTRACT WORKING DAYS: 594 DAYS

APPROVED TIME EXTENSIONS: 40 DAYS

PROJECT STATUS

In August work on the RapidRide J-Line project progressed in all 4 Zones. Work in these zones has been centered on watermain work, electrical, and roadways. OCS foundation installation has continued in the University district.

We continue to update the project schedule in a proactive and proficient manner via weekly meetings that coordinate management staff and field personnel in regard to both the tactical and strategic (master CPM) requirements. Reliable monthly updates and TIA's have been submitted in a timely fashion. As-built dates and network logic accurately reflect work performed along with a near-term forecast that aligns the master CPM schedule with the installation and sequencing realities.

Note that in March 2023 (v.022M) the critical (longest) path transitioned from Zone-3 to Zone-4 (storm). In subsequent updates, up through the previous v.037M JUL 2025 update, the longest path continued to run through Zone-4 (LPTF = [-22]). However, in this update (v.041M) the CPLP has shifted from Zone-4 to Zone-1 – reflecting a 3 WD impact (to-date) due to the status and progress related to pole foundations (LPTF = [-25]). See related TIA #19. Please refer to previous narratives for contemporaneous details associated with a particular update.

The critical/longest path in the J-Line project schedule has shifted from Zone-4 to Zone-1 due to a combination of factors. Negative float on the longest path has increased from [-22] (running through Zone-4 in the v.037M JUL monthly update) to [-25] in Zone-1 (per the current v.041M monthly update). The source of the impact stems from slippage related to Zone-1 pole foundations during the month of August (additional directed potholing and DSC's) that have now extended the critical/longest path. Note also that Zone-1 was previously delayed by storm DSC's (via Design Change 055) although, at the time,

these earlier Zone-1 changes/delays were not driving the longest path. Prior to this update, the longest "most critical" path was controlled by Zone-4 ductbank issues per FM 152 (going back to the v.028 mid-May update and even prior to that; i.e., mid-March v.020 Zone-4 storm).

It is important to note that in the baseline schedule, Zone-3 was "critical" although float in the other zones was also limited. We recognize that, similar to Jansen's mitigation efforts related to the ongoing Zone-4 ductbank issue (i.e., whereby LP negative float was reduced by 69 WD from [-91] in the v.033 update to [-22] in the v.037M JUL update) there may be opportunities to undertake similar mitigation strategies in Zone-1 with coordination and agreement with the owner.

However, it is important to note that Jansen is being transparent in this process and we feel that the best approach is to report schedule slippage on an "apples-to-apples" basis – keeping the downstream baseline network definition intact for initial TIA reporting purposes. This makes the analysis (and any subsequent restorative or remedial actions) relatively simple to understand as the variables are minimized and controlled in a stepwise fashion. Once an impact/delay is initially quantified in this manner, then it is imperative that SDOT and Jansen work together cooperatively to analyze and "exercise" the schedule (i.e., via a joint scheduling meeting) whereby mutual agreement/concurrence can be reached in regard to feasible mitigation possibilities and/or combinations of mitigation, acceleration, time extension, etc. We do not want to make unilateral CPM network adjustments (of a strategic nature) in isolation behind the scenes – which can sometimes be rather complex (along with the related assumptions) – and then try to "fully explain" in writing (to individuals who were not participating in the process) something that is typically very dynamic and interactive. Jansen is committed to working together with SDOT to effectively manage the schedule – and we have a very good/robust schedule to use as a tool for this purpose. At the moment, we are simply reporting an "apples-to-apples" situation with the intent of gaining a shared understanding of the what/why – and then, together, we can craft a workable path forward. See TIA #19 for additional details.

J-LINE LPTF Recap:

a. v.027M (thru TIA #12) = [-5] / Stop Work FM 152.
b. v.028 TIA #13 @ -3 WD = [-8] / Stop Work FM 152.
c. v.029 TIA #14 @ -5 WD = [-13] / Stop Work FM 152.
d. v.030 TIA #15 @ -6 WD = [-19] / Stop Work FM 152.
e. v.030M @ +4 WD = [-15] / duration reduction ID# M-9006 (per SDOT TIA reviews).
f. v.031 TIA #16 @ -5 WD = [-20] / Stop Work FM 152.
g. v.032 TIA #17 @ -5 WD = [-25] / Stop Work FM 152.
h. v.033 TIA #18 @ -66 WD = [-91] / Stop Work FM 152 (SDOT SL No. 033).
i. V.034M @ +8 WD gain = [-83] / SUBM-0679 SDOT review comment response.
j. v.035 & v.036 @ +68 WD = [-15] / (wkly. / SDOT mtg.) mitigation @ Zone-4 Fairview (early start east side).
k. v.037M @ -7 WD = [-22] / account for TC rqmts. in Zone 4 not included previously; Note Zone-1 @ [-20].
l. v,038, 039 & 040 = [-22] / holding the line in Zone-4 (per SL No. 33) and also in Zone-1.
m. v.041M / TIA #19 @ -3 WD = [-25] / CPLP to Zone-1; Z4 remains @ [-22]. Note: Z3 now @ [-17].

Also in this regard, please note the longest and near-critical (independent) paths as follows:

Zone-1 = [-25] / Pole Foundations & Sidewalks
Zone-4 = [-22] / FM 152 Fairview Ductbank, Storm, Roadway, Sidewalks, etc.
Zone-3 = [-8] / Roadway (DSC-309); see weekly v.042 update [-17]
Zone-3 = [+6] / Stage2 & Stage 3 water

Current Period Progress / High-Level Recap:

ZONE-1:
- SDOT directed potholing
- Roadway construction/paving is ongoing (Roosevelt/43rd)
- Pole foundations, potholing, DSC's Stop-work (see TIA #19)
- Sidewalks starting on 9/8/25 (see TIA #19)

ZONE-2:
- Water Stage-1 complete
- Water Stage-2 in-progress
- Roadway construction/paving @ Harvard & Shelby
- Sidewalks @ Fuhrman (DSC-308)

ZONE-3:
- Water Stage-5 complete
- Water Stage-6 in-progress
- Roadway construction/paving @ Galer/Garfield
- Roadway construction/paving @ Garfield/Howe (DSC-309; TF=[-8])

ZONE-4:
- FM 152 Ductbank ongoing through 9/30
- Storm re-start 10/1/25 Aloha to Valley
- Eastside Elec UG and Paving (Yale, Aloha = east side) w/DSC's
- Pole Foundations starting (coordinated with Zone-1 down-time)
- Sidewalks - Yale

Other Notes:
1. NCR's have been added per SDOT instructions/request
2. Updating and populating codes and resource assignments (ongoing; WIP)
3. As-built record data is excellent as evidenced by the inclusion of the NCR's
4. Network logic is adjusted/revised to reflect as-built

SCHEDULE LOG:

UPD / VERSION	Period Impact	LPTF (*)	Comments / Remarks
v.014M JAN (03-FEB-25)	**-11**	**-11**	**January 2025 Update - Days Impacted/Requested**
		+8.5	Impacts Recognized by SDOT (JAN Update)
		-2.5	**SUBTOTAL / Carryover**
v.015 (10-FEB-25)	-2	-4.5	TIA #7
v.016 (17-FEB-25)	-4	-8.5	TIA #8
v.017 (24-FEB-25)	+2	-6.5	ID# 3-ST-1001 DUR 2 WD accel; 0.5 TBD per (TIA #6)
v.018M FEB (03-MAR-25)		**-6.5**	**LPTF = [-7]; Checks (CPM is based on whole-day durations)**
		+3	**Impacts Recognized by SDOT (FEB Update)**
		-3.5	**SUBTOTAL / Carryover**
v.019 (10-MAR-25)	-2	-5.5	TIA #9; LPTF=[-9]; Zone-3
v.020 (17-MAR-25)	0	-5.5	CPLP transitions to Zone-4 Storm [-9]
v.021 (24-MAR-25)	-4	-9.5	TIA #10; LPTF = [-13]
v.022 (31-MAR-25)	+2	-7.5	TIA #10 (revised); LPTF = [-11]
v.022M MAR (31-MAR-25)		**-7.5**	**LPTF = [-8]; Checks (CPM is based on whole-day durations)**
		+6	**Impacts Recognized by SDOT (MAR Update)**
		-1.5	**SUBTOTAL / Carryover**
v.023 (07-APR-25)	-1	-2.5	TIA #11; Zone-4 DSC-164 / CB C21
v.024 (14-APR-25)	0	-2.5	weekly update
v.025 (21-APR-25)	0	-2.5	weekly update
v.026 (28-APR-25)	-3	-5.5	TIA #12; Zone-4 as described (est. dates aligned w/5/5/25 weekly update)
v.027 (05-MAY-25)	+1	-4.5	Recovery of 1 WD based on 6 WD granted vs. 7 WD request (MAR v.022M)
v.027M APR (05-MAY-25)		**-4.5**	
		+4	**Impacts Recognized by SDOT (APR Update)**
		-0.5	**SUBTOTAL / Carryover**
v.028 (12-MAY-25)	-3	-3.5	Weekly update; TIA #13; Zone-4 Stop Work / FM 152
v.029 (19-MAY-25)	-5	-8.5	Weekly update; TIA #14; Zone-4 Stop Work / FM 152
Memorial Day (26-MAY-25)	no update this week; holiday		
v.030 (02-JUN-25)	-6	-14.5	Weekly update; TIA #15; Zone-4 Stop Work / FM 152
v.030M MAY (02-JUN-25)		**-14.5**	
		0	**Impacts Recognized by SDOT (MAY) Update)**
v.031 (09-JUN-25)	-5	-19.5	Weekly update; TIA #16; Zone-4 Stop Work / FM 152
v.032 (16-JUN-25)	-5	-24.5	Weekly update; TIA #17; Zone-4 Stop Work / FM 152
v.033 (23-JUN-25)	-66	-90.5	Weekly update; TIA #18; Zone-4 Stop Work / FM 152 (Per SDOT SL No. 033)
v.034 (30-JUN-25)	0	-91*	Weekly update; Zone-4 Stop Work / FM 152
v.034M JUN (30-JUN-25)	**+8**	**-83***	Schedule revs. per SUBM-0679 SDOT review **(8 WD gain/mitigation)**
		0	**Impacts Recognized by SDOT (JUN) Update)**
v.035 (14-JUL-25)	0	-83*	Weekly update; Zone-4 Stop Work / FM 152
v.035x (21-JUL-25)	+2	-81*	Weekly update; Zone-4 Disconnect South of Mercer
v.035y (21-JUL-25)	+66	-15*	Weekly update; **Zone-4 Fairview East Re-Sequence / Jansen Mitigation**
v.036 (28-JUL-25)	0	-15*	Weekly update
v.037 (04-AUG-25)	-7	-22*	Weekly update; TC Re-sequence for east side sidewalks vs. Ductbank completion
v.037M JUL (04-AUG-25)	**0**	**-22***	**61 WD overall mitigation**
		0	**Impacts Recognized by SDOT (JUL) Updates)**
v.038 (11-AUG-25)	0	-22*	Weekly update; Zone-4 Fairview Ductbank (FM 152; SDOT SL No. 033)
v.039 (18-AUG-25)	0	-22*	Weekly update; Zone-4 Fairview Ductbank (FM 152; SDOT SL No. 033)
v.040 (25-AUG-25)	0	-22*	Weekly update; Zone-4 Fairview Ductbank (FM 152; SDOT SL No. 033)
v.041 (08-SEP-25)	-3	-25*	Weekly update; Zone-1 Pole Foundations (TIA #19)
v.041M AUG (08-SEP-25)	**0**	**-25***	**61 WD overall mitigation**
		TBD	**Impacts Recognized by SDOT (MAY/JUN/JUL) Updates)**

(*) *Note: activity durations and float values are displayed in whole numbers (integer) based on P6 admin preferences. The default unit if time is a "day" (i.e., half-days, i.e., "hours" are not captured). SDOT recognized 8.5 days of impact (out of 11 requested) per the JAN v.14M update. Since that point, the P6 total float display "rounds-up" to a whole number (based on the 5:00 PM "time" of the FOOB constraint on ID# M-9007).*

CRITICAL PATH

The current critical path is graphically shown in the attached Gantt chart filter for critical path.
As discussed previously this month the critical path has shifted from Work Zone 4 to Work Zone 1, initiating in sidewalk work and restoration on 43rd. After finishing the north sidewalks on this area the critical path then moves into the DC 55 added sidewalk work and then continues through sidewalks on 11th, 43rd south sides and Roosevelt sidewalks. As sidewalk wrap up weekend driveway work at 42nd and Roosevelt occurs moving the critical path into SCL signal service work and Signal installations at 43rd and Roosevelt, 11th and 43rd, and Roosevelt and Eastlake. Zone 1 Lighting work for 41st then takes over moving into Hardscapes and electrical work on 42nd and Roosevelt. Zone 1 work then terminates with the milling, paving and striping work for that area and the critical path then moves into the project close out milestones and activities: Substantial Completion, Final Inspection, Punch List, Physical Completion Owner Caused Delays, and Project Completion.

MODIFIED ACTIVIES
& RELATIONSHIPS

Project Differences Report

Comparing J-LINE MONTHLY Update - JULY 2025 (v.037 / 04-AUG-25) to J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Date Mon Sep 15 08:40:09 2025

General Project information

Field Name	**[J-LINE MONTHLY Update - JULY 2025 (v.037 / 04-AUG-25)] [JL-037M]**	**[J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)] [JL-041M]**
Data Date	04-Aug-25	08-Sep-25
Finish	03-May-27	06-May-27

Activity Name

Activity ID	**New Activity Name**	**Old Activity Name**
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	11th - Pole Foundations AFTER SDOT Directed Additional Potholing
1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER Completion of SDOT Directed Additional Potholing	43rd - Pole Foundations (17 ea.) - AFTER Completion of SDOT Directed Additional Potholing
3-WE-1113	Remove Roadway Type 2 - Garfield - Howe (E) Ph.2	Remove Roadway Type 2 - Galer (E) Ph.2
3-WE-1114	Pour Roadway - Garfield - Howe (E) Ph.2	Pour Roadway - Galer (E) Ph.2

Actual Start Date

Activity ID	**Activity Name**	**New Actual Start Date**	**Old Actual Start Date**	**Comments / Notes**
1-PF-0129	43rd - Pole Foundations (17 ea.) - PRIOR to Completion of SDOT Directed Additional Potholing	05-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER Completion of SDOT Directed Additional Potholing	11-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	28-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-RW-0082	Temp Pave - 43rd / 11th to 12th	05-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-RW-0084	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd (West)	11-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-RW-0085	Pour Roadway - Roosevelt & 43rd (West)	22-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-RW-0086	Curb - Roosevelt & 43rd (West)	26-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-RW-0087	Temp Pave - Roosevelt & 43rd (West)	28-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-RW-0098	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (East)	08-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
1-SW-0135	Remove Sidewalk - 43rd / 12th to 11th (N)	08-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-0564	Roadway Demo & Exc - Shelby to Harvard (E)	02-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-0602	TROLLEY REACTIVATION Harvard to Fuhrman (8/29/25)	29-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-0604	Remove/Abandon Waterline & Appurtances - Shelby to Harvard (E)	02-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-614	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.3	18-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-624	Pour Roadway - Harvard to Fuhrman (W) Ph.3	02-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-654	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.2	18-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-664	Pour Roadway - Harvard to Fuhrman (W) Ph.2	02-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-704	Pour Roadway - Harvard to Fuhrman (W) Ph.1	06-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-714	Curb - Harvard to Fuhrman (W) Ph.1	14-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-RW-724	Patch Pave - Harvard to Fuhrman (W) Ph.1	12-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-SW-0738	Remove Sidewalk - Fuhrman SWC	04-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built

2-SW-0739	Trench Electrical - Fuhrman SWC	07-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-SW-0740	Electrical - Fuhrman SWC	11-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-SW-0741	Grade Sidewalks - Fuhrman SWC	13-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-SW-0744	Remove Sidewalk - Fuhrman NWC	28-Jul-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-SW-0745	Trench Electrical - Fuhrman NWC	29-Jul-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-SW-0746	Electrical - Fuhrman NWC	30-Jul-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0469	SPU Customer Notification - Stg 1 Harvard to Hamlin (CC02 & CC03)	06-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0471	Excavate Services - Stg 1 Harvard to Hamlin	05-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	13-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0473	SPU Transfer Services - Stg 1 Harvard to Hamlin (21 ea.)	13-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0474	Patch Pave - Stg 1 Harvard to Hamlin	20-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0526	SPU Water Ops Scheduling Notification - Stg 2 (TM2.1 & TM2.2)	20-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0536	SPU Water Ops Scheduling Notification - Stg 2 (CC05, 06, 07)	15-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0549	Test Stations Watermain Stage 1	21-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0554	SPU Temp Jumper Conn. Sta. 21+50 - Stg 1 Harvard to Hamlin	18-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0606	Install Temp Main TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	20-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0616	Test & Flush TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	28-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0626	Bact Results TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	03-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
2-W-0646	SPU Customer Notification - Stg 2 Hamlin to Edgar (TM2.1 & TM2.2)	08-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-RW-1071	Curb - Galer to Garfield (E)	27-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-RW-1072	Patch Pave - Galer to Garfield (E)	27-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-RW-1074	Roadway Demo & Exc - Garfield to Howe (E)	14-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-RW-1075	Pour Roadway - Garfield to Howe (E)	04-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-RW-1114	Remove/Abandon Waterline & Appurtances - Garfield to Howe (E)	14-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1037	Install Mainline Lateral @ Newton Sta. 700+63 to 700+13 - Stg 5 Blaine to Boston	06-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1043	SPU Connect CC15 - Stg 5 Blaine to Boston	06-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1044	SPU Transfer Services In Stage 5 - Stg 5 Blaine to Boston	07-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1046	SPU Connection Sta. 65+21 Yale Pl. - Stg 5 Blaine to Boston	20-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1047	SPU Temp Jumper Conn. @ Sta. 65+00 - Stg 5 Blaine to Boston	08-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1048	Patch Pave - Stg 5 Blaine to Boston	12-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1050	Transfer Services to TM 6.1 (7 ea.) - Stg 6 Boston to Louisa	19-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1051	SPU Temp Service Laterals (5 ea.) - Stg 6 Boston to Louisa	20-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1052	Install Mainline & Hydrants Sta. 44+64 to 50+00 - Stg 6 Boston to Louisa	22-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1053	Install Mainline & Hydrants Sta. 50+00 to 54+86 - Stg 6 Boston to Louisa	05-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1076	Test Stations Watermain Stage 5	14-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1081	SPU Temp Hydrant Laterals (2 ea.) - Stg 6 Boston to Louisa	21-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1083	Install Thrust Collar Sta. 700+02 - Stg 5 Blaine to Boston	07-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built

3-W-1097	Remove Temp Jumper Sta. 65+21 - Stg 5 Blaine to Boston	11-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1120	Bact Results TM 6.1 - Stg 6 Boston to Louisa	06-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1130	SPU Customer Notification TM 6.1 - Stg 6 Boston to Louisa	11-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-W-1140	SPU Connect TM 6.1 - Stg 6 Boston to Louisa	18-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-WE-1110	Remove Roadway Type 2 - Galer (E) Ph.1	06-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
3-WE-1111	Pour Roadway - Galer (E) Ph.1	07-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-PF-1526	YALE TO ALOHA - EAST SIDE - POLE FOUNDATIONS (3 ea.)	08-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-PF-1536	ALOHA - EAST SIDE Pole Foundations (2 ea,)	08-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-SW-1573	Remove Sidewalk - Yale SEC	26-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-SW-1574	Trench Electrical - Yale SEC	27-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-SW-1575	Electrical - Yale SEC	28-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-SW-1576	Grade Sidewalks - Yale SEC	04-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-WE-1479	Remove Roadway Type 2 - Yale Ph.1 (WE)	23-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-WE-1480	Pour Roadway - Yale Ph.1 (WE)	24-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-WE-1488	Remove Roadway Type 2 - Aloha Ph.1 (WE)	06-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-WE-1489	Pour Roadway - Aloha Ph.1 (WE)	07-Sep-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-WE-1499	COMPLETE CONDUIT YALE EAST SIDE	14-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built
4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	20-Aug-25	Value not specified in the database	AS date assigned to reflect actual/as-built

Actual Finish Date				
Activity ID	**Activity Name**	**New Actual Finish Date**	**Old Actual Finish Date**	**Comments / Notes**
1-PF-0129	43rd - Pole Foundations (17 ea.) - PRIOR to Completion of SDOT Directed Additional Potholing	08-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER Completion of SDOT Directed Additional Potholing	27-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	29-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
1-RW-0082	Temp Pave - 43rd / 11th to 12th	05-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
1-RW-0084	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd (West)	21-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
1-RW-0085	Pour Roadway - Roosevelt & 43rd (West)	25-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
1-RW-0086	Curb - Roosevelt & 43rd (West)	27-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
1-RW-0087	Temp Pave - Roosevelt & 43rd (West)	28-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-RW-0602	TROLLEY REACTIVATION Harvard to Fuhrman (8/29/25)	29-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-RW-614	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.3	29-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-RW-654	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.2	29-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-RW-694	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.1	05-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-RW-704	Pour Roadway - Harvard to Fuhrman (W) Ph.1	11-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-RW-714	Curb - Harvard to Fuhrman (W) Ph.1	15-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-RW-724	Patch Pave - Harvard to Fuhrman (W) Ph.1	13-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-SW-0738	Remove Sidewalk - Fuhrman SWC	06-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-SW-0739	Trench Electrical - Fuhrman SWC	08-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built

2-SW-0740	Electrical - Fuhrman SWC	12-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-SW-0741	Grade Sidewalks - Fuhrman SWC	14-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-SW-0744	Remove Sidewalk - Fuhrman NWC	28-Jul-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-SW-0745	Trench Electrical - Fuhrman NWC	29-Jul-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0468	Bact Results - Stg 1 Harvard to Hamlin	05-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0469	SPU Customer Notification - Stg 1 Harvard to Hamlin (CC02 & CC03)	12-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0471	Excavate Services - Stg 1 Harvard to Hamlin	08-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	13-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0473	SPU Transfer Services - Stg 1 Harvard to Hamlin (21 ea.)	15-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0474	Patch Pave - Stg 1 Harvard to Hamlin	20-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0536	SPU Water Ops Scheduling Notification - Stg 2 (CC05, 06, 07)	05-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0549	Test Stations Watermain Stage 1	21-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0554	SPU Temp Jumper Conn. Sta. 21+50 - Stg 1 Harvard to Hamlin	19-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0606	Install Temp Main TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	27-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0616	Test & Flush TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	02-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
2-W-0626	Bact Results TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	05-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-RW-1070	Pour Roadway - Galer to Garfield (E)	18-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-RW-1071	Curb - Galer to Garfield (E)	27-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-RW-1072	Patch Pave - Galer to Garfield (E)	27-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-RW-1074	Roadway Demo & Exc - Garfield to Howe (E)	08-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-RW-1114	Remove/Abandon Waterline & Appurtances - Garfield to Howe (E)	04-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1037	Install Mainline Lateral @ Newton Sta. 700+63 to 700+13 - Stg 5 Blaine to Boston	06-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1043	SPU Connect CC15 - Stg 5 Blaine to Boston	06-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1044	SPU Transfer Services In Stage 5 - Stg 5 Blaine to Boston	07-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1046	SPU Connection Sta. 65+21 Yale Pl. - Stg 5 Blaine to Boston	20-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1047	SPU Temp Jumper Conn. @ Sta. 65+00 - Stg 5 Blaine to Boston	08-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1048	Patch Pave - Stg 5 Blaine to Boston	13-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1050	Transfer Services to TM 6.1 (7 ea.) - Stg 6 Boston to Louisa	19-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1051	SPU Temp Service Laterals (5 ea.) - Stg 6 Boston to Louisa	20-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1052	Install Mainline & Hydrants Sta. 44+64 to 50+00 - Stg 6 Boston to Louisa	04-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1063	SPU Water Ops Scheduling Notification - Stg 5 (Jumper)	08-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1066	SPU Water Ops Scheduling Notification - Stg 5 (Conn.)	07-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1067	SPU Water Ops Scheduling Notification - Stg 5 (CC15)	05-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1076	Test Stations Watermain Stage 5	14-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1080	SPU Water Ops Scheduling Notification - Stg 6 (Temp Services)	21-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1081	SPU Temp Hydrant Laterals (2 ea.) - Stg 6 Boston to Louisa	21-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1083	Install Thrust Collar Sta. 700+02 - Stg 5 Blaine to Boston	08-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built

3-W-1097	Remove Temp Jumper Sta. 65+21 - Stg 5 Blaine to Boston	11-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1110	Test & Flush TM 6.1 - Stg 6 Boston to Louisa	01-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1120	Bact Results TM 6.1 - Stg 6 Boston to Louisa	08-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1130	SPU Customer Notification TM 6.1 - Stg 6 Boston to Louisa	15-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-W-1140	SPU Connect TM 6.1 - Stg 6 Boston to Louisa	18-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-WE-1110	Remove Roadway Type 2 - Galer (E) Ph.1	06-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
3-WE-1111	Pour Roadway - Galer (E) Ph.1	07-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-SW-1573	Remove Sidewalk - Yale SEC	26-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-SW-1574	Trench Electrical - Yale SEC	27-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-SW-1575	Electrical - Yale SEC	03-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-SW-1576	Grade Sidewalks - Yale SEC	04-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-WE-1479	Remove Roadway Type 2 - Yale Ph.1 (WE)	23-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-WE-1480	Pour Roadway - Yale Ph.1 (WE)	24-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-WE-1488	Remove Roadway Type 2 - Aloha Ph.1 (WE)	06-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-WE-1489	Pour Roadway - Aloha Ph.1 (WE)	07-Sep-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-WE-1499	COMPLETE CONDUIT YALE EAST SIDE	19-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	26-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
FM-TBD	SDOT Directed Potholing - 11th Ave NE	08-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
M-9017	Zone-4 - DB Rescheduling / Admin & Submittals	13-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built
M-9037	Zone-4 - DB Rescheduling / Review TC Plans	13-Aug-25	Value not specified in the database	AF date assigned to reflect actual/as-built

Original Duration				
Activity ID	**Activity Name**	**New Original Duration**	**Old Original Duration**	**Comments / Notes**
1-RW-0089	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (West)	5	3	Duration increased to reflect near-term estimate/forecast (simultaneous with 1-RW-0102)
1-RW-0102	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Campus (East)	5	3	Duration increased to reflect near-term estimate/forecast (simultaneous with 1-RW-0089)
2-SW-0742	Pour Sidewalks/Curb Ramps - Fuhrman SWC	3	4	Duration reduced to reflect near-term estimate/forecast
2-W-0499	Install Watermain, Hydrants & Blocking Sta. 21+64 to 33+19 - Stg 2 Hamlin to Edgar	11	12	Duration reduced to reflect near-term estimate/forecast
2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & Hydrants (7 ea.)	1	3	Duration reduced to reflect near-term estimate/forecast
3-W-1053	Install Mainline & Hydrants Sta. 50+00 to 54+86 - Stg 6 Boston to Louisa	11	15	Duration reduced to reflect near-term estimate/forecast

Activities Added/Deleted		
The following Activities have been added to the project		
Activity ID	**Activity Name**	**Comments / Notes**
1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	Revisions to Zone-1 pole foundations definition reflecting changing conditions
1-PF-0150	11th - Pole Foundations (After Yale to Aloha Zone-4 SDOT Mitigation)	Revisions to Zone-1 pole foundations definition reflecting changing conditions
1-PF-0159	SDOT Stop Work E-mail / Issue Directive/Design	Revisions to Zone-1 pole foundations definition reflecting changing conditions
1-PF-0179	11th / 42nd to 41st - SDOT Directed Stop Work (install 2 pole fdns)	Revisions to Zone-1 pole foundations definition reflecting changing conditions
1-RW-139	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd NEC	Added definition for 43rd NEC & SEC

1-RW-149	Pour Roadway - Roosevelt & 43rd NEC	Added definition for 43rd NEC & SEC
1-RW-159	Curb - Roosevelt & 43rd NEC	Added definition for 43rd NEC & SEC
1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	Added definition for 43rd NEC & SEC
1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	Added definition for 43rd NEC & SEC
1-RW-189	Curb - Roosevelt & 43rd SEC	Added definition for 43rd NEC & SEC
2-W-0519	Install Watermain (prior to temp main commissioning)	Added activity to reflect field conditions
3-RW-1116	Mid-Block Sidewalk Galer to Howe	Added activity to reflect field conditions
4-WE-1518	BOAT SHOW - CANNOT CLOSE ALOHA	Added activity to reflect field conditions
4-WE-1519	Pour Roadway - Aloha / After DCS's 334, 335, 336	Added DSC activity to capture as-built status/conditions
DSC-292	DSC-292 SWC Fuhrman unknown unlocated duct bank	Added DSC activity to capture as-built status/conditions
DSC-293	DSC-293 Stage 1 Sta 19+11 CDF Conflict	Added DSC activity to capture as-built status/conditions
DSC-294	DSC-294 Stage 5 WM, WS-1211 & WS-1210 Sizes	Added DSC activity to capture as-built status/conditions
DSC-295	DSC-295 Stage 1 WM, WS-301 Root Conflicts	Added DSC activity to capture as-built status/conditions
DSC-296	DSC-296 11th Ave, T211-01 Potholing SS conflict	Added DSC activity to capture as-built status/conditions
DSC-297	DSC-297 Stage 1 WM, WS-301 CDF Conflict	Added DSC activity to capture as-built status/conditions
DSC-298	DSC-298 Stage 1 WM, WS-207 Root Conflicts	Added DSC activity to capture as-built status/conditions
DSC-299	DSC-299 Stage 1 WM, WS-205 CDF Conflict	Added DSC activity to capture as-built status/conditions
DSC-300	DSC-300 Stage 5 Unknown unmarked water service	Added DSC activity to capture as-built status/conditions
DSC-301	DSC-301 11th 43rd to 42nd E. Side Sewer conflict w/foudnation T211.02	Added DSC activity to capture as-built status/conditions
DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved foundation creating excavation issues	Added DSC activity to capture as-built status/conditions
DSC-303	DSC-303 43rd/Roosevelt Sinkhole	Added DSC activity to capture as-built status/conditions
DSC-304	DSC-304 Fuhrman SWC, conduits in conflict with handhole	Added DSC activity to capture as-built status/conditions
DSC-305	DSC-305 Fuhrman SWC wooden pole utilitues	Added DSC activity to capture as-built status/conditions
DSC-306	DSC-306 Fuhrman SWC PPB in middle of ramp	Added DSC activity to capture as-built status/conditions
DSC-307	DSC-307 Garfield WQ-B117 Unknown Unlocated Conduit	Added DSC activity to capture as-built status/conditions
DSC-308	DSC-308 NWC Fuhrman, Shallow Fiber Conduit Conflict	Added DSC activity to capture as-built status/conditions
DSC-309	DSC-309 Garfield East Side WQV B117 Conflict with Gas line	Added DSC activity to capture as-built status/conditions
DSC-310	DSC-310 Yale East Side Unknown CB and Ductbank	Added DSC activity to capture as-built status/conditions
DSC-311	DSC-311 43RD Roosevelt to 11th Boulder conflict with foundation T213-03	Added DSC activity to capture as-built status/conditions
DSC-312	DSC-312 NEC Aloha unknown unmarked conduits	Added DSC activity to capture as-built status/conditions
DSC-313	DSC-313 Aloha unknown unlocated Fiber line	Added DSC activity to capture as-built status/conditions
DSC-314	DSC-314 Aloha Unknown unlocated conduit	Added DSC activity to capture as-built status/conditions
DSC-315	DSC-315 Aloha East Contaminated Soils	Added DSC activity to capture as-built status/conditions
DSC-316	DSC-316 Stage 2 Temp Main unlocated unknown water service conflict with temp main	Added DSC activity to capture as-built status/conditions
DSC-317	DSC-317 Howe East side pavement thickness 18"	Added DSC activity to capture as-built status/conditions
DSC-318	DSC-318 Harvard East side shallow DB in conflict with roadway	Added DSC activity to capture as-built status/conditions
DSC-319	DSC-319 Garfield WQV B117 to CB B34 will not work per plan	Added DSC activity to capture as-built status/conditions

DSC-320	DSC-320 Stage 2 temp main CDF Encased existing main	Added DSC activity to capture as-built status/conditions
DSC-321	DSC-321 Unknown Unlocated Water Service STA 28+80 stage 2	Added DSC activity to capture as-built status/conditions
DSC-322	DSC-322 Stage 6 miss-marked water services	Added DSC activity to capture as-built status/conditions
DSC-323	DSC-323 SWC Yale & Fairview 8in Sidewalk	Added DSC activity to capture as-built status/conditions
DSC-324	DSC-324 Leaking Services at T2.1 Hamlin, WS- 503,504	Added DSC activity to capture as-built status/conditions
DSC-325	DSC-325 SEC Yale & Fairview Unlocated Utility	Added DSC activity to capture as-built status/conditions
DSC-326	DSC-326 Stage 6 existing storm in conflict with watermain at Boston	Added DSC activity to capture as-built status/conditions
DSC-327	DSC-327 43rd & Roosevelt Rotten Pole	Added DSC activity to capture as-built status/conditions
DSC-328	DSC-328 SEC 43rd Roosevelt Conduits Cast in Curb	Added DSC activity to capture as-built status/conditions
DSC-329	DSC-329 11th Ave Ground Water in OCS foundations	Added DSC activity to capture as-built status/conditions
DSC-330	DSC-330 WM Stg 2 Unlocated Steel Pipe STA 27+86	Added DSC activity to capture as-built status/conditions
DSC-331	DSC-331 Stage 2 WM 1IN Copper Line at 27+70	Added DSC activity to capture as-built status/conditions
DSC-332	DSC-332 Stage 2 WM 2EA 2IN Steel Pipes near WS-604	Added DSC activity to capture as-built status/conditions
DSC-334	DSC-334 SEC Fairview & Aloha Plugged Inlet	Added DSC activity to capture as-built status/conditions
DSC-335	DSC-335 SEC Fairview & Aloha Comm Conduit Conflict	Added DSC activity to capture as-built status/conditions
DSC-336	DSC-336 Fairview & Aloha Ex. Pole Foundation in Grade	Added DSC activity to capture as-built status/conditions
DSC-337	DSC-337 Stage 6 WM, Power Conflict at 50+79	Added DSC activity to capture as-built status/conditions
DSC-338	DSC-338 Stage 2 WM Unknown Utility at STA 26+90	Added DSC activity to capture as-built status/conditions
DSC-339	DSC-339 Aloha P2904 Ground Water at 13'	Added DSC activity to capture as-built status/conditions
DSC-340	DSC-340 NEC Garfield Ex. MH Elevation Conflict	Added DSC activity to capture as-built status/conditions
DSC-341	DSC-341 43rd & 11th Signal Service Conflict w/ Temp Lighting	Added DSC activity to capture as-built status/conditions
DSC-351	DSC-351 Pole Foundation P-0204 SW 11th & Roosevelt	Added DSC activity to capture as-built status/conditions
NCR-001	NCR-001 CB-B07 - 15" PS Line Damaged	Add/include NCR's per SDOT
NCR-0014015	NCR-014 & NCR-015 Paving	Add/include NCR's per SDOT
NCR-002	NCR-002 CB-B10 - 8" DIP Removed allowing Type 9 in Pipe	Add/include NCR's per SDOT
NCR-003	NCR-003 CB-B30 - 20" PS Line Damaged	Add/include NCR's per SDOT
NCR-004	NCR-004 TR Flex Wedge Restraint Glands incorrectly used	Add/include NCR's per SDOT
NCR-005	NCR-005 Earthquake Joint installed into CB-11 beyond 1' limit	Add/include NCR's per SDOT
NCR-006	NCR-006 Marking tape not installed over conduit run	Add/include NCR's per SDOT
NCR-007	NCR-007 Surveyed 1.81' lower than design	Add/include NCR's per SDOT
NCR-008	NCR-008 Conduits damaged during exposure of CDF duct bank	Add/include NCR's per SDOT
NCR-009	NCR-009 SCL Conduits damaged	Add/include NCR's per SDOT
NCR-010	NCR-010 An active existing Type II SCL handhole was damaged	Add/include NCR's per SDOT
NCR-011	NCR-011 Damaged a known 8" WM - broke existing corp valve	Add/include NCR's per SDOT
NCR-012	NCR-012 Damaged a known 8" WM - broke existing corp valve	Add/include NCR's per SDOT
NCR-013	NCR-013 Damaged pedestrian signal	Add/include NCR's per SDOT
NCR-014	NCR-014 Spalling at joints of PCCP panels	Add/include NCR's per SDOT

NCR-015	NCR-015 Finish of PCCP panel not per specification	Add/include NCR's per SDOT
NCR-016	NCR-016 6" gas main was struck and damaged	Add/include NCR's per SDOT
NCR-017	NCR-017 Utility Strike	Add/include NCR's per SDOT
NCR-018	NCR-018 Saw Cuts for transverse cut are not per approved plan	Add/include NCR's per SDOT
NCR-019	NCR-019 12X4 tees that were installed were the incorrect size per the plan	Add/include NCR's per SDOT
NCR-020	NCR-020 Jansen ruptured a 1 ½" service line	Add/include NCR's per SDOT
NCR-021	NCR-021 Riser is cast to the incorrect height bringing the lid to 1 1/8" above grade.	Add/include NCR's per SDOT
NCR-022	NCR-022 Damage to panel while removing adjacent panel	Add/include NCR's per SDOT
NCR-023	NCR-023 Electrical loop not installed	Add/include NCR's per SDOT

Activities Added/Deleted

The following Activities have been deleted from the project

Activity ID	Activity Name	Comments / Notes
2-W-0496	Excavate CC05, 06, 07 - Stg 2 Hamlin to Edgar	Cut/caps no longer required
2-W-0498	SPU Cut/Cap CC05, 06, 07 - Stg 2 Hamlin to Edgar	Cut/caps no longer required

WBS Added/Deleted

The following WBS have been added to the project

WBS Code	WBS Name	Comments / Notes
17	Roosevelt and 43rd St. SE Corner	Added network definition @ 43rd & Roosevelt – Zone-1
18	Roosevelt and 43rd St. NE Corner	Added network definition @ 43rd & Roosevelt – Zone-1

General Relationship Differences

Lag

Activity ID	Activity Name	Relationship Type	Predecessor Activity Id	Predecessor Activity Name	New Lag	Old Lag	Comments / Notes
3-RW-1075	Pour Roadway - Garfield to Howe (E)	Finish to Start	3-RW-1074	Roadway Demo & Exc - Garfield to Howe (E)	-3	0	FS Overlap to match actual

Activity Relationships Added/Deleted

The following Successor Activity Relationships have been added to the project

Activity ID	Activity Name	Relationship Lag	Relationship Type	Successor Activity Id	Successor Activity Name	Comments / Notes
1-EC-0045	Roosevelt and 41st 1 Ea - Electrical Crossing	0	Start to Start	NCR-012	NCR-012 Damaged a known 8" WM - broke existing corp valve	Logic tie added to incorporate NCR
1-EC-0047	42nd and 11th 2 Each - Electrical Crossing	0	Finish to Start	NCR-006	NCR-006 Marking tape not installed over conduit run	Logic tie added to incorporate NCR
1-EC-DC-055A	Design Change 055 - 43rd & 11th Added Crossing	0	Start to Start	NCR-013	NCR-013 Damaged pedestrian signal	Logic tie added to incorporate NCR
1-PF-0130	11th - Pole Foundations (17 ea.) Prior to SDOT Directed Additional Potholing	0	Finish to Start	DSC-296	DSC-296 11th Ave, T211-01 Potholing SS conflict	Logic tie added to incorporate DSC
1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	0	Finish to Start	1-SW-0135	Remove Sidewalk - 43rd / 12th to 11th (N)	Rev. to Z1 pole fdn def. due to changes
1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	0	Finish to Start	4-PF-1526	YALE TO ALOHA - EAST SIDE - POLE FOUNDATIONS (3 ea.)	Rev. to Z1/Z4 pole fdn flow (mitigate)
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	0	Finish to Start	1-PF-0179	11th / 42nd to 41st - SDOT Directed Stop Work (install 2 pole fdns)	Rev. to Z1 pole fdn def. due to changes
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	0	Start to Start	DSC-329	DSC-329 11th Ave Ground Water in OCS foundations	Logic tie added to incorporate DSC

1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	48	Start to Start	DSC-341	DSC-341 43rd & 11th Signal Service Conflict w/ Temp Lighting	Logic tie added to incorporate DSC
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	0	Finish to Start	1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	Logic tie added to incorporate DSC
1-PF-0150	11th - Pole Foundations (After Yale to Aloha Zone-4 SDOT Mitigation)	0	Finish to Start	1-SW-0147	Remove Sidewalk - 11th & 42nd NEC	Rev. to Z1 pole fdn def. due to changes
1-PF-0150	11th - Pole Foundations (After Yale to Aloha Zone-4 SDOT Mitigation)	0	Finish to Start	DSC-351	DSC-351 Pole Foundation P-0204 SW 11th & Roosevelt	Logic tie added to incorporate DSC
1-PF-0150	11th - Pole Foundations (After Yale to Aloha Zone-4 SDOT Mitigation)	0	Finish to Start	1-PF-0131	Roosevelt - Pole Foundations (21 ea.)	Rev. to Z1 pole fdn def. due to changes
1-PF-0159	SDOT Stop Work E-mail / Issue Directive/Design	0	Finish to Start	1-PF-0179	11th / 42nd to 41st - SDOT Directed Stop Work (install 2 pole fdns)	Rev. to Z1 pole fdn def. due to changes
1-PF-0159	SDOT Stop Work E-mail / Issue Directive/Design	0	Finish to Start	1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	Rev. to Z1 pole fdn def. due to changes
1-PF-0179	11th / 42nd to 41st - SDOT Directed Stop Work (install 2 pole fdns)	0	Finish to Start	1-SW-0153	Remove Sidewalk - 11th & 42nd SEC	Rev. to Z1 pole fdn def. due to changes
1-RW-0058	Remove Roadway, Common Ex, Type 2 - 43rd / Roosevelt to 11th	0	Start to Start	NCR-010	NCR-010 An active existing Type II SCL handhole was damaged	Logic tie added to incorporate NCR
1-RW-0059	Pour Roadway - 43rd / Roosevelt to 11th	0	Finish to Start	NCR-014	NCR-014 Spalling at joints of PCCP panels	Logic tie added to incorporate NCR
1-RW-0059	Pour Roadway - 43rd / Roosevelt to 11th	0	Finish to Start	NCR-015	NCR-015 Finish of PCCP panel not per specification	Logic tie added to incorporate NCR
1-RW-0072	Pour Roadway - 11th & 42nd (Ph.3)	0	Finish to Start	NCR-022	NCR-022 Damage to panel while removing adjacent panel	Logic tie added to incorporate NCR
1-RW-0080	Pour Roadway - 43rd / 11th to 12th	0	Start to Start	NCR-021	NCR-021 Riser is cast to the incorrect height bringing the lid to 1 1/8” above grade.	Logic tie added to incorporate NCR
1-RW-0084	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd (West)	0	Start to Start	DSC-303	DSC-303 43rd/Roosevelt Sinkhole	Logic tie added to incorporate DSC
1-RW-0087	Temp Pave - Roosevelt & 43rd (West)	0	Finish to Start	1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	New logic for added activities
1-RW-0089	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (West)	0	Start to Start	1-RW-0102	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Campus (East)	Swap sequence 11th, Eastlake, Campus
1-RW-0094	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Campus (West)	0	Finish to Start	1-RW-0106	Remove Roadway, Common Ex, Type 2 - Roosevelt & 42nd (E)	Swap sequence 11th, Eastlake, Campus
1-RW-0096	Curb - Eastlake / 11th to NE Campus (West)	0	Finish to Start	1-RW-0110	Pour Roadway - Roosevelt & 41st (E)	Swap sequence 11th, Eastlake, Campus
1-RW-0098	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (East)	0	Finish to Start	1-RW-0094	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Campus (West)	Swap sequence 11th, Eastlake, Campus
1-RW-0099	Pour Roadway - 11th & Eastlake (East)	0	Finish to Start	1-RW-0095	Pour Roadway - Eastlake / 11th to NE Campus (West)	Swap sequence 11th, Eastlake, Campus
1-RW-0100	Curb - 11th & Eastlake (East)	0	Finish to Start	1-RW-0096	Curb - Eastlake / 11th to NE Campus (West)	Swap sequence 11th, Eastlake, Campus
1-RW-139	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd NEC	0	Finish to Start	1-RW-149	Pour Roadway - Roosevelt & 43rd NEC	New logic for added activities
1-RW-139	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd NEC	0	Finish to Start	1-RW-0098	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (East)	New logic for added activities
1-RW-139	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd NEC	0	Finish to Start	NCR-0014015	NCR-014 & NCR-015 Paving	Logic tie added to incorporate NCR
1-RW-149	Pour Roadway - Roosevelt & 43rd NEC	0	Finish to Start	1-RW-159	Curb - Roosevelt & 43rd NEC	New logic for added activities
1-RW-149	Pour Roadway - Roosevelt & 43rd NEC	0	Finish to Start	1-RW-0099	Pour Roadway - 11th & Eastlake (East)	New logic for added activities
1-RW-159	Curb - Roosevelt & 43rd NEC	0	Finish to Start	1-RW-0100	Curb - 11th & Eastlake (East)	New logic for added activities
1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	0	Finish to Start	1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	New logic for added activities
1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	0	Finish to Start	1-RW-0089	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (West)	New logic for added activities
1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	0	Start to Start	1-RW-139	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd NEC	New logic for added activities
1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	0	Finish to Start	1-RW-139	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd NEC	New logic for added activities
1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	0	Finish to Start	DSC-327	DSC-327 43rd & Roosevelt Rotten Pole	Logic tie added to incorporate DSC
1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	0	Finish to Start	1-RW-189	Curb - Roosevelt & 43rd SEC	New logic for added activities
1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	0	Finish to Start	1-RW-0089	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (West)	New logic for added activities
1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	0	Start to Start	1-RW-149	Pour Roadway - Roosevelt & 43rd NEC	New logic for added activities
1-RW-189	Curb - Roosevelt & 43rd SEC	0	Finish to Start	1-RW-0091	Curb - 11th & Eastlake (West)	New logic for added activities
1-W-0033	Install Mainline & Hydrants - Watermain Stg 8	0	Start to Start	NCR-004	NCR-004 TR Flex Wedge Restraint Glands incorrectly used	Logic tie added to incorporate NCR

2-RW-0567	Patch Pave - Shelby to Harvard (E)	0	Finish to Start	2-WE-826	Remove Roadway Type 2 - Fuhrman NEC	Added per weekly update
2-RW-0570	Pour Roadway - Harvard to Fuhrman (E)	0	Finish to Start	NCR-018	NCR-018 Saw Cuts for transverse cut are not per approved plan	Logic tie added to incorporate NCR
2-RW-0582	Patch Pave - Harvard to Fuhrman (W)	0	Finish to Start	2-SW-0744	Remove Sidewalk - Fuhrman NWC	Advance per weekly update as-built
2-RW-614	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.3	0	Finish to Finish	2-RW-0602	TROLLEY REACTIVATION Harvard to Fuhrman (8/29/25)	Added per weekly update; milestone
2-RW-644	Patch Pave - Harvard to Fuhrman (W) Ph.3	32	Finish to Finish	2-RW-0564	Roadway Demo & Exc - Shelby to Harvard (E)	FF+4
2-RW-644	Patch Pave - Harvard to Fuhrman (W) Ph.3	0	Finish to Start	2-CC-0529	Allison - Conduit Crossings	Added per weekly update
2-RW-654	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.2	0	Start to Start	2-RW-614	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.3	As-built logic weekly update
2-RW-654	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.2	0	Start to Start	DSC-318	DSC-318 Harvard East side shallow DB in conflict with roadway	Logic tie added to incorporate DSC
2-RW-664	Pour Roadway - Harvard to Fuhrman (W) Ph.2	0	Finish to Start	2-WE-826	Remove Roadway Type 2 - Fuhrman NEC	Added per weekly update
2-RW-684	Patch Pave - Harvard to Fuhrman (W) Ph.2	32	Finish to Finish	2-RW-0564	Roadway Demo & Exc - Shelby to Harvard (E)	FF+4
2-RW-694	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.1	0	Finish to Start	2-RW-724	Patch Pave - Harvard to Fuhrman (W) Ph.1	As-built logic weekly update
2-RW-704	Pour Roadway - Harvard to Fuhrman (W) Ph.1	0	Finish to Start	2-RW-724	Patch Pave - Harvard to Fuhrman (W) Ph.1	As-built logic weekly update
2-RW-714	Curb - Harvard to Fuhrman (W) Ph.1	0	Finish to Start	2-RW-654	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.2	Added per weekly update
2-RW-724	Patch Pave - Harvard to Fuhrman (W) Ph.1	0	Finish to Start	2-RW-714	Curb - Harvard to Fuhrman (W) Ph.1	Added per weekly update
2-ST-0451	NB Shelby Station CB - Storm	0	Start to Start	NCR-002	NCR-002 CB-B10 - 8" DIP Removed allowing Type 9 in Pipe	Logic tie added to incorporate NCR
2-ST-0452	Hamlin and Eastlake - Storm	0	Finish to Start	NCR-005	NCR-005 Earthquake Joint installed into CB-11 beyond 1' limit	Logic tie added to incorporate NCR
2-ST-0459	Allison and Eastlake - Storm (After to DSC-049)	0	Start to Start	NCR-001	NCR-001 CB-B07 - 15" PS Line Damaged	Logic tie added to incorporate NCR
2-SW-0736	Pour Sidewalks/Curb Ramps - Harvard NWC	0	Finish to Start	2-SCL-0866	Install Meter Cabinet - Harvard NB Station	Added per weekly update rev. seq.
2-SW-0736	Pour Sidewalks/Curb Ramps - Harvard NWC	0	Finish to Start	2-STN-0947	Install Shelters (2 Each) - Harvard NB Station	Added per weekly update rev. seq.
2-SW-0740	Electrical - Fuhrman SWC	0	Start to Start	DSC-305	DSC-305 Fuhrman SWC wooden pole utilitues	Logic tie added to incorporate DSC
2-SW-0740	Electrical - Fuhrman SWC	0	Start to Start	DSC-306	DSC-306 Fuhrman SWC PPB in middle of ramp	Logic tie added to incorporate DSC
2-SW-0740	Electrical - Fuhrman SWC	0	Start to Start	DSC-304	DSC-304 Fuhrman SWC, conduits in conflict with handhole	Logic tie added to incorporate DSC
2-SW-0744	Remove Sidewalk - Fuhrman NWC	0	Start to Start	2-SW-0738	Remove Sidewalk - Fuhrman SWC	Work simultaneous
2-SW-0746	Electrical - Fuhrman NWC	0	Start to Start	DSC-308	DSC-308 NWC Fuhrman, Shallow Fiber Conduit Conflict	Logic tie added to incorporate DSC
2-SW-0748	Pour Sidewalks/Curb Ramps - Fuhrman NWC	0	Start to Start	2-SW-0742	Pour Sidewalks/Curb Ramps - Fuhrman SWC	Work simultaneous
2-W-0470	Excavate Tie-Ins - Stg 1 Harvard to Hamlin	0	Finish to Start	DSC-293	DSC-293 Stage 1 Sta 19+11 CDF Conflict	Logic tie added to incorporate DSC
2-W-0471	Excavate Services - Stg 1 Harvard to Hamlin	0	Start to Start	DSC-297	DSC-297 Stage 1 WM, WS-301 CDF Conflict	Logic tie added to incorporate DSC
2-W-0471	Excavate Services - Stg 1 Harvard to Hamlin	0	Start to Start	DSC-298	DSC-298 Stage 1 WM, WS-207 Root Conflicts	Logic tie added to incorporate DSC
2-W-0471	Excavate Services - Stg 1 Harvard to Hamlin	0	Start to Start	DSC-299	DSC-299 Stage 1 WM, WS-205 CDF Conflict	Logic tie added to incorporate DSC
2-W-0471	Excavate Services - Stg 1 Harvard to Hamlin	0	Start to Start	DSC-295	DSC-295 Stage 1 WM, WS-301 Root Conflicts	Logic tie added to incorporate DSC
2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	0	Start to Start	2-W-0473	SPU Transfer Services - Stg 1 Harvard to Hamlin (21 ea.)	Added per weekly as-built
2-W-0475	Mainline Allison Lateral Sta. Sta. 300+00 to 300+31	0	Finish to Start	NCR-020	NCR-020 Jansen ruptured a 1 ½" service line	Logic tie added to incorporate NCR
2-W-0499	Install Watermain, Hydrants & Blocking Sta. 21+64 to 33+19 - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0550	Mainline Lateral @ Hamlin - Stg 2 Hamlin to Edgar	Added per weekly as-built
2-W-0519	Install Watermain (prior to temp main commissioning)	0	Finish to Start	2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & Hydrants (7 ea.)	Added per weekly as-built
2-W-0519	Install Watermain (prior to temp main commissioning)	0	Start to Start	DSC-330	DSC-330 WM Stg 2 Unlocated Steel Pipe STA 27+86	Logic tie added to incorporate DSC
2-W-0519	Install Watermain (prior to temp main commissioning)	0	Start to Start	DSC-331	DSC-331 Stage 2 WM 1IN Copper Line at 27+70	Logic tie added to incorporate DSC
2-W-0519	Install Watermain (prior to temp main commissioning)	0	Start to Start	DSC-332	DSC-332 Stage 2 WM 2EA 2IN Steel Pipes near WS-604	Logic tie added to incorporate DSC

2-W-0519	Install Watermain (prior to temp main commissioning)	0	Start to Start	DSC-338	DSC-338 Stage 2 WM Unknown Utility at STA 26+90	Logic tie added to incorporate DSC
2-W-0536	SPU Water Ops Scheduling Notification - Stg 2 (CC05, 06, 07)	0	Finish to Start	2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & Hydrants (7 ea.)	Added per weekly as-built
2-W-0550	Mainline Lateral @ Hamlin - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0500	Test & Flush Water Main - Stg 2 Hamlin to Edgar	Added per weekly as-built
2-W-0559	Install Mainline Sta. 21+50 to 19+50 - Stg 1 Harvard to Hamlin	0	Start to Start	NCR-008	NCR-008 Conduits damaged during exposure of CDF duct bank	Logic tie added to incorporate NCR
2-W-0560	Install Thrust Collar & Cure - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0506	SPU Tie-In Main From Stage 1 - Stg 2 Hamlin to Edgar	Added per weekly as-built
2-W-0582	Install Mainline Fuhrman Intersection to Furhman Vault	0	Finish to Start	NCR-007	NCR-007 Surveyed 1.81' lower than design	Logic tie added to incorporate NCR
2-W-0606	Install Temp Main TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	0	Start to Start	DSC-320	DSC-320 Stage 2 temp main CDF Encased existing main	Logic tie added to incorporate DSC
2-W-0616	Test & Flush TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	0	Start to Start	DSC-324	DSC-324 Leaking Services at T2.1 Hamlin, WS- 503,504	Logic tie added to incorporate DSC
2-W-0616	Test & Flush TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0519	Install Watermain (prior to temp main commissioning)	Added per weekly as-built
3-RW-1070	Pour Roadway - Galer to Garfield (E)	0	Start to Start	NCR-023	NCR-023 Electrical loop not installed	Logic tie added to incorporate NCR
3-RW-1072	Patch Pave - Galer to Garfield (E)	0	Finish to Start	3-RW-1079	Roadway Demo & Exc - Galer to Garfield (W)	Added per weekly as-built
3-RW-1072	Patch Pave - Galer to Garfield (E)	24	Finish to Start	3-WE-1110	Remove Roadway Type 2 - Galer (E) Ph.1	Added per weekly as-built
3-RW-1074	Roadway Demo & Exc - Garfield to Howe (E)	0	Start to Start	DSC-307	DSC-307 Garfield WQ-B117 Unknown Unlocated Conduit	Logic tie added to incorporate DSC
3-RW-1076	Curb - Garfield to Howe (E)	0	Finish to Start	3-RW-1116	Mid-Block Sidewalk Galer to Howe	Added activity
3-RW-1116	Mid-Block Sidewalk Galer to Howe	0	Finish to Start	3-RW-1077	Patch Pave - Garfield to Howe (E)	Added activity
3-ST-1035	Garfield to Blaine - Side Storm (DC-013) EAST SIDE	0	Start to Start	NCR-003	NCR-003 CB-B30 - 20" PS Line Damaged	Logic tie added to incorporate NCR
3-W-1025	Install Mainline & Hydrants Sta. 75+40 to 65+21 - Stg 4 Galer to Blaine	0	Start to Start	NCR-011	NCR-011 Damaged a known 8" WM - broke existing corp valve	Logic tie added to incorporate NCR
3-W-1036	Install Mainline, Hydrants & Blocking Sta. 65+07 to 55+00 - Stg 5 Blaine to Boston	0	Start to Start	NCR-019	NCR-019 12X4 tees that were installed were the incorrect size per the plan	Logic tie added to incorporate NCR
3-W-1041	SPU Customer Notification - Stg 5 Blaine to Boston	0	Finish to Start	DSC-294	DSC-294 Stage 5 WM, WS-1211 & WS-1210 Sizes	Logic tie added to incorporate DSC
3-W-1044	SPU Transfer Services In Stage 5 - Stg 5 Blaine to Boston	0	Finish to Start	3-W-1047	SPU Temp Jumper Conn. @ Sta. 65+00 - Stg 5 Blaine to Boston	Stg.5 Water logic changes as-built
3-W-1046	SPU Connection Sta. 65+21 Yale Pl. - Stg 5 Blaine to Boston	0	Finish to Start	3-RW-1075	Pour Roadway - Garfield to Howe (E)	Stg.5 Water logic changes as-built
3-W-1047	SPU Temp Jumper Conn. @ Sta. 65+00 - Stg 5 Blaine to Boston	0	Start to Start	DSC-300	DSC-300 Stage 5 Unknown unmarked water service	Logic tie added to incorporate DSC
3-W-1080	SPU Water Ops Scheduling Notification - Stg 6 (Temp Services)	0	Start to Start	3-W-1051	SPU Temp Service Laterals (5 ea.) - Stg 6 Boston to Louisa	Stg.6 Water logic changes as-built
3-W-1081	SPU Temp Hydrant Laterals (2 ea.) - Stg 6 Boston to Louisa	0	Finish to Start	DSC-322	DSC-322 Stage 6 miss-marked water services	Logic tie added to incorporate DSC
3-W-1085	Install & Cure Thrust Collars - Stg 4 Galer to Blaine	0	Start to Start	NCR-017	NCR-017 Utility Strike	Logic tie added to incorporate NCR
4-CC-1471	Harrison - Conduit Crossings	0	Start to Start	NCR-016	NCR-016 6" gas main was struck and damaged	Logic tie added to incorporate NCR
4-PF-1526	YALE TO ALOHA - EAST SIDE - POLE FOUNDATIONS (3 ea.)	0	Start to Start	4-PF-1536	ALOHA - EAST SIDE Pole Foundations (2 ea,)	Replaced FS with SS
4-PF-1526	YALE TO ALOHA - EAST SIDE - POLE FOUNDATIONS (3 ea.)	0	Finish to Start	4-SW-1567	Remove Sidewalk - Yale NEC	Address pole foundation status Zone-4
4-PF-1529	VALLEY - EAST SIDE Pole Foundations (2 ea.)	0	Finish to Start	4-SW-1593	Remove Sidewalk - Valley NEC	Address pole foundation status Zone-4
4-PF-1536	ALOHA - EAST SIDE Pole Foundations (2 ea,)	0	Finish to Start	1-PF-0150	11th - Pole Foundations (After Yale to Aloha Zone-4 SDOT Mitigation)	Address pole foundation status Zone-4
4-SW-1571	Pour Sidewalks/Curb Ramps - Yale NEC	0	Start to Start	4-SW-1577	Pour Sidewalks/Curb Ramps - Yale SEC	Pour same time
4-SW-1574	Trench Electrical - Yale SEC	0	Finish to Start	DSC-323	DSC-323 SWC Yale & Fairview 8in Sidewalk	Logic tie added to incorporate DSC
4-WE-1480	Pour Roadway - Yale Ph.1 (WE)	0	Finish to Start	4-WE-1518	BOAT SHOW - CANNOT CLOSE ALOHA	BOAT SHOW
4-WE-1480	Pour Roadway - Yale Ph.1 (WE)	0	Finish to Start	4-SW-1573	Remove Sidewalk - Yale SEC	Previous driver v.40
4-WE-1489	Pour Roadway - Aloha Ph.1 (WE)	0	Finish to Start	4-WE-1519	Pour Roadway - Aloha / After DCS's 334, 335, 336	Logic tie added to incorporate DSC
4-WE-1499	COMPLETE CONDUIT YALE EAST SIDE	0	Start to Start	DSC-310	DSC-310 Yale East Side Unknown CB and Ductbank	Logic tie added to incorporate DSC
4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	0	Finish to Start	DSC-334	DSC-334 SEC Fairview & Aloha Plugged Inlet	Logic tie added to incorporate DSC

4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	0	Finish to Start	DSC-336	DSC-336 Fairview & Aloha Ex. Pole Foundation in Grade	Logic tie added to incorporate DSC
4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	0	Finish to Start	DSC-335	DSC-335 SEC Fairview & Aloha Comm Conduit Conflict	Logic tie added to incorporate DSC
4-WE-1518	BOAT SHOW - CANNOT CLOSE ALOHA	0	Finish to Start	4-WE-1488	Remove Roadway Type 2 - Aloha Ph.1 (WE)	BOAT SHOW
4-WE-1518	BOAT SHOW - CANNOT CLOSE ALOHA	0	Finish to Start	DSC-334	DSC-334 SEC Fairview & Aloha Plugged Inlet	BOAT SHOW Logic tie added for DSC
4-WE-1518	BOAT SHOW - CANNOT CLOSE ALOHA	0	Finish to Start	DSC-335	DSC-335 SEC Fairview & Aloha Comm Conduit Conflict	BOAT SHOW Logic tie added for DSC
4-WE-1518	BOAT SHOW - CANNOT CLOSE ALOHA	0	Finish to Start	DSC-336	DSC-336 Fairview & Aloha Ex. Pole Foundation in Grade	BOAT SHOW Logic tie added for DSC
4-WE-1519	Pour Roadway - Aloha / After DCS's 334, 335, 336	0	Finish to Start	4-SW-1579	Remove Sidewalk - Aloha NEC	Logic tie added to incorporate DSC
DSC-286	DSC 286 Harvard Monitoring Well Conflict	0	Finish to Start	DSC-292	DSC-292 SWC Fuhrman unknown unlocated duct bank	Logic tie added to incorporate DSC
DSC-292	DSC-292 SWC Fuhrman unknown unlocated duct bank	0	Finish to Finish	2-RW-694	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.1	Logic tie added to incorporate DSC
DSC-293	DSC-293 Stage 1 Sta 19+11 CDF Conflict	0	Finish to Start	DSC-295	DSC-295 Stage 1 WM, WS-301 Root Conflicts	Logic tie added to incorporate DSC
DSC-294	DSC-294 Stage 5 WM, WS-1211 & WS-1210 Sizes	0	Finish to Start	3-W-1044	SPU Transfer Services In Stage 5 - Stg 5 Blaine to Boston	Logic tie added to incorporate DSC
DSC-295	DSC-295 Stage 1 WM, WS-301 Root Conflicts	0	Finish to Start	2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	Logic tie added to incorporate DSC
DSC-296	DSC-296 11th Ave, T211-01 Potholing SS conflict	0	Finish to Finish	1-PF-0129	43rd - Pole Foundations (17 ea.) - PRIOR to Completion of SDOT Directed Additional Potholing	Logic tie added to incorporate DSC
DSC-296	DSC-296 11th Ave, T211-01 Potholing SS conflict	0	Finish to Start	DSC-301	DSC-301 11th 43rd to 42nd E. Side Sewer conflict w/foudnation T211.02	Logic tie added to incorporate DSC
DSC-296	DSC-296 11th Ave, T211-01 Potholing SS conflict	0	Finish to Start	DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved foundation creating excavation issues	Logic tie added to incorporate DSC
DSC-297	DSC-297 Stage 1 WM, WS-301 CDF Conflict	0	Finish to Start	2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	Logic tie added to incorporate DSC
DSC-298	DSC-298 Stage 1 WM, WS-207 Root Conflicts	0	Finish to Start	2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	Logic tie added to incorporate DSC
DSC-299	DSC-299 Stage 1 WM, WS-205 CDF Conflict	0	Finish to Start	2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	Logic tie added to incorporate DSC
DSC-300	DSC-300 Stage 5 Unknown unmarked water service	0	Finish to Start	3-W-1046	SPU Connection Sta. 65+21 Yale Pl. - Stg 5 Blaine to Boston	Logic tie added to incorporate DSC
DSC-301	DSC-301 11th 43rd to 42nd E. Side Sewer conflict w/foudnation T211.02	0	Finish to Finish	1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER Completion of SDOT Directed Additional Potholing	Logic tie added to incorporate DSC
DSC-301	DSC-301 11th 43rd to 42nd E. Side Sewer conflict w/foudnation T211.02	0	Start to Start	1-PF-0159	SDOT Stop Work E-mail / Issue Directive/Design	Logic tie added to incorporate DSC
DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved foundation creating excavation issues	0	Start to Start	1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER Completion of SDOT Directed Additional Potholing	Logic tie added to incorporate DSC
DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved foundation creating excavation issues	0	Start to Start	1-PF-0159	SDOT Stop Work E-mail / Issue Directive/Design	Logic tie added to incorporate DSC
DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved foundation creating excavation issues	0	Start to Start	DSC-311	DSC-311 43RD Roosevelt to 11th Boulder conflict with foundation T213-03	Logic tie added to incorporate DSC
DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved foundation creating excavation issues	0	Finish to Start	1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	Logic tie added to incorporate DSC
DSC-303	DSC-303 43rd/Roosevelt Sinkhole	0	Finish to Start	1-RW-0085	Pour Roadway - Roosevelt & 43rd (West)	Logic tie added to incorporate DSC
DSC-304	DSC-304 Fuhrman SWC, conduits in conflict with handhole	0	Finish to Start	2-SW-0741	Grade Sidewalks - Fuhrman SWC	Logic tie added to incorporate DSC
DSC-305	DSC-305 Fuhrman SWC wooden pole utilitues	0	Finish to Start	2-SW-0741	Grade Sidewalks - Fuhrman SWC	Logic tie added to incorporate DSC
DSC-306	DSC-306 Fuhrman SWC PPB in middle of ramp	0	Finish to Start	2-SW-0741	Grade Sidewalks - Fuhrman SWC	Logic tie added to incorporate DSC
DSC-307	DSC-307 Garfield WQ-B117 Unknown Unlocated Conduit	0	Finish to Start	DSC-309	DSC-309 Garfield East Side WQV B117 Conflict with Gas line	Logic tie added to incorporate DSC
DSC-308	DSC-308 NWC Fuhrman, Shallow Fiber Conduit Conflict	0	Finish to Start	2-SW-0747	Grade Sidewalks - Fuhrman NWC	Logic tie added to incorporate DSC
DSC-309	DSC-309 Garfield East Side WQV B117 Conflict with Gas line	0	Finish to Finish	3-RW-1075	Pour Roadway - Garfield to Howe (E)	Logic tie added to incorporate DSC
DSC-309	DSC-309 Garfield East Side WQV B117 Conflict with Gas line	0	Start to Start	DSC-317	DSC-317 Howe East side pavement thickness 18"	Logic tie added to incorporate DSC
DSC-309	DSC-309 Garfield East Side WQV B117 Conflict with Gas line	0	Start to Start	DSC-319	DSC-319 Garfield WQV B117 to CB B34 will not work per plan	Logic tie added to incorporate DSC
DSC-310	DSC-310 Yale East Side Unknown CB and Ductbank	0	Finish to Start	4-WE-1479	Remove Roadway Type 2 - Yale Ph.1 (WE)	Logic tie added to incorporate DSC
DSC-310	DSC-310 Yale East Side Unknown CB and Ductbank	0	Finish to Start	DSC-312	DSC-312 NEC Aloha unknown unmarked conduits	Logic tie added to incorporate DSC
DSC-310	DSC-310 Yale East Side Unknown CB and Ductbank	0	Finish to Start	DSC-313	DSC-313 Aloha unknown unlocated Fiber line	Logic tie added to incorporate DSC

DSC-310	DSC-310 Yale East Side Unknown CB and Ductbank	0	Finish to Start	DSC-314	DSC-314 Aloha Unknown unlocated conduit	Logic tie added to incorporate DSC
DSC-311	DSC-311 43RD Roosevelt to 11th Boulder conflict with foundation T213-03	0	Finish to Finish	1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER Completion of SDOT Directed Additional Potholing	Logic tie added to incorporate DSC
DSC-312	DSC-312 NEC Aloha unknown unmarked conduits	0	Finish to Finish	4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	Logic tie added to incorporate DSC
DSC-312	DSC-312 NEC Aloha unknown unmarked conduits	0	Finish to Start	DSC-315	DSC-315 Aloha East Contaminated Soils	Logic tie added to incorporate DSC
DSC-313	DSC-313 Aloha unknown unlocated Fiber line	0	Finish to Finish	4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	Logic tie added to incorporate DSC
DSC-313	DSC-313 Aloha unknown unlocated Fiber line	0	Finish to Start	DSC-315	DSC-315 Aloha East Contaminated Soils	Logic tie added to incorporate DSC
DSC-314	DSC-314 Aloha Unknown unlocated conduit	0	Finish to Finish	4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	Logic tie added to incorporate DSC
DSC-314	DSC-314 Aloha Unknown unlocated conduit	0	Finish to Start	DSC-315	DSC-315 Aloha East Contaminated Soils	Logic tie added to incorporate DSC
DSC-315	DSC-315 Aloha East Contaminated Soils	0	Finish to Finish	4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	Logic tie added to incorporate DSC
DSC-316	DSC-316 Stage 2 Temp Main unlocated unknown water service conflict with temp main	0	Finish to Start	DSC-321	DSC-321 Unknown Unlocated Water Service STA 28+80 stage 2	Logic tie added to incorporate DSC
DSC-317	DSC-317 Howe East side pavement thickness 18"	0	Finish to Start	DSC-340	DSC-340 NEC Garfield Ex. MH Elevation Conflict	Logic tie added to incorporate DSC
DSC-317	DSC-317 Howe East side pavement thickness 18"	0	Finish to Start	3-RW-1075	Pour Roadway - Garfield to Howe (E)	Logic tie added to incorporate DSC
DSC-318	DSC-318 Harvard East side shallow DB in conflict with roadway	0	Finish to Start	2-RW-664	Pour Roadway - Harvard to Fuhrman (W) Ph.2	Logic tie added to incorporate DSC
DSC-319	DSC-319 Garfield WQV B117 to CB B34 will not work per plan	0	Finish to Start	DSC-340	DSC-340 NEC Garfield Ex. MH Elevation Conflict	Logic tie added to incorporate DSC
DSC-319	DSC-319 Garfield WQV B117 to CB B34 will not work per plan	0	Finish to Start	3-RW-1075	Pour Roadway - Garfield to Howe (E)	Logic tie added to incorporate DSC
DSC-320	DSC-320 Stage 2 temp main CDF Encased existing main	0	Start to Start	DSC-316	DSC-316 Stage 2 Temp Main unlocated unknown water service conflict with temp main	Logic tie added to incorporate DSC
DSC-320	DSC-320 Stage 2 temp main CDF Encased existing main	0	Finish to Start	DSC-321	DSC-321 Unknown Unlocated Water Service STA 28+80 stage 2	Logic tie added to incorporate DSC
DSC-321	DSC-321 Unknown Unlocated Water Service STA 28+80 stage 2	0	Finish to Start	2-W-0616	Test & Flush TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	Logic tie added to incorporate DSC
DSC-322	DSC-322 Stage 6 miss-marked water services	0	Finish to Start	DSC-326	DSC-326 Stage 6 existing storm in conflict with watermain at Boston	Logic tie added to incorporate DSC
DSC-322	DSC-322 Stage 6 miss-marked water services	0	Finish to Finish	3-W-1052	Install Mainline & Hydrants Sta. 44+64 to 50+00 - Stg 6 Boston to Louisa	Logic tie added to incorporate DSC
DSC-323	DSC-323 SWC Yale & Fairview 8in Sidewalk	0	Finish to Finish	4-SW-1575	Electrical - Yale SEC	Logic tie added to incorporate DSC
DSC-323	DSC-323 SWC Yale & Fairview 8in Sidewalk	0	Finish to Start	DSC-325	DSC-325 SEC Yale & Fairview Unlocated Utility	Logic tie added to incorporate DSC
DSC-324	DSC-324 Leaking Services at T2.1 Hamlin, WS- 503,504	0	Finish to Start	2-W-0626	Bact Results TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	Logic tie added to incorporate DSC
DSC-325	DSC-325 SEC Yale & Fairview Unlocated Utility	0	Finish to Finish	4-SW-1575	Electrical - Yale SEC	Logic tie added to incorporate DSC
DSC-326	DSC-326 Stage 6 existing storm in conflict with watermain at Boston	0	Finish to Finish	3-W-1052	Install Mainline & Hydrants Sta. 44+64 to 50+00 - Stg 6 Boston to Louisa	Logic tie added to incorporate DSC
DSC-326	DSC-326 Stage 6 existing storm in conflict with watermain at Boston	0	Finish to Start	DSC-337	DSC-337 Stage 6 WM, Power Conflict at 50+79	Logic tie added to incorporate DSC
DSC-327	DSC-327 43rd & Roosevelt Rotten Pole	0	Finish to Start	DSC-328	DSC-328 SEC 43rd Roosevelt Conduits Cast in Curb	Logic tie added to incorporate DSC
DSC-328	DSC-328 SEC 43rd Roosevelt Conduits Cast in Curb	0	Finish to Start	1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	Logic tie added to incorporate DSC
DSC-329	DSC-329 11th Ave Ground Water in OCS foundations	0	Finish to Start	DSC-341	DSC-341 43rd & 11th Signal Service Conflict w/ Temp Lighting	Logic tie added to incorporate DSC
DSC-330	DSC-330 WM Stg 2 Unlocated Steel Pipe STA 27+86	0	Finish to Start	2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & Hydrants (7 ea.)	Logic tie added to incorporate DSC
DSC-331	DSC-331 Stage 2 WM 1IN Copper Line at 27+70	0	Finish to Start	2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & Hydrants (7 ea.)	Logic tie added to incorporate DSC
DSC-332	DSC-332 Stage 2 WM 2EA 2IN Steel Pipes near WS-604	0	Finish to Start	2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & Hydrants (7 ea.)	Logic tie added to incorporate DSC
DSC-334	DSC-334 SEC Fairview & Aloha Plugged Inlet	0	Finish to Start	4-WE-1519	Pour Roadway - Aloha / After DCS's 334, 335, 336	Logic tie added to incorporate DSC
DSC-335	DSC-335 SEC Fairview & Aloha Comm Conduit Conflict	0	Finish to Start	4-WE-1519	Pour Roadway - Aloha / After DCS's 334, 335, 336	Logic tie added to incorporate DSC
DSC-336	DSC-336 Fairview & Aloha Ex. Pole Foundation in Grade	0	Finish to Start	4-WE-1519	Pour Roadway - Aloha / After DCS's 334, 335, 336	Logic tie added to incorporate DSC
DSC-336	DSC-336 Fairview & Aloha Ex. Pole Foundation in Grade	0	Start to Start	DSC-339	DSC-339 Aloha P2904 Ground Water at 13'	Logic tie added to incorporate DSC
DSC-337	DSC-337 Stage 6 WM, Power Conflict at 50+79	0	Finish to Finish	3-W-1053	Install Mainline & Hydrants Sta. 50+00 to 54+86 - Stg 6 Boston to Louisa	Logic tie added to incorporate DSC

DSC-338	DSC-338 Stage 2 WM Unknown Utility at STA 26+90	0	Finish to Start	2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & Hydrants (7 ea.)	Logic tie added to incorporate DSC
DSC-339	DSC-339 Aloha P2904 Ground Water at 13'	0	Finish to Finish	4-PF-1526	YALE TO ALOHA - EAST SIDE - POLE FOUNDATIONS (3 ea.)	Logic tie added to incorporate DSC
DSC-340	DSC-340 NEC Garfield Ex. MH Elevation Conflict	0	Finish to Finish	3-RW-1075	Pour Roadway - Garfield to Howe (E)	Logic tie added to incorporate DSC
DSC-341	DSC-341 43rd & 11th Signal Service Conflict w/ Temp Lighting	0	Finish to Start	DSC-351	DSC-351 Pole Foundation P-0204 SW 11th & Roosevelt	Logic tie added to incorporate DSC
DSC-351	DSC-351 Pole Foundation P-0204 SW 11th & Roosevelt	0	Finish to Start	1-SW-0169	Remove Sidewalk - 43rd / 11to to Roosevelt (S)	Logic tie added to incorporate DSC
DSC-351	DSC-351 Pole Foundation P-0204 SW 11th & Roosevelt	0	Finish to Start	1-PF-0132	Eastlake - Pole Foundations (10 ea.)	Logic tie added to incorporate DSC
FM0059.12	Aloha to Valley (not affected by Stop Work Order) - Storm	0	Start to Start	NCR-009	NCR-009 SCL Conduits damaged	Logic tie added to incorporate NCR
FM-TBD	SDOT Directed Potholing - 11th Ave NE	0	Finish to Start	1-RW-0089	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (West)	Rev. to Z1 pole fdn def. due to changes
NCR-001	NCR-001 CB-B07 - 15" PS Line Damaged	0	Finish to Start	2-ST-0450	Shelby and Eastlake - Storm (After DSC-049)	Logic tie added to incorporate NCR
NCR-0014015	NCR-014 & NCR-015 Paving	0	Finish to Start	1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	Logic tie added to incorporate NCR
NCR-002	NCR-002 CB-B10 - 8" DIP Removed allowing Type 9 in Pipe	0	Finish to Start	2-ST-0452	Hamlin and Eastlake - Storm	Logic tie added to incorporate NCR
NCR-003	NCR-003 CB-B30 - 20" PS Line Damaged	0	Finish to Start	3-ST-1009	Newton - Side Storm (WEST SIDE)	Logic tie added to incorporate NCR
NCR-004	NCR-004 TR Flex Wedge Restraint Glands incorrectly used	0	Finish to Start	1-W-0034	Install Main on 11th - Watermain Stg 8	Logic tie added to incorporate NCR
NCR-005	NCR-005 Earthquake Joint installed into CB-11 beyond 1' limit	0	Finish to Start	2-ST-0455	Louisa St and Eastlake - Storm	Logic tie added to incorporate NCR
NCR-006	NCR-006 Marking tape not installed over conduit run	0	Finish to Finish	1-EC-0057	Misc Vault Backfill & Coring @ 43rd	Logic tie added to incorporate NCR
NCR-007	NCR-007 Surveyed 1.81' lower than design	0	Finish to Start	2-W-0484	Install Mainline - Stg 7 Eastlake/Fuhrman to Harvard	Logic tie added to incorporate NCR
NCR-008	NCR-008 Conduits damaged during exposure of CDF duct bank	0	Finish to Finish	2-W-0649	Suspend Stage 1 (go to Stage 7)	Logic tie added to incorporate NCR
NCR-009	NCR-009 SCL Conduits damaged	0	Finish to Start	4-ST-1465	Westlake and Virginia - Storm	Logic tie added to incorporate NCR
NCR-010	NCR-010 An active existing Type II SCL handhole was damaged	0	Finish to Start	1-RW-0059	Pour Roadway - 43rd / Roosevelt to 11th	Logic tie added to incorporate NCR
NCR-011	NCR-011 Damaged a known 8" WM - broke existing corp valve	0	Finish to Start	3-W-1085	Install & Cure Thrust Collars - Stg 4 Galer to Blaine	Logic tie added to incorporate NCR
NCR-012	NCR-012 Damaged a known 8" WM - broke existing corp valve	0	Finish to Start	NCR-013	NCR-013 Damaged pedestrian signal	Logic tie added to incorporate NCR
NCR-013	NCR-013 Damaged pedestrian signal	0	Finish to Start	1-RW-0063	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.1)	Logic tie added to incorporate NCR
NCR-014	NCR-014 Spalling at joints of PCCP panels	0	Finish to Start	1-RW-0061	Temp Pave - 43rd / Roosevelt to 11th	Logic tie added to incorporate NCR
NCR-015	NCR-015 Finish of PCCP panel not per specification	0	Finish to Start	1-RW-0061	Temp Pave - 43rd / Roosevelt to 11th	Logic tie added to incorporate NCR
NCR-016	NCR-016 6" gas main was struck and damaged	0	Finish to Start	4-CC-1470	Valley - Conduit Crossings	Logic tie added to incorporate NCR
NCR-017	NCR-017 Utility Strike	0	Finish to Start	3-W-1075	Install Main Lateral @ Galer Sta. 900+05 to 900+20 - Stg 4 Galer to Blaine	Logic tie added to incorporate NCR
NCR-018	NCR-018 Saw Cuts for transverse cut are not per approved plan	0	Finish to Start	2-RW-0572	Patch Pave - Harvard to Fuhrman (E)	Logic tie added to incorporate NCR
NCR-019	NCR-019 12X4 tees that were installed were the incorrect size per the plan	0	Finish to Start	3-W-1039	Test & Flush - Stg 5 Blaine to Boston	Logic tie added to incorporate NCR
NCR-020	NCR-020 Jansen ruptured a 1 ½" service line	0	Finish to Start	2-W-0468	Bact Results - Stg 1 Harvard to Hamlin	Logic tie added to incorporate NCR
NCR-021	NCR-021 Riser is cast to the incorrect height bringing the lid to 1 1/8" above grade.	0	Finish to Start	1-RW-0081	Curb - 43rd / 11th to 12th	Logic tie added to incorporate NCR
NCR-022	NCR-022 Damage to panel while removing adjacent panel	0	Finish to Start	1-RW-0082	Temp Pave - 43rd / 11th to 12th	Logic tie added to incorporate NCR
NCR-023	NCR-023 Electrical loop not installed	0	Finish to Start	3-RW-1071	Curb - Galer to Garfield (E)	Logic tie added to incorporate NCR

The following Successor Activity Relationships been deleted from the project						
Activity ID	**Activity Name**	**Relationship Lag**	**Relationship Type**	**Successor Activity Id**	**Successor Activity Name**	**Comments / Notes**
1-RW-0094	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Campus (West)	0	Finish to Start	1-RW-0098	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (East)	Swap sequence 11th, Eastlake, Campus
1-RW-0096	Curb - Eastlake / 11th to NE Campus (West)	0	Finish to Start	1-RW-0100	Curb - 11th & Eastlake (East)	Swap sequence 11th, Eastlake, Campus

1-RW-0098	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (East)	0	Finish to Start	1-RW-0102	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Campus (East)	Swap sequence 11th, Eastlake, Campus
1-RW-0100	Curb - 11th & Eastlake (East)	0	Finish to Start	1-RW-0104	Curb - Eastlake / 11th to NE Campus (East)	Swap sequence 11th, Eastlake, Campus
2-RW-644	Patch Pave - Harvard to Fuhrman (W) Ph.3	0	Finish to Start	2-RW-0564	Roadway Demo & Exc - Shelby to Harvard (E)	PRED not req'd
2-RW-644	Patch Pave - Harvard to Fuhrman (W) Ph.3	0	Finish to Finish	2-RW-0602	TROLLEY REACTIVATION Harvard to Fuhrman (8/29/25)	PRED not req'd
2-RW-654	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.2	0	Finish to Start	2-RW-614	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.3	As-built; seq. change
2-RW-684	Patch Pave - Harvard to Fuhrman (W) Ph.2	0	Finish to Start	2-RW-614	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.3	As-built; seq. change
2-RW-714	Curb - Harvard to Fuhrman (W) Ph.1	0	Finish to Start	2-RW-724	Patch Pave - Harvard to Fuhrman (W) Ph.1	As-built; seq. change
2-SW-0733	Trench Electrical - Harvard NWC	0	Finish to Start	2-SW-0738	Remove Sidewalk - Fuhrman SWC	Logic change to advance work
2-SW-0735	Grade Sidewalks - Harvard NWC	0	Finish to Start	2-SW-0738	Remove Sidewalk - Fuhrman SWC	Logic change to advance work
2-SW-0736	Pour Sidewalks/Curb Ramps - Harvard NWC	0	Finish to Start	2-SW-0742	Pour Sidewalks/Curb Ramps - Fuhrman SWC	Logic change to advance work
2-SW-0739	Trench Electrical - Fuhrman SWC	0	Finish to Start	2-SW-0744	Remove Sidewalk - Fuhrman NWC	Logic change to advance work
2-SW-0742	Pour Sidewalks/Curb Ramps - Fuhrman SWC	0	Finish to Start	2-SW-0744	Remove Sidewalk - Fuhrman NWC	Logic change to advance work
2-SW-0742	Pour Sidewalks/Curb Ramps - Fuhrman SWC	0	Finish to Start	2-SW-0748	Pour Sidewalks/Curb Ramps - Fuhrman NWC	Logic change to advance work
2-W-0470	Excavate Tie-Ins - Stg 1 Harvard to Hamlin	0	Finish to Start	2-W-0496	Excavate CC05, 06, 07 - Stg 2 Hamlin to Edgar	Activity deleted
2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	0	Finish to Start	2-W-0473	SPU Transfer Services - Stg 1 Harvard to Hamlin (21 ea.)	Stg.1 Water logic changes as-built
2-W-0485	Test & Flush Mainline - Stg 7 Eastlake/Fuhrman to Harvard	0	Finish to Start	2-W-0496	Excavate CC05, 06, 07 - Stg 2 Hamlin to Edgar	Activity deleted
2-W-0496	Excavate CC05, 06, 07 - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0498	SPU Cut/Cap CC05, 06, 07 - Stg 2 Hamlin to Edgar	Activity deleted
2-W-0498	SPU Cut/Cap CC05, 06, 07 - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0499	Install Watermain, Hydrants & Blocking Sta. 21+64 to 33+19 - Stg 2 Hamlin to Edgar	Activity deleted
2-W-0536	SPU Water Ops Scheduling Notification - Stg 2 (CC05, 06, 07)	0	Finish to Start	2-W-0498	SPU Cut/Cap CC05, 06, 07 - Stg 2 Hamlin to Edgar	Activity deleted
2-W-0550	Mainline Lateral @ Hamlin - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0499	Install Watermain, Hydrants & Blocking Sta. 21+64 to 33+19 - Stg 2 Hamlin to Edgar	Stg.2 Water logic changes as-built
2-W-0554	SPU Temp Jumper Conn. Sta. 21+50 - Stg 1 Harvard to Hamlin	0	Finish to Start	2-W-0498	SPU Cut/Cap CC05, 06, 07 - Stg 2 Hamlin to Edgar	Activity deleted
2-W-0560	Install Thrust Collar & Cure - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0500	Test & Flush Water Main - Stg 2 Hamlin to Edgar	Stg.2 Water logic changes as-built
2-W-0626	Bact Results TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	0	Finish to Start	2-W-0496	Excavate CC05, 06, 07 - Stg 2 Hamlin to Edgar	Activity deleted
3-RW-1072	Patch Pave - Galer to Garfield (E)	0	Finish to Start	3-RW-1074	Roadway Demo & Exc - Garfield to Howe (E)	Work advanced earlier than forecast
3-RW-1082	Patch Pave - Galer to Garfield (W)	0	Finish to Start	3-WE-1110	Remove Roadway Type 2 - Galer (E) Ph.1	Work advanced earlier than forecast
3-W-1046	SPU Connection Sta. 65+21 Yale Pl. - Stg 5 Blaine to Boston	0	Start to Start	3-W-1047	SPU Temp Jumper Conn. @ Sta. 65+00 - Stg 5 Blaine to Boston	Stg.5 Water logic changes as-built
3-W-1080	SPU Water Ops Scheduling Notification - Stg 6 (Temp Services)	0	Finish to Start	3-W-1051	SPU Temp Service Laterals (5 ea.) - Stg 6 Boston to Louisa	Stg.6 Water logic changes as-built
4-PF-1526	YALE TO ALOHA - EAST SIDE - POLE FOUNDATIONS (3 ea.)	0	Finish to Start	4-PF-1536	ALOHA - EAST SIDE Pole Foundations (2 ea,)	Replaced with SS
4-PF-1529	VALLEY - EAST SIDE Pole Foundations (2 ea.)	0	Finish to Start	4-SW-1567	Remove Sidewalk - Yale NEC	PRED not req'd; as-built seq.
4-SW-1568	Trench Electrical - Yale NEC	0	Finish to Start	4-SW-1573	Remove Sidewalk - Yale SEC	PRED not req'd; as-built seq.
4-SW-1571	Pour Sidewalks/Curb Ramps - Yale NEC	0	Finish to Start	4-SW-1577	Pour Sidewalks/Curb Ramps - Yale SEC	Replaced with SS
DSC-270	DSC-270 11th 43rd to 42nd Pole T-211-06 Side Sewer conflict	0	Start to Finish	1-PF-0130	11th - Pole Foundations (17 ea.) Prior to SDOT Directed Additional Potholing	Cleanup SF tie

CRITICAL PATH

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)														
Milestones														
M-8000	Start Early Submittal Process	0	0	0	0	0	0	11-Sep-24 A				0	0	☑
M-9000	NTP	1	1	0	1	0	1	07-Oct-24 A	07-Oct-24 A			0	0	☑
M-9001	CONTRACT TIME	594	616	-3	223	396	619	07-Oct-24 A	06-May-27	-25	-22	0	-3	☑
M-9003	Substantial Completion	0	0	0	0	0	0		01-Apr-27	-25	-22	-3	-3	☑
M-9013	Final Inspection	1	1	0	0	1	1	02-Apr-27	02-Apr-27	-25	-22	-3	-3	☑
M-9004	Punch List	20	20	0	0	20	20	05-Apr-27	30-Apr-27	-25	-22	-3	-3	☑
M-9005	Physical Completion	0	0	0	0	0	0	03-May-27	03-May-27	-25	-22	-3	-3	☑
M-9006	Owner Caused Delays	4	4	0	0	4	4	03-May-27	06-May-27	-25	-22	-3	-3	☑
M-9007	Project Completion	0	0	0	0	0	0		06-May-27*	-25	-22	-3	-3	☑
Long Lead Material														
Watermain														
PROC-0009	Lay Drawings - Watermain (Submit)	1	1	0	1	0	1	03-Oct-24 A	03-Oct-24 A			0	0	☑
PROC-0010	Lay Drawings Review - Watermain (Review / R&R)	14	16	0	16	0	16	03-Oct-24 A	25-Oct-24 A			0	0	☑
PROC-0020	Lay Drawings Review - Watermain (Resubmittal)	10	8	0	8	0	8	28-Oct-24 A	06-Nov-24 A			0	0	☑
PROC-0030	Lay Drawings Review - Watermain (2nd Review)	15	10	0	10	0	10	07-Nov-24 A	21-Nov-24 A			0	0	☑
PROC-0040	Lay Drawings Review - Watermain (Resubmittal #2)	4	5	0	5	0	5	22-Nov-24 A	02-Dec-24 A			0	0	☑
PROC-0021	Lay Drawings Review - Watermain (3rd Review)	15	16	0	16	0	16	03-Dec-24 A	24-Dec-24 A			0	0	☑
PROC-0011	Procure Watermain - Watermain	21	21	0	21	0	21	24-Dec-24 A	30-Jan-25 A			0	0	☑
Project Start Up														
TCP-001	Garfield Temp Signal Plan Delay	3	3	0	3	0	3	07-Oct-24 A	09-Oct-24 A			0	0	☑
PST-0016	Install Erosion Control	5	5	0	5	0	5	07-Oct-24 A	11-Oct-24 A			0	0	☑
PST-0015	Site Set Up	4	4	0	4	0	4	10-Oct-24 A	16-Oct-24 A			0	0	☑
Zone 1 - 43rd to University Bridge														
Pole Foundation Potholing														
DSC's														
DSC-002	DSC-002 SW Corner 42nd & 11th Comm Cabinet Conflict P-0303	15	194	0	194	0	194	11-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-003	DSC-003 NW Corner 43rd & 11th Conflict w/Retaining Wall	14	193	0	193	0	193	15-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-004	DSC-004 NE Corner 11th & 43rd P-0201 Conflict	13	192	0	192	0	192	16-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-016	DSC-016 SE Corner 42nd & 11th P-0304 Conduit Conflicts	6	185	0	185	0	185	25-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-017	DSC-017 NE Corner Eastlake & 11th T-212-06 Gas Line Conflict	6	185	0	185	0	185	25-Oct-24 A	01-Aug-25 A			0	0	☑
FM-TBD	SDOT Directed Potholing - 11th Ave NE	11	11	6	5	0	5	04-Aug-25 A	08-Aug-25 A		-16	0	6	☑
Storm Work														
1-ST-0044	Complete Storm NEC 43rd & Roosevelt & 42nd	3	3	0	3	0	3	17-Apr-25 A	21-Apr-25 A			0	0	☑
DSC-201	DSC-201 42nd & 11th NWC - CB A8 Thick Road	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	☑
DSC-202	DSC-202 42nd & 11th NWC - CB A8 Conduit Conflict	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	☑
1-ST-DC-055A	DESIGN CHANGE 055	10	37	0	37	0	37	05-May-25 A	26-Jun-25 A			0	0	☑
DSC-206	DSC-206 43rd and and 11th DC 55 Storm conflict with conduit	1	1	0	1	0	1	08-May-25 A	08-May-25 A			0	0	☑
DSC-212	DSC-212 SWC 43rd and 11th Type 250 hood will not work with DC	1	1	0	1	0	1	15-May-25 A	15-May-25 A			0	0	☑
1-ST-DC-055A10	DESIGN CHANGE 055 - SPU WATER RELOCATION	2	2	0	2	0	2	27-Jun-25 A	30-Jun-25 A			0	0	☑
1-ST-DC-055A20	DESIGN CHANGE 055 - 42nd & 11th STORM	2	4	0	4	0	4	30-Jun-25 A	03-Jul-25 A			0	0	☑
Watermain Stage 8														
SPU Ops Notifications														
1-W-0052	SPU Water Ops Scheduling Notification - Stg 8 Cut/Cap	15	14	0	14	0	14	11-Dec-24 A	07-Jan-25 A			0	0	☑
Stage 8 Waterline Installation														
DSC-066	DSC-066 43rd & Roosevelt Stg. 8 Water Conflict w/Hydrant Tee	4	34	0	34	0	34	02-Jan-25 A	24-Feb-25 A			0	0	☑
1-W-0032	SPU Cut/Cap CC01 & CC02 - Watermain Stg 8 (43rd & 11th)	1	1	0	1	0	1	08-Jan-25 A	08-Jan-25 A			0	0	☑
DSC-099	DSC-099 43rd Water Main Conflict With Ductbank	1	1	0	1	0	1	03-Feb-25 A	03-Feb-25 A			0	0	☑
1-W-0033	Install Mainline & Hydrants - Watermain Stg 8	12	17	0	17	0	17	03-Feb-25 A	28-Feb-25 A			0	0	☑
DSC-115	DSC-115 11th Ave @ 43rd Unlocated 3-inch Conduit	1	1	0	1	0	1	24-Feb-25 A	24-Feb-25 A			0	0	☑
DSC-118	DSC-118 43rd & 12th Conduit & Storm Conflict @ Watermain	1	1	0	1	0	1	28-Feb-25 A	28-Feb-25 A			0	0	☑
1-W-0034	Install Main on 11th - Watermain Stg 8	2	2	0	2	0	2	03-Mar-25 A	04-Mar-25 A			0	0	☑
DSC-120	DSC-120 11th & 43rd South Leg Water Conflict w/Ductbank	2	2	0	2	0	2	03-Mar-25 A	04-Mar-25 A			0	0	☑

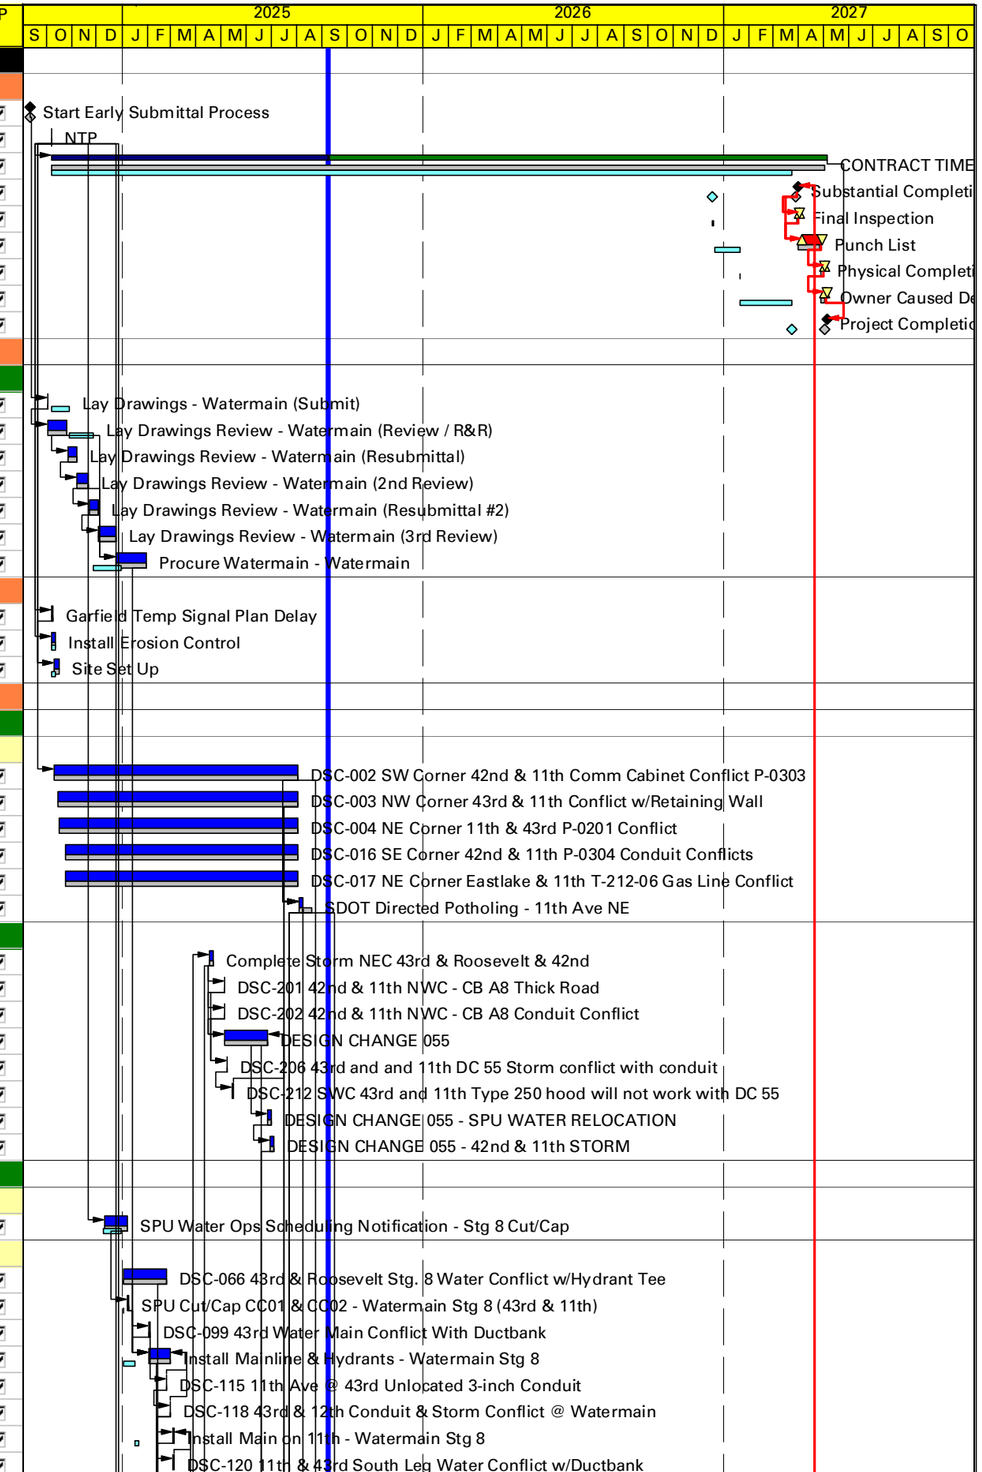

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filters: Longest Path, SELECT (J-LINE), SELECT2.
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-122	DSC-122 43rd & Roosevelt Hydrant Conflict w/Ductbank	1	1	0	1	0	1	04-Mar-25 A	04-Mar-25 A			0	0	☑
1-W-0036	Test & Flush - Watermain Stg 8	2	2	0	2	0	2	05-Mar-25 A	06-Mar-25 A			0	0	☑
1-W-0040	Excavate Tie-Ins - Watermain Stg 8	3	7	0	7	0	7	07-Mar-25 A	17-Mar-25 A			0	0	☑
Electrical Crossings														
1-EC-0048	43rd and 11th 3 Ea - Electrical Crossing	9	9	0	9	0	9	18-Mar-25 A	28-Mar-25 A			0	0	☑
1-EC-0049	Roosevelt and 43rd 3 Ea - Electrical Crossing	7	7	0	7	0	7	24-Mar-25 A	01-Apr-25 A			0	0	☑
DSC-162	DSC-162 43rd and 11th Eastern Conduit Crossing Ductbank Confli	1	1	0	1	0	1	31-Mar-25 A	31-Mar-25 A			0	0	☑
1-EC-0047	42nd and 11th 2 Each - Electrical Crossing	6	6	0	6	0	6	31-Mar-25 A	07-Apr-25 A			0	0	☑
DSC-163	DSC-163 43rd & 11th SEC Ductbank Conflict with Conduit	1	1	0	1	0	1	01-Apr-25 A	01-Apr-25 A			0	0	☑
1-EC-0057	Misc Vault Backfill & Coring @ 43rd	7	7	0	7	0	7	08-Apr-25 A	16-Apr-25 A			0	0	☑
1-EC-0046	Roosevelt and 42nd 1 Ea - Electrical Crossing	18	36	0	36	0	36	17-Apr-25 A	06-Jun-25 A			0	0	☑
1-EC-DC-055A	Design Change 055 - 43rd & 11th Added Crossing	4	4	0	4	0	4	27-May-25 A	30-May-25 A			0	0	☑
DSC-226	DSC-226 NEC 42nd and Roosevelt Unknown brick structure confli	1	1	0	1	0	1	03-Jun-25 A	03-Jun-25 A			0	0	☑
Roadway														
43rd Roosevelt to 11th														
1-RW-0058	Remove Roadway, Common Ex, Type 2 - 43rd / Roosevelt to 11th	6	6	0	6	0	6	01-May-25 A	08-May-25 A			0	0	☑
1-RW-0129	Adjust SCL Vault Adjustments	3	3	0	3	0	3	06-May-25 A	08-May-25 A			0	0	☑
1-RW-0059	Pour Roadway - 43rd / Roosevelt to 11th	4	8	0	8	0	8	09-May-25 A	20-May-25 A			0	0	☑
1-RW-0060	Curb - 43rd / Roosevelt to 11th	2	2	0	2	0	2	21-May-25 A	22-May-25 A			0	0	☑
1-RW-0061	Temp Pave - 43rd / Roosevelt to 11th	1	1	0	1	0	1	23-May-25 A	23-May-25 A			0	0	☑
11th and 42nd Phase 1														
1-RW-0063	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.1)	2	2	0	2	0	2	02-Jun-25 A	03-Jun-25 A			0	0	☑
1-RW-0064	Pour Roadway - 11th & 42nd (Ph.1)	2	2	0	2	0	2	04-Jun-25 A	05-Jun-25 A			0	0	☑
1-RW-0065	Temp Pave - 11th & 42nd (Ph.1)	1	1	0	1	0	1	06-Jun-25 A	06-Jun-25 A			0	0	☑
11th and 42nd Phase 2														
1-RW-0067	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.2)	1	1	0	1	0	1	09-Jun-25 A	09-Jun-25 A			0	0	☑
1-RW-0068	Pour Roadway - 11th & 42nd (Ph.2)	1	1	0	1	0	1	11-Jun-25 A	11-Jun-25 A			0	0	☑
1-RW-0069	Temp Pave - 11th & 42nd (Ph.2)	2	2	0	2	0	2	12-Jun-25 A	13-Jun-25 A			0	0	☑
11th and 42nd Phase 3														
1-RW-0071	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.3)	5	5	0	5	0	5	17-Jun-25 A	24-Jun-25 A			0	0	☑
1-RW-0072	Pour Roadway - 11th & 42nd (Ph.3)	2	2	0	2	0	2	25-Jun-25 A	26-Jun-25 A			0	0	☑
1-RW-0073	Temp Pave - 11th & 42nd (Ph.3)	1	1	0	1	0	1	27-Jun-25 A	27-Jun-25 A			0	0	☑
43rd 11th to 12th														
1-RW-0079	Remove Roadway, Common Ex, Type 2 - 43rd / 11th to 12th	6	7	0	7	0	7	26-Jun-25 A	07-Jul-25 A			0	0	☑
1-RW-0080	Pour Roadway - 43rd / 11th to 12th	17	17	0	17	0	17	08-Jul-25 A	30-Jul-25 A			0	0	☑
DC-XXX	RFI-136 Elevation Issues	13	13	0	13	0	13	10-Jul-25 A	28-Jul-25 A			0	0	☑
1-RW-0081	Curb - 43rd / 11th to 12th	3	3	0	3	0	3	31-Jul-25 A	04-Aug-25 A			0	0	☑
1-RW-0082	Temp Pave - 43rd / 11th to 12th	1	1	0	1	0	1	05-Aug-25 A	05-Aug-25 A		-16	0	0	☑
11th and 42nd Phase 4														
1-RW-0075	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.4)	3	3	0	3	0	3	08-Jul-25 A	10-Jul-25 A			0	0	☑
1-RW-0076	Pour Roadway - 11th & 42nd (Ph.4)	3	3	0	3	0	3	11-Jul-25 A	15-Jul-25 A			0	0	☑
1-RW-0077	Temp Pave - 11th & 42nd (Ph.4)	1	1	0	1	0	1	16-Jul-25 A	16-Jul-25 A			0	0	☑
Pole Foundations														
DSC-266	DSC-266 11th 43rd to 42nd Pole foundation conflicts with comm c	1	1	0	1	0	1	17-Jul-25 A	17-Jul-25 A			0	0	☑
DSC-270	DSC-270 11th 43rd to 42nd Pole T-211-06 Side Sewer conflict	1	1	0	1	0	1	18-Jul-25 A	18-Jul-25 A			0	0	☑
1-PF-0130	11th - Pole Foundations (17 ea.) Prior to SDOT Directed Additiona	11	11	0	11	0	11	21-Jul-25 A	04-Aug-25 A			0	0	☑
1-PF-0129	43rd - Pole Foundations (17 ea.) - PRIOR to Completion of SDOT D	10	10	6	4	0	4	05-Aug-25 A	08-Aug-25 A		-16	0	6	☑
DSC-296	DSC-296 11th Ave, T211-01 Potholing SS conflict	1	0	-1	1	0	1	06-Aug-25 A	06-Aug-25 A					☑
1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER C	7	7	-6	13	0	13	11-Aug-25 A	27-Aug-25 A		-16	6	0	☑
DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved fc	1	0	-15	15	0	15	11-Aug-25 A	29-Aug-25 A					☑
1-PF-0159	SDOT Stop Work E-mail / Issue Directive/Design	1	0	-15	15	0	15	11-Aug-25 A	29-Aug-25 A					☑
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	11	11	9	2	0	2	28-Aug-25 A	29-Aug-25 A		5	0	9	☑
1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	4	0	-4	4	0	4	02-Sep-25 A	05-Sep-25 A					☑
Sidewalks														

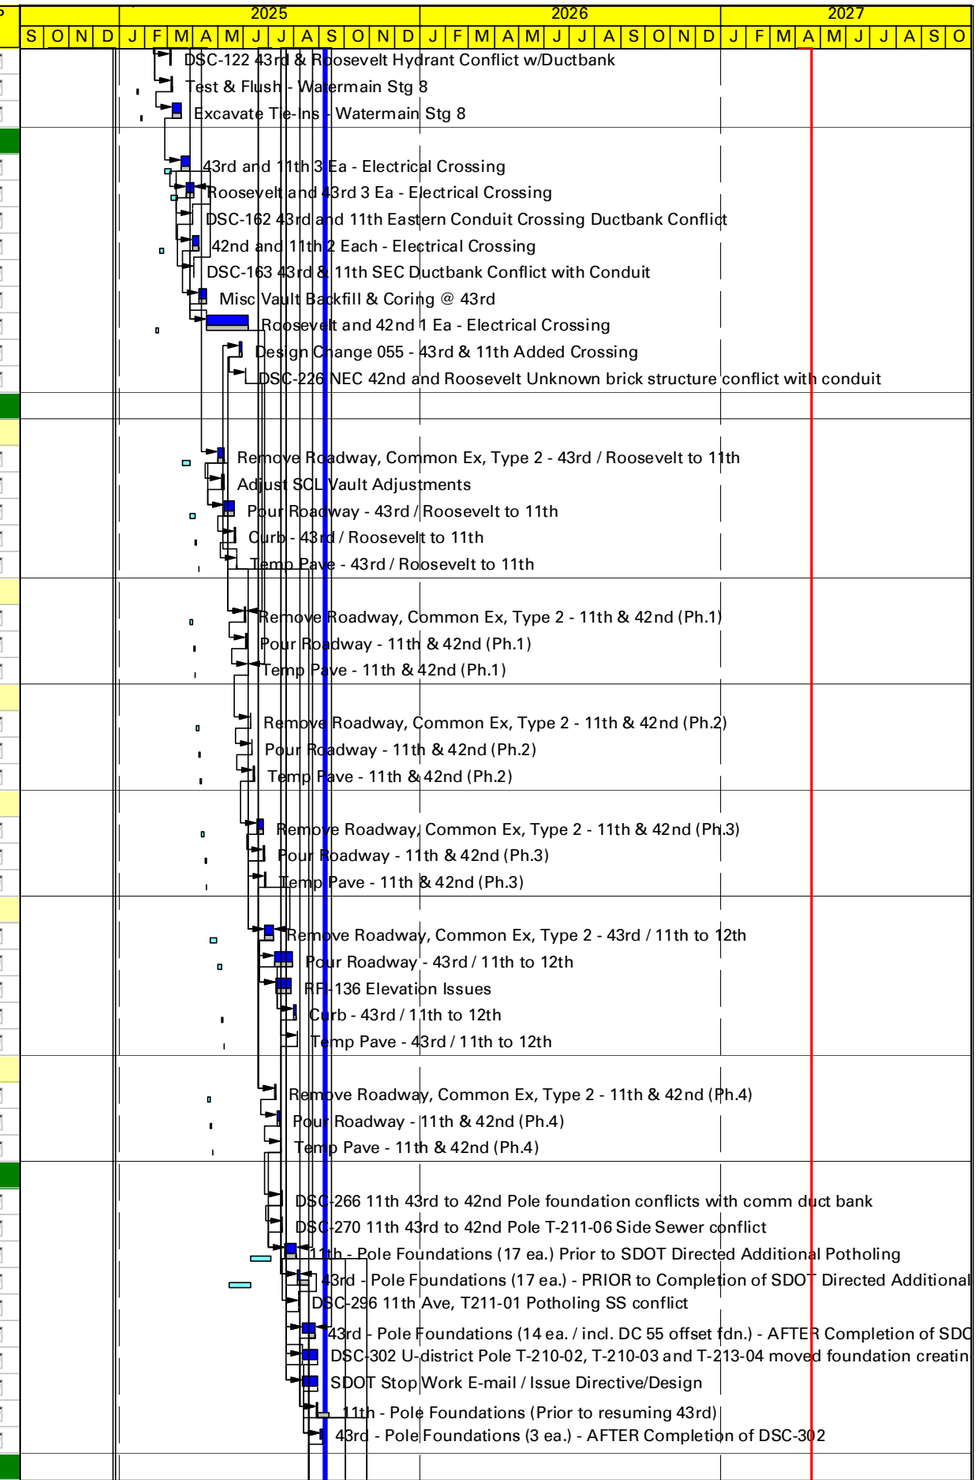

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filters: Longest Path, SELECT (J-LINE), SELECT2.
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
43rd 12th to 11th North Side														
1-SW-0135	Remove Sidewalk - 43rd / 12th to 11th (N)	2	2	0	1	1	2	08-Sep-25 A	09-Sep-25	-22	-16	-6	-6	☑
1-SW-0136	Trench Electrical - 43rd / 12th to 11th (N)	3	3	0	0	3	3	10-Sep-25	12-Sep-25	-22	-16	-6	-6	☑
43rd 11th to Roosevelt North Side														
1-SW-0141	Remove Sidewalk - 43rd / 11th to Roosevelt (N)	1	1	0	0	1	1	15-Sep-25	15-Sep-25	-22	-16	-6	-6	☑
1-SW-0142	Trench Electrical - 43rd / 11th to Roosevelt (N)	2	2	0	0	2	2	16-Sep-25	17-Sep-25	-22	-16	-6	-6	☑
1-SW-0143	Electrical - 43rd / 11th to Roosevelt (N)	7	7	0	0	7	7	18-Sep-25	26-Sep-25	-22	-16	-6	-6	☑
1-SW-0144	Grade Sidewalks - 43rd / 11th to Roosevelt (N)	2	2	0	0	2	2	29-Sep-25	30-Sep-25	-22	-16	-6	-6	☑
Design Change 055 - Sidewalks 11th Ave. / 43rd to 45th East Side														
1-SW-DC-055A	Remove Sidewalk - 11th; 43rd to 45th (E) DC-055	2	2	0	0	2	2	01-Oct-25	02-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055B	Trench Electrical - 11th; 43rd to 45th (E) DC-055	5	5	0	0	5	5	03-Oct-25	09-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055C	Electrical - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	08-Oct-25	14-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055D	Grade Sidewalks - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	10-Oct-25	16-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055E	Pour Sidewalks/Curb Ramps - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	17-Oct-25	22-Oct-25	-22	-16	-6	-6	☑
11th and 42nd NEC														
1-SW-0147	Remove Sidewalk - 11th & 42nd NEC	2	2	0	0	2	2	23-Oct-25	24-Oct-25	-22	-16	-6	-6	☑
1-SW-0148	Trench Electrical - 11th & 42nd NEC	2	2	0	0	2	2	27-Oct-25	28-Oct-25	-22	-16	-6	-6	☑
11th and 42nd SEC														
1-SW-0153	Remove Sidewalk - 11th & 42nd SEC	2	2	0	0	2	2	29-Oct-25	30-Oct-25	-22	-16	-6	-6	☑
1-SW-0154	Trench Electrical - 11th & 42nd SEC	2	2	0	0	2	2	31-Oct-25	03-Nov-25	-22	-16	-6	-6	☑
11th and Eastlake East Side														
1-SW-0159	Remove Sidewalk - 11th & Eastlake ()	2	2	0	0	2	2	04-Nov-25	05-Nov-25	-22	-16	-6	-6	☑
1-SW-0160	Grade Sidewalks - 11th & Eastlake ()	2	2	0	0	2	2	06-Nov-25	07-Nov-25	-22	-16	-6	-6	☑
43rd 12th to 11th South Side														
1-SW-0163	Remove Sidewalk - 43rd / 12th to 11th (S)	2	2	0	0	2	2	10-Nov-25	12-Nov-25	-22	-16	-6	-6	☑
1-SW-0164	Trench Electrical - 43rd / 12th to 11th (S)	3	3	0	0	3	3	13-Nov-25	17-Nov-25	-22	-16	-6	-6	☑
43rd 11th to Roosevelt South Side														
1-SW-0169	Remove Sidewalk - 43rd / 11to to Roosevelt (S)	1	1	0	0	1	1	18-Nov-25	18-Nov-25	-22	-16	-6	-6	☑
1-SW-0170	Trench Electrical - 43rd / 11to to Roosevelt (S)	2	2	0	0	2	2	19-Nov-25	20-Nov-25	-22	-16	-6	-6	☑
1-SW-0171	Electrical - 43rd / 11to to Roosevelt (S)	6	6	0	0	6	6	21-Nov-25	02-Dec-25	-22	-16	-6	-6	☑
1-SW-0172	Grade Sidewalks - 43rd / 11to to Roosevelt (S)	2	2	0	0	2	2	03-Dec-25	04-Dec-25	-22	-16	-6	-6	☑
1-SW-0173	Pour Sidewalks/Curb Ramps - 43rd / 11to to Roosevelt (S)	5	5	0	0	5	5	05-Dec-25	11-Dec-25	-22	-16	-6	-6	☑
11th and 42nd NWC														
1-SW-0175	Remove Sidewalk - 11th & 42nd NWC	1	1	0	0	1	1	21-Nov-25	21-Nov-25	-22	-16	-6	-6	☑
1-SW-0176	Trench Electrical - 11th & 42nd NWC	2	2	0	0	2	2	24-Nov-25	25-Nov-25	-22	-16	-6	-6	☑
1-SW-0179	Pour Sidewalks/Curb Ramps - 11th & 42nd NWC	4	4	0	0	4	4	12-Dec-25	17-Dec-25	-22	-16	-6	-6	☑
11th and 42nd SWC														
1-SW-0181	Remove Sidewalk 11th & 42nd SWC	1	1	0	0	1	1	26-Nov-25	26-Nov-25	-22	-16	-6	-6	☑
1-SW-0182	Trench Electrical 11th & 42nd SWC	2	2	0	0	2	2	01-Dec-25	02-Dec-25	-22	-16	-6	-6	☑
1-SW-0183	Electrical 11th & 42nd SWC	4	4	0	0	4	4	03-Dec-25	08-Dec-25	-22	-16	-6	-6	☑
1-SW-0184	Grade Sidewalks 11th & 42nd SWC	1	1	0	0	1	1	09-Dec-25	09-Dec-25	-22	-16	-6	-6	☑
1-SW-0185	Pour Sidewalks/Curb Ramps - 11th & 42nd SWC	4	4	0	0	4	4	18-Dec-25	23-Dec-25	-22	-16	-6	-6	☑
Roosevelt and 43rd West Side														
1-SW-0187	Remove Sidewalk - Roosevelt & 43rd (W)	1	1	0	0	1	1	10-Dec-25	10-Dec-25	-22	-16	-6	-6	☑
1-SW-0188	Trench Electrical - Roosevelt & 43rd (W)	2	2	0	0	2	2	11-Dec-25	12-Dec-25	-22	-16	-6	-6	☑
1-SW-0189	Electrical - Roosevelt & 43rd (W)	5	5	0	0	5	5	15-Dec-25	19-Dec-25	-22	-16	-6	-6	☑
1-SW-0190	Grade Sidewalks - Roosevelt & 43rd (W)	2	2	0	0	2	2	22-Dec-25	23-Dec-25	-22	-16	-6	-6	☑
1-SW-0191	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd (W)	4	4	0	0	4	4	24-Dec-25	30-Dec-25	-22	-16	-6	-6	☑
Roosevelt and 43rd NWC														
1-SW-0193	Remove Sidewalk - Roosevelt & 43rd NWC	1	1	0	0	1	1	15-Dec-25	15-Dec-25	-22	-16	-6	-6	☑
1-SW-0194	Trench Electrical - Roosevelt & 43rd NWC	1	1	0	0	1	1	16-Dec-25	16-Dec-25	-22	-16	-6	-6	☑
1-SW-0195	Electrical - Roosevelt & 43rd NWC	3	3	0	0	3	3	17-Dec-25	19-Dec-25	-22	-16	-6	-6	☑
1-SW-0196	Grade Sidewalks - Roosevelt & 43rd NWC	1	1	0	0	1	1	22-Dec-25	22-Dec-25	-22	-16	-6	-6	☑
1-SW-0197	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd NWC	3	3	0	0	3	3	23-Dec-25	26-Dec-25	-22	-16	-6	-6	☑

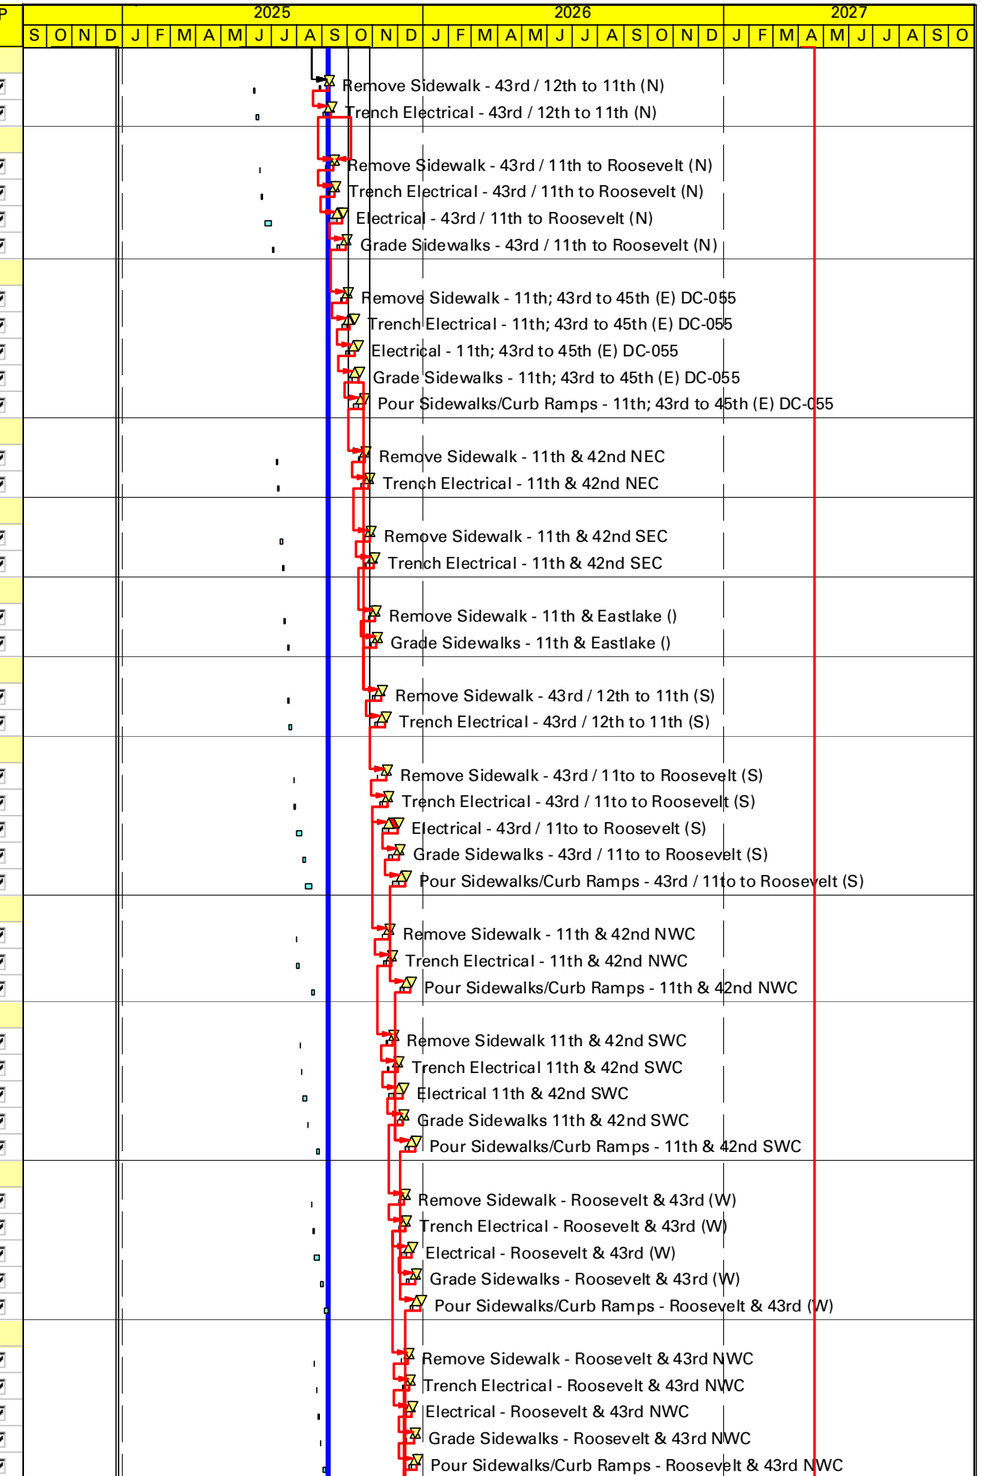

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filters: Longest Path, SELECT (J-LINE), SELECT2.
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Roosevelt and 43rd SWC														
1-SW-0199	Remove Sidewalk - Roosevelt & 43rd SWC	1	1	0	0	1	1	29-Dec-25	29-Dec-25	-22	-16	-6	-6	☑
1-SW-0200	Grade Sidewalks - Roosevelt & 43rd SWC	1	1	0	0	1	1	30-Dec-25	30-Dec-25	-22	-16	-6	-6	☑
1-SW-0201	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd SWC	3	3	0	0	3	3	31-Dec-25	05-Jan-26	-22	-16	-6	-6	☑
Roosevelt and 42nd NWC														
1-SW-0203	Remove Sidewalk - Roosevelt & 42nd NWC	1	1	0	0	1	1	06-Jan-26	06-Jan-26	-22	-16	-6	-6	☑
1-SW-0204	Trench Electrical - Roosevelt & 42nd NWC	1	1	0	0	1	1	07-Jan-26	07-Jan-26	-22	-16	-6	-6	☑
1-SW-0205	Electrical - Roosevelt & 42nd NWC	4	4	0	0	4	4	08-Jan-26	13-Jan-26	-22	-16	-6	-6	☑
1-SW-0206	Grade Sidewalks - Roosevelt & 42nd NWC	1	1	0	0	1	1	14-Jan-26	14-Jan-26	-22	-16	-6	-6	☑
1-SW-0207	Pour Sidewalks/Curb Ramps - Roosevelt & 42nd NWC	1	1	0	0	1	1	15-Jan-26	15-Jan-26	-22	-16	-6	-6	☑
Roosevelt and 42nd SEC														
1-SW-0213	Pour Sidewalks/Curb Ramps - Roosevelt & 42nd SEC	3	3	0	0	3	3	16-Jan-26	21-Jan-26	-22	-16	-6	-6	☑
Roosevelt and 43rd SEC														
1-SW-0215	Remove Sidewalk - Roosevelt & 43rd SEC	1	1	0	0	1	1	22-Jan-26	22-Jan-26	-22	-16	-6	-6	☑
1-SW-0216	Trench Electrical - Roosevelt & 43rd SEC	2	2	0	0	2	2	23-Jan-26	26-Jan-26	-22	-16	-6	-6	☑
1-SW-0217	Electrical - Roosevelt & 43rd SEC	5	5	0	0	5	5	27-Jan-26	02-Feb-26	-22	-16	-6	-6	☑
1-SW-0218	Grade Sidewalks - Roosevelt & 43rd SEC	2	2	0	0	2	2	03-Feb-26	04-Feb-26	-22	-16	-6	-6	☑
Roosevelt and 42nd NEC														
1-SW-0223	Electrical - Roosevelt & 42nd NEC	7	7	0	0	7	7	05-Feb-26	13-Feb-26	-22	-16	-6	-6	☑
1-SW-0224	Grade Sidewalks - Roosevelt & 42nd NEC	2	2	0	0	2	2	17-Feb-26	18-Feb-26	-22	-16	-6	-6	☑
1-SW-0225	Pour Sidewalks/Curb Ramps - Roosevelt & 42nd NEC	5	5	0	0	5	5	19-Feb-26	25-Feb-26	-22	-16	-6	-6	☑
Roosevelt and 42nd SEC #2														
1-SW-0227	Remove Sidewalk - Roosevelt & 42nd SEC	2	2	0	0	2	2	26-Feb-26	27-Feb-26	-22	-16	-6	-6	☑
1-SW-0228	Trench Electrical - Roosevelt & 42nd SEC	3	3	0	0	3	3	02-Mar-26	04-Mar-26	-22	-16	-6	-6	☑
1-SW-0229	Electrical - Roosevelt & 42nd SEC	7	7	0	0	7	7	05-Mar-26	13-Mar-26	-22	-16	-6	-6	☑
1-SW-0230	Grade Sidewalks - Roosevelt & 42nd SEC	2	2	0	0	2	2	16-Mar-26	17-Mar-26	-22	-16	-6	-6	☑
1-SW-0231	Pour Sidewalks/Curb Ramps - Roosevelt & 42nd SEC	5	5	0	0	5	5	18-Mar-26	24-Mar-26	-22	-16	-6	-6	☑
Roosevelt and 41st NEC														
1-SW-0233	Remove Sidewalk - Roosevelt & 41st NEC	2	2	0	0	2	2	05-Mar-26	06-Mar-26	-22	-16	-6	-6	☑
1-SW-0234	Trench Electrical - Roosevelt & 41st NEC	3	3	0	0	3	3	09-Mar-26	11-Mar-26	-22	-16	-6	-6	☑
1-SW-0235	Electrical - Roosevelt & 41st NEC	7	7	0	0	7	7	12-Mar-26	20-Mar-26	-22	-16	-6	-6	☑
1-SW-0236	Grade Sidewalks - Roosevelt & 41st NEC	2	2	0	0	2	2	23-Mar-26	24-Mar-26	-22	-16	-6	-6	☑
1-SW-0237	Pour Sidewalks/Curb Ramps - Roosevelt & 41st NEC	5	5	0	0	5	5	25-Mar-26	31-Mar-26	-22	-16	-6	-6	☑
Weekend Driveway														
Roosevelt 42nd East to 42nd West East Side														
1-WE-0275	Remove Sidewalk - Roosevelt / 42nd E to 42nd W (E)	1	1	0	0	1	1	04-Apr-26	04-Apr-26	-10	-8	-2	-2	☑
1-WE-0276	Pour Driveway - Roosevelt / 42nd E to 42nd W (E)	1	1	0	0	1	1	05-Apr-26	05-Apr-26	-10	-8	-2	-2	☑
SCL Services - Zone 1														
43rd and Roosevelt SDOT Signal Service														
1-SCL-0283	Install Meter Cabinet - 43rd & Roosevelt Signal	1	1	0	0	1	1	06-Apr-26	06-Apr-26	-25	-20	-5	-5	☑
1-SCL-0284	SDOT Inspection - 43rd & Roosevelt Signal	5	5	0	0	5	5	07-Apr-26	13-Apr-26	-25	-20	-5	-5	☑
1-SCL-0285	SDCI Inspection - 43rd & Roosevelt Signal	5	5	0	0	5	5	14-Apr-26	20-Apr-26	-25	-20	-5	-5	☑
1-SCL-0286	SCL Inspection - 43rd & Roosevelt Signal	21	21	0	0	21	21	21-Apr-26	19-May-26	-25	-20	-5	-5	☑
1-SCL-0287	SCL Heat Up Cabinet - 43rd & Roosevelt Signal	21	21	0	0	21	21	20-May-26	15-Jul-26	-25	-20	-5	-5	☑
1-SCL-0288	Remove Old Service Gear - 43rd & Roosevelt Signal	1	1	0	0	1	1	16-Jul-26	16-Jul-26	-25	-20	-5	-5	☑
Signals														
Roosevelt and 43rd														
1-SIG-0347	Install Poles - Roosevelt & 43rd Signal	4	4	0	0	4	4	17-Jul-26	22-Jul-26	-25	-20	-5	-5	☑
1-SIG-0348	Build Signal - Roosevelt & 43rd Signal	10	10	0	0	10	10	23-Jul-26	05-Aug-26	-25	-20	-5	-5	☑
1-SIG-0349	SDOT Inspection - Roosevelt & 43rd Signal	5	5	0	0	5	5	06-Aug-26	12-Aug-26	-25	-20	-5	-5	☑
1-SIG-0350	SDOT Commission - Roosevelt & 43rd Signal	10	10	0	0	10	10	13-Aug-26	26-Aug-26	-25	-20	-5	-5	☑
1-SIG-0351	Demo Old Signal & Temp Signal - Roosevelt & 43rd Signal	2	2	0	0	2	2	27-Aug-26	28-Aug-26	-25	-20	-5	-5	☑
11th and 43rd														
1-SIG-0353	Install Poles - 11th & 43rd Signal	3	3	0	0	3	3	31-Aug-26	02-Sep-26	-25	-20	-5	-5	☑

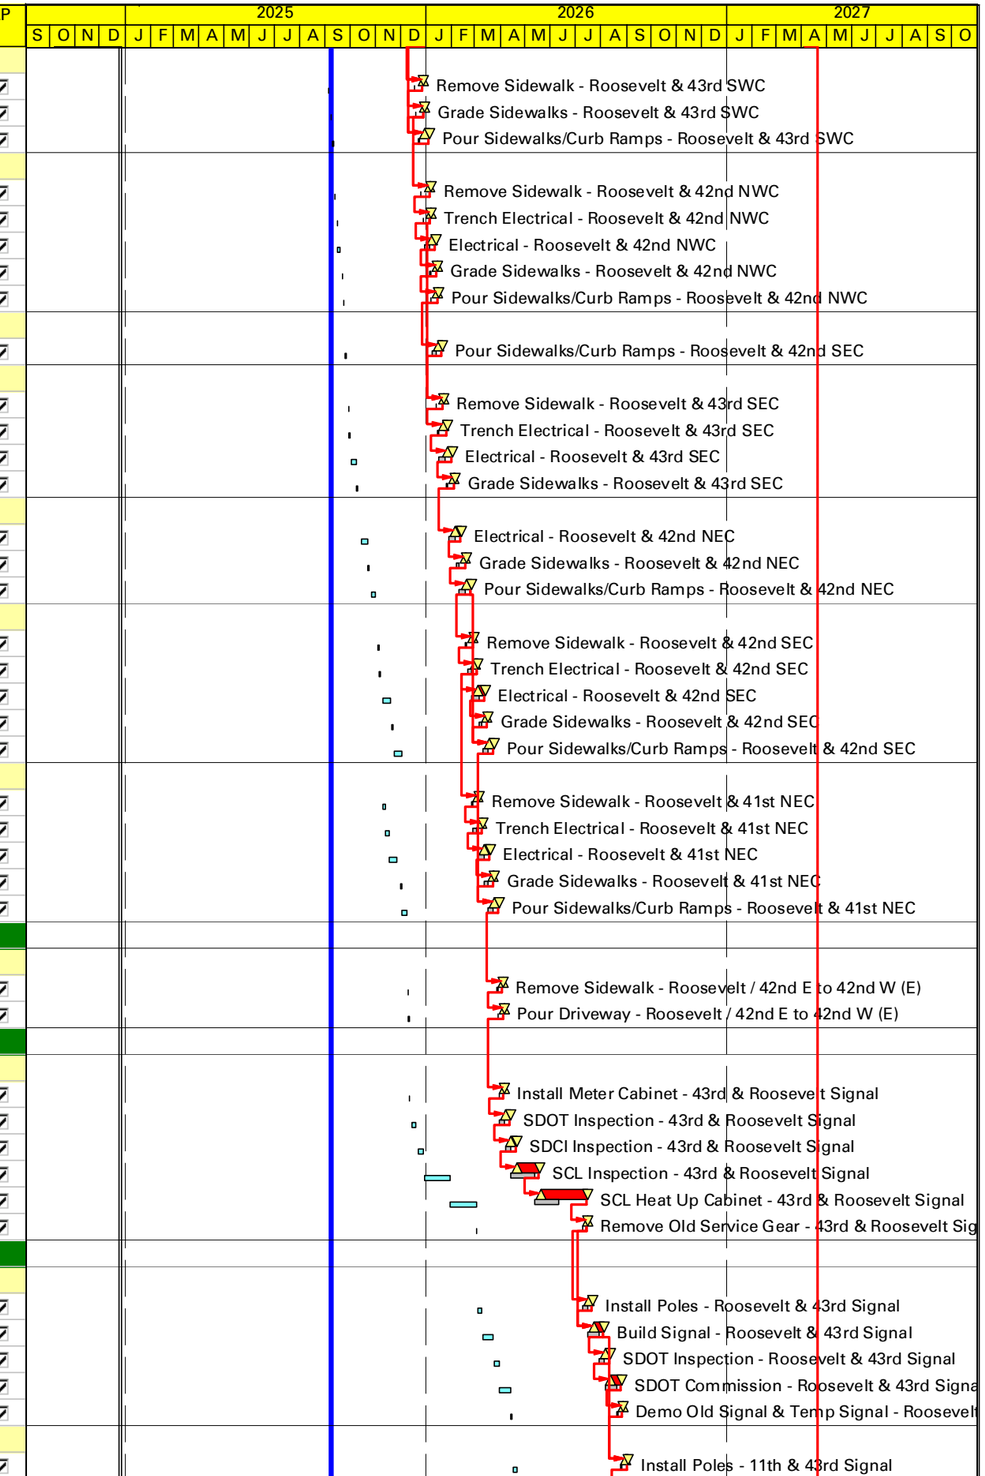

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filters: Longest Path, SELECT (J-LINE), SELECT2.
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-SIG-0354	Build Signal - 11th & 43rd Signal	12	12	0	0	12	12	03-Sep-26	21-Sep-26	-25	-20	-5	-5	☑
1-SIG-0355	SDOT Inspection - 11th & 43rd Signal	5	5	0	0	5	5	22-Sep-26	28-Sep-26	-25	-20	-5	-5	☑
1-SIG-0356	SDOT Commission - 11th & 43rd Signal	10	10	0	0	10	10	29-Sep-26	13-Oct-26	-25	-20	-5	-5	☑
1-SIG-0357	Demo Old Signal & Temp Signal - 11th & 43rd Signal	4	4	0	0	4	4	14-Oct-26	19-Oct-26	-25	-20	-5	-5	☑
Roosevelt and Eastlake														
1-SIG-0377	Install Poles - Roosevelt & Eastlake Signal	2	2	0	0	2	2	20-Oct-26	21-Oct-26	-25	-20	-5	-5	☑
1-SIG-0378	Build Signal - Roosevelt & Eastlake Signal	10	10	0	0	10	10	22-Oct-26	04-Nov-26	-25	-20	-5	-5	☑
1-SIG-0379	SDOT Inspection - Roosevelt & Eastlake Signal	5	5	0	0	5	5	05-Nov-26	12-Nov-26	-25	-20	-5	-5	☑
1-SIG-0380	SDOT Commission - Roosevelt & Eastlake Signal	10	10	0	0	10	10	13-Nov-26	30-Nov-26	-25	-20	-5	-5	☑
1-SIG-0381	Demo Old Signal & Temp Signal - Roosevelt & Eastlake Signal	2	2	0	0	2	2	01-Dec-26	02-Dec-26	-25	-20	-5	-5	☑
Lighting														
41st and Roosevelt Schematic														
1-EL-0394	Build Schematic, Poles, Luminaires Wiring - 41st & Roosevelt Sch	10	10	0	0	10	10	03-Dec-26	16-Dec-26	-25	-20	-5	-5	☑
1-EL-0395	SCL Final Inspection - 41st & Roosevelt Schematic	10	10	0	0	10	10	17-Dec-26	31-Dec-26	-25	-20	-5	-5	☑
1-EL-0396	SCL Commission Lighting - 41st & Roosevelt Schematic	15	15	0	0	15	15	04-Jan-27	25-Jan-27	-25	-20	-5	-5	☑
1-EL-0397	Demo Old Lighting - 41st & Roosevelt Schematic	2	2	0	0	2	2	26-Jan-27	27-Jan-27	-25	-20	-5	-5	☑
Hardscapes After Electrical Demo														
42nd and Roosevelt West														
1-HS-0432	Demo Foundations - 42nd & Roosevelt (W)	1	1	0	0	1	1	28-Jan-27	28-Jan-27	-25	-20	-5	-5	☑
1-HS-0433	Pour Sidewalks - 42nd & Roosevelt (W)	1	1	0	0	1	1	29-Jan-27	29-Jan-27	-25	-20	-5	-5	☑
Milling-Paving-Striping														
1-PV-0435	Milling - Zone 1	3	3	0	0	3	3	01-Feb-27	03-Feb-27	-25	-20	-5	-5	☑
1-PBL-0436	PBL Barrier - Zone 1	6	6	0	0	6	6	04-Feb-27	11-Feb-27	-25	-20	-5	-5	☑
1-PV-0437	Asphalt Paving - Zone 1	4	4	0	0	4	4	12-Feb-27	18-Feb-27	-25	-20	-5	-5	☑
1-PV-0438	Asphalt Cure - Zone 1	20	20	0	0	20	20	19-Feb-27	18-Mar-27	-25	-20	-5	-5	☑
1-PM-0439	Channelization - Zone 1	10	10	0	0	10	10	19-Mar-27	01-Apr-27	-25	-20	-5	-5	☑
Zone 4 - Galer to 3rd														
Storm														
DSC-082	DSC-082 SWC Yale Unknown Unlocated Copper Line	3	3	0	3	0	3	16-Jan-25 A	21-Jan-25 A			0	0	☑
4-ST-1462	Eastlake to Yale - Storm (partial w/FM070)	2	15	0	15	0	15	16-Jan-25 A	10-Feb-25 A			0	0	☑
DSC-085	DSC-085 SWC Yale CB C14 Corrugated Pipe Conflict	1	1	0	1	0	1	21-Jan-25 A	21-Jan-25 A			0	0	☑
DSC-090	DSC-090 North of Yale CB C01 Conflict with Existing Pipe	1	1	0	1	0	1	27-Jan-25 A	27-Jan-25 A			0	0	☑
DSC-092	DSC-092 North of Aloha CB C03 Conflict With Ductbank	4	4	0	4	0	4	29-Jan-25 A	03-Feb-25 A			0	0	☑
DSC-095	DSC-095 NWC Yale & Fairview Unknown Ductbank	1	1	0	1	0	1	31-Jan-25 A	31-Jan-25 A			0	0	☑
DSC-101	DSC-101 NWC Yale Unknown Steel Line CB C02	2	2	0	2	0	2	07-Feb-25 A	10-Feb-25 A			0	0	☑
DSC-105	DSC-105 Yale Fairview WQV 101 core tap conflicts	1	1	0	1	0	1	13-Feb-25 A	13-Feb-25 A			0	0	☑
4-ST-1463	Yale to Aloha - Storm (partial w/FM070)	22	11	0	11	0	11	14-Feb-25 A	03-Mar-25 A			0	0	☑
DSC-110	DSC-110 Yale to Aloha WQV C101 Ductbank Conflict	3	3	0	3	0	3	18-Feb-25 A	20-Feb-25 A			0	0	☑
DSC-114	DSC-114 Ward & Fairview CB-C4 Ductbank Conflict	2	2	0	2	0	2	24-Feb-25 A	25-Feb-25 A			0	0	☑
DSC-117	DSC-117 Yale to Aloha CB C5 Conflict Comm Line	1	1	0	1	0	1	26-Feb-25 A	26-Feb-25 A			0	0	☑
DSC-119	DSC-119 Fairview & Ward CB C5 Conduit Conflict	1	1	0	1	0	1	28-Feb-25 A	28-Feb-25 A			0	0	☑
FM0059.1	FM-0059 Stop Work - SDOT Redesign Storm (partial w/FM070)	15	31	0	31	0	31	14-Jan-25 A	03-Mar-25 A			0	0	☑
FM0059.4	STOP WORK - SDOT RE-DESIGN (FM-0059 & FM-0124)	3	22	0	22	0	22	03-Mar-25 A	01-Apr-25 A			0	0	☑
4-ST-1464	Aloha to Valley - Storm (AFTER RE-DESIGN / FM-0059 & FM-0124)	10	10	0	10	0	10	28-Apr-25 A	09-May-25 A			0	0	☐
DSC-191	DSC-191 Aloha to Valley CB C9 conduit conflict	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	☐
DSC-200	DSC-200 Aloha to Valley CB C10 Duct Bank Conflict	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	☐
DSC-203	DSC-203 Fairview, Aloha-Valley CB-C10 Unlocated DB	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	☐
DSC-207	DSC-207 Fairview CB C13 unknown unlocated conduit conflicts	1	1	0	1	0	1	09-May-25 A	09-May-25 A			0	0	☐
DSC-164	DSC-164 PCO0240.01 Yale to Aloha CB C6 Conflict w/Ductbank	1	1	0	1	0	1	02-Apr-25 A	02-Apr-25 A			0	0	☑
DSC-166	DSC-166 Yale to Aloha WQC C102 unknown Ductbank	1	1	0	1	0	1	04-Apr-25 A	04-Apr-25 A			0	0	☑
DSC-169	DSC-169 Ward Inlet C3 unknown conduit conflict	1	1	0	1	0	1	07-Apr-25 A	07-Apr-25 A			0	0	☑
DSC-170	DSC-170 Ward Inlet C3 Unknown Conduit Conflict #2	1	1	0	1	0	1	08-Apr-25 A	08-Apr-25 A			0	0	☑
DSC-175	DSC-175 NWC Ward CB C-4 Conflict with Ductbank	20	19	0	19	0	19	15-Apr-25 A	09-May-25 A			0	0	☑
FM-152	FM 152 Stop Work Fairview	17	99	0	83	16	99	09-May-25 A	30-Sep-25	-24	-24	0	0	☐

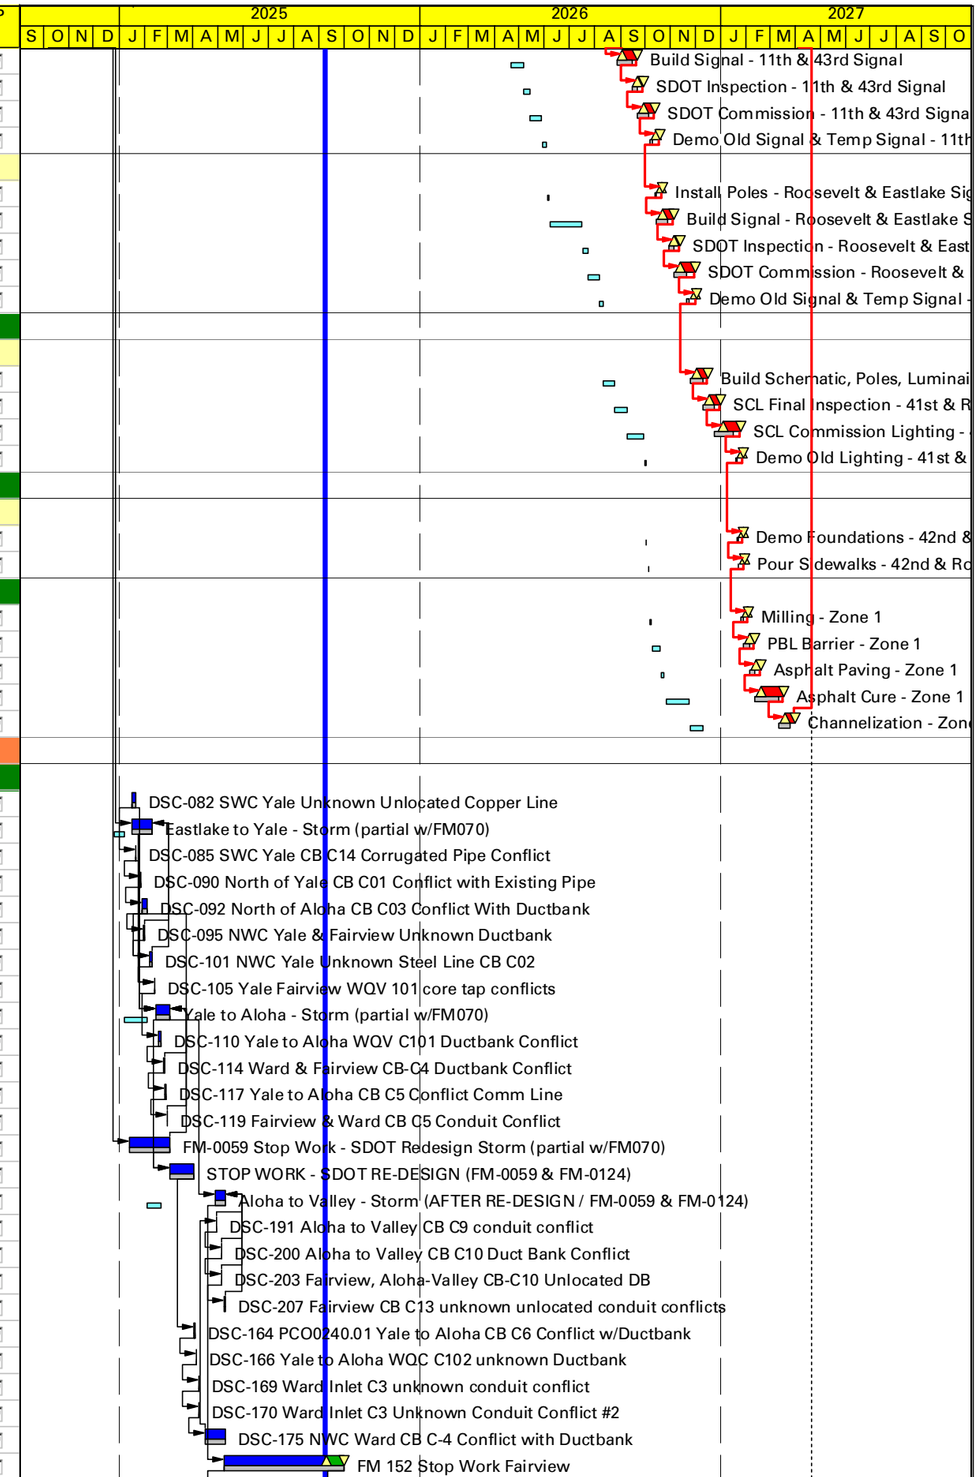

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filters: Longest Path, SELECT (J-LINE), SELECT2.
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
FM-152A	Fairview Comm Ductbank Resolution / Mobilize	12	99	0	83	16	99	09-May-25 A	30-Sep-25	-24	-24	0	0	☐
4-ST-1484	Aloha to Valley - Storm (AFTER FM 152)	5	5	0	0	5	5	01-Oct-25	07-Oct-25	-24	-24	0	0	☐
Conduit Crossings														
4-CC-1478	Yale - Complete Conduit Crossings After Ductbank Relocation	3	3	0	0	3	3	08-Oct-25	10-Oct-25	-24	-24	0	0	☐
4-CC-1479	Aloha - Complete Conduit Crossings After Ductbank Relocation	3	3	0	0	3	3	14-Oct-25	16-Oct-25	-24	-24	0	0	☐
Roadway														
Eastlake to Valley West Side														
4-RW-1474	Demo, Common Ex, Type 2 - Eastlake to Valley (W)	16	16	0	0	16	16	17-Oct-25	07-Nov-25	-24	-24	0	0	☐
4-RW-1475	Pour Roadway - Eastlake to Valley (W)	6	6	0	0	6	6	10-Nov-25	18-Nov-25	-24	-24	0	0	☐
4-RW-1476	Curb - Eastlake to Valley (W)	3	3	0	0	3	3	19-Nov-25	21-Nov-25	-24	-24	0	0	☐
Weekend Paving														
Yale Phase 2														
4-WE-1482	Remove Roadway Type 2 - Yale Ph.2 (WE)	1	1	0	0	1	1	22-Nov-25	22-Nov-25	-10	-10	0	0	☐
4-WE-1483	Pour Roadway - Yale Ph.2 (WE)	1	1	0	0	1	1	23-Nov-25	23-Nov-25	-10	-10	0	0	☐
Yale Phase 3														
4-WE-1485	Remove Roadway Type 2 - Yale Ph.3 (WE)	1	1	0	0	1	1	29-Nov-25	29-Nov-25	-10	-10	0	0	☐
4-WE-1486	Pour Roadway - Yale Ph.3 (WE)	1	1	0	0	1	1	30-Nov-25	30-Nov-25	-10	-10	0	0	☐
Aloha Phase 2														
4-WE-1491	Remove Roadway Type 2 - Aloha Ph.2 (WE)	1	1	0	0	1	1	06-Dec-25	06-Dec-25	-10	-10	0	0	☐
4-WE-1492	Pour Roadway - Aloha Ph.2 (WE)	1	1	0	0	1	1	07-Dec-25	07-Dec-25	-10	-10	0	0	☐
Valley to Roy Phase 2														
4-WE-1497	Remove Roadway Type 2 - Valley to Roy Ph.2 (WE)	1	1	0	0	1	1	13-Dec-25	13-Dec-25	-10	-10	0	0	☐
4-WE-1498	Pour Roadway - Valley to Roy Ph.2 (WE)	1	1	0	0	1	1	14-Dec-25	14-Dec-25	-10	-10	0	0	☐
Harrison Phase 1														
4-WE-1500	Remove Roadway Type 2 - Harrison Ph.1 (WE)	1	1	0	0	1	1	20-Dec-25	20-Dec-25	-10	-10	0	0	☐
4-WE-1501	Pour Roadway - Harrison Ph.1 (WE)	1	1	0	0	1	1	21-Dec-25	21-Dec-25	-10	-10	0	0	☐
Harrison Phase 2														
4-WE-1503	Remove Roadway Type 2 - Harrison Ph.2 (WE)	1	1	0	0	1	1	27-Dec-25	27-Dec-25	-10	-10	0	0	☐
4-WE-1504	Pour Roadway - Harrison Ph.2 (WE)	1	1	0	0	1	1	28-Dec-25	28-Dec-25	-10	-10	0	0	☐
Sidewalks														
Aloha NEC														
4-SW-1579	Remove Sidewalk - Aloha NEC	2	2	0	0	2	2	24-Nov-25	25-Nov-25	-22	-22	0	0	☐
4-SW-1580	Trench Electrical - Aloha NEC	3	3	0	0	3	3	26-Nov-25	02-Dec-25	-22	-22	0	0	☐
4-SW-1581	Excavate Shelter Foundations - Aloha NEC	1	1	0	0	1	1	03-Dec-25	03-Dec-25	-22	-22	0	0	☐
4-SW-1582	Form Pour Shelter Foundations - Aloha NEC	3	3	0	0	3	3	04-Dec-25	08-Dec-25	-22	-22	0	0	☐
4-SW-1583	Electrical - Aloha NEC	5	5	0	0	5	5	09-Dec-25	15-Dec-25	-22	-22	0	0	☐
4-SW-1584	Grade Sidewalks - Aloha NEC	2	2	0	0	2	2	16-Dec-25	17-Dec-25	-22	-22	0	0	☐
4-SW-1585	Pour Sidewalks/Curb Ramps - Aloha NEC	5	5	0	0	5	5	18-Dec-25	24-Dec-25	-22	-22	0	0	☐
Aloha SEC														
4-SW-1587	Remove Sidewalk - Aloha SEC	1	1	0	0	1	1	26-Dec-25	26-Dec-25	-22	-22	0	0	☐
4-SW-1588	Trench Electrical - Aloha SEC	2	2	0	0	2	2	29-Dec-25	30-Dec-25	-22	-22	0	0	☐
4-SW-1590	Grade Sidewalks - Aloha SEC	1	1	0	0	1	1	08-Jan-26	08-Jan-26	-22	-22	0	0	☐
4-SW-1591	Pour Sidewalks/Curb Ramps - Aloha SEC	3	3	0	0	3	3	09-Jan-26	13-Jan-26	-22	-22	0	0	☐
Harrison NEC														
4-SW-1613	Remove Sidewalk Harrison NEC	2	2	0	0	2	2	31-Dec-25	02-Jan-26	-22	-22	0	0	☐
4-SW-1614	Trench Electrical Harrison NEC	2	2	0	0	2	2	05-Jan-26	06-Jan-26	-22	-22	0	0	☐
4-SW-1615	Excavate Shelter Foundations Harrison NEC	1	1	0	0	1	1	07-Jan-26	07-Jan-26	-22	-22	0	0	☐
Valley NEC														
4-SW-1593	Remove Sidewalk - Valley NEC	1	1	0	0	1	1	14-Jan-26	14-Jan-26	-22	-22	0	0	☐
4-SW-1594	Trench Electrical - Valley NEC	2	2	0	0	2	2	15-Jan-26	16-Jan-26	-22	-22	0	0	☐
4-SW-1595	Electrical - Valley NEC	4	4	0	0	4	4	20-Jan-26	23-Jan-26	-22	-22	0	0	☐
4-SW-1596	Grade Sidewalks - Valley NEC	1	1	0	0	1	1	26-Jan-26	26-Jan-26	-22	-22	0	0	☐
4-SW-1597	Pour Sidewalks/Curb Ramps - Valley NEC	3	3	0	0	3	3	27-Jan-26	29-Jan-26	-22	-22	0	0	☐
Valley SEC to Mercer														

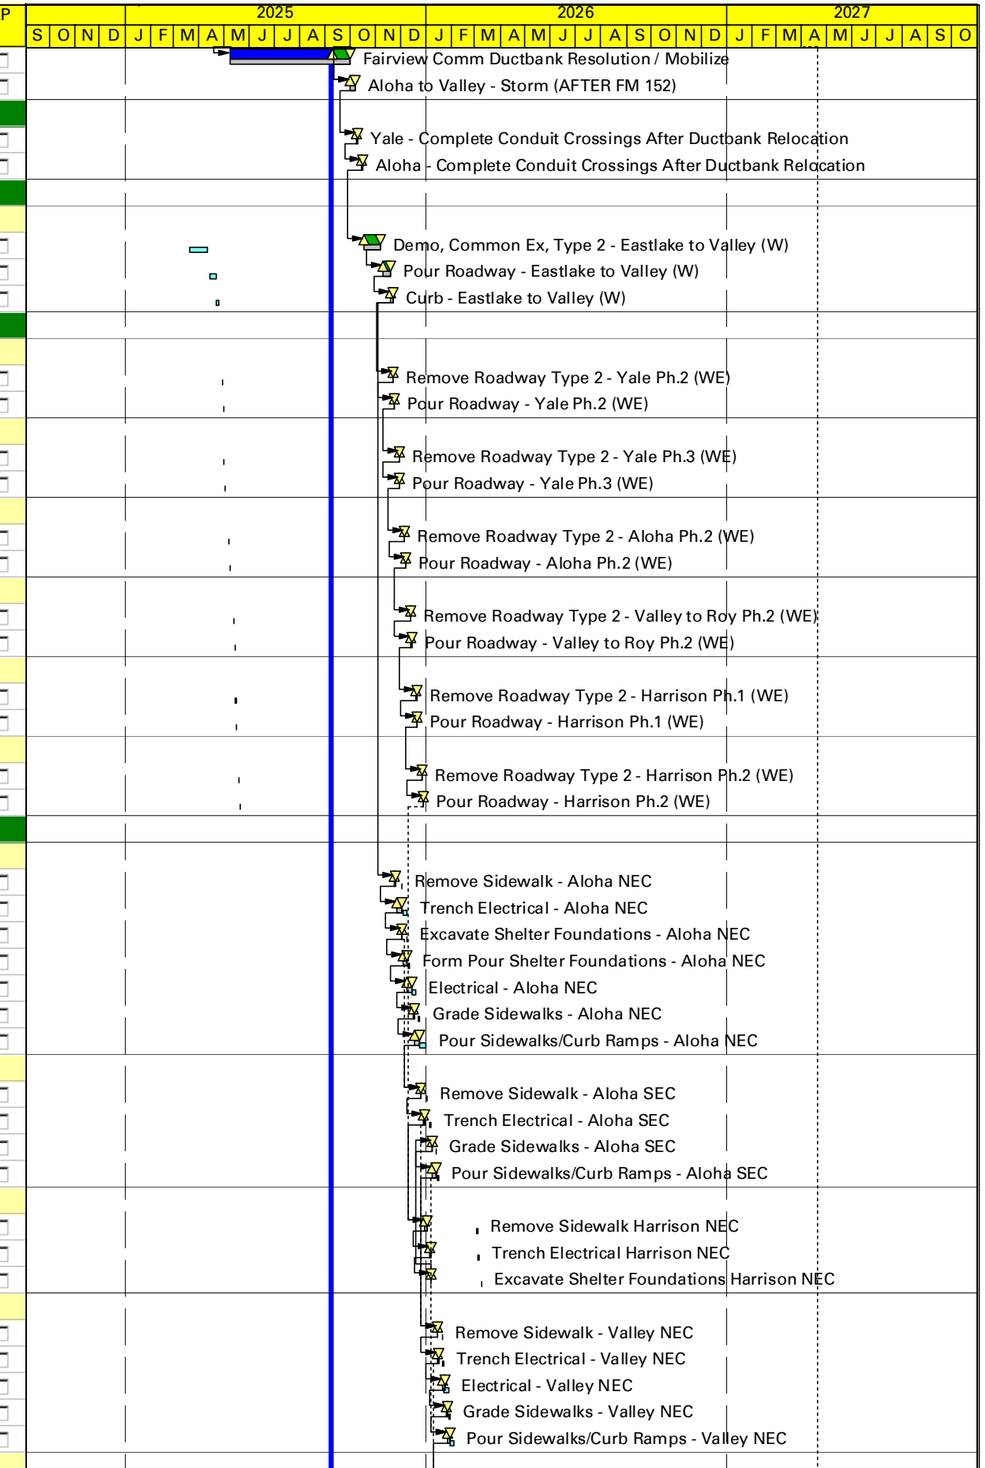

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filters: Longest Path, SELECT (J-LINE), SELECT2.
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
4-SW-1599	Remove Sidewalk Valley SEC to Mercer	1	1	0	0	1	1	30-Jan-26	30-Jan-26	-22	-22	0	0	
4-SW-1600	Trench Electrical Valley SEC to Mercer	2	2	0	0	2	2	02-Feb-26	03-Feb-26	-22	-22	0	0	
4-SW-1601	Electrical Valley SEC to Mercer	4	4	0	0	4	4	04-Feb-26	09-Feb-26	-22	-22	0	0	
4-SW-1602	Grade Sidewalks Valley SEC to Mercer	1	1	0	0	1	1	10-Feb-26	10-Feb-26	-22	-22	0	0	
4-SW-1603	Pour Sidewalks/Curb Ramps - Valley SEC to Mercer	4	4	0	0	4	4	11-Feb-26	17-Feb-26	-22	-22	0	0	
Yale NWC														
4-SW-1522	Remove Sidewalk - Yale NWC	1	1	0	0	1	1	18-Feb-26	18-Feb-26	-22	-22	0	0	
4-SW-1523	Trench Electrical - Yale NWC	2	2	0	0	2	2	19-Feb-26	20-Feb-26	-22	-22	0	0	
Yale SWC														
4-SW-1528	Remove Sidewalk - Yale SWC	3	3	0	0	3	3	23-Feb-26	25-Feb-26	-22	-22	0	0	
4-SW-1529	Trench Electrical - Yale SWC	3	3	0	0	3	3	26-Feb-26	02-Mar-26	-22	-22	0	0	
Ward West Side														
4-SW-1534	Remove Sidewalk - Ward (W)	3	3	0	0	3	3	03-Mar-26	05-Mar-26	-22	-22	0	0	
4-SW-1535	Trench Electrical - Ward (W)	3	3	0	0	3	3	06-Mar-26	10-Mar-26	-22	-22	0	0	
4-SW-1536	Electrical - Ward (W)	5	5	0	0	5	5	11-Mar-26	17-Mar-26	-22	-22	0	0	
4-SW-1537	Grade Sidewalks - Ward (W)	1	1	0	0	1	1	18-Mar-26	18-Mar-26	-22	-22	0	0	
Aloha NWC														
4-SW-1540	Remove Sidewalk - Aloha NWC	3	3	0	0	3	3	19-Mar-26	23-Mar-26	-22	-22	0	0	
4-SW-1541	Trench Electrical - Aloha NWC	3	3	0	0	3	3	24-Mar-26	26-Mar-26	-22	-22	0	0	
4-SW-1542	Electrical - Aloha NWC	18	18	0	0	18	18	27-Mar-26	21-Apr-26	-22	-22	0	0	
4-SW-1543	Grade Sidewalks - Aloha NWC	3	3	0	0	3	3	22-Apr-26	24-Apr-26	-22	-22	0	0	
Aloha SWC														
4-SW-1546	Remove Sidewalk - Aloha SWC	3	3	0	0	3	3	27-Apr-26	29-Apr-26	-22	-22	0	0	
4-SW-1547	Trench Electrical - Aloha SWC	3	3	0	0	3	3	30-Apr-26	04-May-26	-22	-22	0	0	
4-SW-1548	Electrical - Aloha SWC	8	8	0	0	8	8	05-May-26	14-May-26	-22	-22	0	0	
4-SW-1549	Grade Sidewalks - Aloha SWC	3	3	0	0	3	3	15-May-26	19-May-26	-22	-22	0	0	
Fairview Place NWC														
4-SW-1552	Remove Sidewalk Fairview Pl. NWC	3	3	0	0	3	3	20-May-26	22-May-26	-22	-22	0	0	
4-SW-1553	Trench Electrical Fairview Pl. NWC	3	3	0	0	3	3	26-May-26	28-May-26	-22	-22	0	0	
4-SW-1554	Electrical Fairview Pl. NWC	8	8	0	0	8	8	29-May-26	09-Jun-26	-22	-22	0	0	
4-SW-1555	Grade Sidewalks Fairview Pl. NWC	3	3	0	0	3	3	10-Jun-26	09-Jul-26	-22	-22	0	0	
Fairview Place to Valley														
4-SW-1558	Remove Sidewalk Fairview Pl. to Valley	2	2	0	0	2	2	10-Jul-26	13-Jul-26	-22	-22	0	0	
4-SW-1559	Trench Electrical Fairview Pl. to Valley	2	2	0	0	2	2	14-Jul-26	15-Jul-26	-22	-22	0	0	
4-SW-1560	Electrical Fairview Pl. to Valley	5	5	0	0	5	5	16-Jul-26	22-Jul-26	-22	-22	0	0	
4-SW-1561	Grade Sidewalks Fairview Pl. to Valley	2	2	0	0	2	2	23-Jul-26	24-Jul-26	-22	-22	0	0	
4-SW-1562	Pour Sidewalks/Curb Ramps - Fairview Pl. to Valley	4	4	0	0	4	4	27-Jul-26	30-Jul-26	-22	-22	0	0	
Aloha Center Median														
4-SW-1605	Remove Sidewalk - Aloha Center Median	2	2	0	0	2	2	31-Jul-26	03-Aug-26	-22	-22	0	0	
4-SW-1606	Trench Electrical - Aloha Center Median	3	3	0	0	3	3	04-Aug-26	06-Aug-26	-22	-22	0	0	
4-SW-1607	Excavate Shelter Foundations - Aloha Center Median	1	1	0	0	1	1	07-Aug-26	07-Aug-26	-22	-22	0	0	
4-SW-1608	Form Pour Shelter Foundations - Aloha Center Median	3	3	0	0	3	3	10-Aug-26	12-Aug-26	-22	-22	0	0	
4-SW-1609	Electrical - Aloha Center Median	5	5	0	0	5	5	13-Aug-26	19-Aug-26	-22	-22	0	0	
4-SW-1610	Grade Sidewalks - Aloha Center Median	2	2	0	0	2	2	20-Aug-26	21-Aug-26	-22	-22	0	0	
Harrison SEC														
4-SW-1621	Remove Sidewalk - Harrison SEC	1	1	0	0	1	1	24-Aug-26	24-Aug-26	-22	-22	0	0	
4-SW-1622	Pour Sidewalks/Curb Ramps - Harrison SEC	2	2	0	0	2	2	25-Aug-26	26-Aug-26	-22	-22	0	0	
Harrison SWC														
4-SW-1624	Remove Sidewalk - Harrison SWC	2	2	0	0	2	2	27-Aug-26	28-Aug-26	-22	-22	0	0	
4-SW-1625	Trench Electrical - Harrison SWC	2	2	0	0	2	2	31-Aug-26	01-Sep-26	-22	-22	0	0	
4-SW-1626	Excavate Shelter Foundations - Harrison SWC	1	1	0	0	1	1	02-Sep-26	02-Sep-26	-22	-22	0	0	
Virginia and Boren SEC														
4-SW-1632	Remove Sidewalk - Virginia & Boren SEC	2	2	0	0	2	2	03-Sep-26	04-Sep-26	-22	-22	0	0	
4-SW-1633	Trench Electrical - Virginia & Boren SEC	2	2	0	0	2	2	08-Sep-26	09-Sep-26	-22	-22	0	0	

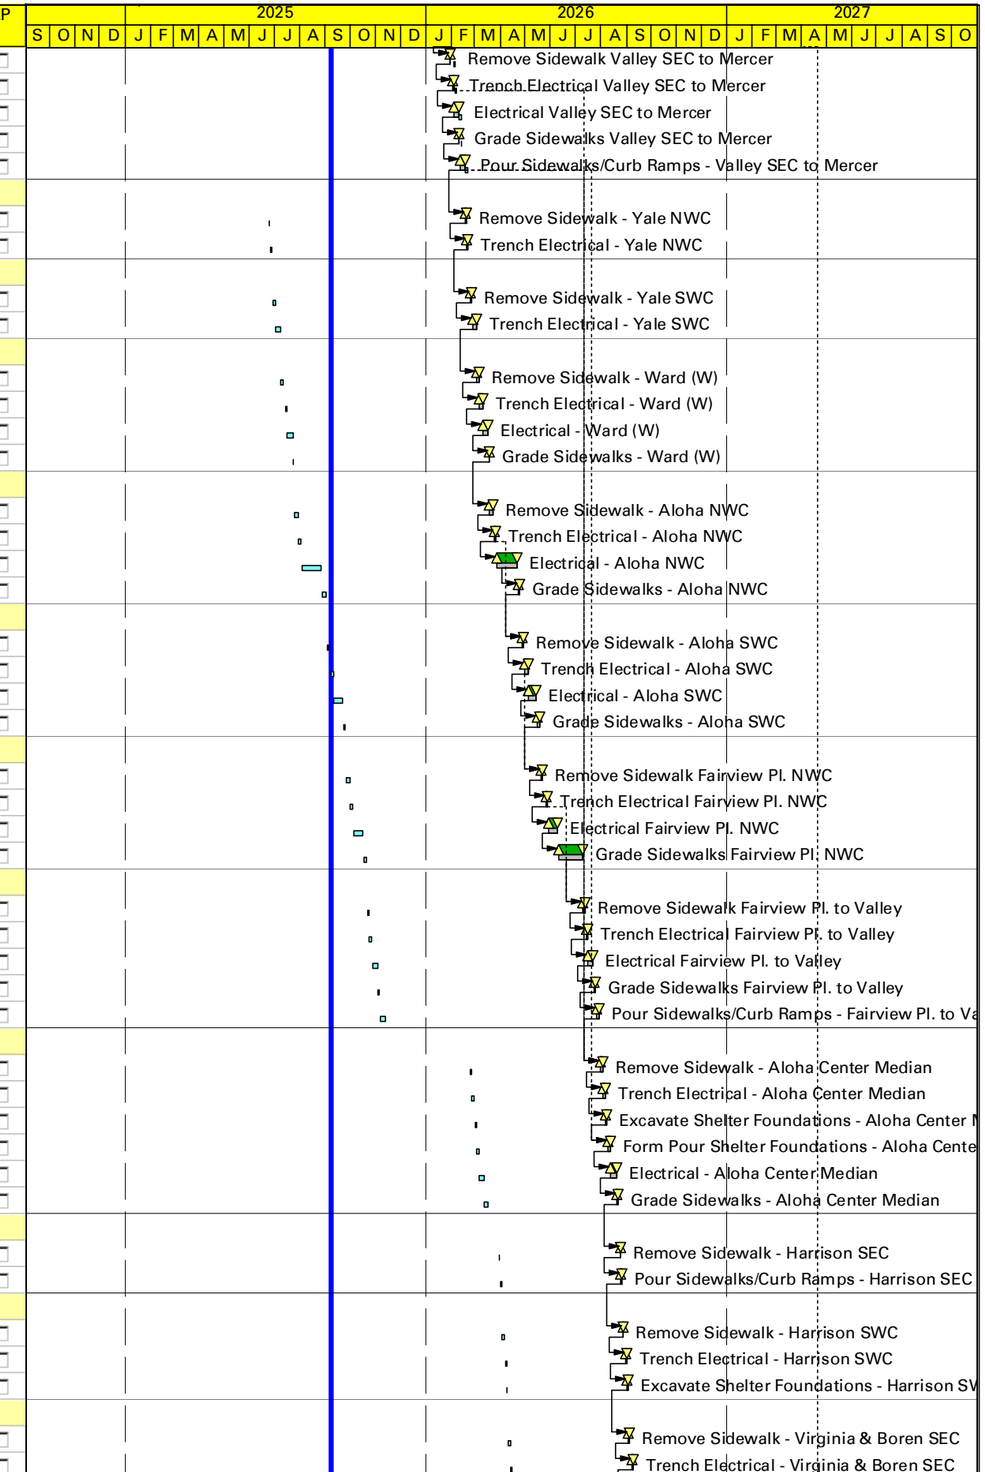

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filters: Longest Path, SELECT (J-LINE), SELECT2.
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
4-SW-1634	Excavate Shelter Foundations - Virginia & Boren SEC	1	1	0	0	1	1	10-Sep-26	10-Sep-26	-22	-22	0	0	☐
Virgina and Terry SEC														
4-SW-1640	Remove Sidewalk - Virginia & Terry SEC	2	2	0	0	2	2	11-Sep-26	14-Sep-26	-22	-22	0	0	☐
4-SW-1641	Trench Electrical - Virginia & Terry SEC	2	2	0	0	2	2	15-Sep-26	16-Sep-26	-22	-22	0	0	☐
4-SW-1642	Excavate Shelter Foundations - Virginia & Terry SEC	1	1	0	0	1	1	17-Sep-26	17-Sep-26	-22	-22	0	0	☐
Virginia and Westlake SEC														
4-SW-1648	Remove Sidewalk - Virginia & Westlake SEC	1	1	0	0	1	1	18-Sep-26	18-Sep-26	-22	-22	0	0	☐
4-SW-1649	Trench Electrical - Virginia & Westlake SEC	2	2	0	0	2	2	21-Sep-26	22-Sep-26	-22	-22	0	0	☐
Virginia and 6th NEC														
4-SW-1654	Remove Sidewalk - Virginia & 6th NEC	2	2	0	0	2	2	23-Sep-26	24-Sep-26	-22	-22	0	0	☐
4-SW-1655	Trench Electrical - Virginia & 6th NEC	2	2	0	0	2	2	25-Sep-26	28-Sep-26	-22	-22	0	0	☐
4-SW-1656	Excavate Shelter Foundations - Virginia & 6th NEC	1	1	0	0	1	1	29-Sep-26	29-Sep-26	-22	-22	0	0	☐
Stewert and 7th NWC														
4-SW-1662	Remove Sidewalk - Stewart & 7th NWC	2	2	0	0	2	2	30-Sep-26	01-Oct-26	-22	-22	0	0	☐
4-SW-1663	Trench Electrical - Stewart & 7th NWC	2	2	0	0	2	2	02-Oct-26	05-Oct-26	-22	-22	0	0	☐
4-SW-1664	Excavate Shelter Foundations - Stewart & 7th NWC	1	1	0	0	1	1	06-Oct-26	06-Oct-26	-22	-22	0	0	☐
4-SW-1665	Form Pour Shelter Foundations - Stewart & 7th NWC	4	4	0	0	4	4	07-Oct-26	13-Oct-26	-22	-22	0	0	☐
4-SW-1666	Electrical - Stewart & 7th NWC	6	6	0	0	6	6	14-Oct-26	21-Oct-26	-22	-22	0	0	☐
4-SW-1667	Grade Sidewalks - Stewart & 7th NWC	1	1	0	0	1	1	22-Oct-26	22-Oct-26	-22	-22	0	0	☐
4-SW-1668	Pour Sidewalks/Curb Ramps - Stewart & 7th NWC	5	5	0	0	5	5	23-Oct-26	29-Oct-26	-22	-22	0	0	☐
4-SW-1669	Slate Paving - Stewart & 7th NWC	5	5	0	0	5	5	30-Oct-26	05-Nov-26	-22	-22	0	0	☐
SCL Services														
7th SB Station														
4-SCL-1739	Install Meter Cabinet - 7th SB Station	1	1	0	0	1	1	06-Nov-26	06-Nov-26	-22	-22	0	0	☐
4-SCL-1740	SDOT Inspection - 7th SB Station	5	5	0	0	5	5	09-Nov-26	16-Nov-26	-22	-22	0	0	☐
4-SCL-1741	SDCI Inspection - 7th SB Station	5	5	0	0	5	5	17-Nov-26	23-Nov-26	-22	-22	0	0	☐
4-SCL-1742	SCL Inspection - 7th SB Station	21	21	0	0	21	21	24-Nov-26	24-Dec-26	-22	-22	0	0	☐
4-SCL-1743	SCL Heat Up Cabinet - 7th SB Station	21	21	0	0	21	21	28-Dec-26	27-Jan-27	-22	-22	0	0	☐
Station Electrical														
7th and Stewart SB														
4-SE-1918	Install Electrical - 7th & Stewart SB Station	5	5	0	0	5	5	28-Jan-27	03-Feb-27	-22	-22	0	0	☐
4-SE-1919	KCM Inspection - 7th & Stewart SB Station	5	5	0	0	5	5	04-Feb-27	10-Feb-27	-22	-22	0	0	☐
4-SE-1920	Commission Station Electrical - 7th & Stewart SB Station	1	1	0	0	1	1	11-Feb-27	11-Feb-27	-22	-22	0	0	☐
Hardscapes After Electrical Demo														
Yale														
4-HS-1923	Remove Foundations - Yale	1	1	0	0	1	1	12-Feb-27	12-Feb-27	-22	-22	0	0	☐
4-HS-1924	Prep Sidewalks - Yale	1	1	0	0	1	1	16-Feb-27	16-Feb-27	-22	-22	0	0	☐
4-HS-1925	Pour Sidewalks - Yale	1	1	0	0	1	1	17-Feb-27	17-Feb-27	-22	-22	0	0	☐
Ward														
4-HS-1927	Remove Foundations - Ward	1	1	0	0	1	1	16-Feb-27	16-Feb-27	-22	-22	0	0	☐
4-HS-1928	Prep Sidewalks - Ward	1	1	0	0	1	1	17-Feb-27	17-Feb-27	-22	-22	0	0	☐
4-HS-1929	Pour Sidewalks - Ward	1	1	0	0	1	1	18-Feb-27	18-Feb-27	-22	-22	0	0	☐
Aloha														
4-HS-1931	Remove Foundations - Aloha	1	1	0	0	1	1	17-Feb-27	17-Feb-27	-22	-22	0	0	☐
4-HS-1932	Prep Sidewalks - Aloha	1	1	0	0	1	1	18-Feb-27	18-Feb-27	-22	-22	0	0	☐
4-HS-1933	Pour Sidewalks - Aloha	1	1	0	0	1	1	19-Feb-27	19-Feb-27	-22	-22	0	0	☐
Valley														
4-HS-1935	Remove Foundations - Valley	1	1	0	0	1	1	18-Feb-27	18-Feb-27	-22	-22	0	0	☐
4-HS-1936	Prep Sidewalks - Valley	1	1	0	0	1	1	19-Feb-27	19-Feb-27	-22	-22	0	0	☐
4-HS-1937	Pour Sidewalks - Valley	1	1	0	0	1	1	22-Feb-27	22-Feb-27	-22	-22	0	0	☐
PBL Buffers														
4-PBL-1939	Pour PBL Buffers - Zone 4	10	10	0	0	10	10	23-Feb-27	08-Mar-27	-22	-22	0	0	☐
Chanalization														
4-PM-1941	Channelization - Zone 4	15	15	0	0	15	15	09-Mar-27	29-Mar-27	-22	-22	0	0	☐

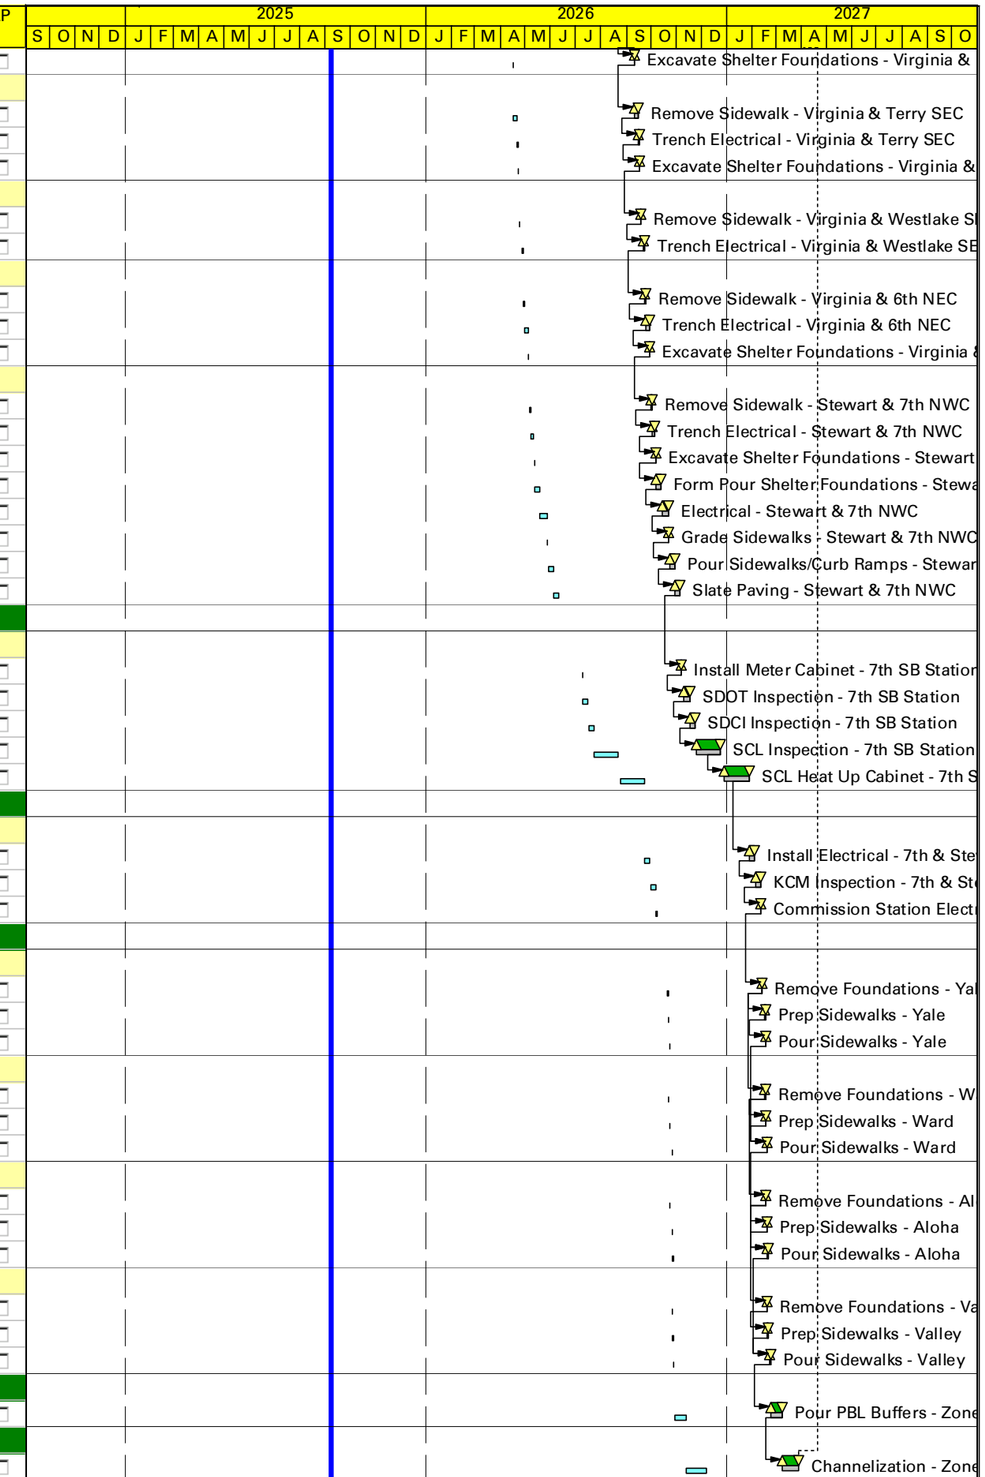

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filters: Longest Path, SELECT (J-LINE), SELECT2.
Layout: J-LINE-WBS-STD
© Primavera Systems, Inc.

JANSEN

120-DAY LOOK AHEAD

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)														
Milestones														
M-9001	CONTRACT TIME	594	616	-3	223	396	619	07-Oct-24 A	06-May-27	-25	-22	0	-3	☑
M-9017	Zone-4 - DB Rescheduling / Admin & Submittals	20	20	2	18	0	18	21-Jul-25 A	13-Aug-25 A		18	0	2	☐
M-9027	Zone-4 - DB Rescheduling / Submit TC Plans	5	5	0	5	0	5	22-Jul-25 A	28-Jul-25 A			0	0	☐
M-9037	Zone-4 - DB Rescheduling / Review TC Plans	15	15	3	12	0	12	29-Jul-25 A	13-Aug-25 A		18	0	3	☐
Long Lead Material														
Poles														
PROC-0007	Procure Poles	120	120	0	75	45	120	21-May-25 A	12-Nov-25	125	125	0	0	☐
Zone 1 - 43rd to University Bridge														
Pole Foundation Potholing														
DSC's														
DSC-002	DSC-002 SW Corner 42nd & 11th Comm Cabinet Conflict P-0303	15	194	0	194	0	194	11-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-003	DSC-003 NW Corner 43rd & 11th Conflict w/Retaining Wall	14	193	0	193	0	193	15-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-004	DSC-004 NE Corner 11th & 43rd P-0201 Conflict	13	192	0	192	0	192	16-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-005	DSC-005 SE Corner 43rd & Roosevelt P-0112 Conflict	12	191	0	191	0	191	17-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-006	DSC-006 NW Corner 11th & 43rd P-0203 Conflict	11	190	0	190	0	190	18-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-008	DSC-008 NW Corner 43rd & Roosevelt P-1002 Conflict	11	190	0	190	0	190	18-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-011	DSC-011 43rd Mid-Block Roosevelt to 11th N. Side T-213-04 Confli	9	188	0	188	0	188	22-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-012	DSC-012 NW Corner 11th & 43rd P-0203 Conflicts	8	187	0	187	0	187	23-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-016	DSC-016 SE Corner 42nd & 11th P-0304 Conduit Conflicts	6	185	0	185	0	185	25-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-017	DSC-017 NE Corner Eastlake & 11th T-212-06 Gas Line Conflict	6	185	0	185	0	185	25-Oct-24 A	01-Aug-25 A			0	0	☑
FM-TBD	SDOT Directed Potholing - 11th Ave NE	11	11	6	5	0	5	04-Aug-25 A	08-Aug-25 A		-16	0	6	☑
Roadway														
43rd Roosevelt to 11th														
NCR-0014015	NCR-014 & NCR-015 Paving	5	0	-5	1	4	5	08-Sep-25 A	12-Sep-25	0				☐
11th and 42nd Phase 3														
NCR-022	NCR-022 Damage to panel while removing adjacent panel	1	0	-1	1	0	1	31-Jul-25 A	31-Jul-25 A					☑
43rd 11th to 12th														
1-RW-0080	Pour Roadway - 43rd / 11th to 12th	17	17	0	17	0	17	08-Jul-25 A	30-Jul-25 A			0	0	☑
DC-XXX	RFI-136 Elevation Issues	13	13	0	13	0	13	10-Jul-25 A	28-Jul-25 A			0	0	☑
NCR-021	NCR-021 Riser is cast to the incorrect height bringing the lid to 1 1	1	0	-1	1	0	1	24-Jul-25 A	24-Jul-25 A					☑
1-RW-0081	Curb - 43rd / 11th to 12th	3	3	0	3	0	3	31-Jul-25 A	04-Aug-25 A			0	0	☑
1-RW-0082	Temp Pave - 43rd / 11th to 12th	1	1	0	1	0	1	05-Aug-25 A	05-Aug-25 A		-16	0	0	☑
11th and 42nd Phase 4														
1-RW-0075	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.4)	3	3	0	3	0	3	08-Jul-25 A	10-Jul-25 A			0	0	☑
1-RW-0076	Pour Roadway - 11th & 42nd (Ph.4)	3	3	0	3	0	3	11-Jul-25 A	15-Jul-25 A			0	0	☑
1-RW-0077	Temp Pave - 11th & 42nd (Ph.4)	1	1	0	1	0	1	16-Jul-25 A	16-Jul-25 A			0	0	☑
Roosevelt and 43rd Western Half														
1-RW-0084	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd (West)	3	3	-6	9	0	9	11-Aug-25 A	21-Aug-25 A		14	6	0	☐
DSC-303	DSC-303 43rd/Roosevelt Sinkhole	6	0	-6	6	0	6	12-Aug-25 A	19-Aug-25 A					☐
1-RW-0085	Pour Roadway - Roosevelt & 43rd (West)	2	2	0	2	0	2	22-Aug-25 A	25-Aug-25 A		19	0	0	☐
1-RW-0086	Curb - Roosevelt & 43rd (West)	1	1	-1	2	0	2	26-Aug-25 A	27-Aug-25 A		19	0	-1	☐
1-RW-0087	Temp Pave - Roosevelt & 43rd (West)	1	1	0	1	0	1	28-Aug-25 A	28-Aug-25 A		19	-1	-1	☐
Roosevelt and 43rd St. SE Corner														
1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	3	0	-3	3	0	3	29-Aug-25 A	03-Sep-25 A					☐
DSC-327	DSC-327 43rd & Roosevelt Rotten Pole	1	0	-1	1	0	1	03-Sep-25 A	03-Sep-25 A					☐
DSC-328	DSC-328 SEC 43rd Roosevelt Conduits Cast in Curb	1	0	-1	1	0	1	04-Sep-25 A	04-Sep-25 A					☐
1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	2	0	-2	0	2	2	15-Sep-25	16-Sep-25	0				☐
1-RW-189	Curb - Roosevelt & 43rd SEC	2	0	-2	0	2	2	17-Sep-25	18-Sep-25	7				☐
Roosevelt and 43rd St. NE Corner														
1-RW-139	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd NEC	2	0	-2	2	0	2	04-Sep-25 A	05-Sep-25 A					☐
1-RW-149	Pour Roadway - Roosevelt & 43rd NEC	2	0	-2	0	2	2	15-Sep-25	16-Sep-25	8				☐
1-RW-159	Curb - Roosevelt & 43rd NEC	2	0	-2	0	2	2	17-Sep-25	18-Sep-25	8				☐

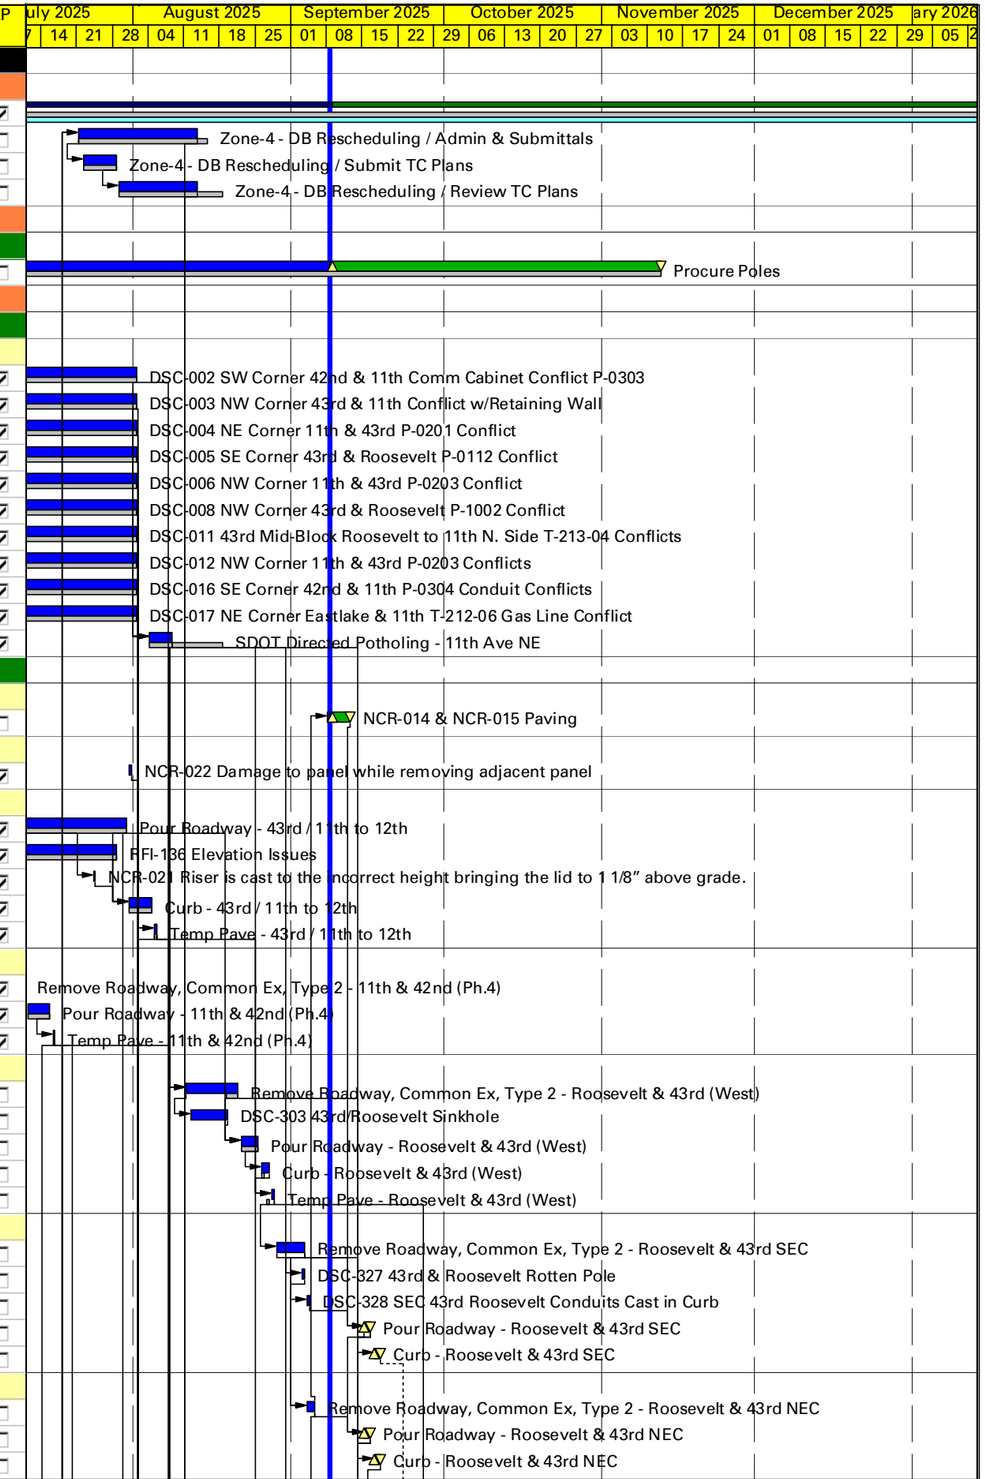

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
11th and Eastlake West Side														
DSC-275	DSC 275 11th Ave Water Service CDF conflict	1	1	0	1	0	1	23-Jul-25 A	23-Jul-25 A			0	0	☐
1-RW-0089	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (West)	5	3	-2	0	5	5	17-Sep-25	23-Sep-25	0	14	-17	-19	☐
1-RW-0090	Pour Roadway - 11th & Eastlake (West)	2	2	0	0	2	2	24-Sep-25	25-Sep-25	2	16	-19	-19	☐
1-RW-0091	Curb - 11th & Eastlake (West)	2	2	0	0	2	2	26-Sep-25	29-Sep-25	2	16	-19	-19	☐
1-RW-0092	Temp Pave - 11th & Eastlake (West)	1	1	0	0	1	1	30-Sep-25	30-Sep-25	2	16	-19	-19	☐
Eastlake 11th to NE Campus Pkwy East Side														
1-RW-0102	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Cai	5	3	-2	0	5	5	17-Sep-25	23-Sep-25	3	14	-9	-11	☐
1-RW-0103	Pour Roadway - Eastlake / 11th to NE Campus (East)	2	2	0	0	2	2	24-Sep-25	25-Sep-25	4	15	-11	-11	☐
1-RW-0104	Curb - Eastlake / 11th to NE Campus (East)	2	2	0	0	2	2	26-Sep-25	29-Sep-25	4	15	-11	-11	☐
11th and Eastlake East Side														
1-RW-0098	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (East)	2	2	0	1	1	2	08-Sep-25 A	09-Sep-25	10	14	-4	-4	☐
1-RW-0099	Pour Roadway - 11th & Eastlake (East)	2	2	0	0	2	2	17-Sep-25	18-Sep-25	8	16	-9	-9	☐
1-RW-0100	Curb - 11th & Eastlake (East)	2	2	0	0	2	2	19-Sep-25	22-Sep-25	8	16	-9	-9	☐
Eastlake 11th to NE Campus Pkwy West Side														
1-RW-0094	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Cai	3	3	0	0	3	3	24-Sep-25	26-Sep-25	0	14	-19	-19	☐
1-RW-0095	Pour Roadway - Eastlake / 11th to NE Campus (West)	2	2	0	0	2	2	29-Sep-25	30-Sep-25	2	16	-19	-19	☐
1-RW-0096	Curb - Eastlake / 11th to NE Campus (West)	2	2	0	0	2	2	01-Oct-25	02-Oct-25	2	16	-19	-19	☐
Roosevelt and 42nd St East Side														
1-RW-0106	Remove Roadway, Common Ex, Type 2 - Roosevelt & 42nd (E)	2	2	0	0	2	2	29-Sep-25	30-Sep-25	0	14	-14	-14	☐
1-RW-0107	Pour Roadway - Roosevelt & 42nd (E)	1	1	0	0	1	1	01-Oct-25	01-Oct-25	3	15	-12	-12	☐
Roosevelt and 41st East Side														
1-RW-0109	Remove Roadway, Common Ex, Type 2 - Roosevelt & 41st (E)	2	2	0	0	2	2	01-Oct-25	02-Oct-25	0	14	-14	-14	☐
1-RW-0110	Pour Roadway - Roosevelt & 41st (E)	1	1	0	0	1	1	03-Oct-25	03-Oct-25	2	15	-13	-13	☐
Roosevelt and Campus Pkwy East Side														
1-RW-0112	Remove Roadway, Common Ex, Type 2 - Roosevelt & Campus (E)	2	2	0	0	2	2	03-Oct-25	06-Oct-25	0	14	-14	-14	☐
1-RW-0113	Pour Roadway - Roosevelt & Campus (E)	1	1	0	0	1	1	07-Oct-25	07-Oct-25	1	15	-14	-14	☐
Roosevelt and 42nd St West Side														
1-RW-0115	Remove Roadway, Common Ex, Type 2 - Roosevelt & 42nd (W)	2	2	0	0	2	2	07-Oct-25	08-Oct-25	0	14	-14	-14	☐
1-RW-0116	Pour Roadway - Roosevelt & 42nd (W)	2	2	0	0	2	2	09-Oct-25	10-Oct-25	0	14	-14	-14	☐
Roosevelt and 41st West Side														
1-RW-0118	Remove Roadway, Common Ex, Type 2 - Roosevelt & 41st (W)	2	2	0	0	2	2	09-Oct-25	10-Oct-25	0	14	-14	-14	☐
1-RW-0119	Pour Roadway - Roosevelt & 41st (W)	2	2	0	0	2	2	14-Oct-25	15-Oct-25	0	14	-14	-14	☐
Weekend Roadway Work														
43rd 11th to 12th Road Panels														
1-WE-0125	Remove Roadway Type 2 - 43rd / 11th to 12th	1	1	0	1	0	1	02-Aug-25 A	02-Aug-25 A			0	0	☑
1-WE-0126	Pour Roadway - 43rd / 11th to 12th	1	1	0	1	0	1	03-Aug-25 A	03-Aug-25 A			0	0	☑
Pole Foundations														
DSC-266	DSC-266 11th 43rd to 42nd Pole foundation conflicts with comm c	1	1	0	1	0	1	17-Jul-25 A	17-Jul-25 A			0	0	☑
DSC-270	DSC-270 11th 43rd to 42nd Pole T-211-06 Side Sewer conflict	1	1	0	1	0	1	18-Jul-25 A	18-Jul-25 A			0	0	☑
1-PF-0130	11th - Pole Foundations (17 ea.) Prior to SDOT Directed Additiona	11	11	0	11	0	11	21-Jul-25 A	04-Aug-25 A			0	0	☑
1-PF-0129	43rd - Pole Foundations (17 ea.) - PRIOR to Completion of SDOT D	10	10	6	4	0	4	05-Aug-25 A	08-Aug-25 A		-16	0	6	☑
DSC-296	DSC-296 11th Ave, T211-01 Potholing SS conflict	1	0	-1	1	0	1	06-Aug-25 A	06-Aug-25 A					☑
DSC-301	DSC-301 11th 43rd to 42nd E. Side Sewer conflict w/foundation T2	1	0	-1	1	0	1	11-Aug-25 A	11-Aug-25 A					☑
1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER C	7	7	-6	13	0	13	11-Aug-25 A	27-Aug-25 A		-16	6	0	☑
DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved fc	1	0	-15	15	0	15	11-Aug-25 A	29-Aug-25 A					☑
1-PF-0159	SDOT Stop Work E-mail / Issue Directive/Design	1	0	-15	15	0	15	11-Aug-25 A	29-Aug-25 A					☑
DSC-311	DSC-311 43RD Roosevelt to 11th Boulder conflict with foundation	1	0	-1	1	0	1	19-Aug-25 A	19-Aug-25 A					☑
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	11	11	9	2	0	2	28-Aug-25 A	29-Aug-25 A		5	0	9	☑
1-PF-0179	11th / 42nd to 41st - SDOT Directed Stop Work (install 2 pole fdns)	4	0	-4	4	0	4	02-Sep-25 A	05-Sep-25 A					☐
1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	4	0	-4	4	0	4	02-Sep-25 A	05-Sep-25 A					☑
DSC-329	DSC-329 11th Ave Ground Water in OCS foundations	1	0	-1	1	0	1	04-Sep-25 A	04-Sep-25 A					☐
DSC-341	DSC-341 43rd & 11th Signal Service Conflict w/ Temp Lighting	5	0	-5	1	4	5	08-Sep-25 A	12-Sep-25	20				☐
1-PF-0150	11th - Pole Foundations (After Yale to Aloha Zone-4 SDOT Mitigat	10	0	-10	0	10	10	15-Sep-25	26-Sep-25	-5				☐

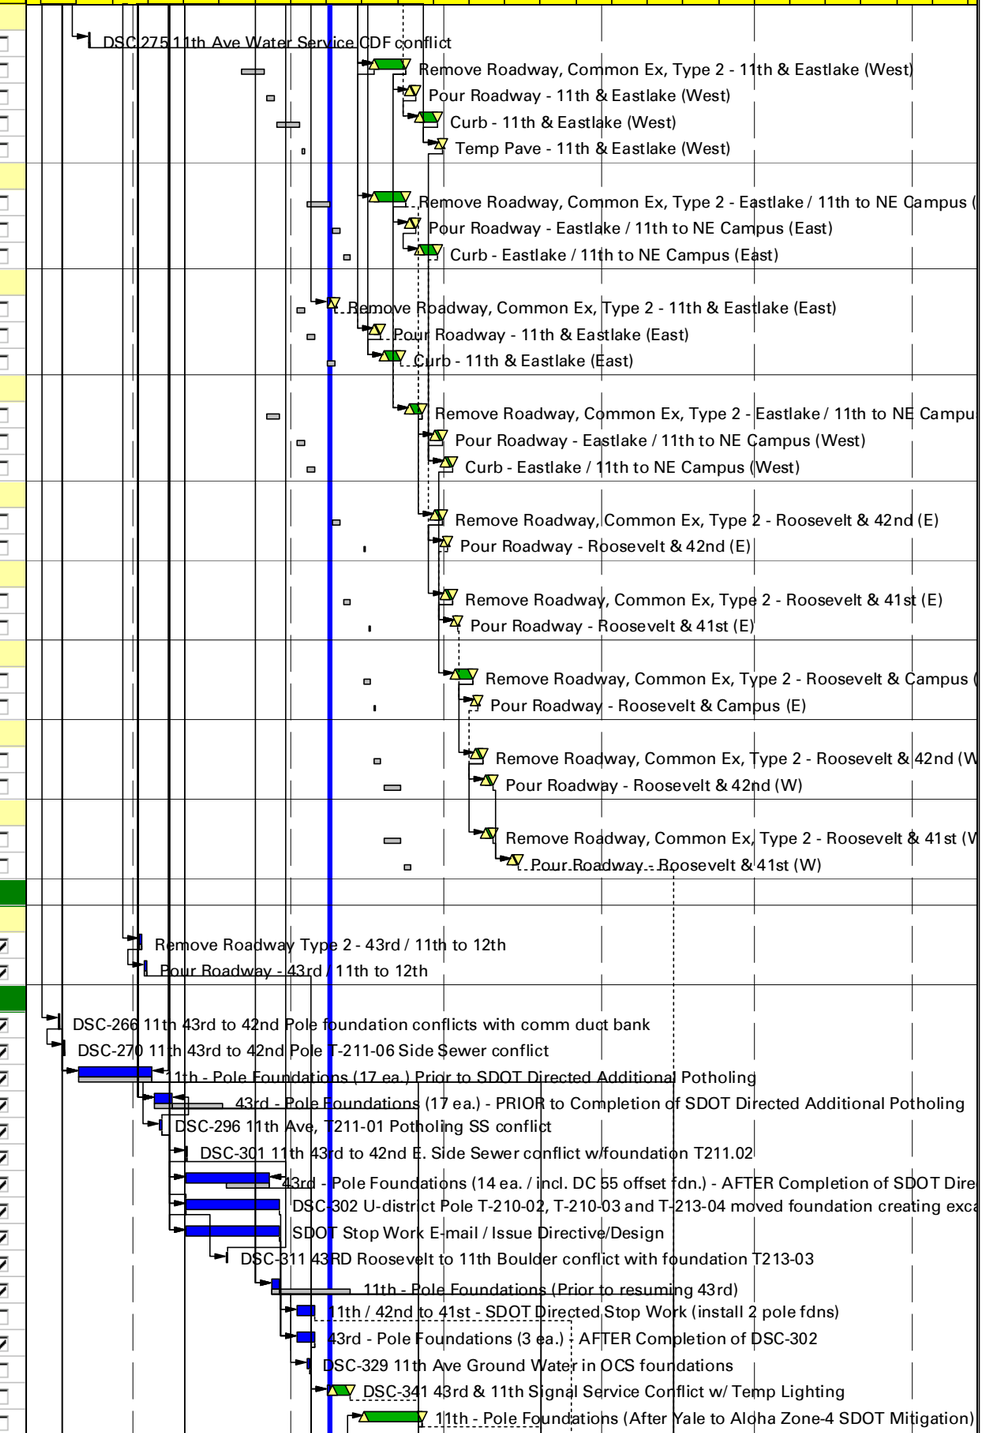

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-351	DSC-351 Pole Foundation P-0204 SW 11th & Roosevelt	2	0	-2	0	2	2	29-Sep-25	30-Sep-25	10				☐
1-PF-0131	Roosevelt - Pole Foundations (21 ea.)	21	21	0	0	21	21	29-Sep-25	28-Oct-25	-5	5	-10	-10	☐
1-PF-0132	Eastlake - Pole Foundations (10 ea.)	10	10	0	0	10	10	29-Oct-25	12-Nov-25	-5	5	-10	-10	☐
Sidewalks														
43rd 12th to 11th North Side														
1-SW-0135	Remove Sidewalk - 43rd / 12th to 11th (N)	2	2	0	1	1	2	08-Sep-25 A	09-Sep-25	-22	-16	-6	-6	☑
1-SW-0136	Trench Electrical - 43rd / 12th to 11th (N)	3	3	0	0	3	3	10-Sep-25	12-Sep-25	-22	-16	-6	-6	☑
1-SW-0137	Electrical - 43rd / 12th to 11th (N)	3	3	0	0	3	3	15-Sep-25	17-Sep-25	-17	-11	-6	-6	☐
1-SW-0138	Grade Sidewalks - 43rd / 12th to 11th (N)	2	2	0	0	2	2	18-Sep-25	19-Sep-25	-17	-11	-6	-6	☐
1-SW-0139	Pour Sidewalks/Curb Ramps - 43rd / 12th to 11th (N)	4	4	0	0	4	4	22-Sep-25	25-Sep-25	-14	-8	-6	-6	☐
43rd 11th to Roosevelt North Side														
1-SW-0141	Remove Sidewalk - 43rd / 11th to Roosevelt (N)	1	1	0	0	1	1	15-Sep-25	15-Sep-25	-22	-16	-6	-6	☑
1-SW-0142	Trench Electrical - 43rd / 11th to Roosevelt (N)	2	2	0	0	2	2	16-Sep-25	17-Sep-25	-22	-16	-6	-6	☑
1-SW-0143	Electrical - 43rd / 11th to Roosevelt (N)	7	7	0	0	7	7	18-Sep-25	26-Sep-25	-22	-16	-6	-6	☑
1-SW-0144	Grade Sidewalks - 43rd / 11th to Roosevelt (N)	2	2	0	0	2	2	29-Sep-25	30-Sep-25	-22	-16	-6	-6	☑
1-SW-0145	Pour Sidewalks/Curb Ramps - 43rd / 11th to Roosevelt (N)	6	6	0	0	6	6	01-Oct-25	08-Oct-25	-17	-11	-6	-6	☐
Design Change 055 - Sidewalks 11th Ave. / 43rd to 45th East Side														
1-SW-DC-055A	Remove Sidewalk - 11th; 43rd to 45th (E) DC-055	2	2	0	0	2	2	01-Oct-25	02-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055B	Trench Electrical - 11th; 43rd to 45th (E) DC-055	5	5	0	0	5	5	03-Oct-25	09-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055C	Electrical - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	08-Oct-25	14-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055D	Grade Sidewalks - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	10-Oct-25	16-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055E	Pour Sidewalks/Curb Ramps - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	17-Oct-25	22-Oct-25	-22	-16	-6	-6	☑
11th and 42nd NEC														
1-SW-0147	Remove Sidewalk - 11th & 42nd NEC	2	2	0	0	2	2	23-Oct-25	24-Oct-25	-22	-16	-6	-6	☑
1-SW-0148	Trench Electrical - 11th & 42nd NEC	2	2	0	0	2	2	27-Oct-25	28-Oct-25	-22	-16	-6	-6	☑
1-SW-0149	Electrical - 11th & 42nd NEC	3	3	0	0	3	3	29-Oct-25	31-Oct-25	-14	-8	-6	-6	☐
1-SW-0150	Grade Sidewalks - 11th & 42nd NEC	1	1	0	0	1	1	03-Nov-25	03-Nov-25	-14	-8	-6	-6	☐
1-SW-0151	Pour Sidewalks/Curb Ramps - 11th & 42nd NEC	3	3	0	0	3	3	04-Nov-25	06-Nov-25	-14	-8	-6	-6	☐
11th and 42nd SEC														
1-SW-0153	Remove Sidewalk - 11th & 42nd SEC	2	2	0	0	2	2	29-Oct-25	30-Oct-25	-22	-16	-6	-6	☑
1-SW-0154	Trench Electrical - 11th & 42nd SEC	2	2	0	0	2	2	31-Oct-25	03-Nov-25	-22	-16	-6	-6	☑
1-SW-0155	Electrical - 11th & 42nd SEC	5	5	0	0	5	5	04-Nov-25	10-Nov-25	-17	-11	-6	-6	☐
1-SW-0156	Grade Sidewalks - 11th & 42nd SEC	1	1	0	0	1	1	12-Nov-25	12-Nov-25	-17	-11	-6	-6	☐
1-SW-0157	Pour Sidewalks/Curb Ramps - 11th & 42nd SEC	3	3	0	0	3	3	13-Nov-25	17-Nov-25	-17	-11	-6	-6	☐
11th and Eastlake East Side														
1-SW-0159	Remove Sidewalk - 11th & Eastlake ()	2	2	0	0	2	2	04-Nov-25	05-Nov-25	-22	-16	-6	-6	☑
1-SW-0160	Grade Sidewalks - 11th & Eastlake ()	2	2	0	0	2	2	06-Nov-25	07-Nov-25	-22	-16	-6	-6	☑
1-SW-0161	Pour Sidewalks/Curb Ramps - 11th & Eastlake ()	2	2	0	0	2	2	18-Nov-25	19-Nov-25	-17	-11	-6	-6	☐
43rd 12th to 11th South Side														
1-SW-0163	Remove Sidewalk - 43rd / 12th to 11th (S)	2	2	0	0	2	2	10-Nov-25	12-Nov-25	-22	-16	-6	-6	☑
1-SW-0164	Trench Electrical - 43rd / 12th to 11th (S)	3	3	0	0	3	3	13-Nov-25	17-Nov-25	-22	-16	-6	-6	☑
1-SW-0165	Electrical - 43rd / 12th to 11th (S)	5	5	0	0	5	5	18-Nov-25	24-Nov-25	-21	-15	-6	-6	☐
1-SW-0166	Grade Sidewalks - 43rd / 12th to 11th (S)	1	1	0	0	1	1	25-Nov-25	25-Nov-25	-21	-15	-6	-6	☐
1-SW-0167	Pour Sidewalks/Curb Ramps - 43rd / 12th to 11th (S)	4	4	0	0	4	4	26-Nov-25	03-Dec-25	-21	-15	-6	-6	☐
43rd 11th to Roosevelt South Side														
1-SW-0169	Remove Sidewalk - 43rd / 11to to Roosevelt (S)	1	1	0	0	1	1	18-Nov-25	18-Nov-25	-22	-16	-6	-6	☑
1-SW-0170	Trench Electrical - 43rd / 11to to Roosevelt (S)	2	2	0	0	2	2	19-Nov-25	20-Nov-25	-22	-16	-6	-6	☑
1-SW-0171	Electrical - 43rd / 11to to Roosevelt (S)	6	6	0	0	6	6	21-Nov-25	02-Dec-25	-22	-16	-6	-6	☑
1-SW-0172	Grade Sidewalks - 43rd / 11to to Roosevelt (S)	2	2	0	0	2	2	03-Dec-25	04-Dec-25	-22	-16	-6	-6	☑
1-SW-0173	Pour Sidewalks/Curb Ramps - 43rd / 11to to Roosevelt (S)	5	5	0	0	5	5	05-Dec-25	11-Dec-25	-22	-16	-6	-6	☑
11th and 42nd NWC														
1-SW-0175	Remove Sidewalk - 11th & 42nd NWC	1	1	0	0	1	1	21-Nov-25	21-Nov-25	-22	-16	-6	-6	☑
1-SW-0176	Trench Electrical - 11th & 42nd NWC	2	2	0	0	2	2	24-Nov-25	25-Nov-25	-22	-16	-6	-6	☑
1-SW-0177	Electrical - 11th & 42nd NWC	4	4	0	0	4	4	26-Nov-25	03-Dec-25	-17	-11	-6	-6	☐

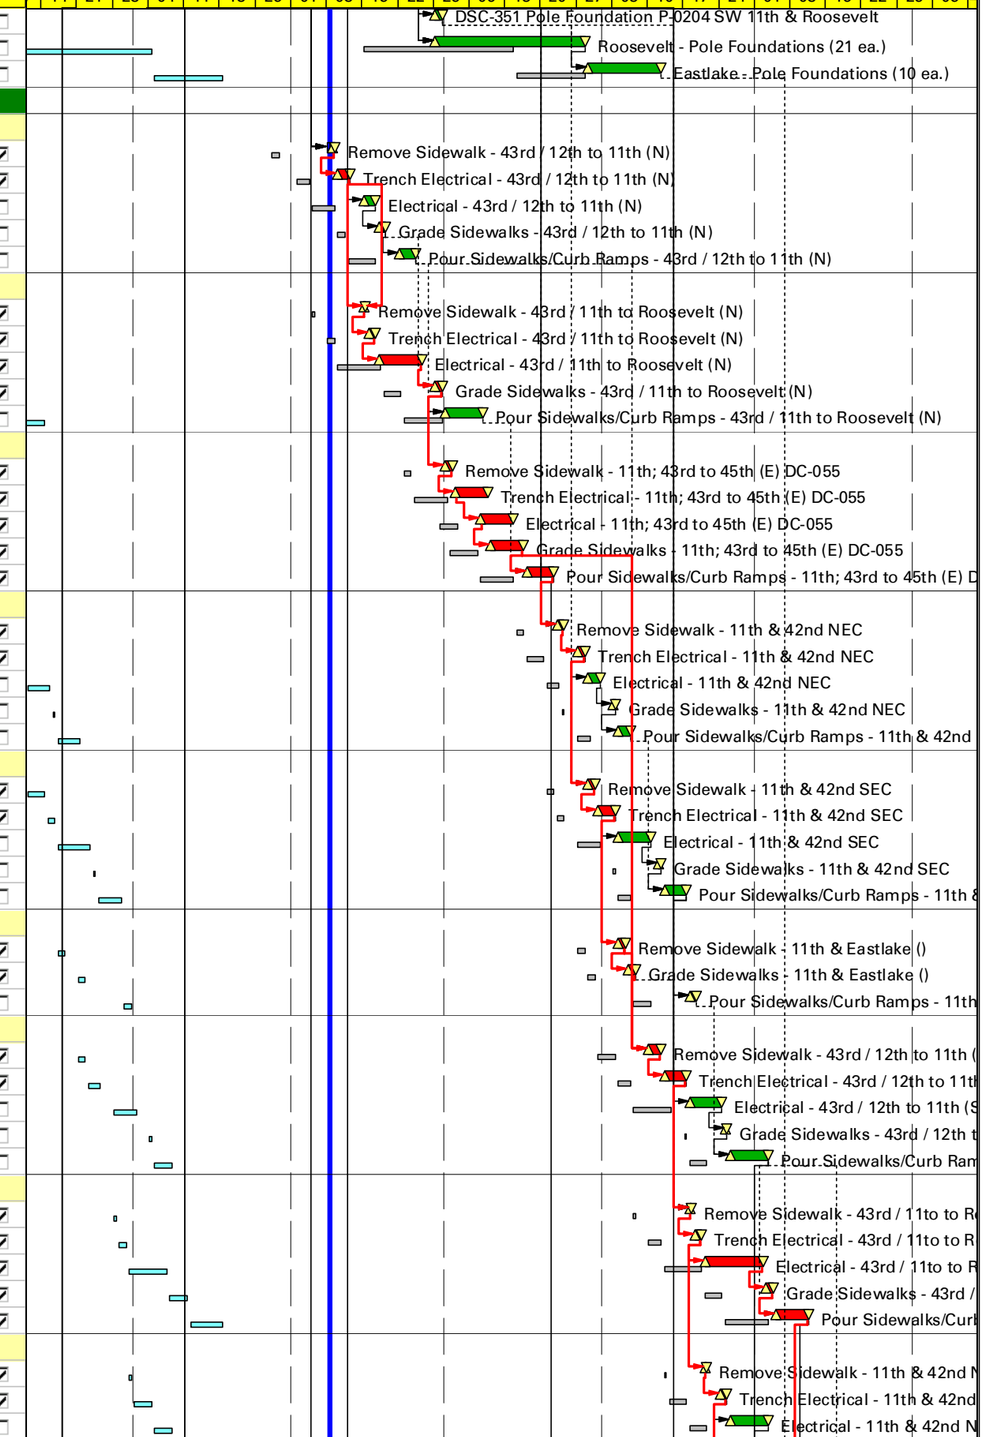

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© Primavera Systems, Inc.

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-SW-0178	Grade Sidewalks - 11th & 42nd NWC	1	1	0	0	1	1	04-Dec-25	04-Dec-25	-17	-11	-6	-6	☐
1-SW-0179	Pour Sidewalks/Curb Ramps - 11th & 42nd NWC	4	4	0	0	4	4	12-Dec-25	17-Dec-25	-22	-16	-6	-6	☑
11th and 42nd SWC														
1-SW-0181	Remove Sidewalk 11th & 42nd SWC	1	1	0	0	1	1	26-Nov-25	26-Nov-25	-22	-16	-6	-6	☑
1-SW-0182	Trench Electrical 11th & 42nd SWC	2	2	0	0	2	2	01-Dec-25	02-Dec-25	-22	-16	-6	-6	☑
1-SW-0183	Electrical 11th & 42nd SWC	4	4	0	0	4	4	03-Dec-25	08-Dec-25	-22	-16	-6	-6	☑
1-SW-0184	Grade Sidewalks 11th & 42nd SWC	1	1	0	0	1	1	09-Dec-25	09-Dec-25	-22	-16	-6	-6	☑
1-SW-0185	Pour Sidewalks/Curb Ramps - 11th & 42nd SWC	4	4	0	0	4	4	18-Dec-25	23-Dec-25	-22	-16	-6	-6	☑
Roosevelt and 43rd West Side														
1-SW-0187	Remove Sidewalk - Roosevelt & 43rd (W)	1	1	0	0	1	1	10-Dec-25	10-Dec-25	-22	-16	-6	-6	☑
1-SW-0188	Trench Electrical - Roosevelt & 43rd (W)	2	2	0	0	2	2	11-Dec-25	12-Dec-25	-22	-16	-6	-6	☑
1-SW-0189	Electrical - Roosevelt & 43rd (W)	5	5	0	0	5	5	15-Dec-25	19-Dec-25	-22	-16	-6	-6	☑
1-SW-0190	Grade Sidewalks - Roosevelt & 43rd (W)	2	2	0	0	2	2	22-Dec-25	23-Dec-25	-22	-16	-6	-6	☑
1-SW-0191	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd (W)	4	4	0	0	4	4	24-Dec-25	30-Dec-25	-22	-16	-6	-6	☑
Roosevelt and 43rd NWC														
1-SW-0193	Remove Sidewalk - Roosevelt & 43rd NWC	1	1	0	0	1	1	15-Dec-25	15-Dec-25	-22	-16	-6	-6	☑
1-SW-0194	Trench Electrical - Roosevelt & 43rd NWC	1	1	0	0	1	1	16-Dec-25	16-Dec-25	-22	-16	-6	-6	☑
1-SW-0195	Electrical - Roosevelt & 43rd NWC	3	3	0	0	3	3	17-Dec-25	19-Dec-25	-22	-16	-6	-6	☑
1-SW-0196	Grade Sidewalks - Roosevelt & 43rd NWC	1	1	0	0	1	1	22-Dec-25	22-Dec-25	-22	-16	-6	-6	☑
1-SW-0197	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd NWC	3	3	0	0	3	3	23-Dec-25	26-Dec-25	-22	-16	-6	-6	☑
Roosevelt and 43rd SWC														
1-SW-0199	Remove Sidewalk - Roosevelt & 43rd SWC	1	1	0	0	1	1	29-Dec-25	29-Dec-25	-22	-16	-6	-6	☑
1-SW-0200	Grade Sidewalks - Roosevelt & 43rd SWC	1	1	0	0	1	1	30-Dec-25	30-Dec-25	-22	-16	-6	-6	☑
1-SW-0201	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd SWC	3	3	0	0	3	3	31-Dec-25	05-Jan-26	-22	-16	-6	-6	☑
Roosevelt and 42nd NWC														
1-SW-0203	Remove Sidewalk - Roosevelt & 42nd NWC	1	1	0	0	1	1	06-Jan-26	06-Jan-26	-22	-16	-6	-6	☑
Weekend Driveway														
Driveways 11th / 43rd to 45th (DC-055)														
1-WE-DC-055A	Remove Sidewalk - 11th; 43rd to 45th (E) DC-055	1	1	0	0	1	1	25-Oct-25	25-Oct-25	30	32	-2	-2	☐
1-WE-DC-055B	Pour Driveway - 11th; 43rd to 45th (E) DC055	1	1	0	0	1	1	26-Oct-25	26-Oct-25	30	32	-2	-2	☐
43rd Roosevelt to 11th														
1-WE-0269	Remove Sidewalk - 43rd / Roosevelt to 11th (driveway)	1	1	0	0	1	1	13-Dec-25	13-Dec-25	18	20	-2	-2	☐
1-WE-0270	Pour Driveway - 43rd / Roosevelt to 11th (driveway)	1	1	0	0	1	1	14-Dec-25	14-Dec-25	18	20	-2	-2	☐
43rd 11th to 12th														
1-WE-0272	Remove Sidewalk - 43rd / 11th to 12th	1	1	0	0	1	1	20-Dec-25	20-Dec-25	18	20	-2	-2	☐
1-WE-0273	Pour Driveway - 43rd / 11th to 12th	1	1	0	0	1	1	21-Dec-25	21-Dec-25	18	20	-2	-2	☐
SCL Services - Zone 1														
43rd and 11th SDOT Signal Service														
1-SCL-0290	Install Meter Cabinet - 43rd & 11th Signal	1	1	0	0	1	1	04-Dec-25	04-Dec-25	92	98	-6	-6	☐
1-SCL-0291	SDOT Inspection - 43rd & 11th Signal	5	5	0	0	5	5	05-Dec-25	11-Dec-25	92	98	-6	-6	☐
1-SCL-0292	SDCI Inspection - 43rd & 11th Signal	5	5	0	0	5	5	12-Dec-25	18-Dec-25	92	98	-6	-6	☐
1-SCL-0293	SCL Inspection - 43rd & 11th Signal	21	21	0	0	21	21	19-Dec-25	21-Jan-26	92	98	-6	-6	☐
42nd and 11th SDOT Service														
1-SCL-0297	Install Meter Cabinet - 42nd & 11th	1	1	0	0	1	1	18-Nov-25	18-Nov-25	127	133	-6	-6	☐
1-SCL-0298	SDOT Inspection - 42nd & 11th	5	5	0	0	5	5	19-Nov-25	25-Nov-25	127	133	-6	-6	☐
1-SCL-0299	SDCI Inspection - 42nd & 11th	5	5	0	0	5	5	26-Nov-25	04-Dec-25	127	133	-6	-6	☐
1-SCL-0300	SCL Inspection - 42nd & 11th	21	21	0	0	21	21	05-Dec-25	06-Jan-26	127	133	-6	-6	☐
Zone 2 - Fuhrman to Lynn														
Watermain														
2-RW-0602	TROLLEY REACTIVATION Harvard to Fuhrman (8/29/25)	0	0	0	0	0	0		29-Aug-25 A		0	0	0	☐
Stage 1 Eastlake From Harvard to North of Intersection of Hamlin (6+60 to 21+50)														
SPU Ops Notifications														
2-W-0529	SPU Water Ops Scheduling Notification - Stg 1 (CC02 & CC03)	15	15	0	15	0	15	15-Jul-25 A	04-Aug-25 A			0	0	☐
Waterline Installation														

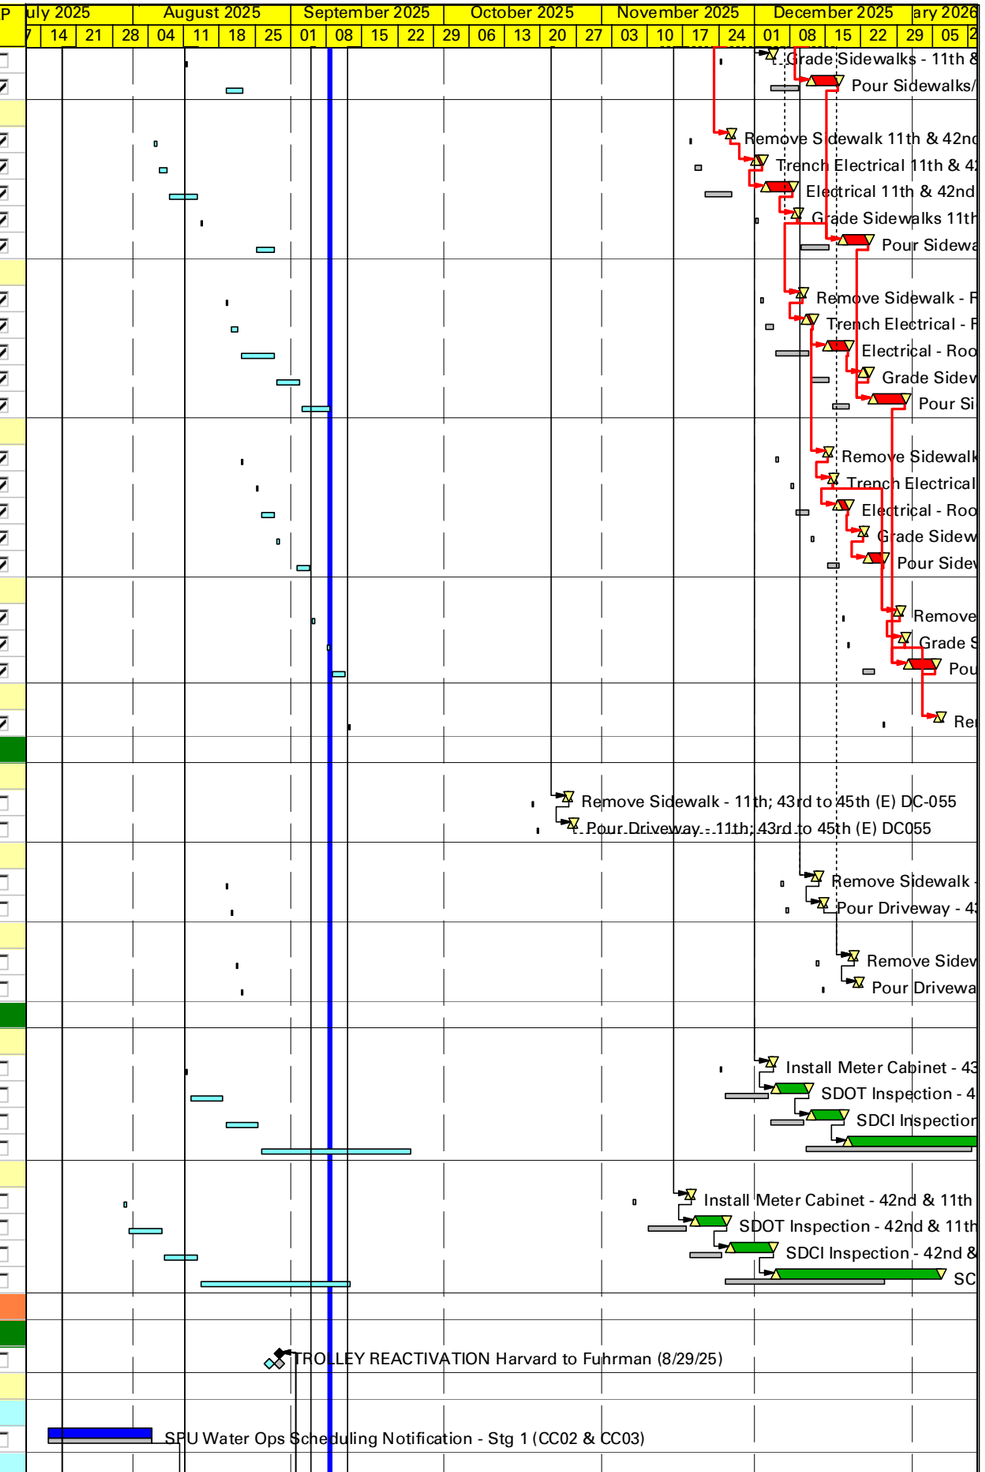

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort; BL1 LOE; BL2 LOE; Actual Level of Effort; Actual Work; Remaining Work; Critical Remaining Work; Milestone; Previous MS; Previous Bar; Baseline MS; Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-W-0562	SPU Cut and Cap CC01, 02, 03, 04	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	
2-W-0462	Install Water Vaults (1 Ea) - Stg 1 Allison	6	6	0	6	0	6	11-Jul-25 A	18-Jul-25 A			0	0	
2-W-0464	Install Mainline Allison Lateral Sta. 200+26 to 200+15 - Stg 1 Harva	2	2	0	2	0	2	17-Jul-25 A	18-Jul-25 A			0	0	
DSC-269	DSC-269 Stage 1 Waterline CDF conflict STA 14+70	1	1	0	1	0	1	18-Jul-25 A	18-Jul-25 A			0	0	
2-W-0475	Mainline Allison Lateral Sta. Sta. 300+00 to 300+31	1	1	0	1	0	1	21-Jul-25 A	21-Jul-25 A			0	0	
DSC-271	DSC 271 Stage 1 WM, 2EA unlocated Steel Lines Sta 14+50	1	1	0	1	0	1	21-Jul-25 A	21-Jul-25 A			0	0	
2-W-0467	Test & Flush - Stg 1 Harvard to Hamlin	8	8	0	8	0	8	22-Jul-25 A	31-Jul-25 A			0	0	
NCR-020	NCR-020 Jansen ruptured a 1 ½" service line	1	0	-1	1	0	1	25-Jul-25 A	25-Jul-25 A					
DSC-281	DSC 281 Stage 1, 12+85 Unlocated Conduits & 2in Steel Line	1	1	0	1	0	1	29-Jul-25 A	29-Jul-25 A			0	0	
2-W-0470	Excavate Tie-Ins - Stg 1 Harvard to Hamlin	2	2	0	2	0	2	01-Aug-25 A	04-Aug-25 A			0	0	
2-W-0468	Bact Results - Stg 1 Harvard to Hamlin	3	3	0	3	0	3	01-Aug-25 A	05-Aug-25 A		1	0	0	
DSC-288	DSC 288 Stage 1, 2840 Eastlake Leaking Service behind meter	1	1	0	1	0	1	04-Aug-25 A	04-Aug-25 A			0	0	
DSC-293	DSC-293 Stage 1 Sta 19+11 CDF Conflict	1	0	-1	1	0	1	04-Aug-25 A	04-Aug-25 A					
DSC-295	DSC-295 Stage 1 WM, WS-301 Root Conflicts	1	0	-1	1	0	1	05-Aug-25 A	05-Aug-25 A					
2-W-0471	Excavate Services - Stg 1 Harvard to Hamlin	4	4	0	4	0	4	05-Aug-25 A	08-Aug-25 A		3	0	0	
2-W-0469	SPU Customer Notification - Stg 1 Harvard to Hamlin (CC02 & CC(	5	5	0	5	0	5	06-Aug-25 A	12-Aug-25 A		1	0	0	
DSC-297	DSC-297 Stage 1 WM, WS-301 CDF Conflict	1	0	-1	1	0	1	07-Aug-25 A	07-Aug-25 A					
DSC-298	DSC-298 Stage 1 WM, WS-207 Root Conflicts	1	0	-1	1	0	1	07-Aug-25 A	07-Aug-25 A					
DSC-299	DSC-299 Stage 1 WM, WS-205 CDF Conflict	1	0	-1	1	0	1	07-Aug-25 A	07-Aug-25 A					
2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	1	1	0	1	0	1	13-Aug-25 A	13-Aug-25 A		1	0	0	
2-W-0473	SPU Transfer Services - Stg 1 Harvard to Hamlin (21 ea.)	6	6	3	3	0	3	13-Aug-25 A	15-Aug-25 A		1	1	4	
2-W-0554	SPU Temp Jumper Conn. Sta. 21+50 - Stg 1 Harvard to Hamlin	2	2	0	2	0	2	18-Aug-25 A	19-Aug-25 A		1	4	4	
2-W-0474	Patch Pave - Stg 1 Harvard to Hamlin	1	1	0	1	0	1	20-Aug-25 A	20-Aug-25 A		57	4	4	
2-W-0549	Test Stations Watermain Stage 1	5	5	4	1	0	1	21-Aug-25 A	21-Aug-25 A		135	4	8	
Stage 2 North of Hamlin to Edgar (21+50 to 33+19)														
SPU Ops Notifications														
2-W-0536	SPU Water Ops Scheduling Notification - Stg 2 (CC05, 06, 07)	15	15	0	15	0	15	15-Aug-25 A	05-Sep-25 A		8	4	4	
2-W-0526	SPU Water Ops Scheduling Notification - Stg 2 (TM2.1 & TM2.2)	15	15	0	13	2	15	20-Aug-25 A	10-Sep-25	8	1	4	4	
2-W-0524	SPU Water Ops Scheduling Notification - Stg 2 (CC05 Tie-in)	15	15	0	0	15	15	26-Sep-25	17-Oct-25	13	8	5	5	
Waterline Installation														
2-W-0606	Install Temp Main TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	5	5	-1	6	0	6	20-Aug-25 A	27-Aug-25 A		1	4	3	
DSC-316	DSC-316 Stage 2 Temp Main unlocated unknown water service cc	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
DSC-320	DSC-320 Stage 2 temp main CDF Encased existing main	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
DSC-321	DSC-321 Unknown Unlocated Water Service STA 28+80 stage 2	1	0	-1	1	0	1	27-Aug-25 A	27-Aug-25 A					
2-W-0616	Test & Flush TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	2	2	-1	3	0	3	28-Aug-25 A	02-Sep-25 A		1	3	2	
DSC-324	DSC-324 Leaking Services at T2.1 Hamlin, WS- 503,504	1	0	-1	1	0	1	29-Aug-25 A	29-Aug-25 A					
2-W-0626	Bact Results TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	3	3	0	3	0	3	03-Sep-25 A	05-Sep-25 A		1	2	2	
2-W-0519	Install Watermain (prior to temp main commissioning)	8	0	-8	4	4	8	03-Sep-25 A	12-Sep-25	6				
DSC-330	DSC-330 WM Stg 2 Unlocated Steel Pipe STA 27+86	1	0	-1	1	0	1	05-Sep-25 A	05-Sep-25 A					
DSC-331	DSC-331 Stage 2 WM 1IN Copper Line at 27+70	1	0	-1	1	0	1	05-Sep-25 A	05-Sep-25 A					
DSC-332	DSC-332 Stage 2 WM 2EA 2IN Steel Pipes near WS-604	1	0	-1	1	0	1	05-Sep-25 A	05-Sep-25 A					
DSC-338	DSC-338 Stage 2 WM Unknown Utility at STA 26+90	1	0	-1	1	0	1	08-Sep-25 A	08-Sep-25 A					
2-W-0646	SPU Customer Notification - Stg 2 Hamlin to Edgar (TM2.1 & TM2	5	5	0	1	4	5	08-Sep-25 A	12-Sep-25	6	1	2	2	
2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & H	1	3	2	0	1	1	15-Sep-25	15-Sep-25	6	1	2	4	
2-W-0656	SPU Install Temp Hydrant & Service Laterals (2 ea.) - Stg 2 Hamlir	1	1	0	0	1	1	16-Sep-25	16-Sep-25	6	1	4	4	
2-W-0499	Install Watermain, Hydrants & Blocking Sta. 21+64 to 33+19 - Stg :	11	12	1	0	11	11	17-Sep-25	01-Oct-25	6	1	5	6	
2-W-0550	Mainline Lateral @ Hamlin - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	02-Oct-25	02-Oct-25	6	1	-7	-7	
2-W-0500	Test & Flush Water Main - Stg 2 Hamlin to Edgar	2	2	0	0	2	2	03-Oct-25	06-Oct-25	6	1	5	5	
2-W-0560	Install Thrust Collar & Cure - Stg 2 Hamlin to Edgar	5	5	0	0	5	5	03-Oct-25	09-Oct-25	22	8	-7	-7	
2-W-0503	Excavate Services and Tie-Ins - Stg 2 Hamlin to Edgar	2	2	0	0	2	2	07-Oct-25	08-Oct-25	6	1	5	5	
2-W-0501	Bact Results - Stg 2 Hamlin to Edgar	3	3	0	0	3	3	07-Oct-25	09-Oct-25	13	8	5	5	
2-W-0502	SPU Customer Notification - Stg 2 Hamlin to Edgar (CC05 Main)	5	5	0	0	5	5	10-Oct-25	17-Oct-25	13	8	5	5	
2-W-0504	SPU Tie-In Watermain at CC05 - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	20-Oct-25	20-Oct-25	13	8	5	5	
2-W-0505	SPU Transfer Water Services - Stg 2 Hamlin to Edgar (12 ea.)	3	3	0	0	3	3	21-Oct-25	23-Oct-25	13	8	5	5	

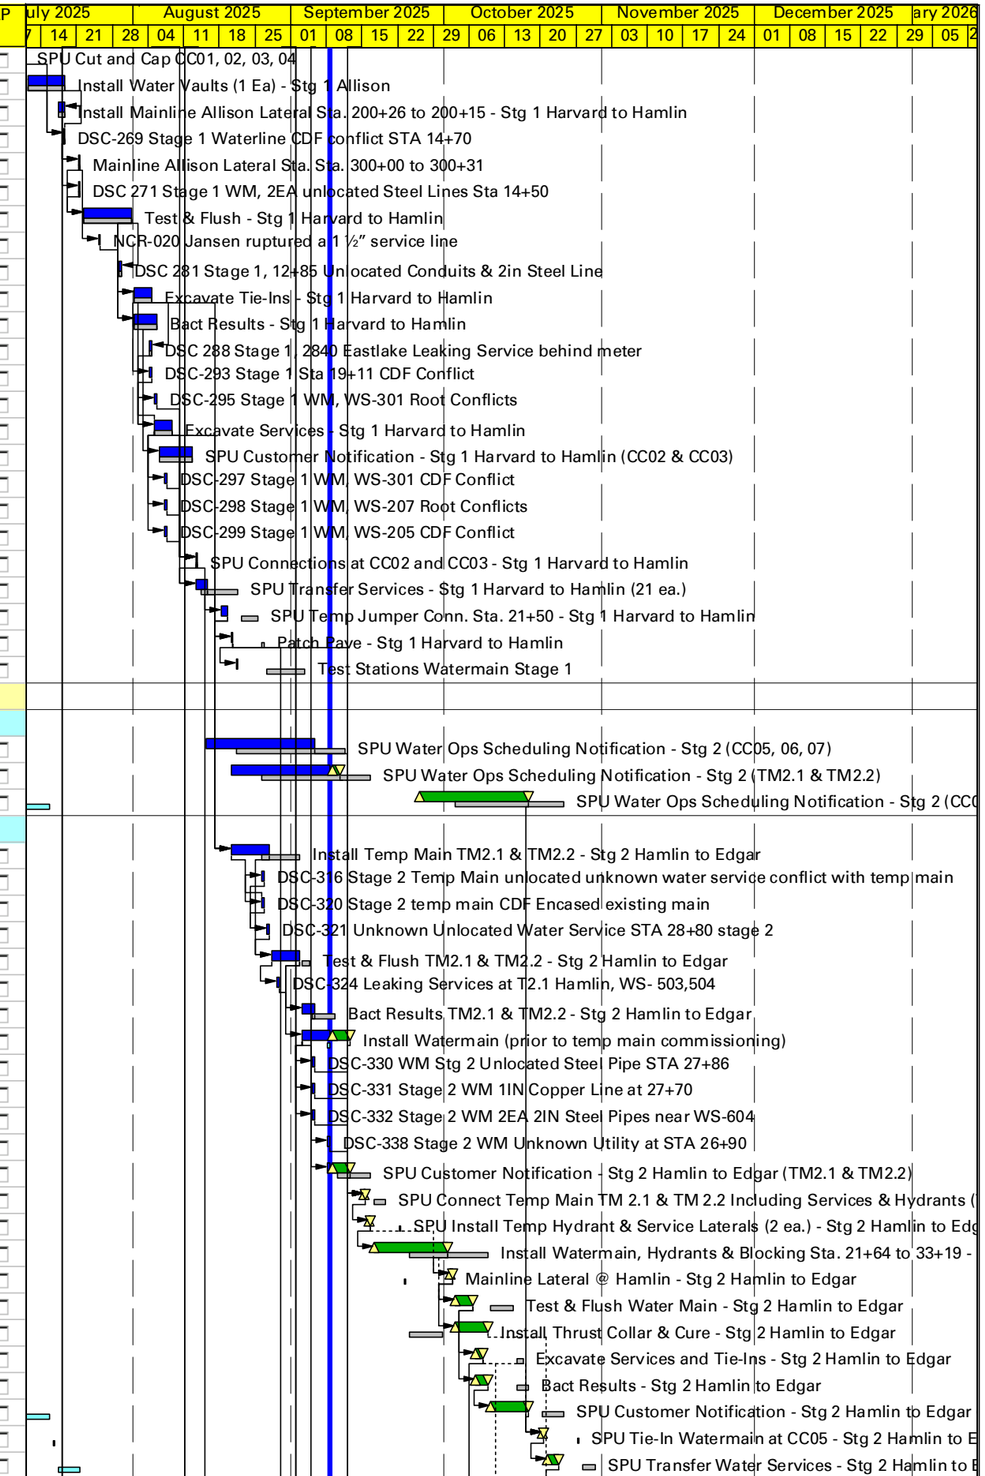

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-W-0506	SPU Tie-In Main From Stage 1 - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	24-Oct-25	24-Oct-25	13	8	5	5	
2-W-0557	SPU Jumper Conn. Sta. 33+19 - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	27-Oct-25	27-Oct-25	13	8	5	5	
2-W-0567	Remove Temp Mains - Stg 2 Hamlin to Edgar	5	5	0	0	5	5	28-Oct-25	03-Nov-25	13	8	5	5	
2-W-0507	Patch Pave - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	04-Nov-25	04-Nov-25	13	8	5	5	
2-W-0546	Test Stations Watermain Stage 2	5	5	0	0	5	5	05-Nov-25	12-Nov-25	94	89	5	5	
Stage 3 Eastlake Edgar to Louisa (33+19 to 44+50)														
SPU Ops Notifications														
2-W-0527	SPU Water Ops Scheduling Notification - Stg 3 (CC08, 09, 10)	15	15	0	0	15	15	06-Oct-25	27-Oct-25	17	12	5	5	
2-W-0531	SPU Water Ops Scheduling Notification - Stg 3 (CC07 Conn.)	15	15	0	0	15	15	12-Nov-25	04-Dec-25	6	1	5	5	
Waterline Installation														
2-W-0659	Excavate Temp Hydrants & Services - Stg 3 Edgar to Louisa	2	2	0	0	2	2	09-Oct-25	10-Oct-25	6	1	5	5	
2-W-0509	Excavate CC08, 09, 10 - Stg 3 Edgar to Louisa	1	1	0	0	1	1	14-Oct-25	14-Oct-25	21	16	5	5	
2-W-0669	SPU Install Temp Hydrant & Service Laterals - Stg 3 Edgar to Loui	2	2	0	0	2	2	14-Oct-25	15-Oct-25	6	1	5	5	
2-W-0512	Install Watermain & Hydrants From Sta. 33+33 to 44+50 - Stg 3 Ed	20	20	0	0	20	20	16-Oct-25	13-Nov-25	6	1	5	5	
2-W-0533	SPU Customer Notification - Stg 3 Edgar to Louisa (CC08, 09, 10)	5	5	0	0	5	5	21-Oct-25	27-Oct-25	17	12	5	5	
2-W-0511	SPU Cut/Cap CC08, 09, 10 - Stg 3 Edgar to Louisa	1	1	0	0	1	1	28-Oct-25	28-Oct-25	17	12	5	5	
2-W-0543	Lateral Main @ Roanoke Sta. 600+13 to 600+61 - Stg 3 Edgar to Lo	1	1	0	0	1	1	14-Nov-25	14-Nov-25	6	1	5	5	
2-W-0513	Test & Flush Main - Stg 3 Edgar to Louisa	2	2	0	0	2	2	17-Nov-25	18-Nov-25	6	1	5	5	
2-W-0514	Bact Results - Stg 3 Edgar to Louisa	3	3	0	0	3	3	19-Nov-25	21-Nov-25	6	1	5	5	
2-W-0515	SPU Customer Notification - Stg 3 Edgar to Louisa (CC07 Main)	5	5	0	0	5	5	24-Nov-25	02-Dec-25	6	1	5	5	
2-W-0516	Excavate Services and Connections - Stg 3 Edgar to Louisa	2	2	0	0	2	2	03-Dec-25	04-Dec-25	6	1	5	5	
2-W-0517	SPU Connect Main at CC09 & 2 Hydrants - Stg 3 Edgar to Louisa	2	2	0	0	2	2	05-Dec-25	08-Dec-25	6	1	5	5	
2-W-0518	SPU Transfer Services - Stg 3 Edgar to Louisa (30 ea.)	6	6	0	0	6	6	09-Dec-25	16-Dec-25	6	1	5	5	
2-W-0520	SPU Tie-In at Sta. 33+19 - Stg 3 Edgar to Louisa	1	1	0	0	1	1	17-Dec-25	17-Dec-25	6	1	5	5	
2-W-0521	SPU Install Temp Jumper Sta. 44+50 - Stg 3 Edgar to Louisa	1	1	0	0	1	1	18-Dec-25	18-Dec-25	6	1	5	5	
2-W-0523	Patch Pave - Stg 3 Edgar to Louisa	1	1	0	0	1	1	19-Dec-25	19-Dec-25	6	1	5	5	
2-W-0547	Test Stations Watermain Stage 3	5	5	0	0	5	5	22-Dec-25	29-Dec-25	67	62	5	5	
Conduit Crossings														
2-CC-0529	Allison - Conduit Crossings	4	4	0	0	4	4	15-Sep-25	18-Sep-25	45	57	-12	-12	
2-CC-0527	Louisa - Conduit Crossings	2	2	0	0	2	2	23-Oct-25	24-Oct-25	37	24	13	13	
2-CC-0528	Lynn - Conduit Crossings	6	6	0	0	6	6	27-Oct-25	03-Nov-25	41	28	13	13	
2-CC-0525	Hamlin - Conduit Crossings	7	7	0	0	7	7	05-Nov-25	14-Nov-25	13	8	5	5	
2-CC-0526	Roanoke - Conduit Crossings	4	4	0	0	4	4	22-Dec-25	26-Dec-25	6	1	5	5	
Roadway														
Shelby to Edgar East Side														
2-RW-0614	Complete SCL Pole Relocation 1 ea. (by SCL) - Shelby to Edgar	0	0	0	0	0	0		14-Nov-25	13	8	5	5	
2-RW-0534	Roadway Demo & Exc - Shelby to Edgar (E)	10	10	0	0	10	10	17-Nov-25	02-Dec-25	13	8	5	5	
2-RW-0584	Remove/Abandon Waterline & Appurtances - Shelby to Edgar (E)	10	10	0	0	10	10	17-Nov-25	02-Dec-25	22	17	5	5	
2-RW-0535	Pour Roadway - Shelby to Edgar (E)	6	6	0	0	6	6	03-Dec-25	10-Dec-25	22	17	5	5	
2-RW-0536	Curb - Shelby to Edgar (E)	2	2	0	0	2	2	11-Dec-25	12-Dec-25	22	17	5	5	
2-RW-0537	Patch Pave - Shelby to Edgar (E)	1	1	0	0	1	1	15-Dec-25	15-Dec-25	38	33	5	5	
Edgar to Louisa East Side														
2-RW-0539	Roadway Demo & Exc - Edgar to Louisa (E)	10	10	0	0	10	10	03-Dec-25	16-Dec-25	13	8	5	5	
2-RW-0589	Remove/Abandon Waterline & Appurtances - Edgar to Louisa (E)	10	10	0	0	10	10	03-Dec-25	16-Dec-25	20	15	5	5	
2-RW-0540	Pour Roadway - Edgar to Louisa (E)	6	6	0	0	6	6	17-Dec-25	24-Dec-25	20	15	5	5	
2-RW-0541	Curb - Edgar to Louisa (E)	2	2	0	0	2	2	26-Dec-25	29-Dec-25	29	24	5	5	
2-RW-0542	Patch Pave - Edgar to Louisa (E)	1	1	0	0	1	1	30-Dec-25	30-Dec-25	29	24	5	5	
Louisa to Lynn East Side														
2-RW-0544	Roadway Demo & Exc - Louisa to Lynn (E)	8	8	0	0	8	8	29-Dec-25	08-Jan-26	6	1	5	5	
2-RW-0594	Remove/Abandon Waterline & Appurtances - Louisa to Lynn (E)	8	8	0	0	8	8	29-Dec-25	08-Jan-26	11	6	5	5	
Harvard to Fuhrman West Side														
2-RW-0579	Roadway Demo & Exc - Harvard to Fuhrman (W)	9	9	0	9	0	9	07-Jul-25 A	17-Jul-25 A			0	0	
DSC-263	DSC-263 Fuhrman West Side Reinforced pavement	1	1	0	1	0	1	14-Jul-25 A	14-Jul-25 A			0	0	
DSC-273	DSC 273 Harvard & Eastlake Pole Foundation Removal	1	1	0	1	0	1	17-Jul-25 A	17-Jul-25 A			0	0	

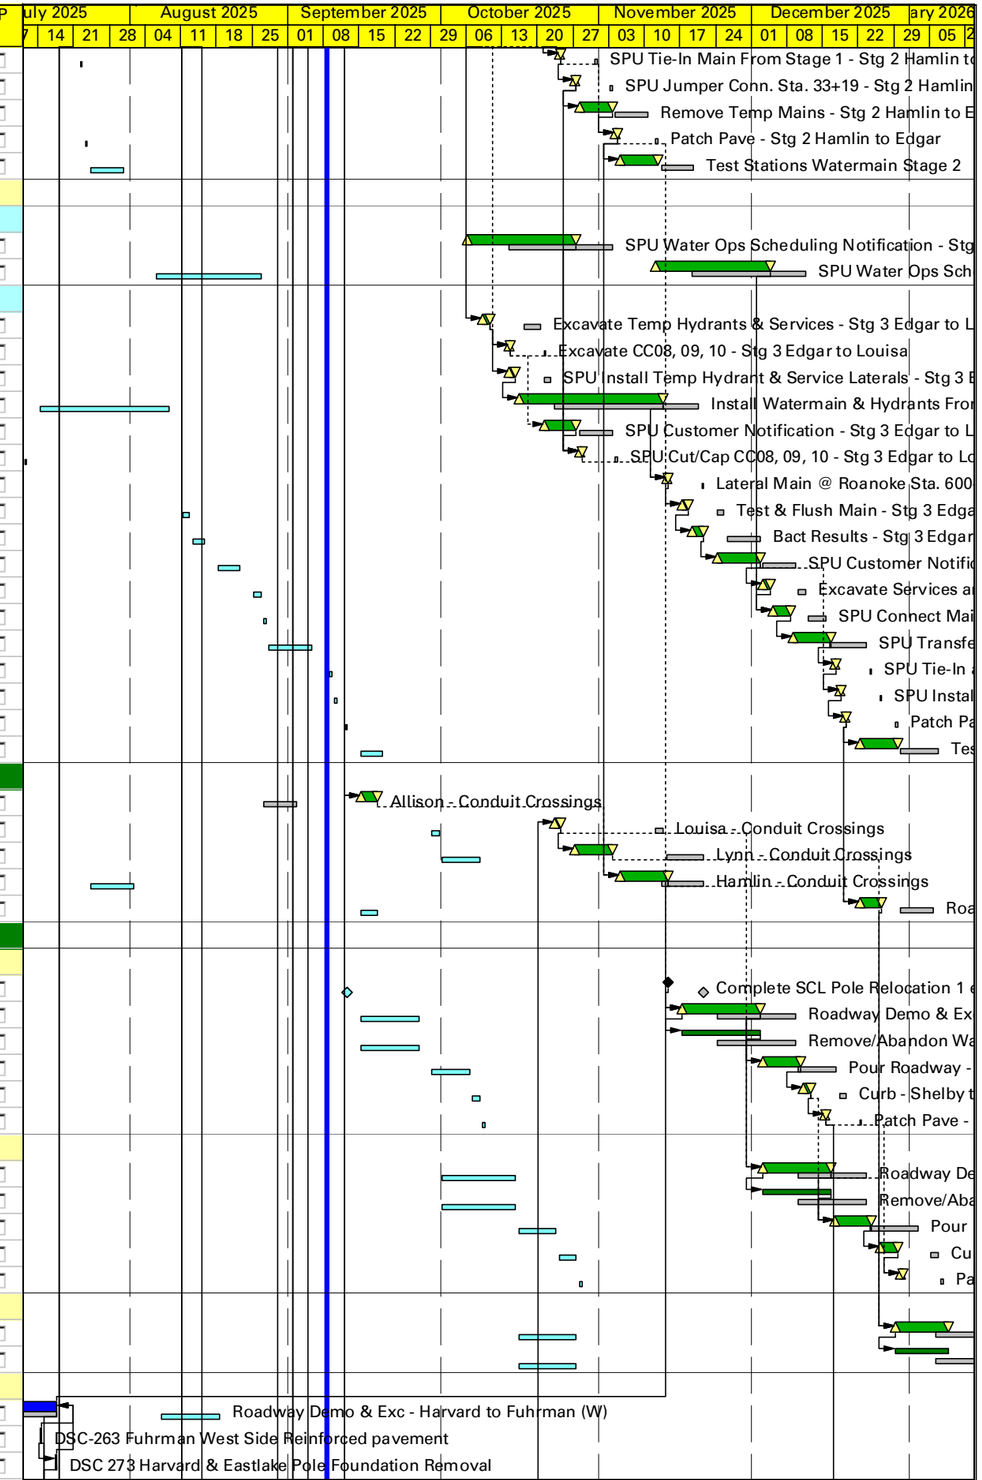

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-268	DSC-268 Fuhrman CDF conflict with Roadway	1	1	0	1	0	1	18-Jul-25 A	18-Jul-25 A			0	0	
2-RW-0580	Pour Roadway - Harvard to Fuhrman (W)	4	4	0	4	0	4	18-Jul-25 A	23-Jul-25 A			0	0	
2-RW-0581	Curb - Harvard to Fuhrman (W)	2	2	0	2	0	2	24-Jul-25 A	25-Jul-25 A			0	0	
DSC-279	DSC 279 Fuhrman-Harvard West Side RR Ties, Thick Conc	1	1	0	1	0	1	25-Jul-25 A	25-Jul-25 A			0	0	
DSC-280	DSC 280 Fuhrman-Harvard West Side Duct Bank Conflict with Roa	1	1	0	1	0	1	25-Jul-25 A	25-Jul-25 A			0	0	
2-RW-0582	Patch Pave - Harvard to Fuhrman (W)	1	1	0	1	0	1	28-Jul-25 A	28-Jul-25 A			0	0	
Harvard														
Phase-1														
2-RW-694	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.1	6	6	0	6	0	6	29-Jul-25 A	05-Aug-25 A		0	0	0	
2-RW-704	Pour Roadway - Harvard to Fuhrman (W) Ph.1	2	2	-2	4	0	4	06-Aug-25 A	11-Aug-25 A		0	0	-2	
2-RW-724	Patch Pave - Harvard to Fuhrman (W) Ph.1	1	1	-1	2	0	2	12-Aug-25 A	13-Aug-25 A		0	-1	-2	
2-RW-714	Curb - Harvard to Fuhrman (W) Ph.1	1	1	-1	2	0	2	14-Aug-25 A	15-Aug-25 A		0	-4	-5	
DSC-286	DSC 286 Harvard Monitoring Well Conflict	1	1	0	1	0	1	31-Jul-25 A	31-Jul-25 A			0	0	
DSC-292	DSC-292 SWC Fuhrman unknown unlocated duct bank	1	0	-1	1	0	1	04-Aug-25 A	04-Aug-25 A					
Phase-2														
2-RW-654	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.2	3	3	-7	10	0	10	18-Aug-25 A	29-Aug-25 A		0	-4	-11	
2-RW-664	Pour Roadway - Harvard to Fuhrman (W) Ph.2	2	2	-5	5	2	7	02-Sep-25 A	10-Sep-25	74	0	-11	-16	
2-RW-674	Curb - Harvard to Fuhrman (W) Ph.2	1	1	0	0	1	1	11-Sep-25	11-Sep-25	74	0	-16	-16	
2-RW-684	Patch Pave - Harvard to Fuhrman (W) Ph.2	1	1	0	0	1	1	12-Sep-25	12-Sep-25	74	0	-16	-16	
DSC-318	DSC-318 Harvard East side shallow DB in conflict with roadway	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
Phase-3														
2-RW-614	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.3	3	3	-7	10	0	10	18-Aug-25 A	29-Aug-25 A		0	3	-4	
2-RW-624	Pour Roadway - Harvard to Fuhrman (W) Ph.3	2	2	-5	5	2	7	02-Sep-25 A	10-Sep-25	45	0	-4	-9	
2-RW-634	Curb - Harvard to Fuhrman (W) Ph.3	1	1	0	0	1	1	11-Sep-25	11-Sep-25	45	0	-9	-9	
2-RW-644	Patch Pave - Harvard to Fuhrman (W) Ph.3	1	1	0	0	1	1	12-Sep-25	12-Sep-25	45	0	-9	-9	
Shelby to Harvard East Side														
2-RW-0564	Roadway Demo & Exc - Shelby to Harvard (E)	8	8	-5	5	8	13	02-Sep-25 A	18-Sep-25	74	79	0	-5	
2-RW-0604	Remove/Abandon Waterline & Appurtances - Shelby to Harvard (E)	8	8	-5	5	8	13	02-Sep-25 A	18-Sep-25	74	79	0	-5	
2-RW-0565	Pour Roadway - Shelby to Harvard (E)	4	4	0	0	4	4	19-Sep-25	24-Sep-25	74	79	-5	-5	
2-RW-0566	Curb - Shelby to Harvard (E)	2	2	0	0	2	2	25-Sep-25	26-Sep-25	74	79	-5	-5	
2-RW-0567	Patch Pave - Shelby to Harvard (E)	1	1	0	0	1	1	29-Sep-25	29-Sep-25	74	79	-5	-5	
Shelby to Harvard West Side														
2-SW-0794	Complete SCL Pole Relocation 3 ea. (by SCL) - Harvard SWC	0	0	0	0	0	0		29-Sep-25	74	79	-5	-5	
2-RW-0574	Roadway Demo & Exc - Shelby to Harvard (W)	10	10	0	0	10	10	30-Sep-25	14-Oct-25	74	79	-5	-5	
2-RW-0575	Pour Roadway - Shelby to Harvard (W)	5	5	0	0	5	5	15-Oct-25	21-Oct-25	74	79	-5	-5	
2-RW-0576	Curb - Shelby to Harvard (W)	2	2	0	0	2	2	22-Oct-25	23-Oct-25	74	79	-5	-5	
2-RW-0577	Patch Pave - Shelby to Harvard (W)	1	1	0	0	1	1	24-Oct-25	24-Oct-25	74	79	-5	-5	
Weekend Roadway Work														
Fuhrman West Side														
DSC-284	DSC 284 NWC Fuhrman Reinforced Concrete Slab in SW	1	1	0	1	0	1	30-Jul-25 A	30-Jul-25 A			0	0	
DSC-285	DSC 285 NWC Fuhrman Abandoned Brick CB Structure	1	1	0	1	0	1	30-Jul-25 A	30-Jul-25 A			0	0	
DSC-290	DSC 290 Fuhrman Intersection W, thick concrete and Ties	1	1	0	1	0	1	01-Aug-25 A	01-Aug-25 A			0	0	
DSC-291	DSC 291 Fuhrman Intersection W, 2-in Steel line conflict	1	1	0	1	0	1	01-Aug-25 A	01-Aug-25 A			0	0	
2-WE-806	Remove Roadway Type 2 - Fuhrman West Side	1	1	0	1	0	1	02-Aug-25 A	02-Aug-25 A			0	0	
2-WE-816	Pour Roadway - Fuhrman West Side	1	1	0	1	0	1	03-Aug-25 A	03-Aug-25 A			0	0	
Fuhrman NEC														
2-WE-826	Remove Roadway Type 2 - Fuhrman NEC	1	1	0	0	1	1	04-Oct-25	04-Oct-25	38	54	-16	-16	
2-WE-836	Pour Roadway - Fuhrman NEC	1	1	0	0	1	1	05-Oct-25	05-Oct-25	38	54	-16	-16	
Fuhrman SEC														
2-WE-846	Remove Roadway Type 2 - Fuhrman SEC	1	1	0	0	1	1	11-Oct-25	11-Oct-25	38	54	-16	-16	
2-WE-856	Pour Roadway - Fuhrman SEC	1	1	0	0	1	1	12-Oct-25	12-Oct-25	38	54	-16	-16	
Hamlin Phase 1														
2-WE-0585	Remove Roadway Type 2 - Hamlin Ph.1 (WE)	1	1	0	0	1	1	20-Dec-25	20-Dec-25	20	18	2	2	
2-WE-0586	Pour Roadway - Hamlin Ph.1 (WE)	1	1	0	0	1	1	21-Dec-25	21-Dec-25	20	18	2	2	

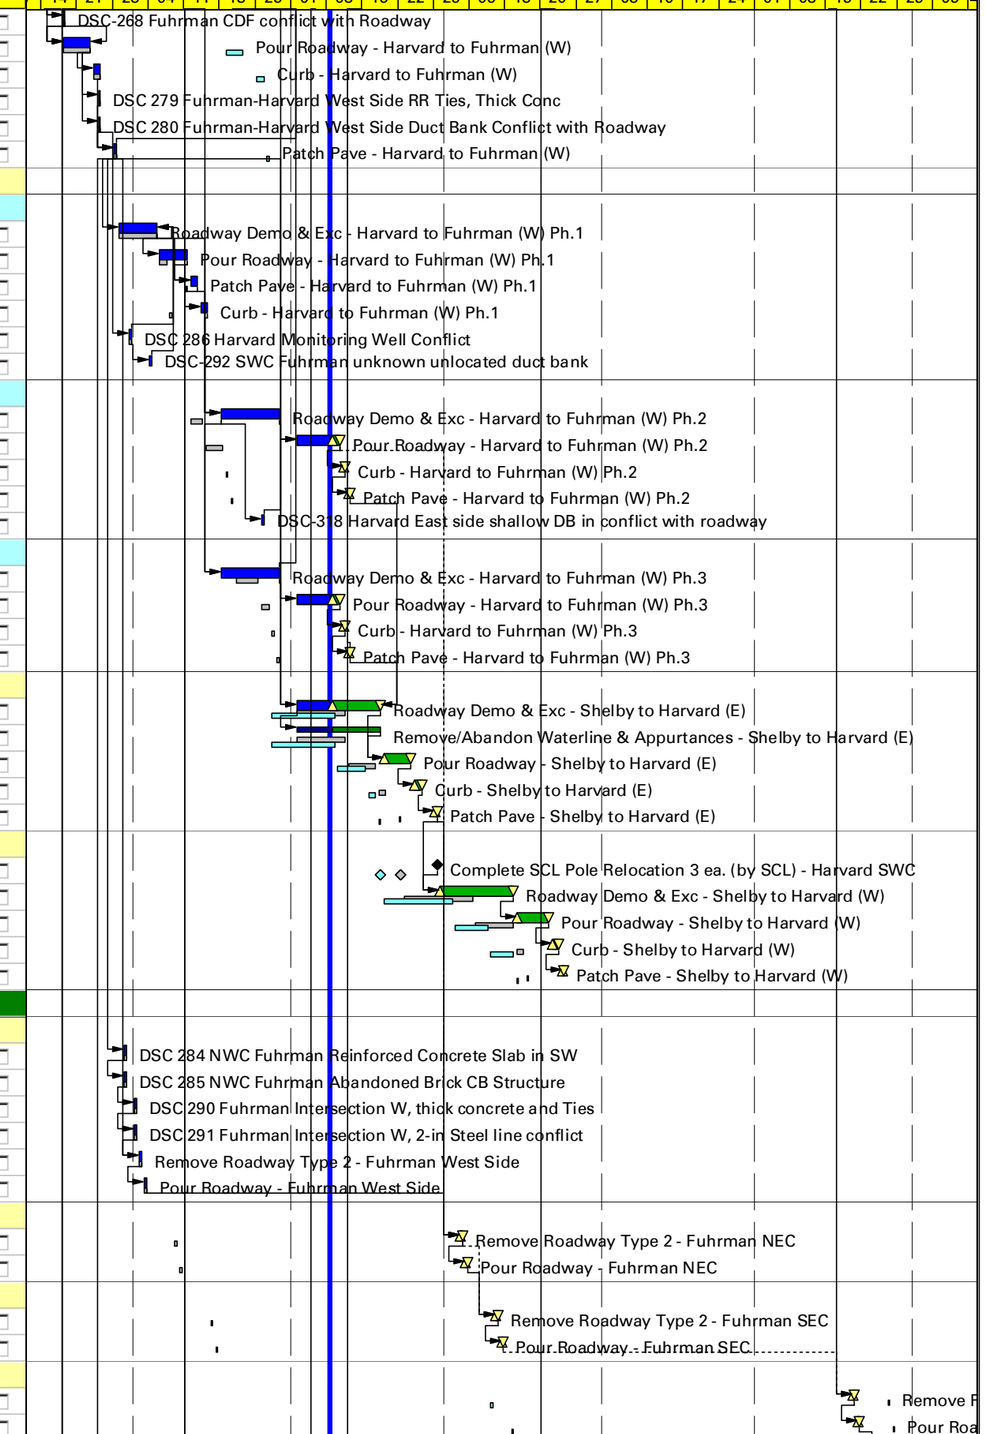

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Hamilin Phase 2														
2-WE-0588	Remove Roadway Type 2 - Hamlin Ph.2 (WE)	1	1	0	0	1	1	27-Dec-25	27-Dec-25	20	18	2	2	
2-WE-0589	Pour Roadway - Hamlin Ph.2 (WE)	1	1	0	0	1	1	28-Dec-25	28-Dec-25	20	18	2	2	
Hamlin Phase 3														
2-WE-0591	Remove Roadway Type 2 - Hamlin Ph.3 (WE)	1	1	0	0	1	1	03-Jan-26	03-Jan-26	20	18	2	2	
2-WE-0592	Pour Roadway - Hamlin Ph.3 (WE)	1	1	0	0	1	1	04-Jan-26	04-Jan-26	20	18	2	2	
Sidewalks														
Fuhrman NWC														
2-SW-0744	Remove Sidewalk - Fuhrman NWC	1	1	0	1	0	1	28-Jul-25 A	28-Jul-25 A		39	196	196	
2-SW-0745	Trench Electrical - Fuhrman NWC	1	1	0	1	0	1	29-Jul-25 A	29-Jul-25 A		39	196	196	
2-SW-0746	Electrical - Fuhrman NWC	2	2	-29	28	3	31	30-Jul-25 A	11-Sep-25	173	39	196	167	
DSC-308	DSC-308 NWC Fuhrman, Shallow Fiber Conduit Conflict	11	0	-19	16	3	19	15-Aug-25 A	11-Sep-25	173				
2-SW-0747	Grade Sidewalks - Fuhrman NWC	1	1	0	0	1	1	12-Sep-25	12-Sep-25	173	39	167	167	
2-SW-0748	Pour Sidewalks/Curb Ramps - Fuhrman NWC	3	3	0	0	3	3	15-Sep-25	17-Sep-25	173	103	167	167	
Fuhrman SWC														
2-SW-0738	Remove Sidewalk - Fuhrman SWC	2	2	-1	3	0	3	04-Aug-25 A	06-Aug-25 A		14	179	178	
2-SW-0739	Trench Electrical - Fuhrman SWC	1	1	-1	2	0	2	07-Aug-25 A	08-Aug-25 A		14	178	177	
2-SW-0740	Electrical - Fuhrman SWC	3	3	1	2	0	2	11-Aug-25 A	12-Aug-25 A		14	177	178	
DSC-304	DSC-304 Fuhrman SWC, conduits in conflict with handhole	1	0	-1	1	0	1	12-Aug-25 A	12-Aug-25 A					
DSC-305	DSC-305 Fuhrman SWC wooden pole utilities	1	0	-1	1	0	1	12-Aug-25 A	12-Aug-25 A					
DSC-306	DSC-306 Fuhrman SWC PPB in middle of ramp	1	0	-1	1	0	1	12-Aug-25 A	12-Aug-25 A					
2-SW-0741	Grade Sidewalks - Fuhrman SWC	2	2	0	2	0	2	13-Aug-25 A	14-Aug-25 A		14	178	178	
2-SW-0742	Pour Sidewalks/Curb Ramps - Fuhrman SWC	3	4	1	0	3	3	15-Sep-25	17-Sep-25	173	14	158	159	
Zone 3 - Lynn to Galer														
Water Main														
Stage 4 Galer to South of Blaine (65+21 to 75+63)														
Waterline Installation														
3-W-1077	Test Stations Watermain Stage 4	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	
Stage 5 South of Blaine to Boston (55+00 to 65+21)														
SPU Ops Notifications														
3-W-1067	SPU Water Ops Scheduling Notification - Stg 5 (CC15)	15	15	0	15	0	15	16-Jul-25 A	05-Aug-25 A		22	0	0	
3-W-1066	SPU Water Ops Scheduling Notification - Stg 5 (Conn.)	12	12	0	12	0	12	23-Jul-25 A	07-Aug-25 A		22	0	0	
3-W-1063	SPU Water Ops Scheduling Notification - Stg 5 (Jumper)	11	11	0	11	0	11	25-Jul-25 A	08-Aug-25 A		22	0	0	
Waterline Installation														
DSC-261	DSC-261 Stage 5 Unknown Steel Pipe 60+39 (1914 Eastlake)	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	
3-W-1036	Install Mainline, Hydrants & Blocking Sta. 65+07 to 55+00 - Stg 5 E	9	9	0	9	0	9	10-Jul-25 A	22-Jul-25 A			0	0	
DSC-264	DSC-264 Stage 5 unknown steel pipe STA 58+29	1	1	0	1	0	1	16-Jul-25 A	16-Jul-25 A			0	0	
DSC-265	DSC-265 Stage 5 CDF Conflict	1	1	0	1	0	1	16-Jul-25 A	16-Jul-25 A			0	0	
NCR-019	NCR-019 12X4 tees that were installed were the incorrect size per	1	0	-1	1	0	1	17-Jul-25 A	17-Jul-25 A					
DSC-272	DSC 272 Stage 5 unknown unlocated steel line	1	1	0	1	0	1	21-Jul-25 A	21-Jul-25 A			0	0	
DSC-274	DSC 274 Unknown unlocated water service 55+85	1	1	0	1	0	1	22-Jul-25 A	22-Jul-25 A			0	0	
3-W-1039	Test & Flush - Stg 5 Blaine to Boston	2	2	0	2	0	2	23-Jul-25 A	24-Jul-25 A			0	0	
3-W-1040	Bact Results - Stg 5 Blaine to Boston (Main)	2	2	0	2	0	2	25-Jul-25 A	28-Jul-25 A			0	0	
3-W-1042	Excavate Tie-Ins and Services - Stg 5 Blaine to Boston	6	6	0	6	0	6	25-Jul-25 A	01-Aug-25 A			0	0	
3-W-1041	SPU Customer Notification - Stg 5 Blaine to Boston	5	5	0	5	0	5	29-Jul-25 A	04-Aug-25 A			0	0	
DSC-294	DSC-294 Stage 5 WM, WS-1211 & WS-1210 Sizes	1	0	-1	1	0	1	05-Aug-25 A	05-Aug-25 A					
3-W-1037	Install Mainline Lateral @ Newton Sta. 700+63 to 700+13 - Stg 5 B	1	1	0	1	0	1	06-Aug-25 A	06-Aug-25 A		23	0	0	
3-W-1043	SPU Connect CC15 - Stg 5 Blaine to Boston	1	1	0	1	0	1	06-Aug-25 A	06-Aug-25 A		22	0	0	
3-W-1044	SPU Transfer Services In Stage 5 - Stg 5 Blaine to Boston	1	1	0	1	0	1	07-Aug-25 A	07-Aug-25 A		22	0	0	
3-W-1083	Install Thrust Collar Sta. 700+02 - Stg 5 Blaine to Boston	2	2	0	2	0	2	07-Aug-25 A	08-Aug-25 A		23	0	0	
3-W-1047	SPU Temp Jumper Conn. @ Sta. 65+00 - Stg 5 Blaine to Boston	1	1	0	1	0	1	08-Aug-25 A	08-Aug-25 A		22	0	0	
DSC-300	DSC-300 Stage 5 Unknown unmarked water service	7	0	-8	8	0	8	08-Aug-25 A	19-Aug-25 A					
3-W-1097	Remove Temp Jumper Sta. 65+21 - Stg 5 Blaine to Boston	1	1	0	1	0	1	11-Aug-25 A	11-Aug-25 A		22	0	0	
3-W-1048	Patch Pave - Stg 5 Blaine to Boston	2	2	0	2	0	2	12-Aug-25 A	13-Aug-25 A		22	0	0	

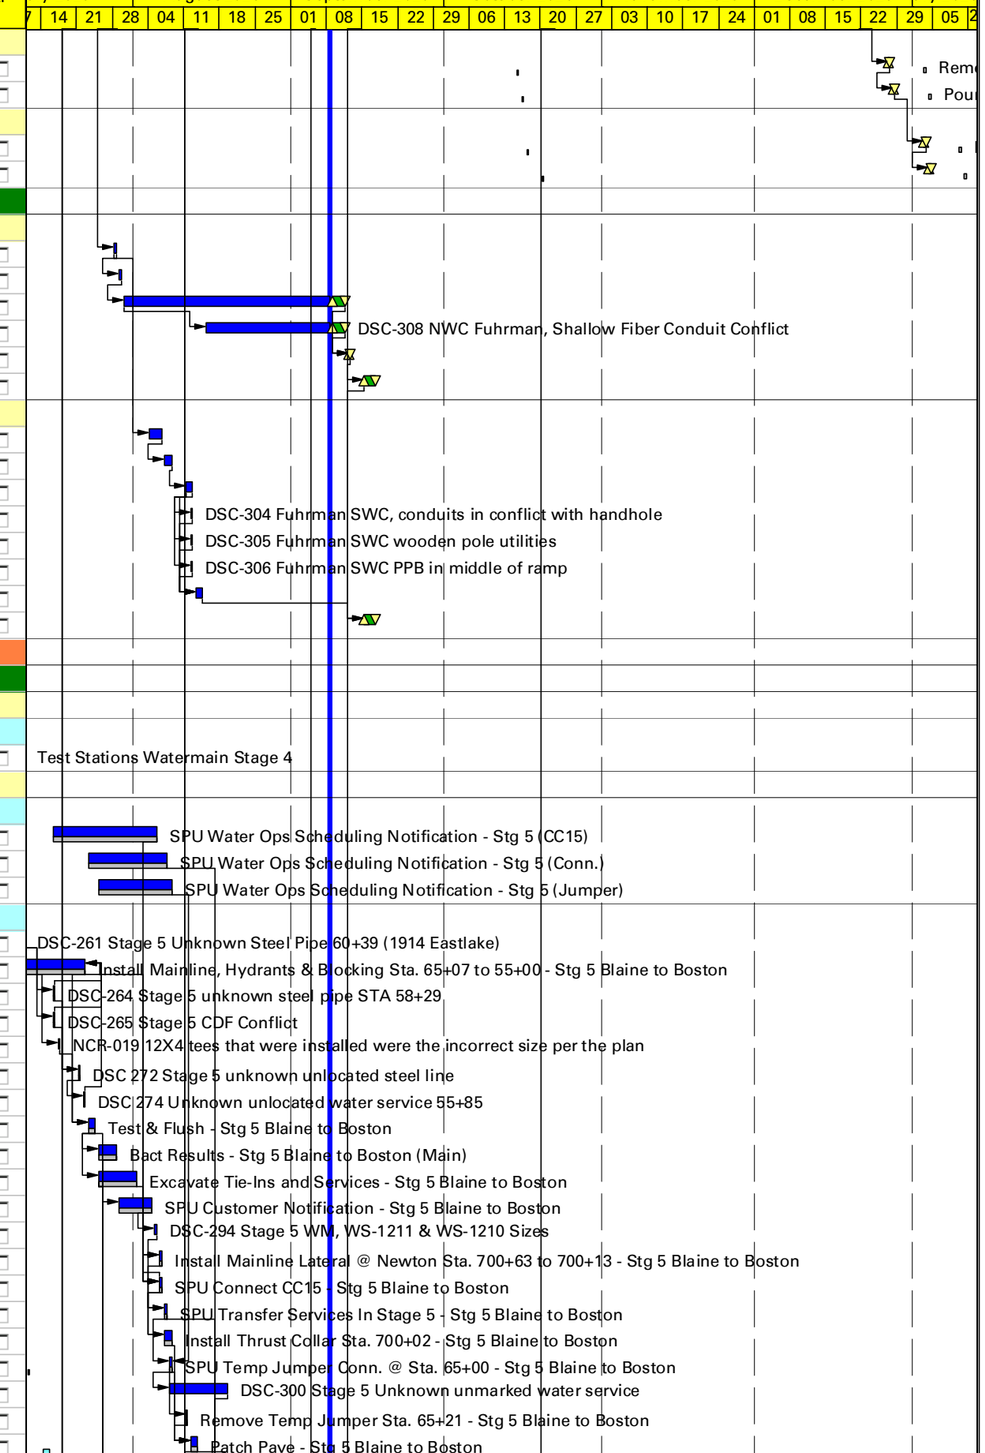

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-W-1076	Test Stations Watermain Stage 5	5	5	4	1	0	1	14-Aug-25 A	14-Aug-25 A		156	0	4	
3-W-1046	SPU Connection Sta. 65+21 Yale Pl. - Stg 5 Blaine to Boston	1	1	0	1	0	1	20-Aug-25 A	20-Aug-25 A		22	-8	-8	
Stage 6 Boston to Louisa (44+50 to 55+00)														
SPU Ops Notifications														
3-W-1080	SPU Water Ops Scheduling Notification - Stg 6 (Temp Services)	15	15	0	15	0	15	01-Aug-25 A	21-Aug-25 A		13	0	0	
3-W-1068	SPU Water Ops Scheduling Notification - Stg 6 (Conn.)	15	15	0	0	15	15	15-Sep-25	03-Oct-25	26	13	13	13	
3-W-1071	SPU Water Ops Scheduling Notification - Stg 6 (Conn.)	15	15	0	0	15	15	24-Sep-25	15-Oct-25	26	13	13	13	
Waterline Installation														
DSC-282	DSC 282 Stage 6, New 6in Fire Service Not in Plans	1	1	0	1	0	1	29-Jul-25 A	29-Jul-25 A			0	0	
DSC-283	DSC 283 Stage 6, WS-1302 leaking repair sleeve	1	1	0	1	0	1	29-Jul-25 A	29-Jul-25 A			0	0	
3-W-1100	Install TM 6.1 - Stg 6 Boston to Louisa	3	3	0	3	0	3	29-Jul-25 A	31-Jul-25 A			0	0	
DSC-287	DSC 287 Stage 6, 2EA Steel line conflict STA 49+75	1	1	0	1	0	1	31-Jul-25 A	31-Jul-25 A			0	0	
3-W-1110	Test & Flush TM 6.1 - Stg 6 Boston to Louisa	3	3	2	1	0	1	01-Aug-25 A	01-Aug-25 A		13	0	2	
DSC-289	DSC 289 Stage 6, WS-1010 Pinched EX Shallow Service	1	1	0	1	0	1	01-Aug-25 A	01-Aug-25 A			0	0	
3-W-1120	Bact Results TM 6.1 - Stg 6 Boston to Louisa	3	3	0	3	0	3	06-Aug-25 A	08-Aug-25 A		13	0	0	
3-W-1130	SPU Customer Notification TM 6.1 - Stg 6 Boston to Louisa	5	5	0	5	0	5	11-Aug-25 A	15-Aug-25 A		13	0	0	
3-W-1140	SPU Connect TM 6.1 - Stg 6 Boston to Louisa	1	1	0	1	0	1	18-Aug-25 A	18-Aug-25 A		13	0	0	
3-W-1050	Transfer Services to TM 6.1 (7 ea.) - Stg 6 Boston to Louisa	3	3	2	1	0	1	19-Aug-25 A	19-Aug-25 A		13	0	2	
3-W-1051	SPU Temp Service Laterals (5 ea.) - Stg 6 Boston to Louisa	2	2	1	1	0	1	20-Aug-25 A	20-Aug-25 A		13	2	3	
3-W-1081	SPU Temp Hydrant Laterals (2 ea.) - Stg 6 Boston to Louisa	1	1	0	1	0	1	21-Aug-25 A	21-Aug-25 A		13	3	3	
3-W-1052	Install Mainline & Hydrants Sta. 44+64 to 50+00 - Stg 6 Boston to	15	15	6	9	0	9	22-Aug-25 A	04-Sep-25 A		13	3	9	
DSC-322	DSC-322 Stage 6 miss-marked water services	1	0	-1	1	0	1	27-Aug-25 A	27-Aug-25 A					
DSC-326	DSC-326 Stage 6 existing storm in conflict with watermain at Bost	1	0	-1	1	0	1	03-Sep-25 A	03-Sep-25 A					
3-W-1053	Install Mainline & Hydrants Sta. 50+00 to 54+86 - Stg 6 Boston to	11	15	4	2	9	11	05-Sep-25 A	19-Sep-25	26	13	9	13	
DSC-337	DSC-337 Stage 6 WM, Power Conflict at 50+79	1	0	-1	1	0	1	08-Sep-25 A	08-Sep-25 A					
3-W-1054	Test & Flush - Stg 6 Boston to Louisa	2	2	0	0	2	2	22-Sep-25	23-Sep-25	26	13	13	13	
3-W-1055	Bact Results - Stg 6 Boston to Louisa	3	3	0	0	3	3	24-Sep-25	26-Sep-25	26	13	13	13	
3-W-1057	Excavate Connections and Services - Stg 6 Boston to Louisa	3	3	0	0	3	3	24-Sep-25	26-Sep-25	31	18	13	13	
3-W-1056	SPU Customer Notification - Stg 6 Boston to Louisa	5	5	0	0	5	5	29-Sep-25	03-Oct-25	26	13	13	13	
3-W-1058	Connection at Sta. 55+00 - Stg 6 Boston to Louisa	1	1	0	0	1	1	06-Oct-25	06-Oct-25	26	13	13	13	
3-W-1059	SPU Transfer Services - Stg 6 Boston to Louisa (22 ea.)	6	6	0	0	6	6	07-Oct-25	15-Oct-25	26	13	13	13	
3-W-1060	SPU Connection at Sta. 44+00 - Stg 6 Boston to Louisa	1	1	0	0	1	1	16-Oct-25	16-Oct-25	26	13	13	13	
3-W-1061	Remove Temp Main - Stg 6 Boston to Louisa	2	2	0	0	2	2	17-Oct-25	20-Oct-25	26	13	13	13	
3-W-1062	Patch Pave - Stg 6 Boston to Louisa	2	2	0	0	2	2	21-Oct-25	22-Oct-25	26	13	13	13	
3-W-1090	Test Stations Watermain Stage 6	5	5	0	0	5	5	23-Oct-25	29-Oct-25	142	129	13	13	
Conduit Crossings														
3-CC-1064	Galer - Conduit Crossings	13	13	0	13	0	13	26-Jun-25 A	15-Jul-25 A			0	0	
3-CC-1065	Garfield - Conduit Crossings	10	10	0	10	0	10	07-Jul-25 A	18-Jul-25 A			0	0	
3-CC-1066	Lynn - Conduit Crossings	5	5	0	0	5	5	23-Oct-25	29-Oct-25	26	13	13	13	
Roadway														
Galer to Garfield East Side														
3-RW-1139	Complete SCL Pole Relocation 1 ea. (by SCL) - Galer to Garfield	0	0	0	0	0	0		18-Jul-25 A			0	0	
3-RW-1069	Roadway Demo & Exc - Galer to Garfield (E)	7	7	0	7	0	7	21-Jul-25 A	29-Jul-25 A			0	0	
3-RW-1109	Remove/Abandon Waterline & Appurtances - Galer to Garfield (E)	7	7	0	7	0	7	21-Jul-25 A	29-Jul-25 A			0	0	
DSC-276	DSC 276 Galer-Garfield Demolition, Red CDF Conflict	1	1	0	1	0	1	23-Jul-25 A	23-Jul-25 A			0	0	
DSC-277	DSC 277 Galer-Garfield Irrigation line cast in existing roadway	1	1	0	1	0	1	24-Jul-25 A	24-Jul-25 A			0	0	
DSC-278	DSC 278 Galer Eastside Gasline in conflict with the roadway	1	1	0	1	0	1	24-Jul-25 A	24-Jul-25 A			0	0	
3-RW-1070	Pour Roadway - Galer to Garfield (E)	10	10	-1	11	0	11	04-Aug-25 A	18-Aug-25 A		-5	0	-1	
NCR-023	NCR-023 Electrical loop not installed	1	0	-1	1	0	1	07-Aug-25 A	07-Aug-25 A					
3-RW-1071	Curb - Galer to Garfield (E)	2	2	1	1	0	1	27-Aug-25 A	27-Aug-25 A		-5	-7	-6	
3-RW-1072	Patch Pave - Galer to Garfield (E)	1	1	0	1	0	1	27-Aug-25 A	27-Aug-25 A		-5	-5	-5	
Garfield to Howe East Side														
3-RW-1114	Remove/Abandon Waterline & Appurtances - Garfield to Howe (E)	10	10	-4	14	0	14	14-Aug-25 A	04-Sep-25 A		-5	5	1	
3-RW-1074	Roadway Demo & Exc - Garfield to Howe (E)	10	10	-7	17	0	17	14-Aug-25 A	08-Sep-25 A		-5	5	-2	

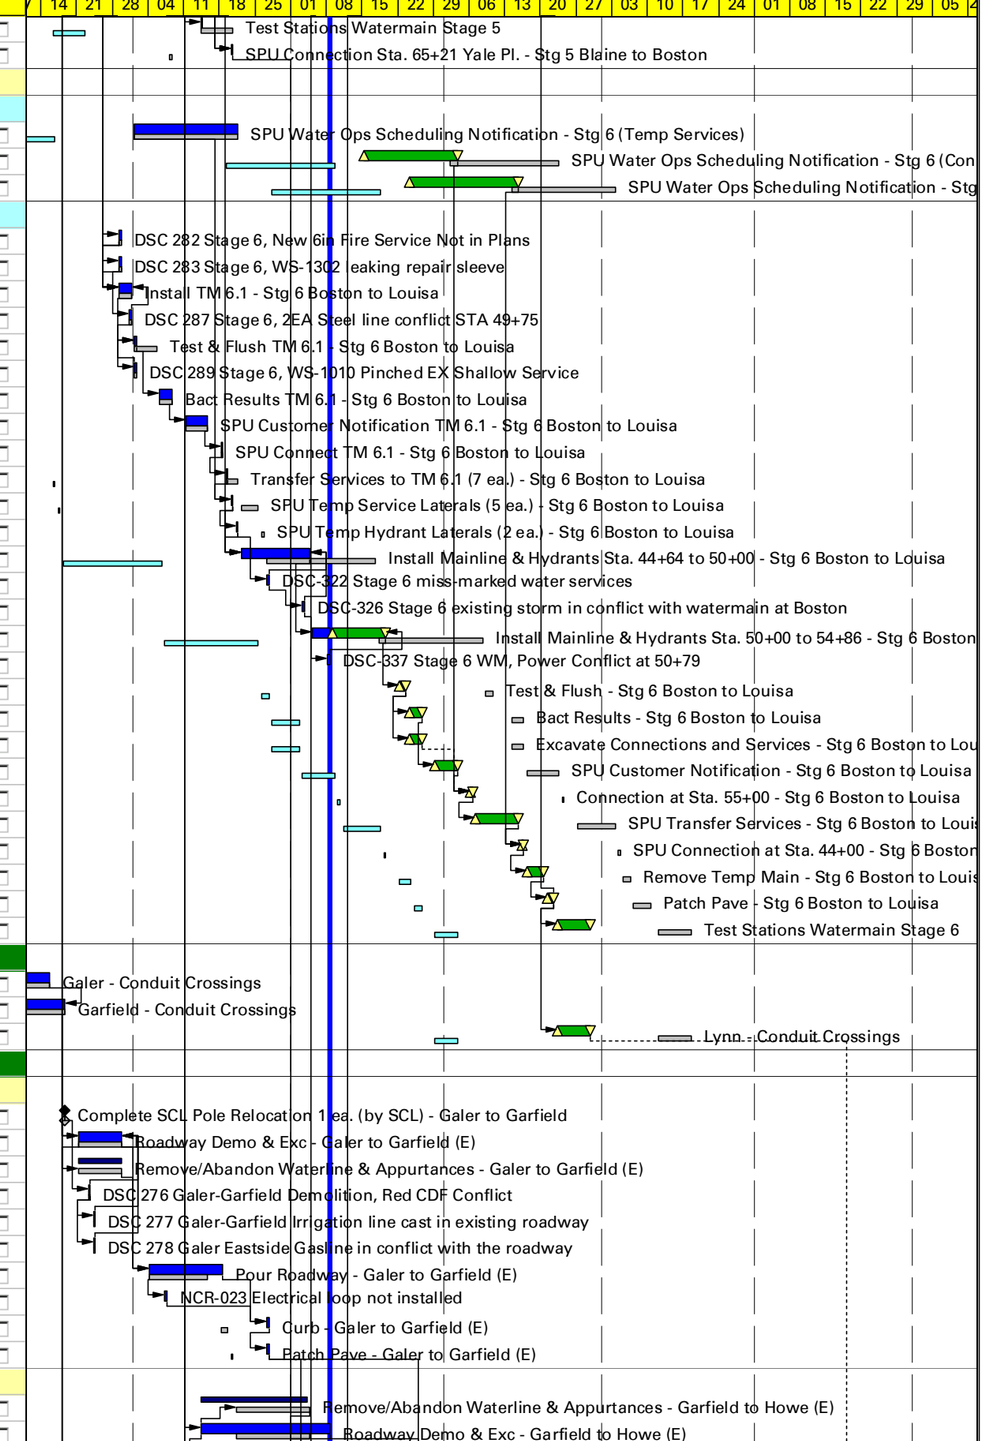

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work | BL1 LOE | Milestone | BL2 LOE | Previous MS | Actual Level of Effort | Previous Bar | Actual Work | Baseline MS | Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-307	DSC-307 Garfield WQ-B117 Unknown Unlocated Conduit	1	0	-1	1	0	1	15-Aug-25 A	15-Aug-25 A					
DSC-309	DSC-309 Garfield East Side WQV B117 Conflict with Gas line	1	0	-17	15	2	17	18-Aug-25 A	10-Sep-25	-8				
DSC-317	DSC-317 Howe East side pavement thickness 18"	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
DSC-319	DSC-319 Garfield WQV B117 to CB B34 will not work per plan	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
3-RW-1075	Pour Roadway - Garfield to Howe (E)	5	5	-4	3	6	9	04-Sep-25 A	16-Sep-25	-8	-5	1	-3	
DSC-340	DSC-340 NEC Garfield Ex. MH Elevation Conflict	1	0	-1	1	0	1	08-Sep-25 A	08-Sep-25 A					
3-RW-1076	Curb - Garfield to Howe (E)	2	2	0	0	2	2	17-Sep-25	18-Sep-25	-5	0	-3	-3	
RFI-069	Install WQ B117 and B113 after RFI-059	8	8	0	0	8	8	17-Sep-25	26-Sep-25	-8	-5	-3	-3	
3-RW-1116	Mid-Block Sidewalk Galer to Howe	2	0	-2	0	2	2	19-Sep-25	22-Sep-25	-5				
3-RW-1077	Patch Pave - Garfield to Howe (E)	1	1	0	0	1	1	23-Sep-25	23-Sep-25	-5	0	-5	-5	
Galer to Garfield West Side														
3-RW-1079	Roadway Demo & Exc - Galer to Garfield (W)	10	10	0	0	10	10	29-Sep-25	10-Oct-25	-8	-5	-3	-3	
3-RW-1080	Pour Roadway - Galer to Garfield (W)	6	6	0	0	6	6	14-Oct-25	21-Oct-25	9	12	-3	-3	
3-RW-1081	Curb - Galer to Garfield (W)	2	2	0	0	2	2	22-Oct-25	23-Oct-25	9	12	-3	-3	
3-RW-1082	Patch Pave - Galer to Garfield (W)	1	1	0	0	1	1	24-Oct-25	24-Oct-25	9	12	-3	-3	
Garfield to Howe West Side														
3-RW-1084	Roadway Demo & Exc - Garfield to Howe (W)	10	10	0	0	10	10	14-Oct-25	27-Oct-25	-8	-5	-3	-3	
3-RW-1085	Pour Roadway - Garfield to Howe (W)	5	5	0	0	5	5	28-Oct-25	03-Nov-25	1	4	-3	-3	
3-RW-1086	Curb - Garfield to Howe (W)	2	2	0	0	2	2	04-Nov-25	05-Nov-25	1	4	-3	-3	
3-RW-1087	Patch Pave - Garfield to Howe (W)	1	1	0	0	1	1	06-Nov-25	06-Nov-25	1	4	-3	-3	
Howe to Boston East Side														
3-RW-1089	Roadway Demo & Exc - Howe to Boston (E)	10	10	0	0	10	10	28-Oct-25	10-Nov-25	-8	-5	-3	-3	
3-RW-1119	Remove/Abandon Waterline & Appurtances - Howe to Boston (E)	10	10	0	0	10	10	28-Oct-25	10-Nov-25	-8	-5	-3	-3	
3-RW-1090	Pour Roadway - Howe to Boston (E)	5	5	0	0	5	5	12-Nov-25	18-Nov-25	-8	-5	-3	-3	
3-RW-1091	Curb - Howe to Boston (E)	2	2	0	0	2	2	19-Nov-25	20-Nov-25	-8	-5	-3	-3	
3-RW-1092	Patch Pave - Howe to Boston (E)	1	1	0	0	1	1	21-Nov-25	21-Nov-25	-8	-5	-3	-3	
Howe to Boston West Side														
3-RW-1094	Roadway Demo & Exc - Howe to Boston (W)	5	5	0	0	5	5	24-Nov-25	02-Dec-25	-8	-5	-3	-3	
3-RW-1095	Pour Roadway - Howe to Boston (W)	10	10	0	0	10	10	03-Dec-25	16-Dec-25	-8	-5	-3	-3	
3-RW-1096	Curb - Howe to Boston (W)	2	2	0	0	2	2	17-Dec-25	18-Dec-25	-8	-5	-3	-3	
3-RW-1097	Patch Pave - Howe to Boston (W)	1	1	0	0	1	1	19-Dec-25	19-Dec-25	-8	-5	-3	-3	
Boston to Lynn East Side														
3-RW-1099	Roadway Demo & Exc - Boston to Lynn (E)	8	8	0	0	8	8	22-Dec-25	02-Jan-26	-8	-5	-3	-3	
3-RW-1129	Remove/Abandon Waterline & Appurtances -Boston to Lynn (E)	8	8	0	0	8	8	22-Dec-25	02-Jan-26	-8	-5	-3	-3	
3-RW-1100	Pour Roadway - Boston to Lynn (E)	3	3	0	0	3	3	05-Jan-26	07-Jan-26	-8	-5	-3	-3	
Weekend Roadway Work														
Galer East Side Phase 1														
3-WE-1110	Remove Roadway Type 2 - Galer (E) Ph.1	1	1	0	1	0	1	06-Sep-25 A	06-Sep-25 A		26	14	14	
3-WE-1111	Pour Roadway - Galer (E) Ph.1	1	1	0	1	0	1	07-Sep-25 A	07-Sep-25 A		26	14	14	
Galer East Side Phase 2														
3-WE-1113	Remove Roadway Type 2 - Garfield - Howe (E) Ph.2	1	1	0	0	1	1	13-Sep-25	13-Sep-25	40	26	14	14	
3-WE-1114	Pour Roadway - Garfield - Howe (E) Ph.2	1	1	0	0	1	1	14-Sep-25	14-Sep-25	40	26	14	14	
Fairview West Side Phase 1														
3-WE-1116	Remove Roadway Type 2 - Fairview (W) Ph.1	1	1	0	0	1	1	20-Sep-25	20-Sep-25	40	26	14	14	
3-WE-1117	Pour Roadway - Fairview (W) Ph.1	1	1	0	0	1	1	21-Sep-25	21-Sep-25	40	26	14	14	
Fairview West Side Phase 2														
3-WE-1119	Remove Roadway Type 2 - Fairview (W) Ph.2	1	1	0	0	1	1	27-Sep-25	27-Sep-25	40	26	14	14	
3-WE-1120	Pour Roadway - Fairview (W) Ph.2	1	1	0	0	1	1	28-Sep-25	28-Sep-25	40	26	14	14	
Zone 4 - Galer to 3rd														
Storm														
FM-152	FM 152 Stop Work Fairview	17	99	0	83	16	99	09-May-25 A	30-Sep-25	-24	-24	0	0	
FM-152A	Fairview Comm Ductbank Resolution / Mobilize	12	99	0	83	16	99	09-May-25 A	30-Sep-25	-24	-24	0	0	
4-DB-1000	FM 152 ADDED DUCTBANK SCOPE (Definition & Duration TBD)	0	0	0	0	0	0	01-Oct-25	01-Oct-25	-24	-24	0	0	
4-ST-1484	Aloha to Valley - Storm (AFTER FM 152)	5	5	0	0	5	5	01-Oct-25	07-Oct-25	-24	-24	0	0	

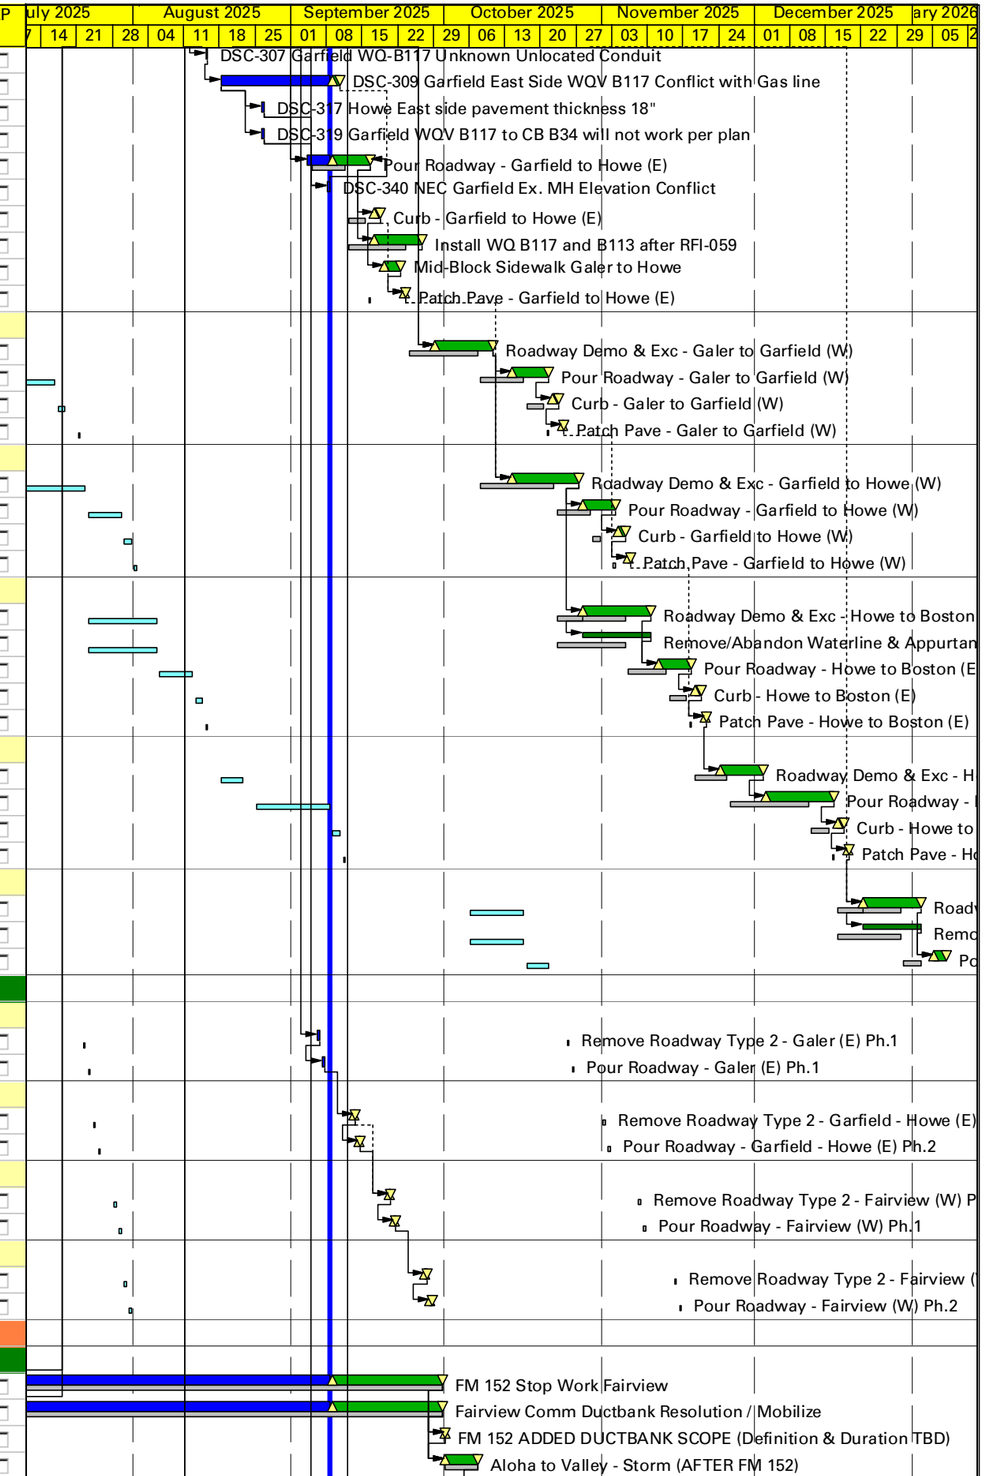

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Conduit Crossings														
4-CC-1481	Harrison Undercrossing	17	17	0	17	0	17	07-Jul-25 A	29-Jul-25 A			0	0	
DSC-260	DSC-260 Harrison undercrossing unknown 6" clay	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	
DSC-262	DSC-262 Harrison 5R Conduit Conflict	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	
DSC-267	DSC-267 Fairview & Harrison, Re-dig Trench for SCL Core	1	1	0	1	0	1	17-Jul-25 A	17-Jul-25 A			0	0	
4-CC-1478	Yale - Complete Conduit Crossings After Ductbank Relocation	3	3	0	0	3	3	08-Oct-25	10-Oct-25	-24	-24	0	0	
4-CC-1479	Aloha - Complete Conduit Crossings After Ductbank Relocation	3	3	0	0	3	3	14-Oct-25	16-Oct-25	-24	-24	0	0	
Roadway														
Eastlake to Valley West Side														
4-RW-1474	Demo, Common Ex, Type 2 - Eastlake to Valley (W)	16	16	0	0	16	16	17-Oct-25	07-Nov-25	-24	-24	0	0	
4-RW-1475	Pour Roadway - Eastlake to Valley (W)	6	6	0	0	6	6	10-Nov-25	18-Nov-25	-24	-24	0	0	
4-RW-1476	Curb - Eastlake to Valley (W)	3	3	0	0	3	3	19-Nov-25	21-Nov-25	-24	-24	0	0	
Weekend Paving														
Yale Phase 1														
4-WE-1499	COMPLETE CONDUIT YALE EAST SIDE	5	5	1	4	0	4	14-Aug-25 A	19-Aug-25 A		18	3	4	
DSC-310	DSC-310 Yale East Side Unknown CB and Ductbank	1	0	-1	1	0	1	18-Aug-25 A	18-Aug-25 A					
4-WE-1479	Remove Roadway Type 2 - Yale Ph.1 (WE)	1	1	0	1	0	1	23-Aug-25 A	23-Aug-25 A		6	2	2	
4-WE-1480	Pour Roadway - Yale Ph.1 (WE)	1	1	0	1	0	1	24-Aug-25 A	24-Aug-25 A		6	2	2	
Yale Phase 2														
4-WE-1482	Remove Roadway Type 2 - Yale Ph.2 (WE)	1	1	0	0	1	1	22-Nov-25	22-Nov-25	-10	-10	0	0	
4-WE-1483	Pour Roadway - Yale Ph.2 (WE)	1	1	0	0	1	1	23-Nov-25	23-Nov-25	-10	-10	0	0	
Yale Phase 3														
4-WE-1485	Remove Roadway Type 2 - Yale Ph.3 (WE)	1	1	0	0	1	1	29-Nov-25	29-Nov-25	-10	-10	0	0	
4-WE-1486	Pour Roadway - Yale Ph.3 (WE)	1	1	0	0	1	1	30-Nov-25	30-Nov-25	-10	-10	0	0	
Aloha Phase 1														
DSC-312	DSC-312 NEC Aloha unknown unmarked conduits	1	0	-1	1	0	1	20-Aug-25 A	20-Aug-25 A					
DSC-313	DSC-313 Aloha unknown unlocated Fiber line	1	0	-1	1	0	1	20-Aug-25 A	20-Aug-25 A					
DSC-314	DSC-314 Aloha Unknown unlocated conduit	1	0	-1	1	0	1	20-Aug-25 A	20-Aug-25 A					
4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	5	5	0	5	0	5	20-Aug-25 A	26-Aug-25 A		18	4	4	
DSC-315	DSC-315 Aloha East Contaminated Soils	1	0	-1	1	0	1	21-Aug-25 A	21-Aug-25 A					
4-WE-1518	BOAT SHOW - CANNOT CLOSE ALOHA	2	0	-2	2	0	2	30-Aug-25 A	31-Aug-25 A					
DSC-334	DSC-334 SEC Fairview & Aloha Plugged Inlet	5	0	-5	2	3	5	05-Sep-25 A	11-Sep-25	25				
DSC-335	DSC-335 SEC Fairview & Aloha Comm Conduit Conflict	5	0	-5	2	3	5	05-Sep-25 A	11-Sep-25	25				
DSC-336	DSC-336 Fairview & Aloha Ex. Pole Foundation in Grade	5	0	-5	2	3	5	05-Sep-25 A	11-Sep-25	-1				
4-WE-1488	Remove Roadway Type 2 - Aloha Ph.1 (WE)	1	1	0	1	0	1	06-Sep-25 A	06-Sep-25 A		6	0	0	
4-WE-1489	Pour Roadway - Aloha Ph.1 (WE)	1	1	0	1	0	1	07-Sep-25 A	07-Sep-25 A		6	0	0	
4-WE-1519	Pour Roadway - Aloha / After DCS's 334, 335, 336	2	0	-2	0	2	2	12-Sep-25	15-Sep-25	25				
Aloha Phase 2														
4-WE-1491	Remove Roadway Type 2 - Aloha Ph.2 (WE)	1	1	0	0	1	1	06-Dec-25	06-Dec-25	-10	-10	0	0	
4-WE-1492	Pour Roadway - Aloha Ph.2 (WE)	1	1	0	0	1	1	07-Dec-25	07-Dec-25	-10	-10	0	0	
Valley to Roy Phase 1														
4-WE-1494	Remove Roadway Type 2 - Valley to Roy Ph.1 (WE)	1	1	0	0	1	1	13-Sep-25	13-Sep-25	14	6	0	0	
4-WE-1495	Pour Roadway - Valley to Roy Ph.1 (WE)	1	1	0	0	1	1	14-Sep-25	14-Sep-25	14	6	0	0	
Valley to Roy Phase 2														
4-WE-1497	Remove Roadway Type 2 - Valley to Roy Ph.2 (WE)	1	1	0	0	1	1	13-Dec-25	13-Dec-25	-10	-10	0	0	
4-WE-1498	Pour Roadway - Valley to Roy Ph.2 (WE)	1	1	0	0	1	1	14-Dec-25	14-Dec-25	-10	-10	0	0	
Harrison Phase 1														
4-WE-1500	Remove Roadway Type 2 - Harrison Ph.1 (WE)	1	1	0	0	1	1	20-Dec-25	20-Dec-25	-10	-10	0	0	
4-WE-1501	Pour Roadway - Harrison Ph.1 (WE)	1	1	0	0	1	1	21-Dec-25	21-Dec-25	-10	-10	0	0	
Harrison Phase 2														
4-WE-1503	Remove Roadway Type 2 - Harrison Ph.2 (WE)	1	1	0	0	1	1	27-Dec-25	27-Dec-25	-10	-10	0	0	
4-WE-1504	Pour Roadway - Harrison Ph.2 (WE)	1	1	0	0	1	1	28-Dec-25	28-Dec-25	-10	-10	0	0	
Virginia and Boren														
4-WE-1506	Remove Roadway Type 2 - Virginia & Boren (WE)	1	1	0	0	1	1	03-Jan-26	03-Jan-26	60	60	0	0	

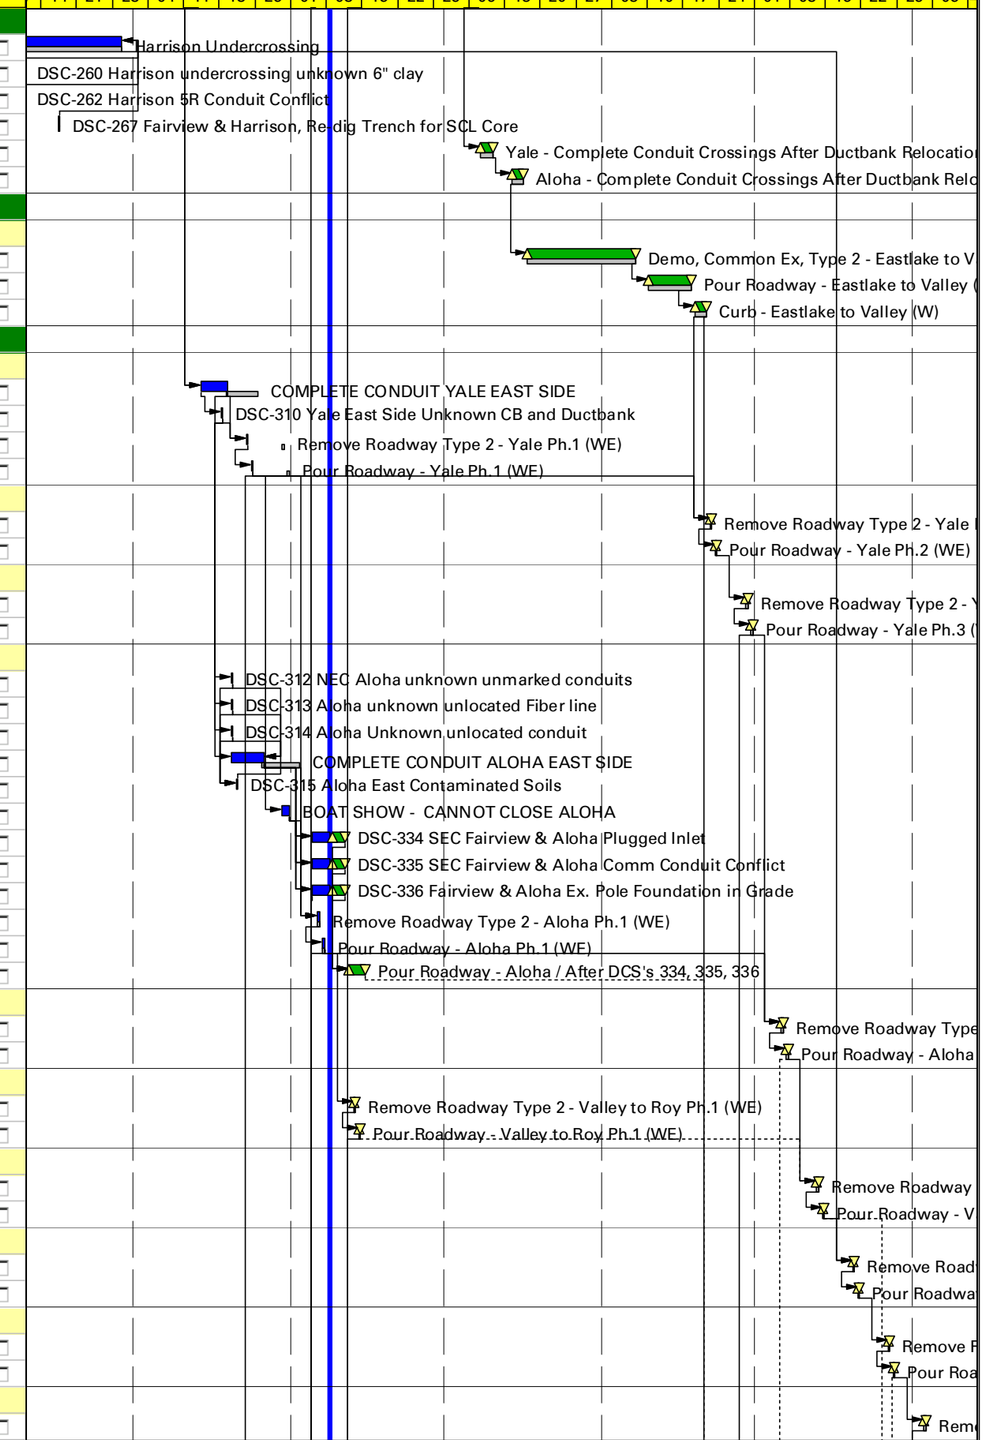

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© Primavera Systems, Inc.

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
4-WE-1507	Pour Roadway - Virginia & Boren (WE)	1	1	0	0	1	1	04-Jan-26	04-Jan-26	60	60	0	0	
Pole Foundations														
DSC-339	DSC-339 Aloha P2904 Ground Water at 13'	1	0	-1	1	0	1	08-Sep-25 A	08-Sep-25 A					
4-PF-1526	YALE TO ALOHA - EAST SIDE - POLE FOUNDATIONS (3 ea.)	4	4	-1	1	4	5	08-Sep-25 A	12-Sep-25	-5	15	0	-1	
4-PF-1536	ALOHA - EAST SIDE Pole Foundations (2 ea,)	3	3	-2	1	4	5	08-Sep-25 A	12-Sep-25	-5	15	4	2	
4-PF-1529	VALLEY - EAST SIDE Pole Foundations (2 ea.)	2	2	0	0	2	2	15-Sep-25	16-Sep-25	57	15	2	2	
4-PF-1515	Yale - Pole Foundations (4 ea.)	6	6	0	0	6	6	01-Dec-25	08-Dec-25	5	5	0	0	
4-PF-1516	Yale to Aloha - WEST SIDE Pole Foundations (3 ea.)	4	4	0	0	4	4	09-Dec-25	12-Dec-25	5	5	0	0	
4-PF-1517	Aloha - WEST SIDE Pole Foundations (6 ea,)	9	9	0	0	9	9	15-Dec-25	26-Dec-25	5	5	0	0	
4-PF-1518	Aloha to Valley - Pole Foundations (3 ea.)	5	5	0	0	5	5	29-Dec-25	05-Jan-26	5	5	0	0	
4-PF-1519	Valley - WEST SIDE Pole Foundations (1 ea.)	2	2	0	0	2	2	06-Jan-26	07-Jan-26	5	5	0	0	
Sidewalks														
Yale NEC														
4-SW-1567	Remove Sidewalk - Yale NEC	1	1	0	0	1	1	15-Sep-25	15-Sep-25	22	15	4	4	
4-SW-1568	Trench Electrical - Yale NEC	2	2	0	0	2	2	16-Sep-25	17-Sep-25	22	15	4	4	
4-SW-1569	Electrical - Yale NEC	4	4	0	0	4	4	18-Sep-25	23-Sep-25	22	15	4	4	
4-SW-1570	Grade Sidewalks - Yale NEC	1	1	0	0	1	1	24-Sep-25	24-Sep-25	22	15	4	4	
4-SW-1571	Pour Sidewalks/Curb Ramps - Yale NEC	3	3	0	0	3	3	25-Sep-25	29-Sep-25	22	15	4	4	
Yale SEC														
4-SW-1573	Remove Sidewalk - Yale SEC	1	1	0	1	0	1	26-Aug-25 A	26-Aug-25 A		17	20	20	
4-SW-1574	Trench Electrical - Yale SEC	1	1	0	1	0	1	27-Aug-25 A	27-Aug-25 A		17	20	20	
DSC-323	DSC-323 SWC Yale & Fairview 8in Sidewalk	1	0	-1	1	0	1	28-Aug-25 A	28-Aug-25 A					
4-SW-1575	Electrical - Yale SEC	3	3	-1	4	0	4	28-Aug-25 A	03-Sep-25 A		17	20	19	
DSC-325	DSC-325 SEC Yale & Fairview Unlocated Utility	1	0	-1	1	0	1	29-Aug-25 A	29-Aug-25 A					
4-SW-1576	Grade Sidewalks - Yale SEC	1	1	0	1	0	1	04-Sep-25 A	04-Sep-25 A		17	19	19	
4-SW-1577	Pour Sidewalks/Curb Ramps - Yale SEC	2	2	0	0	2	2	25-Sep-25	26-Sep-25	22	15	7	7	
Aloha NEC														
4-SW-1579	Remove Sidewalk - Aloha NEC	2	2	0	0	2	2	24-Nov-25	25-Nov-25	-22	-22	0	0	
4-SW-1580	Trench Electrical - Aloha NEC	3	3	0	0	3	3	26-Nov-25	02-Dec-25	-22	-22	0	0	
4-SW-1581	Excavate Shelter Foundations - Aloha NEC	1	1	0	0	1	1	03-Dec-25	03-Dec-25	-22	-22	0	0	
4-SW-1582	Form Pour Shelter Foundations - Aloha NEC	3	3	0	0	3	3	04-Dec-25	08-Dec-25	-22	-22	0	0	
4-SW-1583	Electrical - Aloha NEC	5	5	0	0	5	5	09-Dec-25	15-Dec-25	-22	-22	0	0	
4-SW-1584	Grade Sidewalks - Aloha NEC	2	2	0	0	2	2	16-Dec-25	17-Dec-25	-22	-22	0	0	
4-SW-1585	Pour Sidewalks/Curb Ramps - Aloha NEC	5	5	0	0	5	5	18-Dec-25	24-Dec-25	-22	-22	0	0	
Aloha SEC														
4-SW-1587	Remove Sidewalk - Aloha SEC	1	1	0	0	1	1	26-Dec-25	26-Dec-25	-22	-22	0	0	
4-SW-1588	Trench Electrical - Aloha SEC	2	2	0	0	2	2	29-Dec-25	30-Dec-25	-22	-22	0	0	
4-SW-1589	Electrical - Aloha SEC	4	4	0	0	4	4	31-Dec-25	06-Jan-26	-21	-21	0	0	
Harrison NEC														
4-SW-1613	Remove Sidewalk Harrison NEC	2	2	0	0	2	2	31-Dec-25	02-Jan-26	-22	-22	0	0	
4-SW-1614	Trench Electrical Harrison NEC	2	2	0	0	2	2	05-Jan-26	06-Jan-26	-22	-22	0	0	

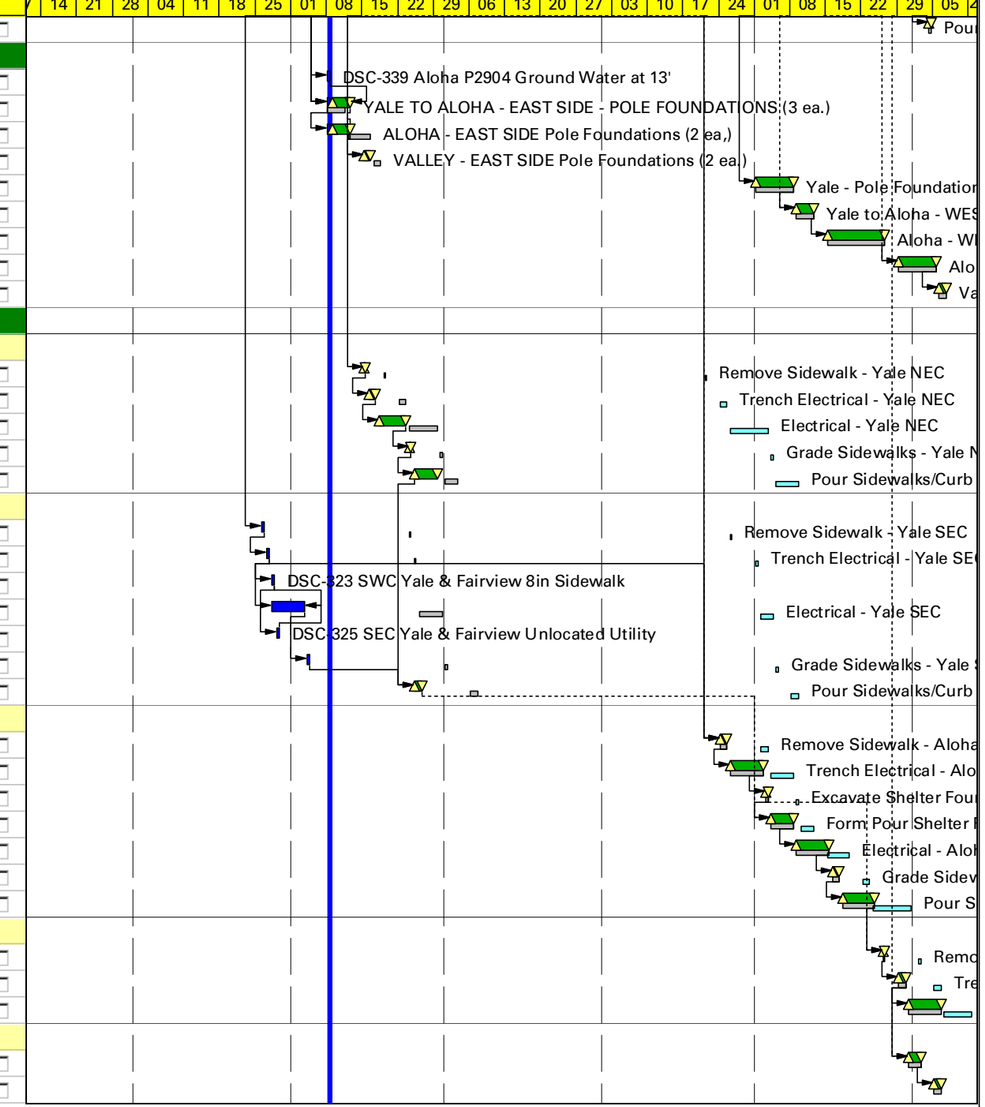

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: DATE RANGE 120 (J-LINE).
Layout: J-LINE-WBS-120
© *Primavera Systems, Inc.*

JANSEN

ALL ACTIVITIES

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)														
Milestones														
M-8000	Start Early Submittal Process	0	0	0	0	0	0	11-Sep-24 A				0	0	☑
M-9000	NTP	1	1	0	1	0	1	07-Oct-24 A	07-Oct-24 A			0	0	☑
M-9001	CONTRACT TIME	594	616	-3	223	396	619	07-Oct-24 A	06-May-27	-25	-22	0	-3	☑
M-9017	Zone-4 - DB Rescheduling / Admin & Submittals	20	20	2	18	0	18	21-Jul-25 A	13-Aug-25 A		18	0	2	☐
M-9027	Zone-4 - DB Rescheduling / Submit TC Plans	5	5	0	5	0	5	22-Jul-25 A	28-Jul-25 A			0	0	☐
M-9037	Zone-4 - DB Rescheduling / Review TC Plans	15	15	3	12	0	12	29-Jul-25 A	13-Aug-25 A		18	0	3	☐
M-9002	Planting Window Start	0	0	0	0	0	0	01-Oct-26*		78	78	0	0	☐
M-9003	Substantial Completion	0	0	0	0	0	0		01-Apr-27	-25	-22	-3	-3	☑
M-9013	Final Inspection	1	1	0	0	1	1	02-Apr-27	02-Apr-27	-25	-22	-3	-3	☑
M-9004	Punch List	20	20	0	0	20	20	05-Apr-27	30-Apr-27	-25	-22	-3	-3	☑
M-9005	Physical Completion	0	0	0	0	0	0	03-May-27	03-May-27	-25	-22	-3	-3	☑
M-9006	Owner Caused Delays	4	4	0	0	4	4	03-May-27	06-May-27	-25	-22	-3	-3	☑
M-9007	Project Completion	0	0	0	0	0	0		06-May-27*	-25	-22	-3	-3	☑
Long Lead Material														
PROC-0003	Owner Provided Kit of Parts & Pylons - Stations	20	20	0	0	20	20	13-Mar-26	09-Apr-26	108	103	5	5	☐
Poles														
PROC-0005	Pole Shop Drawings - Submit	1	1	0	1	0	1	16-Dec-24 A	16-Dec-24 A			0	0	☐
PROC-0006	Pole Shop Drawing Review (after FM-0051) (MC)	20	22	0	22	0	22	17-Dec-24 A	24-Jan-25 A			0	0	☐
PROC-0016	Pole Shop Drawing Resubmit RFI #065	5	25	0	25	0	25	27-Jan-25 A	05-Mar-25 A			0	0	☐
PROC-0027	Pole Shop Drawing Resubmit RFI #076	10	12	0	12	0	12	06-Mar-25 A	21-Mar-25 A			0	0	☐
PROC-0057	SDOT Re-Design - Poles	5	20	0	20	0	20	24-Mar-25 A	18-Apr-25 A			0	0	☐
PROC-0037	Pole Shop Drawing Resubmit Valmont Shop Dwgs per RFI #076	20	23	0	23	0	23	24-Mar-25 A	23-Apr-25 A			0	0	☐
PROC-0047	Pole Release Confirmation per RFI #088	17	12	0	12	0	12	27-Mar-25 A	11-Apr-25 A			0	0	☐
PROC-0017	Pole Shop Drawing Review	20	19	0	19	0	19	24-Apr-25 A	20-May-25 A			0	0	☐
PROC-0007	Procure Poles	120	120	0	75	45	120	21-May-25 A	12-Nov-25	125	125	0	0	☐
Watermain														
PROC-0009	Lay Drawings - Watermain (Submit)	1	1	0	1	0	1	03-Oct-24 A	03-Oct-24 A			0	0	☑
PROC-0010	Lay Drawings Review - Watermain (Review / R&R)	14	16	0	16	0	16	03-Oct-24 A	25-Oct-24 A			0	0	☑
PROC-0020	Lay Drawings Review - Watermain (Resubmittal)	10	8	0	8	0	8	28-Oct-24 A	06-Nov-24 A			0	0	☑
PROC-0030	Lay Drawings Review - Watermain (2nd Review)	15	10	0	10	0	10	07-Nov-24 A	21-Nov-24 A			0	0	☑
PROC-0040	Lay Drawings Review - Watermain (Resubmittal #2)	4	5	0	5	0	5	22-Nov-24 A	02-Dec-24 A			0	0	☑
PROC-0021	Lay Drawings Review - Watermain (3rd Review)	15	16	0	16	0	16	03-Dec-24 A	24-Dec-24 A			0	0	☑
PROC-0011	Procure Watermain - Watermain	21	21	0	21	0	21	24-Dec-24 A	30-Jan-25 A			0	0	☑
Water Quality Vaults														
PROC-0083	Water Quality Vaults (Submit)	5	1	0	1	0	1	11-Sep-24 A	11-Sep-24 A			0	0	☑
PROC-0023	Water Quality Vaults (Review / R&R / Design Changes)	5	14	0	14	0	14	11-Sep-24 A	30-Sep-24 A			0	0	☑
PROC-0033	Water Quality Vaults (Design Change 08)	15	11	0	11	0	11	01-Oct-24 A	16-Oct-24 A			0	0	☑
PROC-0043	Water Quality Vaults (Design Change 13)	3	3	0	3	0	3	17-Oct-24 A	21-Oct-24 A			0	0	☑
PROC-0053	Water Quality Vaults (Resubmit Per Design Changes)	3	3	0	3	0	3	22-Oct-24 A	24-Oct-24 A			0	0	☑
PROC-0073	Water Quality Vaults (Resubmittal Review)	15	6	0	6	0	6	25-Oct-24 A	01-Nov-24 A			0	0	☑
PROC-0013	Water Quality Vaults (FAB & Deliver)	40	21	0	21	0	21	04-Nov-24 A	05-Dec-24 A			0	0	☑
Project Start Up														
TCP-001	Garfield Temp Signal Plan Delay	3	3	0	3	0	3	07-Oct-24 A	09-Oct-24 A			0	0	☑
PST-0016	Install Erosion Control	5	5	0	5	0	5	07-Oct-24 A	11-Oct-24 A			0	0	☑
PST-0015	Site Set Up	4	4	0	4	0	4	10-Oct-24 A	16-Oct-24 A			0	0	☑
Zone 1 - 43rd to University Bridge														
Pole Foundation Potholing														
1-PH-0019	43rd St - Pole Foundation Potholing	8	8	0	8	0	8	15-Oct-24 A	24-Oct-24 A			0	0	☑
1-PH-0020	11th Ave - Pole Foundation Potholing	5	5	0	5	0	5	25-Oct-24 A	31-Oct-24 A			0	0	☑
DSC-022	DSC-022 41st & Roosevelt Sewer Conflict P-0601	4	4	0	4	0	4	30-Oct-24 A	04-Nov-24 A			0	0	☑
1-PH-0021	Roosevelt - Pole Foundation Potholing	12	12	0	12	0	12	30-Oct-24 A	15-Nov-24 A			0	0	☑
FM0009	FM-0009 Roosevelt - Pole Foundation Potholing (ADDED 7 POLES)	6	6	0	6	0	6	02-Dec-24 A	09-Dec-24 A			0	0	☑

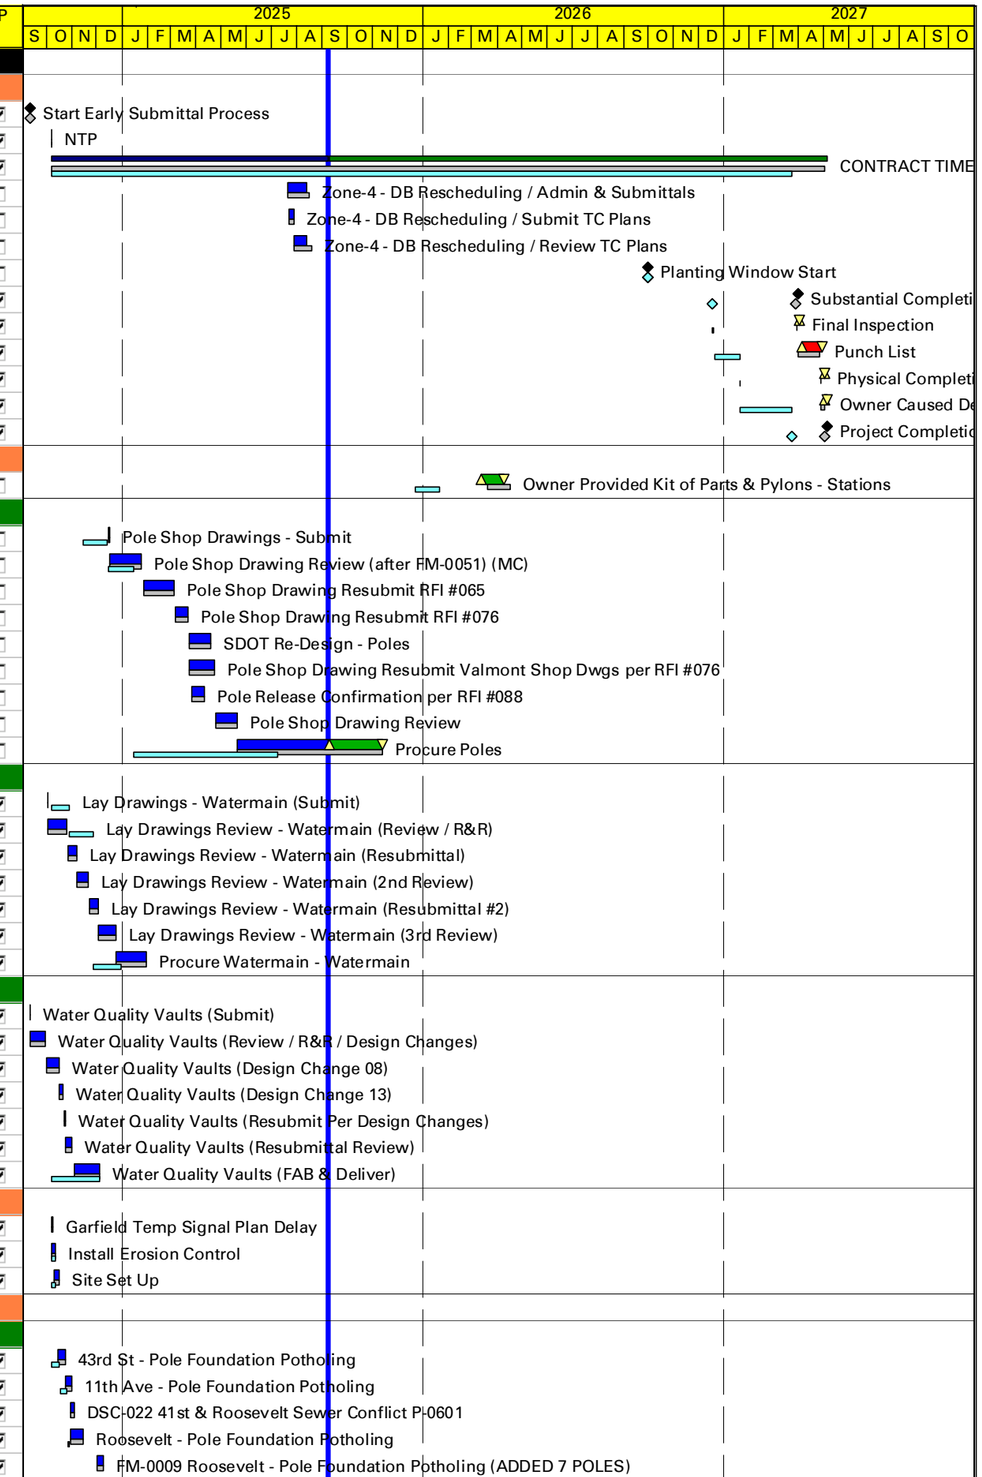

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
FM0012	FM-0012 Additional Utility Investigation	5	5	0	5	0	5	10-Dec-24 A	16-Dec-24 A			0	0	☑
FM0051-Z1	FM-0051 Potholing (Zone 1)	3	3	0	3	0	3	14-Jan-25 A	16-Jan-25 A			0	0	☐
DSC's														
DSC-001	DSC-001 SW Corner 42nd & 11th Private Sign Conflict w/Pole Fdn	9	9	0	9	0	9	11-Oct-24 A	24-Oct-24 A			0	0	☑
DSC-002	DSC-002 SW Corner 42nd & 11th Comm Cabinet Conflict P-0303	15	194	0	194	0	194	11-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-003	DSC-003 NW Corner 43rd & 11th Conflict w/Retaining Wall	14	193	0	193	0	193	15-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-004	DSC-004 NE Corner 11th & 43rd P-0201 Conflict	13	192	0	192	0	192	16-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-007	DSC-007 NE Corner 11th & 43rd P-0201 CDF Conflict	3	3	0	3	0	3	17-Oct-24 A	21-Oct-24 A			0	0	☑
DSC-005	DSC-005 SE Corner 43rd & Roosevelt P-0112 Conflict	12	191	0	191	0	191	17-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-006	DSC-006 NW Corner 11th & 43rd P-0203 Conflict	11	190	0	190	0	190	18-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-008	DSC-008 NW Corner 43rd & Roosevelt P-1002 Conflict	11	190	0	190	0	190	18-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-011	DSC-011 43rd Mid-Block Roosevelt to 11th N. Side T-213-04 Confli	9	188	0	188	0	188	22-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-012	DSC-012 NW Corner 11th & 43rd P-0203 Conflicts	8	187	0	187	0	187	23-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-013	DSC-013 NE Corner Roosevelt & 43rd Concrete Obstruction P-109	2	2	0	2	0	2	24-Oct-24 A	25-Oct-24 A			0	0	☑
DSC-016	DSC-016 SE Corner 42nd & 11th P-0304 Conduit Conflicts	6	185	0	185	0	185	25-Oct-24 A	01-Aug-25 A			0	0	☑
DSC-017	DSC-017 NE Corner Eastlake & 11th T-212-06 Gas Line Conflict	6	185	0	185	0	185	25-Oct-24 A	01-Aug-25 A			0	0	☑
FM-TBD	SDOT Directed Potholing - 11th Ave NE	11	11	6	5	0	5	04-Aug-25 A	08-Aug-25 A		-16	0	6	☑
Storm Work														
DSC-032	DSC-032 SEC 11th & 43rd Unknown Unlocated Ductbank Conflict	1	1	0	1	0	1	18-Nov-24 A	18-Nov-24 A			0	0	☑
1-ST-0023	11th and 43rd - Storm (DSC-032, 036, 037, 039)	5	5	0	5	0	5	18-Nov-24 A	22-Nov-24 A			0	0	☑
DSC-036	DSC-036 Ductbank Conflict SWC 43rd & 11th	1	1	0	1	0	1	20-Nov-24 A	20-Nov-24 A			0	0	☑
DSC-037	DSC-037 Ductbank Conflict NWC 43rd & 11th	1	1	0	1	0	1	21-Nov-24 A	21-Nov-24 A			0	0	☑
DSC-039	DSC-039 Ductbank Conflict NWC 43rd & 11th	1	1	0	1	0	1	21-Nov-24 A	21-Nov-24 A			0	0	☑
1-ST-0024	Roosevelt and 43rd - Storm (prior to DSC-040)	3	3	0	3	0	3	25-Nov-24 A	27-Nov-24 A			0	0	☑
DSC-040	DSC-040 Ductbank Conflict NEC 43rd & Roosevelt	5	58	0	58	0	58	25-Nov-24 A	28-Feb-25 A			0	0	☑
DSC-044	DSC-044 SWC 42nd & 11th Elec. Conduit Conflict A9	1	1	0	1	0	1	02-Dec-24 A	02-Dec-24 A			0	0	☑
1-ST-0025	11th and 42nd - Storm	4	6	0	6	0	6	02-Dec-24 A	09-Dec-24 A			0	0	☑
DSC-045	DSC-045 SWC 42nd & 11the Stoem Conflidt w/Clay Pipe	1	1	0	1	0	1	03-Dec-24 A	03-Dec-24 A			0	0	☑
DSC-054	DSC-054 SWC 41st & 11th Gas Conflict w/Inlet Pipe	1	1	0	1	0	1	10-Dec-24 A	10-Dec-24 A			0	0	☑
1-ST-0026	11th and 41st - Storm	4	4	0	4	0	4	10-Dec-24 A	13-Dec-24 A			0	0	☑
DSC -055	DSC-055 NWC 41st & 11th Inlet Pipe A-12 Conflict	1	1	0	1	0	1	12-Dec-24 A	12-Dec-24 A			0	0	☑
1-ST-0028	Roosevelt and 41st - Storm	4	9	0	9	0	9	16-Dec-24 A	03-Jan-25 A			0	0	☑
DSC-058	DSC-058 SWC 41st & Roosevelt Ductbank Conflict w/CB Conn.	1	1	0	1	0	1	17-Dec-24 A	17-Dec-24 A			0	0	☑
DSC-063	DSC-063 41st & Roosevelt CB A6 Exist. Storm Main Leaking	2	2	0	2	0	2	19-Dec-24 A	20-Dec-24 A			0	0	☑
DSC-065	DSC-065 SWC 42nd Roosevelt Pole Conflict w/CB A5 (DC-031)	3	14	0	14	0	14	24-Dec-24 A	21-Jan-25 A			0	0	☑
1-ST-0027	Eastlake and 41st - Storm	4	10	0	10	0	10	02-Jan-25 A	15-Jan-25 A			0	0	☑
DSC-172	DSC-172 43rd & Roosevelt Unknown conduit conflicts w/CB	1	1	0	1	0	1	14-Apr-25 A	14-Apr-25 A			0	0	☑
1-ST-0034	Roosevelt and 43rd - Storm (after DSC-040) DC-035	3	3	0	3	0	3	14-Apr-25 A	16-Apr-25 A			0	0	☑
1-ST-0029	Roosevelt and 42nd - Storm	3	3	0	3	0	3	17-Apr-25 A	21-Apr-25 A			0	0	☑
1-ST-0044	Complete Storm NEC 43rd & Roosevelt & 42nd	3	3	0	3	0	3	17-Apr-25 A	21-Apr-25 A			0	0	☑
DSC-201	DSC-201 42nd & 11th NWC - CB A8 Thick Road	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	☑
DSC-202	DSC-202 42nd & 11th NWC - CB A8 Conduit Conflict	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	☑
1-ST-DC-055A	DESIGN CHANGE 055	10	37	0	37	0	37	05-May-25 A	26-Jun-25 A			0	0	☑
1-ST-DC-055B	Design Change 055 - 43rd & 11th Storm	1	1	0	1	0	1	08-May-25 A	08-May-25 A			0	0	☑
DSC-206	DSC-206 43rd and and 11th DC 55 Storm conflict with conduit	1	1	0	1	0	1	08-May-25 A	08-May-25 A			0	0	☑
DSC-212	DSC-212 SWC 43rd and 11th Type 250 hood will not work with DC	1	1	0	1	0	1	15-May-25 A	15-May-25 A			0	0	☑
1-ST-DC-055A10	DESIGN CHANGE 055 - SPU WATER RELOCATION	2	2	0	2	0	2	27-Jun-25 A	30-Jun-25 A			0	0	☑
1-ST-DC-055A20	DESIGN CHANGE 055 - 42nd & 11th STORM	2	4	0	4	0	4	30-Jun-25 A	03-Jul-25 A			0	0	☑
Watermain Stage 8														
SPU Ops Notifications														
1-W-0052	SPU Water Ops Scheduling Notification - Stg 8 Cut/Cap	15	14	0	14	0	14	11-Dec-24 A	07-Jan-25 A			0	0	☑
1-W-0051	SPU Water Ops Scheduling Notification - Stg 8 Connections	15	15	0	15	0	15	26-Feb-25 A	18-Mar-25 A			0	0	☑
Stage 8 Waterline Installation														
DSC-066	DSC-066 43rd & Roosevelt Stg. 8 Water Conflict w/Hydrant Tee	4	34	0	34	0	34	02-Jan-25 A	24-Feb-25 A			0	0	☑

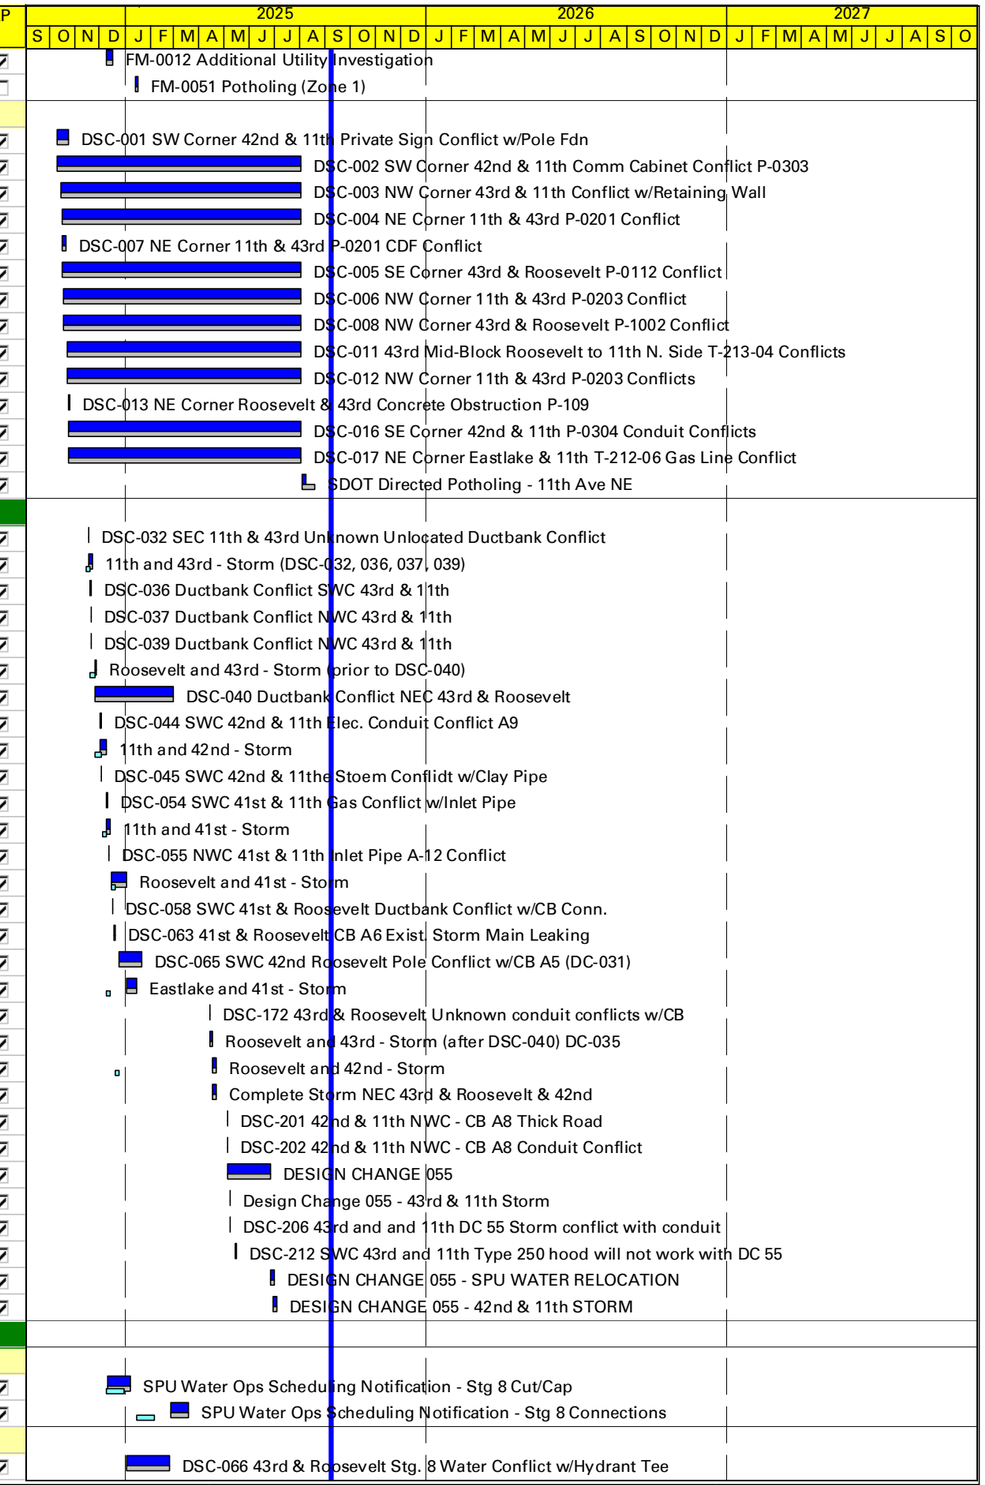

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-W-0031	Excavate CC01 & CC02 - Watermain Stg 8	1	1	0	1	0	1	03-Jan-25 A	03-Jan-25 A			0	0	☑
1-W-0032	SPU Cut/Cap CC01 & CC02 - Watermain Stg 8 (43rd & 11th)	1	1	0	1	0	1	08-Jan-25 A	08-Jan-25 A			0	0	☑
DSC-099	DSC-099 43rd Water Main Conflict With Ductbank	1	1	0	1	0	1	03-Feb-25 A	03-Feb-25 A			0	0	☑
1-W-0033	Install Mainline & Hydrants - Watermain Stg 8	12	17	0	17	0	17	03-Feb-25 A	28-Feb-25 A			0	0	☑
NCR-004	NCR-004 TR Flex Wedge Restraint Glands incorrectly used	1	0	0	0	0	0	05-Feb-25 A	05-Feb-25 A					☑
DSC-113	DSC-113 11th Ave @ 43rd CDF Ductbank Conflict	2	2	0	2	0	2	21-Feb-25 A	24-Feb-25 A			0	0	☑
DSC-115	DSC-115 11th Ave @ 43rd Unlocated 3-inch Conduit	1	1	0	1	0	1	24-Feb-25 A	24-Feb-25 A			0	0	☑
DSC-118	DSC-118 43rd & 12th Conduit & Storm Conflict @ Watermain	1	1	0	1	0	1	28-Feb-25 A	28-Feb-25 A			0	0	☑
1-W-0034	Install Main on 11th - Watermain Stg 8	2	2	0	2	0	2	03-Mar-25 A	04-Mar-25 A			0	0	☑
DSC-120	DSC-120 11th & 43rd South Leg Water Conflict w/Ductbank	2	2	0	2	0	2	03-Mar-25 A	04-Mar-25 A			0	0	☑
DSC-122	DSC-122 43rd & Roosevelt Hydrant Conflict w/Ductbank	1	1	0	1	0	1	04-Mar-25 A	04-Mar-25 A			0	0	☑
1-W-0036	Test & Flush - Watermain Stg 8	2	2	0	2	0	2	05-Mar-25 A	06-Mar-25 A			0	0	☑
1-W-0037	Bact Results - Watermain Stg 8	1	1	0	1	0	1	07-Mar-25 A	07-Mar-25 A			0	0	☑
1-W-0040	Excavate Tie-Ins - Watermain Stg 8	3	7	0	7	0	7	07-Mar-25 A	17-Mar-25 A			0	0	☑
1-W-0039	SPU Customer Notification - Watermain Stg 8	5	5	0	5	0	5	10-Mar-25 A	14-Mar-25 A			0	0	☑
DSC-145	DSC-145 12th & 43rd Exist. Watermain not in Loc. Shown on Dwg	1	1	0	1	0	1	19-Mar-25 A	19-Mar-25 A			0	0	☑
1-W-0041	Connections at Roosevelt, 11th and 12th - Watermain Stg 8 (4 ea.)	2	2	0	2	0	2	20-Mar-25 A	21-Mar-25 A			0	0	☑
1-W-0042	Patch Pave - Watermain Stg 8	2	2	0	2	0	2	24-Mar-25 A	25-Mar-25 A			0	0	☑
1-W-0062	Test Stations Watermain Stg 8	2	2	0	2	0	2	26-Mar-25 A	27-Mar-25 A			0	0	☑
Electrical Crossings														
DSC-142	DSC-142 NWC 43rd 11th unknown ductbank conflict with conduit	6	6	0	6	0	6	18-Mar-25 A	25-Mar-25 A			0	0	☑
1-EC-0048	43rd and 11th 3 Ea - Electrical Crossing	9	9	0	9	0	9	18-Mar-25 A	28-Mar-25 A			0	0	☑
DSC-146	DSC-146 NEC 43rd and 11th Storm and Conduit Conflict with new	1	1	0	1	0	1	19-Mar-25 A	19-Mar-25 A			0	0	☑
1-EC-0049	Roosevelt and 43rd 3 Ea - Electrical Crossing	7	7	0	7	0	7	24-Mar-25 A	01-Apr-25 A			0	0	☑
DSC-162	DSC-162 43rd and 11th Eastern Conduit Crossing Ductbank Confli	1	1	0	1	0	1	31-Mar-25 A	31-Mar-25 A			0	0	☑
1-EC-0047	42nd and 11th 2 Each - Electrical Crossing	6	6	0	6	0	6	31-Mar-25 A	07-Apr-25 A			0	0	☑
DSC-163	DSC-163 43rd & 11th SEC Ductbank Conflict with Conduit	1	1	0	1	0	1	01-Apr-25 A	01-Apr-25 A			0	0	☑
NCR-006	NCR-006 Marking tape not installed over conduit run	1	0	-1	1	0	1	08-Apr-25 A	08-Apr-25 A					☑
1-EC-0057	Misc Vault Backfill & Coring @ 43rd	7	7	0	7	0	7	08-Apr-25 A	16-Apr-25 A			0	0	☑
1-EC-0046	Roosevelt and 42nd 1 Ea - Electrical Crossing	18	36	0	36	0	36	17-Apr-25 A	06-Jun-25 A			0	0	☑
1-EC-0054	Eastlake & 41st - Electrical Crossing	8	8	0	8	0	8	21-Apr-25 A	30-Apr-25 A			0	0	☑
1-EC-0045	Roosevelt and 41st 1 Ea - Electrical Crossing	7	7	0	7	0	7	28-Apr-25 A	06-May-25 A			0	0	☑
1-CC-0054	Roosevelt and Eastlake - Conduit Road Crossing	7	7	0	7	0	7	28-Apr-25 A	06-May-25 A			0	0	☐
DSC-190	DSC-190 Roosevelt and 42nd Waterline conflict with Conduit	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	☑
DSC-195	DSC-195 41st and Roosevelt unmarked water service	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	☑
NCR-012	NCR-012 Damaged a known 8" WM - broke existing corp valve	1	0	-1	1	0	1	29-Apr-25 A	29-Apr-25 A					☑
1-EC-DC-055A	Design Change 055 - 43rd & 11th Added Crossing	4	4	0	4	0	4	27-May-25 A	30-May-25 A			0	0	☑
NCR-013	NCR-013 Damaged pedestrian signal	1	0	-1	1	0	1	28-May-25 A	28-May-25 A					☑
DSC-222	DSC-222 42nd Roosevelt East Side Unknown steel conduit	1	1	0	1	0	1	03-Jun-25 A	03-Jun-25 A			0	0	☑
DSC-226	DSC-226 NEC 42nd and Roosevelt Unknown brick structure confli	1	1	0	1	0	1	03-Jun-25 A	03-Jun-25 A			0	0	☑
Roadway														
43rd Roosevelt to 11th														
DSC-197	DSC-197 Roosevelt to 11th on 43rd SCL vault	1	1	0	1	0	1	01-May-25 A	01-May-25 A			0	0	☑
1-RW-0058	Remove Roadway, Common Ex, Type 2 - 43rd / Roosevelt to 11th	6	6	0	6	0	6	01-May-25 A	08-May-25 A			0	0	☑
NCR-010	NCR-010 An active existing Type II SCL handhole was damaged	1	0	-1	1	0	1	02-May-25 A	02-May-25 A					☑
1-RW-0129	Adjust SCL Vault Adjustments	3	3	0	3	0	3	06-May-25 A	08-May-25 A			0	0	☑
1-RW-0059	Pour Roadway - 43rd / Roosevelt to 11th	4	8	0	8	0	8	09-May-25 A	20-May-25 A			0	0	☑
NCR-014	NCR-014 Spalling at joints of PCCP panels	1	0	-1	1	0	1	21-May-25 A	21-May-25 A					☑
NCR-015	NCR-015 Finish of PCCP panel not per specification	1	0	-1	1	0	1	21-May-25 A	21-May-25 A					☑
1-RW-0060	Curb - 43rd / Roosevelt to 11th	2	2	0	2	0	2	21-May-25 A	22-May-25 A			0	0	☑
1-RW-0061	Temp Pave - 43rd / Roosevelt to 11th	1	1	0	1	0	1	23-May-25 A	23-May-25 A			0	0	☑
NCR-0014015	NCR-014 & NCR-015 Paving	5	0	-5	1	4	5	08-Sep-25 A	12-Sep-25	0				☐
11th and 42nd Phase 1														
1-RW-0063	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.1)	2	2	0	2	0	2	02-Jun-25 A	03-Jun-25 A			0	0	☑

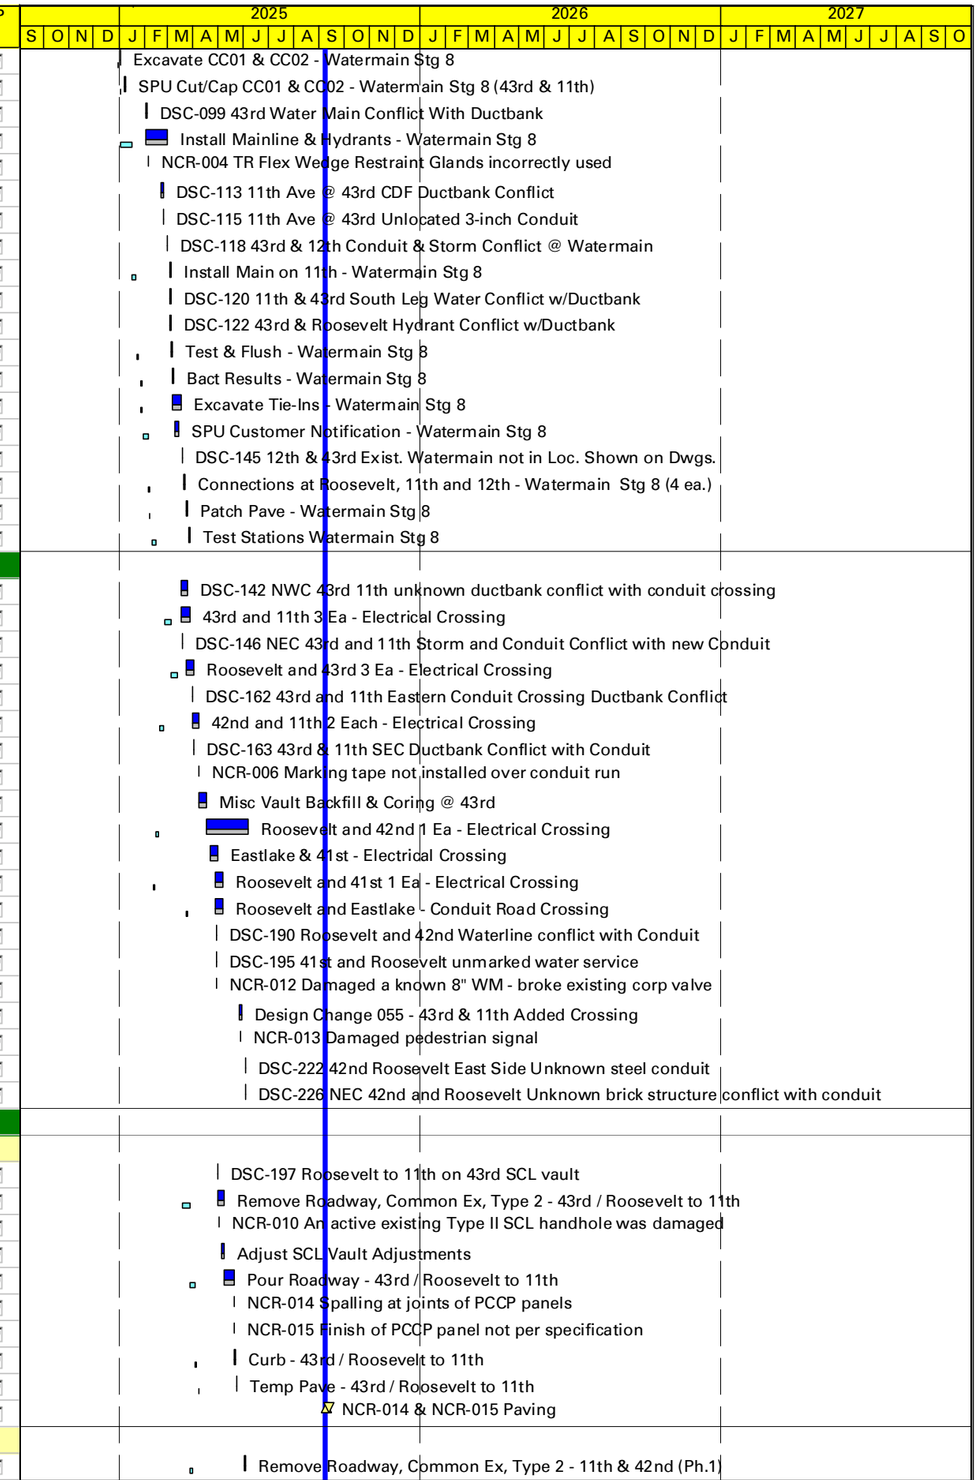

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-RW-0064	Pour Roadway - 11th & 42nd (Ph.1)	2	2	0	2	0	2	04-Jun-25 A	05-Jun-25 A			0	0	☑
1-RW-0065	Temp Pave - 11th & 42nd (Ph.1)	1	1	0	1	0	1	06-Jun-25 A	06-Jun-25 A			0	0	☑
11th and 42nd Phase 2														
1-RW-0067	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.2)	1	1	0	1	0	1	09-Jun-25 A	09-Jun-25 A			0	0	☑
1-RW-0068	Pour Roadway - 11th & 42nd (Ph.2)	1	1	0	1	0	1	11-Jun-25 A	11-Jun-25 A			0	0	☑
1-RW-0069	Temp Pave - 11th & 42nd (Ph.2)	2	2	0	2	0	2	12-Jun-25 A	13-Jun-25 A			0	0	☑
11th and 42nd Phase 3														
1-RW-0071	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.3)	5	5	0	5	0	5	17-Jun-25 A	24-Jun-25 A			0	0	☑
1-RW-0072	Pour Roadway - 11th & 42nd (Ph.3)	2	2	0	2	0	2	25-Jun-25 A	26-Jun-25 A			0	0	☑
1-RW-0073	Temp Pave - 11th & 42nd (Ph.3)	1	1	0	1	0	1	27-Jun-25 A	27-Jun-25 A			0	0	☑
NCR-022	NCR-022 Damage to panel while removing adjacent panel	1	0	-1	1	0	1	31-Jul-25 A	31-Jul-25 A					☑
43rd 11th to 12th														
DSC-237	DSC-237 43rd and 11th Tree roots conflict with Roadway	1	1	0	1	0	1	24-Jun-25 A	24-Jun-25 A			0	0	☑
DSC-245	DSC-245 43rd 11th to 12 unknown steel pipe in conflict with new r	1	1	0	1	0	1	26-Jun-25 A	26-Jun-25 A			0	0	☑
DSC-246	DSC-246 43rd 11th to 12th gas lines in conflict with roadway	1	1	0	1	0	1	26-Jun-25 A	26-Jun-25 A			0	0	☑
1-RW-0079	Remove Roadway, Common Ex, Type 2 - 43rd / 11th to 12th	6	7	0	7	0	7	26-Jun-25 A	07-Jul-25 A			0	0	☑
1-RW-0080	Pour Roadway - 43rd / 11th to 12th	17	17	0	17	0	17	08-Jul-25 A	30-Jul-25 A			0	0	☑
DC-XXX	RFI-136 Elevation Issues	13	13	0	13	0	13	10-Jul-25 A	28-Jul-25 A			0	0	☑
NCR-021	NCR-021 Riser is cast to the incorrect height bringing the lid to 1 1	1	0	-1	1	0	1	24-Jul-25 A	24-Jul-25 A					☑
1-RW-0081	Curb - 43rd / 11th to 12th	3	3	0	3	0	3	31-Jul-25 A	04-Aug-25 A			0	0	☑
1-RW-0082	Temp Pave - 43rd / 11th to 12th	1	1	0	1	0	1	05-Aug-25 A	05-Aug-25 A		-16	0	0	☑
11th and 42nd Phase 4														
1-RW-0075	Remove Roadway, Common Ex, Type 2 - 11th & 42nd (Ph.4)	3	3	0	3	0	3	08-Jul-25 A	10-Jul-25 A			0	0	☑
1-RW-0076	Pour Roadway - 11th & 42nd (Ph.4)	3	3	0	3	0	3	11-Jul-25 A	15-Jul-25 A			0	0	☑
1-RW-0077	Temp Pave - 11th & 42nd (Ph.4)	1	1	0	1	0	1	16-Jul-25 A	16-Jul-25 A			0	0	☑
Roosevelt and 43rd Western Half														
1-RW-0084	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd (West)	3	3	-6	9	0	9	11-Aug-25 A	21-Aug-25 A		14	6	0	☐
DSC-303	DSC-303 43rd/Roosevelt Sinkhole	6	0	-6	6	0	6	12-Aug-25 A	19-Aug-25 A					☐
1-RW-0085	Pour Roadway - Roosevelt & 43rd (West)	2	2	0	2	0	2	22-Aug-25 A	25-Aug-25 A		19	0	0	☐
1-RW-0086	Curb - Roosevelt & 43rd (West)	1	1	-1	2	0	2	26-Aug-25 A	27-Aug-25 A		19	0	-1	☐
1-RW-0087	Temp Pave - Roosevelt & 43rd (West)	1	1	0	1	0	1	28-Aug-25 A	28-Aug-25 A		19	-1	-1	☐
Roosevelt and 43rd St. SE Corner														
1-RW-169	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd SEC	3	0	-3	3	0	3	29-Aug-25 A	03-Sep-25 A					☐
DSC-327	DSC-327 43rd & Roosevelt Rotten Pole	1	0	-1	1	0	1	03-Sep-25 A	03-Sep-25 A					☐
DSC-328	DSC-328 SEC 43rd Roosevelt Conduits Cast in Curb	1	0	-1	1	0	1	04-Sep-25 A	04-Sep-25 A					☐
1-RW-179	Pour Roadway - Roosevelt & 43rd SEC	2	0	-2	0	2	2	15-Sep-25	16-Sep-25	0				☐
1-RW-189	Curb - Roosevelt & 43rd SEC	2	0	-2	0	2	2	17-Sep-25	18-Sep-25	7				☐
Roosevelt and 43rd St. NE Corner														
1-RW-139	Remove Roadway, Common Ex, Type 2 - Roosevelt & 43rd NEC	2	0	-2	2	0	2	04-Sep-25 A	05-Sep-25 A					☐
1-RW-149	Pour Roadway - Roosevelt & 43rd NEC	2	0	-2	0	2	2	15-Sep-25	16-Sep-25	8				☐
1-RW-159	Curb - Roosevelt & 43rd NEC	2	0	-2	0	2	2	17-Sep-25	18-Sep-25	8				☐
11th and Eastlake West Side														
DSC-275	DSC 275 11th Ave Water Service CDF conflict	1	1	0	1	0	1	23-Jul-25 A	23-Jul-25 A			0	0	☐
1-RW-0089	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (West)	5	3	-2	0	5	5	17-Sep-25	23-Sep-25	0	14	-17	-19	☐
1-RW-0090	Pour Roadway - 11th & Eastlake (West)	2	2	0	0	2	2	24-Sep-25	25-Sep-25	2	16	-19	-19	☐
1-RW-0091	Curb - 11th & Eastlake (West)	2	2	0	0	2	2	26-Sep-25	29-Sep-25	2	16	-19	-19	☐
1-RW-0092	Temp Pave - 11th & Eastlake (West)	1	1	0	0	1	1	30-Sep-25	30-Sep-25	2	16	-19	-19	☐
Eastlake 11th to NE Campus Pkwy East Side														
1-RW-0102	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Cai	5	3	-2	0	5	5	17-Sep-25	23-Sep-25	3	14	-9	-11	☐
1-RW-0103	Pour Roadway - Eastlake / 11th to NE Campus (East)	2	2	0	0	2	2	24-Sep-25	25-Sep-25	4	15	-11	-11	☐
1-RW-0104	Curb - Eastlake / 11th to NE Campus (East)	2	2	0	0	2	2	26-Sep-25	29-Sep-25	4	15	-11	-11	☐
11th and Eastlake East Side														
1-RW-0098	Remove Roadway, Common Ex, Type 2 - 11th & Eastlake (East)	2	2	0	1	1	2	08-Sep-25 A	09-Sep-25	10	14	-4	-4	☐
1-RW-0099	Pour Roadway - 11th & Eastlake (East)	2	2	0	0	2	2	17-Sep-25	18-Sep-25	8	16	-9	-9	☐

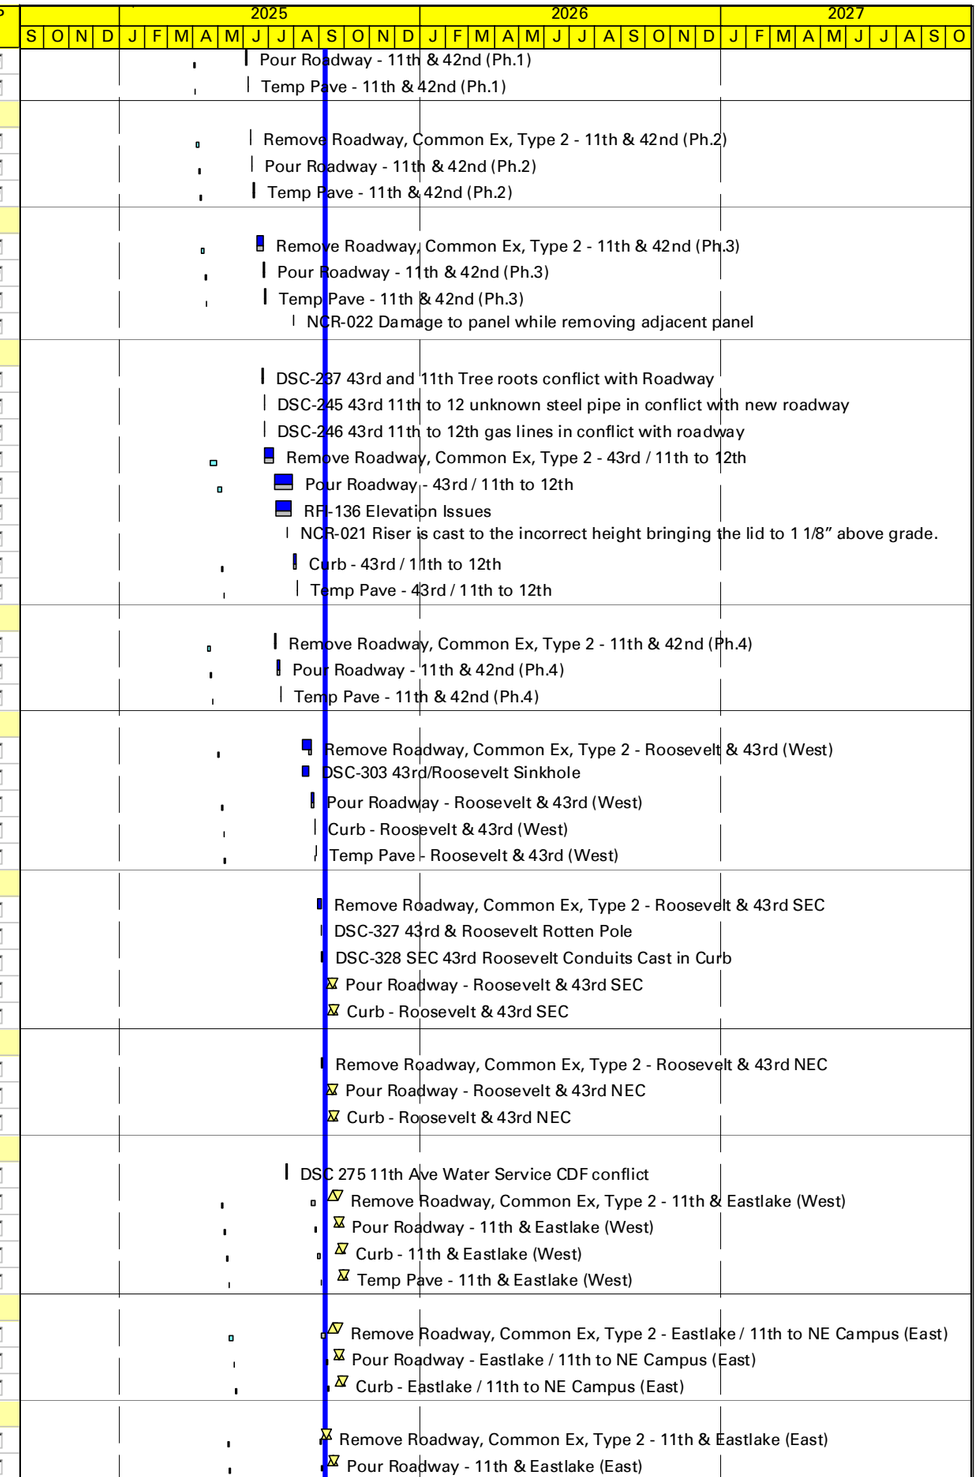

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work | BL1 LOE | Milestone | BL2 LOE | Previous MS | Actual Level of Effort | Previous Bar | Actual Work | Baseline MS | Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-RW-0100	Curb - 11th & Eastlake (East)	2	2	0	0	2	2	19-Sep-25	22-Sep-25	8	16	-9	-9	☐
Eastlake 11th to NE Campus Pkwy West Side														
1-RW-0094	Remove Roadway, Common Ex, Type 2 - Eastlake / 11th to NE Ca	3	3	0	0	3	3	24-Sep-25	26-Sep-25	0	14	-19	-19	☐
1-RW-0095	Pour Roadway - Eastlake / 11th to NE Campus (West)	2	2	0	0	2	2	29-Sep-25	30-Sep-25	2	16	-19	-19	☐
1-RW-0096	Curb - Eastlake / 11th to NE Campus (West)	2	2	0	0	2	2	01-Oct-25	02-Oct-25	2	16	-19	-19	☐
Roosevelt and 42nd St East Side														
1-RW-0106	Remove Roadway, Common Ex, Type 2 - Roosevelt & 42nd (E)	2	2	0	0	2	2	29-Sep-25	30-Sep-25	0	14	-14	-14	☐
1-RW-0107	Pour Roadway - Roosevelt & 42nd (E)	1	1	0	0	1	1	01-Oct-25	01-Oct-25	3	15	-12	-12	☐
Roosevelt and 41st East Side														
1-RW-0109	Remove Roadway, Common Ex, Type 2 - Roosevelt & 41st (E)	2	2	0	0	2	2	01-Oct-25	02-Oct-25	0	14	-14	-14	☐
1-RW-0110	Pour Roadway - Roosevelt & 41st (E)	1	1	0	0	1	1	03-Oct-25	03-Oct-25	2	15	-13	-13	☐
Roosevelt and Campus Pkwy East Side														
1-RW-0112	Remove Roadway, Common Ex, Type 2 - Roosevelt & Campus (E)	2	2	0	0	2	2	03-Oct-25	06-Oct-25	0	14	-14	-14	☐
1-RW-0113	Pour Roadway - Roosevelt & Campus (E)	1	1	0	0	1	1	07-Oct-25	07-Oct-25	1	15	-14	-14	☐
Roosevelt and 42nd St West Side														
1-RW-0115	Remove Roadway, Common Ex, Type 2 - Roosevelt & 42nd (W)	2	2	0	0	2	2	07-Oct-25	08-Oct-25	0	14	-14	-14	☐
1-RW-0116	Pour Roadway - Roosevelt & 42nd (W)	2	2	0	0	2	2	09-Oct-25	10-Oct-25	0	14	-14	-14	☐
Roosevelt and 41st West Side														
1-RW-0118	Remove Roadway, Common Ex, Type 2 - Roosevelt & 41st (W)	2	2	0	0	2	2	09-Oct-25	10-Oct-25	0	14	-14	-14	☐
1-RW-0119	Pour Roadway - Roosevelt & 41st (W)	2	2	0	0	2	2	14-Oct-25	15-Oct-25	0	14	-14	-14	☐
Weekend Roadway Work														
43rd Roosevelt to 11th Driveway Road Panels														
1-WE-0122	Remove Roadway Type 2 - 43rd / Roosevelt to 11th (driveways)	1	0	0	0	0	0	29-May-25 A	29-May-25 A			0	0	☑
1-WE-0123	Pour Roadway - 43rd / Roosevelt to 11th (driveways)	1	0	0	0	0	0	30-May-25 A	30-May-25 A			0	0	☑
43rd 11th to 12th Road Panels														
1-WE-0125	Remove Roadway Type 2 - 43rd / 11th to 12th	1	1	0	1	0	1	02-Aug-25 A	02-Aug-25 A			0	0	☑
1-WE-0126	Pour Roadway - 43rd / 11th to 12th	1	1	0	1	0	1	03-Aug-25 A	03-Aug-25 A			0	0	☑
Pole Foundations														
DSC-266	DSC-266 11th 43rd to 42nd Pole foundation conflicts with comm c	1	1	0	1	0	1	17-Jul-25 A	17-Jul-25 A			0	0	☑
DSC-270	DSC-270 11th 43rd to 42nd Pole T-211-06 Side Sewer conflict	1	1	0	1	0	1	18-Jul-25 A	18-Jul-25 A			0	0	☑
1-PF-0130	11th - Pole Foundations (17 ea.) Prior to SDOT Directed Additiona	11	11	0	11	0	11	21-Jul-25 A	04-Aug-25 A			0	0	☑
1-PF-0129	43rd - Pole Foundations (17 ea.) - PRIOR to Completion of SDOT D	10	10	6	4	0	4	05-Aug-25 A	08-Aug-25 A		-16	0	6	☑
DSC-296	DSC-296 11th Ave, T211-01 Potholing SS conflict	1	0	-1	1	0	1	06-Aug-25 A	06-Aug-25 A					☑
DSC-301	DSC-301 11th 43rd to 42nd E. Side Sewer conflict w/foundation T2	1	0	-1	1	0	1	11-Aug-25 A	11-Aug-25 A					☑
1-PF-0139	43rd - Pole Foundations (14 ea. / incl. DC 55 offset fdn.) - AFTER C	7	7	-6	13	0	13	11-Aug-25 A	27-Aug-25 A		-16	6	0	☑
DSC-302	DSC-302 U-district Pole T-210-02, T-210-03 and T-213-04 moved fc	1	0	-15	15	0	15	11-Aug-25 A	29-Aug-25 A					☑
1-PF-0159	SDOT Stop Work E-mail / Issue Directive/Design	1	0	-15	15	0	15	11-Aug-25 A	29-Aug-25 A					☑
DSC-311	DSC-311 43RD Roosevelt to 11th Boulder conflict with foundation	1	0	-1	1	0	1	19-Aug-25 A	19-Aug-25 A					☑
1-PF-0140	11th - Pole Foundations (Prior to resuming 43rd)	11	11	9	2	0	2	28-Aug-25 A	29-Aug-25 A		5	0	9	☑
1-PF-0179	11th / 42nd to 41st - SDOT Directed Stop Work (install 2 pole fdns)	4	0	-4	4	0	4	02-Sep-25 A	05-Sep-25 A					☐
1-PF-0139A	43rd - Pole Foundations (3 ea.) - AFTER Completion of DSC-302	4	0	-4	4	0	4	02-Sep-25 A	05-Sep-25 A					☑
DSC-329	DSC-329 11th Ave Ground Water in OCS foundations	1	0	-1	1	0	1	04-Sep-25 A	04-Sep-25 A					☐
DSC-341	DSC-341 43rd & 11th Signal Service Conflict w/ Temp Lighting	5	0	-5	1	4	5	08-Sep-25 A	12-Sep-25	20				☐
1-PF-0150	11th - Pole Foundations (After Yale to Aloha Zone-4 SDOT Mitigat	10	0	-10	0	10	10	15-Sep-25	26-Sep-25	-5				☐
DSC-351	DSC-351 Pole Foundation P-0204 SW 11th & Roosevelt	2	0	-2	0	2	2	29-Sep-25	30-Sep-25	10				☐
1-PF-0131	Roosevelt - Pole Foundations (21 ea.)	21	21	0	0	21	21	29-Sep-25	28-Oct-25	-5	5	-10	-10	☐
1-PF-0132	Eastlake - Pole Foundations (10 ea.)	10	10	0	0	10	10	29-Oct-25	12-Nov-25	-5	5	-10	-10	☐
Sidewalks														
43rd 12th to 11th North Side														
1-SW-0135	Remove Sidewalk - 43rd / 12th to 11th (N)	2	2	0	1	1	2	08-Sep-25 A	09-Sep-25	-22	-16	-6	-6	☑
1-SW-0136	Trench Electrical - 43rd / 12th to 11th (N)	3	3	0	0	3	3	10-Sep-25	12-Sep-25	-22	-16	-6	-6	☑
1-SW-0137	Electrical - 43rd / 12th to 11th (N)	3	3	0	0	3	3	15-Sep-25	17-Sep-25	-17	-11	-6	-6	☐
1-SW-0138	Grade Sidewalks - 43rd / 12th to 11th (N)	2	2	0	0	2	2	18-Sep-25	19-Sep-25	-17	-11	-6	-6	☐
1-SW-0139	Pour Sidewalks/Curb Ramps - 43rd / 12th to 11th (N)	4	4	0	0	4	4	22-Sep-25	25-Sep-25	-14	-8	-6	-6	☐

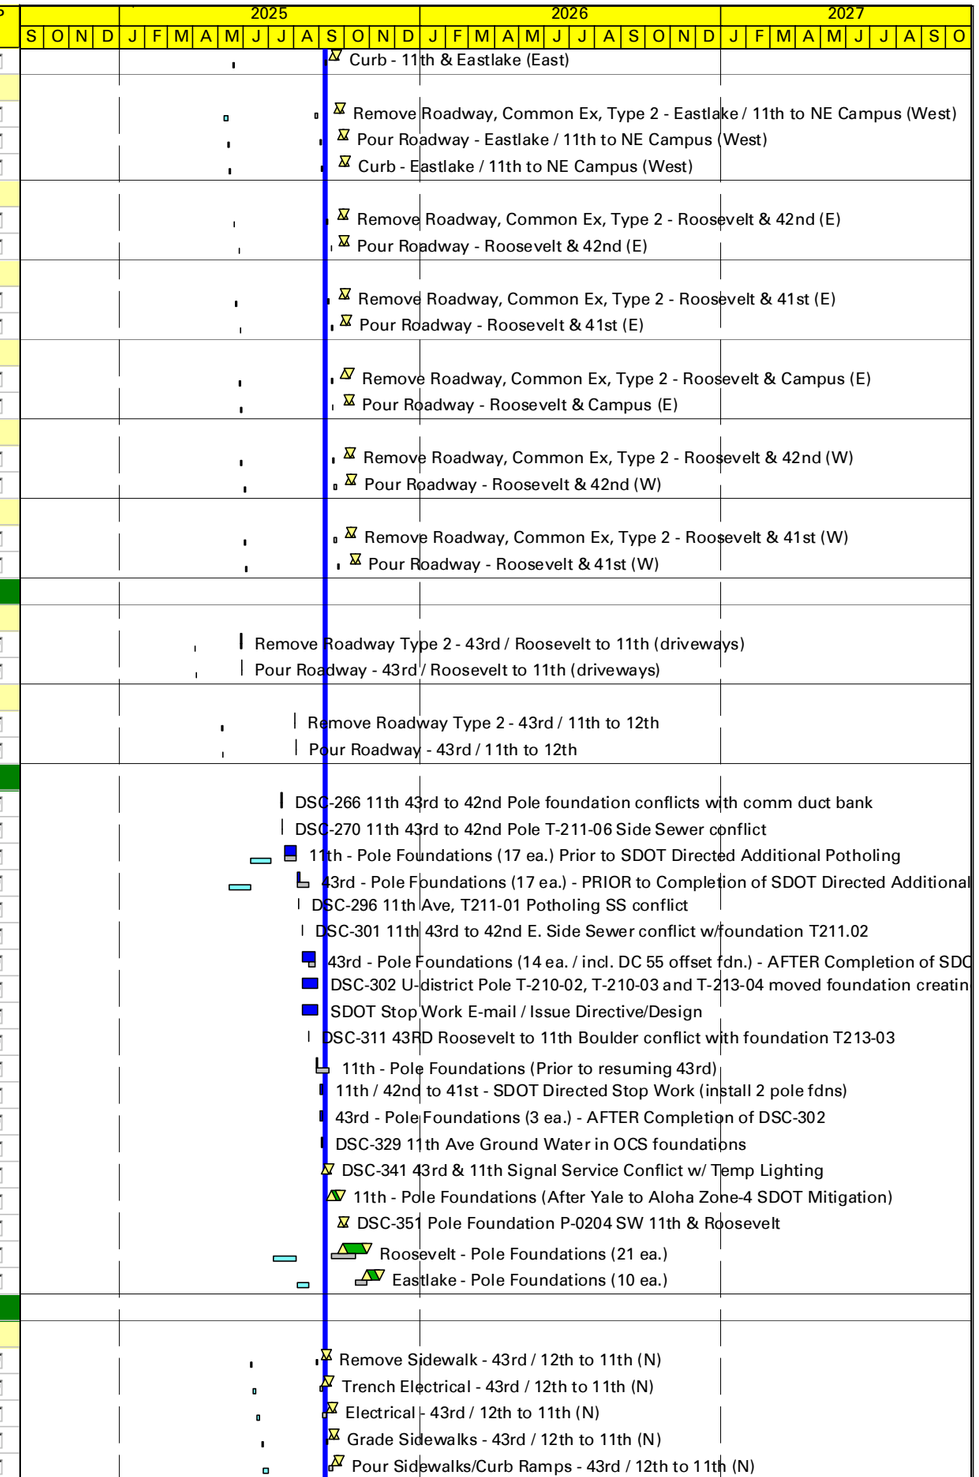

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
43rd 11th to Roosevelt North Side														
1-SW-0141	Remove Sidewalk - 43rd / 11th to Roosevelt (N)	1	1	0	0	1	1	15-Sep-25	15-Sep-25	-22	-16	-6	-6	☑
1-SW-0142	Trench Electrical - 43rd / 11th to Roosevelt (N)	2	2	0	0	2	2	16-Sep-25	17-Sep-25	-22	-16	-6	-6	☑
1-SW-0143	Electrical - 43rd / 11th to Roosevelt (N)	7	7	0	0	7	7	18-Sep-25	26-Sep-25	-22	-16	-6	-6	☑
1-SW-0144	Grade Sidewalks - 43rd / 11th to Roosevelt (N)	2	2	0	0	2	2	29-Sep-25	30-Sep-25	-22	-16	-6	-6	☑
1-SW-0145	Pour Sidewalks/Curb Ramps - 43rd / 11th to Roosevelt (N)	6	6	0	0	6	6	01-Oct-25	08-Oct-25	-17	-11	-6	-6	☐
Design Change 055 - Sidewalks 11th Ave. / 43rd to 45th East Side														
1-SW-DC-055A	Remove Sidewalk - 11th; 43rd to 45th (E) DC-055	2	2	0	0	2	2	01-Oct-25	02-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055B	Trench Electrical - 11th; 43rd to 45th (E) DC-055	5	5	0	0	5	5	03-Oct-25	09-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055C	Electrical - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	08-Oct-25	14-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055D	Grade Sidewalks - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	10-Oct-25	16-Oct-25	-22	-16	-6	-6	☑
1-SW-DC-055E	Pour Sidewalks/Curb Ramps - 11th; 43rd to 45th (E) DC-055	4	4	0	0	4	4	17-Oct-25	22-Oct-25	-22	-16	-6	-6	☑
11th and 42nd NEC														
1-SW-0147	Remove Sidewalk - 11th & 42nd NEC	2	2	0	0	2	2	23-Oct-25	24-Oct-25	-22	-16	-6	-6	☑
1-SW-0148	Trench Electrical - 11th & 42nd NEC	2	2	0	0	2	2	27-Oct-25	28-Oct-25	-22	-16	-6	-6	☑
1-SW-0149	Electrical - 11th & 42nd NEC	3	3	0	0	3	3	29-Oct-25	31-Oct-25	-14	-8	-6	-6	☐
1-SW-0150	Grade Sidewalks - 11th & 42nd NEC	1	1	0	0	1	1	03-Nov-25	03-Nov-25	-14	-8	-6	-6	☐
1-SW-0151	Pour Sidewalks/Curb Ramps - 11th & 42nd NEC	3	3	0	0	3	3	04-Nov-25	06-Nov-25	-14	-8	-6	-6	☐
11th and 42nd SEC														
1-SW-0153	Remove Sidewalk - 11th & 42nd SEC	2	2	0	0	2	2	29-Oct-25	30-Oct-25	-22	-16	-6	-6	☑
1-SW-0154	Trench Electrical - 11th & 42nd SEC	2	2	0	0	2	2	31-Oct-25	03-Nov-25	-22	-16	-6	-6	☑
1-SW-0155	Electrical - 11th & 42nd SEC	5	5	0	0	5	5	04-Nov-25	10-Nov-25	-17	-11	-6	-6	☐
1-SW-0156	Grade Sidewalks - 11th & 42nd SEC	1	1	0	0	1	1	12-Nov-25	12-Nov-25	-17	-11	-6	-6	☐
1-SW-0157	Pour Sidewalks/Curb Ramps - 11th & 42nd SEC	3	3	0	0	3	3	13-Nov-25	17-Nov-25	-17	-11	-6	-6	☐
11th and Eastlake East Side														
1-SW-0159	Remove Sidewalk - 11th & Eastlake ()	2	2	0	0	2	2	04-Nov-25	05-Nov-25	-22	-16	-6	-6	☑
1-SW-0160	Grade Sidewalks - 11th & Eastlake ()	2	2	0	0	2	2	06-Nov-25	07-Nov-25	-22	-16	-6	-6	☑
1-SW-0161	Pour Sidewalks/Curb Ramps - 11th & Eastlake ()	2	2	0	0	2	2	18-Nov-25	19-Nov-25	-17	-11	-6	-6	☐
43rd 12th to 11th South Side														
1-SW-0163	Remove Sidewalk - 43rd / 12th to 11th (S)	2	2	0	0	2	2	10-Nov-25	12-Nov-25	-22	-16	-6	-6	☑
1-SW-0164	Trench Electrical - 43rd / 12th to 11th (S)	3	3	0	0	3	3	13-Nov-25	17-Nov-25	-22	-16	-6	-6	☑
1-SW-0165	Electrical - 43rd / 12th to 11th (S)	5	5	0	0	5	5	18-Nov-25	24-Nov-25	-21	-15	-6	-6	☐
1-SW-0166	Grade Sidewalks - 43rd / 12th to 11th (S)	1	1	0	0	1	1	25-Nov-25	25-Nov-25	-21	-15	-6	-6	☐
1-SW-0167	Pour Sidewalks/Curb Ramps - 43rd / 12th to 11th (S)	4	4	0	0	4	4	26-Nov-25	03-Dec-25	-21	-15	-6	-6	☐
43rd 11th to Roosevelt South Side														
1-SW-0169	Remove Sidewalk - 43rd / 11to to Roosevelt (S)	1	1	0	0	1	1	18-Nov-25	18-Nov-25	-22	-16	-6	-6	☑
1-SW-0170	Trench Electrical - 43rd / 11to to Roosevelt (S)	2	2	0	0	2	2	19-Nov-25	20-Nov-25	-22	-16	-6	-6	☑
1-SW-0171	Electrical - 43rd / 11to to Roosevelt (S)	6	6	0	0	6	6	21-Nov-25	02-Dec-25	-22	-16	-6	-6	☑
1-SW-0172	Grade Sidewalks - 43rd / 11to to Roosevelt (S)	2	2	0	0	2	2	03-Dec-25	04-Dec-25	-22	-16	-6	-6	☑
1-SW-0173	Pour Sidewalks/Curb Ramps - 43rd / 11to to Roosevelt (S)	5	5	0	0	5	5	05-Dec-25	11-Dec-25	-22	-16	-6	-6	☑
11th and 42nd NWC														
1-SW-0175	Remove Sidewalk - 11th & 42nd NWC	1	1	0	0	1	1	21-Nov-25	21-Nov-25	-22	-16	-6	-6	☑
1-SW-0176	Trench Electrical - 11th & 42nd NWC	2	2	0	0	2	2	24-Nov-25	25-Nov-25	-22	-16	-6	-6	☑
1-SW-0177	Electrical - 11th & 42nd NWC	4	4	0	0	4	4	26-Nov-25	03-Dec-25	-17	-11	-6	-6	☐
1-SW-0178	Grade Sidewalks - 11th & 42nd NWC	1	1	0	0	1	1	04-Dec-25	04-Dec-25	-17	-11	-6	-6	☐
1-SW-0179	Pour Sidewalks/Curb Ramps - 11th & 42nd NWC	4	4	0	0	4	4	12-Dec-25	17-Dec-25	-22	-16	-6	-6	☑
11th and 42nd SWC														
1-SW-0181	Remove Sidewalk 11th & 42nd SWC	1	1	0	0	1	1	26-Nov-25	26-Nov-25	-22	-16	-6	-6	☑
1-SW-0182	Trench Electrical 11th & 42nd SWC	2	2	0	0	2	2	01-Dec-25	02-Dec-25	-22	-16	-6	-6	☑
1-SW-0183	Electrical 11th & 42nd SWC	4	4	0	0	4	4	03-Dec-25	08-Dec-25	-22	-16	-6	-6	☑
1-SW-0184	Grade Sidewalks 11th & 42nd SWC	1	1	0	0	1	1	09-Dec-25	09-Dec-25	-22	-16	-6	-6	☑
1-SW-0185	Pour Sidewalks/Curb Ramps - 11th & 42nd SWC	4	4	0	0	4	4	18-Dec-25	23-Dec-25	-22	-16	-6	-6	☑
Roosevelt and 43rd West Side														
1-SW-0187	Remove Sidewalk - Roosevelt & 43rd (W)	1	1	0	0	1	1	10-Dec-25	10-Dec-25	-22	-16	-6	-6	☑

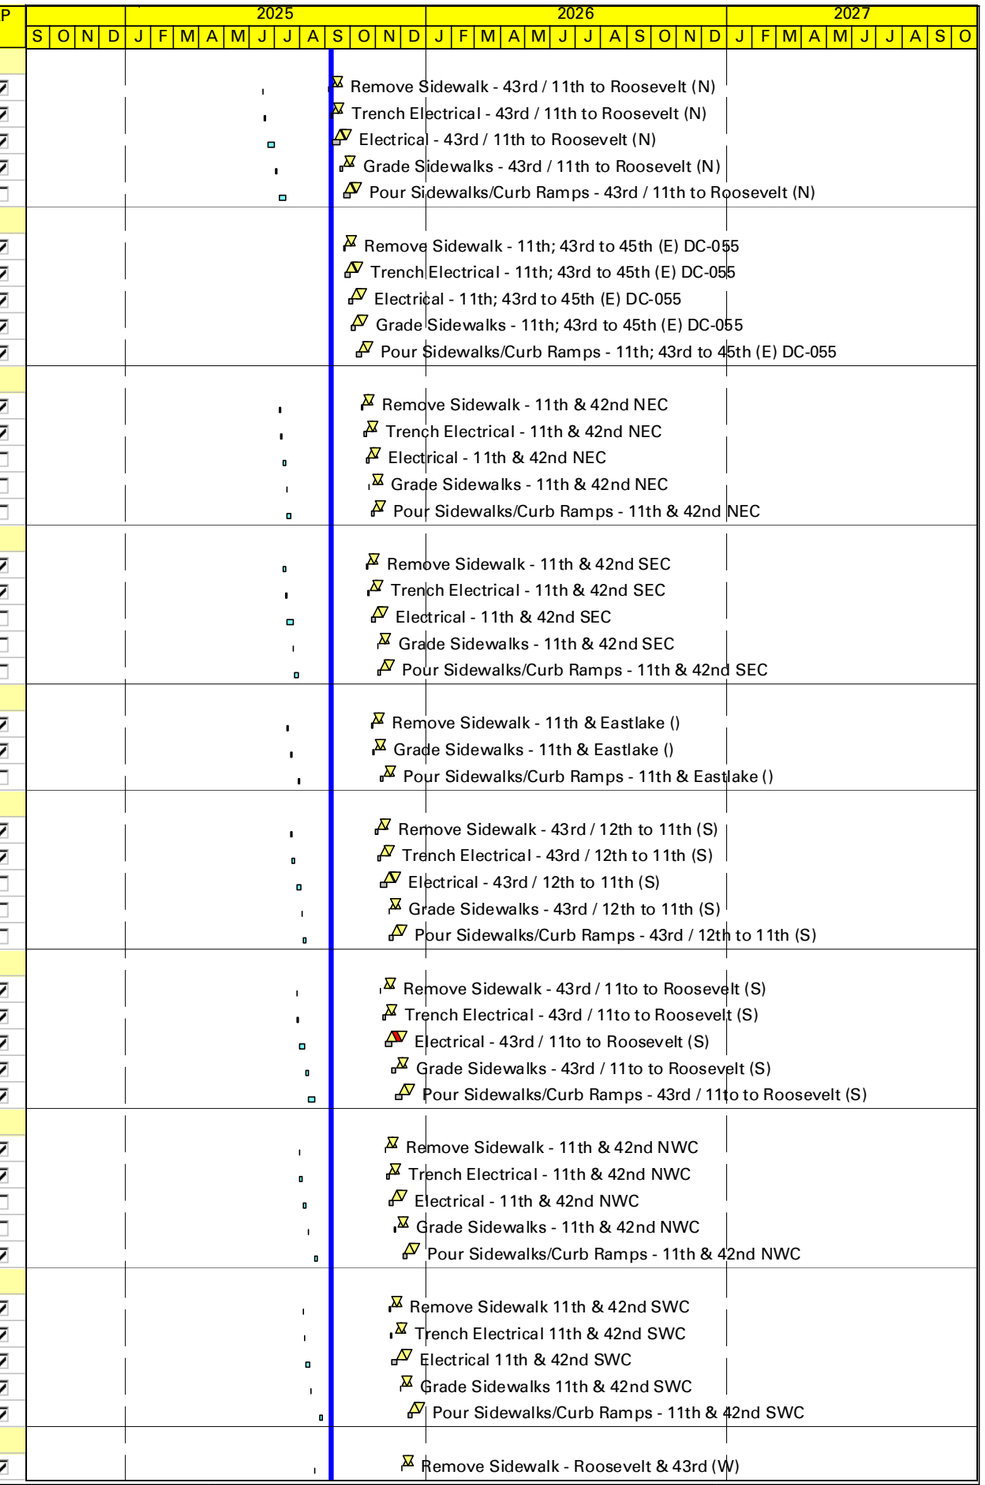

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort; BL1 LOE; BL2 LOE; Actual Level of Effort; Actual Work; Remaining Work; Critical Remaining Work; Milestone; Previous MS; Previous Bar; Baseline MS; Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-SW-0188	Trench Electrical - Roosevelt & 43rd (W)	2	2	0	0	2	2	11-Dec-25	12-Dec-25	-22	-16	-6	-6	☑
1-SW-0189	Electrical - Roosevelt & 43rd (W)	5	5	0	0	5	5	15-Dec-25	19-Dec-25	-22	-16	-6	-6	☑
1-SW-0190	Grade Sidewalks - Roosevelt & 43rd (W)	2	2	0	0	2	2	22-Dec-25	23-Dec-25	-22	-16	-6	-6	☑
1-SW-0191	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd (W)	4	4	0	0	4	4	24-Dec-25	30-Dec-25	-22	-16	-6	-6	☑
Roosevelt and 43rd NWC														
1-SW-0193	Remove Sidewalk - Roosevelt & 43rd NWC	1	1	0	0	1	1	15-Dec-25	15-Dec-25	-22	-16	-6	-6	☑
1-SW-0194	Trench Electrical - Roosevelt & 43rd NWC	1	1	0	0	1	1	16-Dec-25	16-Dec-25	-22	-16	-6	-6	☑
1-SW-0195	Electrical - Roosevelt & 43rd NWC	3	3	0	0	3	3	17-Dec-25	19-Dec-25	-22	-16	-6	-6	☑
1-SW-0196	Grade Sidewalks - Roosevelt & 43rd NWC	1	1	0	0	1	1	22-Dec-25	22-Dec-25	-22	-16	-6	-6	☑
1-SW-0197	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd NWC	3	3	0	0	3	3	23-Dec-25	26-Dec-25	-22	-16	-6	-6	☑
Roosevelt and 43rd SWC														
1-SW-0199	Remove Sidewalk - Roosevelt & 43rd SWC	1	1	0	0	1	1	29-Dec-25	29-Dec-25	-22	-16	-6	-6	☑
1-SW-0200	Grade Sidewalks - Roosevelt & 43rd SWC	1	1	0	0	1	1	30-Dec-25	30-Dec-25	-22	-16	-6	-6	☑
1-SW-0201	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd SWC	3	3	0	0	3	3	31-Dec-25	05-Jan-26	-22	-16	-6	-6	☑
Roosevelt and 42nd NWC														
1-SW-0203	Remove Sidewalk - Roosevelt & 42nd NWC	1	1	0	0	1	1	06-Jan-26	06-Jan-26	-22	-16	-6	-6	☑
1-SW-0204	Trench Electrical - Roosevelt & 42nd NWC	1	1	0	0	1	1	07-Jan-26	07-Jan-26	-22	-16	-6	-6	☑
1-SW-0205	Electrical - Roosevelt & 42nd NWC	4	4	0	0	4	4	08-Jan-26	13-Jan-26	-22	-16	-6	-6	☑
1-SW-0206	Grade Sidewalks - Roosevelt & 42nd NWC	1	1	0	0	1	1	14-Jan-26	14-Jan-26	-22	-16	-6	-6	☑
1-SW-0207	Pour Sidewalks/Curb Ramps - Roosevelt & 42nd NWC	1	1	0	0	1	1	15-Jan-26	15-Jan-26	-22	-16	-6	-6	☑
Roosevelt and 42nd SEC														
1-SW-0209	Remove Sidewalk - Roosevelt & 42nd SEC	1	1	0	0	1	1	08-Jan-26	08-Jan-26	-21	-15	-6	-6	☐
1-SW-0210	Trench Electrical - Roosevelt & 42nd SEC	1	1	0	0	1	1	09-Jan-26	09-Jan-26	-21	-15	-6	-6	☐
1-SW-0211	Electrical - Roosevelt & 42nd SEC	2	2	0	0	2	2	12-Jan-26	13-Jan-26	-21	-15	-6	-6	☐
1-SW-0212	Grade Sidewalks - Roosevelt & 42nd SEC	1	1	0	0	1	1	14-Jan-26	14-Jan-26	-21	-15	-6	-6	☐
1-SW-0213	Pour Sidewalks/Curb Ramps - Roosevelt & 42nd SEC	3	3	0	0	3	3	16-Jan-26	21-Jan-26	-22	-16	-6	-6	☑
Roosevelt and 43rd SEC														
1-SW-0215	Remove Sidewalk - Roosevelt & 43rd SEC	1	1	0	0	1	1	22-Jan-26	22-Jan-26	-22	-16	-6	-6	☑
1-SW-0216	Trench Electrical - Roosevelt & 43rd SEC	2	2	0	0	2	2	23-Jan-26	26-Jan-26	-22	-16	-6	-6	☑
1-SW-0217	Electrical - Roosevelt & 43rd SEC	5	5	0	0	5	5	27-Jan-26	02-Feb-26	-22	-16	-6	-6	☑
1-SW-0218	Grade Sidewalks - Roosevelt & 43rd SEC	2	2	0	0	2	2	03-Feb-26	04-Feb-26	-22	-16	-6	-6	☑
1-SW-0219	Pour Sidewalks/Curb Ramps - Roosevelt & 43rd SEC	4	4	0	0	4	4	05-Feb-26	10-Feb-26	-17	-11	-6	-6	☐
Roosevelt and 42nd NEC														
1-SW-0221	Remove Sidewalk - Roosevelt & 42nd NEC	2	2	0	0	2	2	27-Jan-26	28-Jan-26	-20	-14	-6	-6	☐
1-SW-0222	Trench Electrical - Roosevelt & 42nd NEC	3	3	0	0	3	3	29-Jan-26	02-Feb-26	-20	-14	-6	-6	☐
1-SW-0223	Electrical - Roosevelt & 42nd NEC	7	7	0	0	7	7	05-Feb-26	13-Feb-26	-22	-16	-6	-6	☑
1-SW-0224	Grade Sidewalks - Roosevelt & 42nd NEC	2	2	0	0	2	2	17-Feb-26	18-Feb-26	-22	-16	-6	-6	☑
1-SW-0225	Pour Sidewalks/Curb Ramps - Roosevelt & 42nd NEC	5	5	0	0	5	5	19-Feb-26	25-Feb-26	-22	-16	-6	-6	☑
Roosevelt and 42nd SEC #2														
1-SW-0227	Remove Sidewalk - Roosevelt & 42nd SEC	2	2	0	0	2	2	26-Feb-26	27-Feb-26	-22	-16	-6	-6	☑
1-SW-0228	Trench Electrical - Roosevelt & 42nd SEC	3	3	0	0	3	3	02-Mar-26	04-Mar-26	-22	-16	-6	-6	☑
1-SW-0229	Electrical - Roosevelt & 42nd SEC	7	7	0	0	7	7	05-Mar-26	13-Mar-26	-22	-16	-6	-6	☑
1-SW-0230	Grade Sidewalks - Roosevelt & 42nd SEC	2	2	0	0	2	2	16-Mar-26	17-Mar-26	-22	-16	-6	-6	☑
1-SW-0231	Pour Sidewalks/Curb Ramps - Roosevelt & 42nd SEC	5	5	0	0	5	5	18-Mar-26	24-Mar-26	-22	-16	-6	-6	☑
Roosevelt and 41st NEC														
1-SW-0233	Remove Sidewalk - Roosevelt & 41st NEC	2	2	0	0	2	2	05-Mar-26	06-Mar-26	-22	-16	-6	-6	☑
1-SW-0234	Trench Electrical - Roosevelt & 41st NEC	3	3	0	0	3	3	09-Mar-26	11-Mar-26	-22	-16	-6	-6	☑
1-SW-0235	Electrical - Roosevelt & 41st NEC	7	7	0	0	7	7	12-Mar-26	20-Mar-26	-22	-16	-6	-6	☑
1-SW-0236	Grade Sidewalks - Roosevelt & 41st NEC	2	2	0	0	2	2	23-Mar-26	24-Mar-26	-22	-16	-6	-6	☑
1-SW-0237	Pour Sidewalks/Curb Ramps - Roosevelt & 41st NEC	5	5	0	0	5	5	25-Mar-26	31-Mar-26	-22	-16	-6	-6	☑
41st Roosevelt to 11th South Side														
1-SW-0239	Remove Sidewalk 41st / Roosevelt to 11th (S)	2	2	0	0	2	2	12-Mar-26	13-Mar-26	-15	-9	-6	-6	☐
1-SW-0240	Trench Electrical 41st / Roosevelt to 11th (S)	3	3	0	0	3	3	16-Mar-26	18-Mar-26	-15	-9	-6	-6	☐
1-SW-0241	Electrical 41st / Roosevelt to 11th (S)	7	7	0	0	7	7	19-Mar-26	27-Mar-26	-15	-9	-6	-6	☐

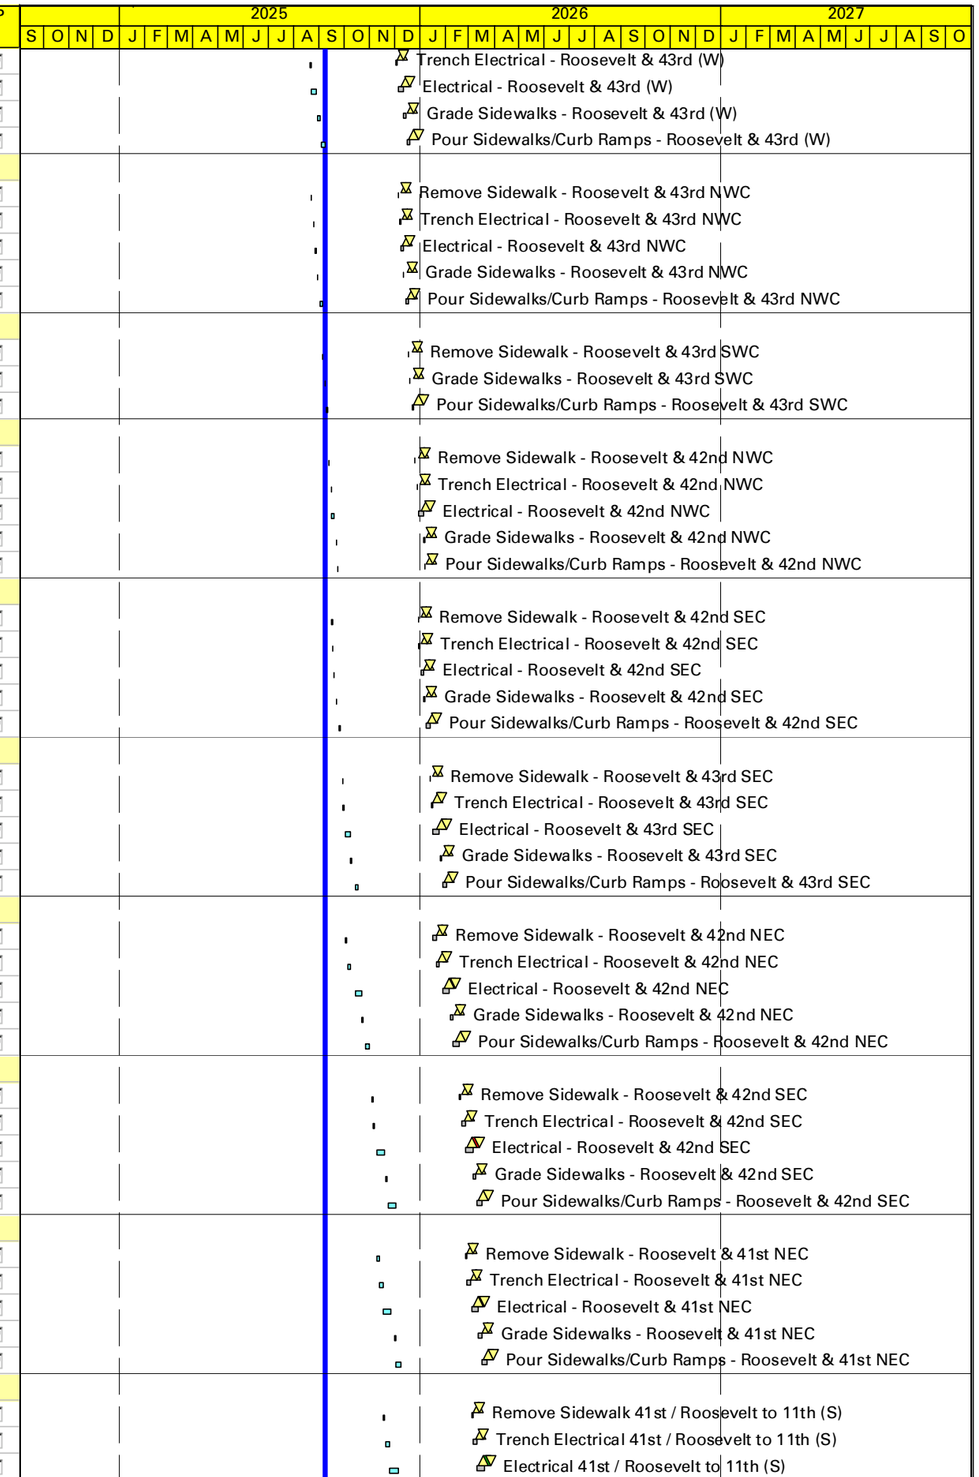

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-SW-0242	Grade Sidewalks 41st / Roosevelt to 11th (S)	2	2	0	0	2	2	30-Mar-26	31-Mar-26	-15	-9	-6	-6	☐
1-SW-0243	Pour Sidewalks/Curb Ramps - 41st / Roosevelt to 11th (S)	5	5	0	0	5	5	01-Apr-26	07-Apr-26	-15	-9	-6	-6	☐
41st Station SB Hardscapes														
1-SW-0245	Remove Sidewalk - 41st Station SB	1	1	0	0	1	1	08-Apr-26	08-Apr-26	-15	-9	-6	-6	☐
1-SW-0246	Excavate Foundations - 41st Station SB	1	1	0	0	1	1	09-Apr-26	09-Apr-26	-15	-9	-6	-6	☐
1-SW-0247	Trench Electrical - 41st Station SB	3	3	0	0	3	3	10-Apr-26	14-Apr-26	-15	-9	-6	-6	☐
1-SW-0248	Install Electrical - 41st Station SB	8	8	0	0	8	8	15-Apr-26	24-Apr-26	-15	-9	-6	-6	☐
1-SW-0249	Form Foundations - 41st Station SB	1	1	0	0	1	1	27-Apr-26	27-Apr-26	-15	-9	-6	-6	☐
1-SW-0250	Install Rebar - 41st Station SB	1	1	0	0	1	1	28-Apr-26	28-Apr-26	-15	-9	-6	-6	☐
1-SW-0251	Pour Foundations - 41st Station SB	2	2	0	0	2	2	29-Apr-26	30-Apr-26	-15	-9	-6	-6	☐
1-SW-0252	Grade Station Hardscapes - 41st Station SB	2	2	0	0	2	2	01-May-26	04-May-26	-15	-9	-6	-6	☐
1-SW-0253	Pour Hardscapes - 41st Station SB	4	4	0	0	4	4	05-May-26	08-May-26	-6	0	-6	-6	☐
41st Station NB Hardscapes														
1-SW-0255	Remove Roadway - 41st Station NB	1	1	0	0	1	1	05-May-26	05-May-26	-15	-9	-6	-6	☐
1-SW-0256	Excavate Foundations - 41st Station NB	1	1	0	0	1	1	06-May-26	06-May-26	-15	-9	-6	-6	☐
1-SW-0257	Trench Electrical - 41st Station NB	3	3	0	0	3	3	07-May-26	11-May-26	-15	-9	-6	-6	☐
1-SW-0258	Install Electrical - 41st Station NB	8	8	0	0	8	8	12-May-26	21-May-26	-15	-9	-6	-6	☐
1-SW-0259	Form Foundations - 41st Station NB	1	1	0	0	1	1	22-May-26	22-May-26	-15	-9	-6	-6	☐
1-SW-0260	Install Rebar - 41st Station NB	1	1	0	0	1	1	26-May-26	26-May-26	-15	-9	-6	-6	☐
1-SW-0261	Pour Foundations - 41st Station NB	1	1	0	0	1	1	27-May-26	27-May-26	-15	-9	-6	-6	☐
1-SW-0262	Grade Station Hardscapes - 41st Station NB	5	5	0	0	5	5	28-May-26	03-Jun-26	-15	-9	-6	-6	☐
1-SW-0263	Pour Hardscapes - 41st Station NB	15	15	0	0	15	15	04-Jun-26	21-Jul-26	-15	-9	-6	-6	☐
1-SW-0264	Handrail Shop Drawings - 41st Station NB	20	20	0	0	20	20	22-Jul-26	18-Aug-26	64	70	-6	-6	☐
1-SW-0265	Fabricate Handrail - 41st Station NB	60	60	0	0	60	60	19-Aug-26	13-Nov-26	64	70	-6	-6	☐
1-SW-0266	Install Handrail - 41st Station NB	4	4	0	0	4	4	16-Nov-26	19-Nov-26	64	70	-6	-6	☐
Weekend Driveway														
Driveways 11th / 43rd to 45th (DC-055)														
1-WE-DC-055A	Remove Sidewalk - 11th; 43rd to 45th (E) DC-055	1	1	0	0	1	1	25-Oct-25	25-Oct-25	30	32	-2	-2	☐
1-WE-DC-055B	Pour Driveway - 11th; 43rd to 45th (E) DC055	1	1	0	0	1	1	26-Oct-25	26-Oct-25	30	32	-2	-2	☐
43rd Roosevelt to 11th														
1-WE-0269	Remove Sidewalk - 43rd / Roosevelt to 11th (driveway)	1	1	0	0	1	1	13-Dec-25	13-Dec-25	18	20	-2	-2	☐
1-WE-0270	Pour Driveway - 43rd / Roosevelt to 11th (driveway)	1	1	0	0	1	1	14-Dec-25	14-Dec-25	18	20	-2	-2	☐
43rd 11th to 12th														
1-WE-0272	Remove Sidewalk - 43rd / 11th to 12th	1	1	0	0	1	1	20-Dec-25	20-Dec-25	18	20	-2	-2	☐
1-WE-0273	Pour Driveway - 43rd / 11th to 12th	1	1	0	0	1	1	21-Dec-25	21-Dec-25	18	20	-2	-2	☐
Roosevelt 42nd East to 42nd West East Side														
1-WE-0275	Remove Sidewalk - Roosevelt / 42nd E to 42nd W (E)	1	1	0	0	1	1	04-Apr-26	04-Apr-26	-10	-8	-2	-2	☑
1-WE-0276	Pour Driveway - Roosevelt / 42nd E to 42nd W (E)	1	1	0	0	1	1	05-Apr-26	05-Apr-26	-10	-8	-2	-2	☑
Lanscaping-Irrigation														
1-LS-0279	Install Irrigation - Zone 1	10	10	0	0	10	10	22-Jul-26	04-Aug-26	118	124	-6	-6	☐
1-LS-0280	Trees and Shrubs - Zone 1	20	20	0	0	20	20	01-Oct-26	29-Oct-26	78	78	0	0	☐
SCL Services - Zone 1														
43rd and Roosevelt SDOT Signal Service														
1-SCL-0283	Install Meter Cabinet - 43rd & Roosevelt Signal	1	1	0	0	1	1	06-Apr-26	06-Apr-26	-25	-20	-5	-5	☑
1-SCL-0284	SDOT Inspection - 43rd & Roosevelt Signal	5	5	0	0	5	5	07-Apr-26	13-Apr-26	-25	-20	-5	-5	☑
1-SCL-0285	SDCI Inspection - 43rd & Roosevelt Signal	5	5	0	0	5	5	14-Apr-26	20-Apr-26	-25	-20	-5	-5	☑
1-SCL-0286	SCL Inspection - 43rd & Roosevelt Signal	21	21	0	0	21	21	21-Apr-26	19-May-26	-25	-20	-5	-5	☑
1-SCL-0287	SCL Heat Up Cabinet - 43rd & Roosevelt Signal	21	21	0	0	21	21	20-May-26	15-Jul-26	-25	-20	-5	-5	☑
1-SCL-0288	Remove Old Service Gear - 43rd & Roosevelt Signal	1	1	0	0	1	1	16-Jul-26	16-Jul-26	-25	-20	-5	-5	☑
43rd and 11th SDOT Signal Service														
1-SCL-0290	Install Meter Cabinet - 43rd & 11th Signal	1	1	0	0	1	1	04-Dec-25	04-Dec-25	92	98	-6	-6	☐
1-SCL-0291	SDOT Inspection - 43rd & 11th Signal	5	5	0	0	5	5	05-Dec-25	11-Dec-25	92	98	-6	-6	☐
1-SCL-0292	SDCI Inspection - 43rd & 11th Signal	5	5	0	0	5	5	12-Dec-25	18-Dec-25	92	98	-6	-6	☐
1-SCL-0293	SCL Inspection - 43rd & 11th Signal	21	21	0	0	21	21	19-Dec-25	21-Jan-26	92	98	-6	-6	☐

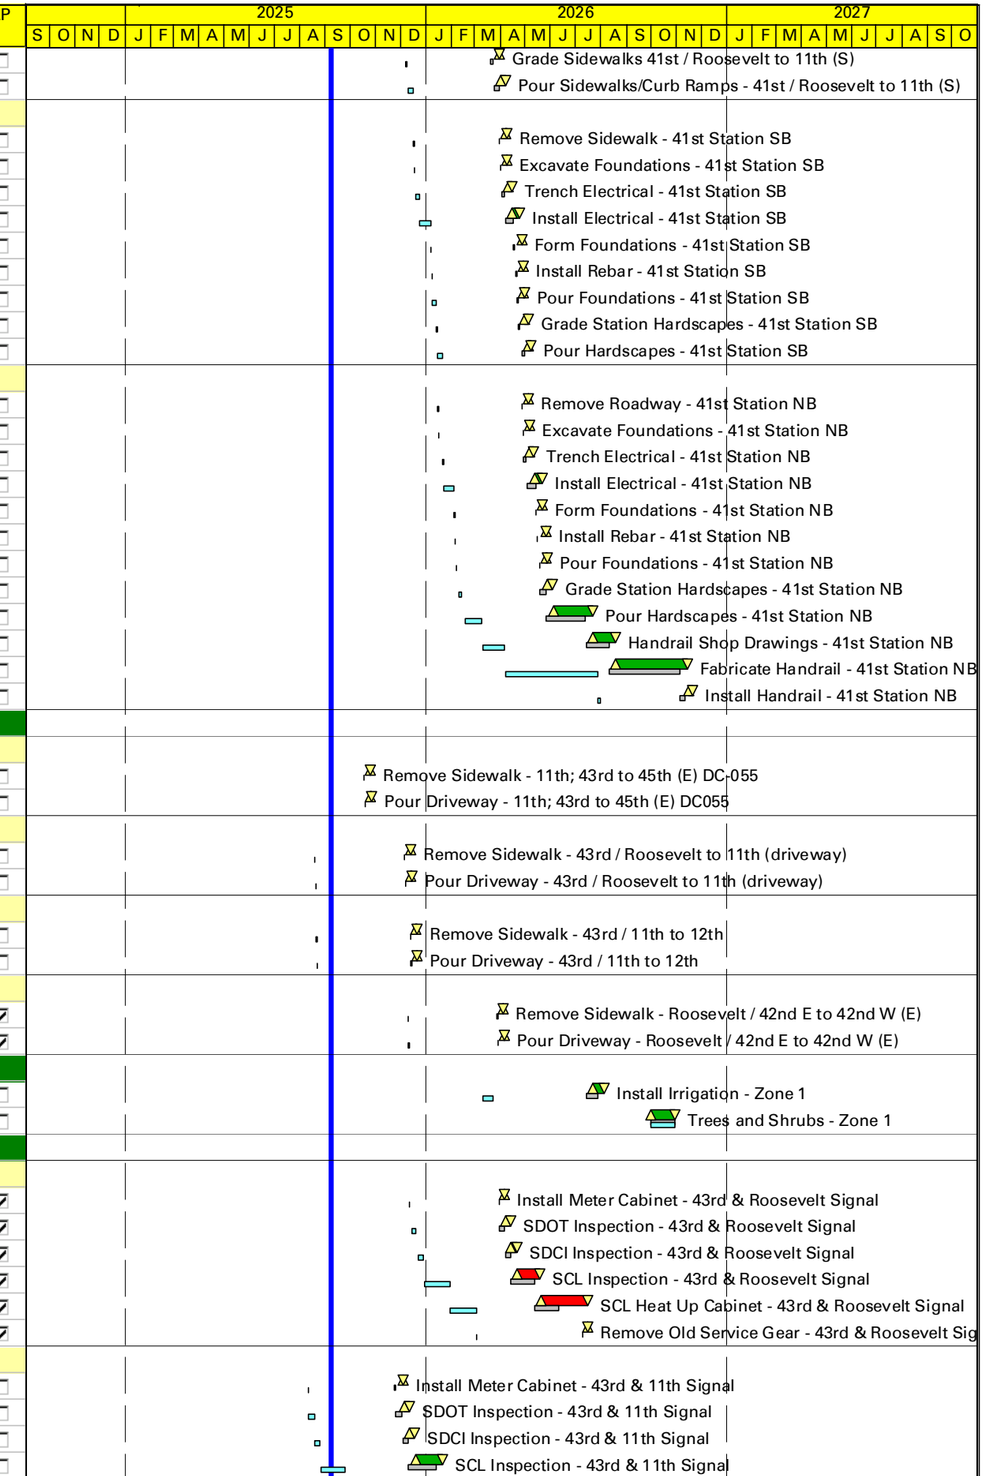

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work | BL1 LOE | Milestone | BL2 LOE | Previous MS | Actual Level of Effort | Previous Bar | Actual Work | Baseline MS | Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-SCL-0294	SCL Heat Up Cabinet - 43rd & 11th Signal	21	21	0	0	21	21	22-Jan-26	20-Feb-26	92	98	-6	-6	☐
1-SCL-0295	Remove Old Service Gear - 43rd & 11th Signal	1	1	0	0	1	1	23-Feb-26	23-Feb-26	92	98	-6	-6	☐
42nd and 11th SDOT Service														
1-SCL-0297	Install Meter Cabinet - 42nd & 11th	1	1	0	0	1	1	18-Nov-25	18-Nov-25	127	133	-6	-6	☐
1-SCL-0298	SDOT Inspection - 42nd & 11th	5	5	0	0	5	5	19-Nov-25	25-Nov-25	127	133	-6	-6	☐
1-SCL-0299	SDCI Inspection - 42nd & 11th	5	5	0	0	5	5	26-Nov-25	04-Dec-25	127	133	-6	-6	☐
1-SCL-0300	SCL Inspection - 42nd & 11th	21	21	0	0	21	21	05-Dec-25	06-Jan-26	127	133	-6	-6	☐
1-SCL-0301	SCL Heat Up Cabinet - 42nd & 11th	21	21	0	0	21	21	07-Jan-26	05-Feb-26	127	133	-6	-6	☐
1-SCL-0302	Remove Old Service Gear - 42nd & 11th	1	1	0	0	1	1	06-Feb-26	06-Feb-26	127	133	-6	-6	☐
42nd East and Roosevelt SDOT Service														
1-SCL-0304	Install Meter Cabinet - 42nd E & Roosevelt	1	1	0	0	1	1	16-Jan-26	16-Jan-26	35	41	-6	-6	☐
1-SCL-0305	SDOT Inspection - 42nd E & Roosevelt	5	5	0	0	5	5	20-Jan-26	26-Jan-26	35	41	-6	-6	☐
1-SCL-0306	SDCI Inspection - 42nd E & Roosevelt	5	5	0	0	5	5	27-Jan-26	02-Feb-26	35	41	-6	-6	☐
1-SCL-0307	SCL Inspection - 42nd E & Roosevelt	21	21	0	0	21	21	03-Feb-26	04-Mar-26	35	41	-6	-6	☐
1-SCL-0308	SCL Heat Up Cabinet - 42nd E & Roosevelt	21	21	0	0	21	21	05-Mar-26	02-Apr-26	35	41	-6	-6	☐
1-SCL-0309	Remove Old Service Gear - 42nd E & Roosevelt	1	1	0	0	1	1	03-Apr-26	03-Apr-26	35	41	-6	-6	☐
42nd West and Roosevelt SDOT Service														
1-SCL-0311	Install Meter Cabinet - 42nd W & Roosevelt	1	1	0	0	1	1	25-Mar-26	25-Mar-26	-10	-4	-6	-6	☐
1-SCL-0312	SDOT Inspection - 42nd W & Roosevelt	5	5	0	0	5	5	26-Mar-26	01-Apr-26	-10	-4	-6	-6	☐
1-SCL-0313	SDCI Inspection - 42nd W & Roosevelt	5	5	0	0	5	5	02-Apr-26	08-Apr-26	-10	-4	-6	-6	☐
1-SCL-0314	SCL Inspection - 42nd W & Roosevelt	21	21	0	0	21	21	09-Apr-26	07-May-26	-10	-4	-6	-6	☐
1-SCL-0315	SCL Heat Up Cabinet - 42nd W & Roosevelt	21	21	0	0	21	21	08-May-26	08-Jun-26	-10	-4	-6	-6	☐
1-SCL-0316	Remove Old Service Gear - 42nd W & Roosevelt	1	1	0	0	1	1	09-Jun-26	09-Jun-26	-10	-4	-6	-6	☐
41st and Roosevelt SDOT Service														
1-SCL-0318	Install Meter Cabinet - 41st & Roosevelt	1	1	0	0	1	1	08-Apr-26	08-Apr-26	11	17	-6	-6	☐
1-SCL-0319	SDOT Inspection - 41st & Roosevelt	5	5	0	0	5	5	09-Apr-26	15-Apr-26	11	17	-6	-6	☐
1-SCL-0320	SDCI Inspection - 41st & Roosevelt	5	5	0	0	5	5	16-Apr-26	22-Apr-26	11	17	-6	-6	☐
1-SCL-0321	SCL Inspection - 41st & Roosevelt	21	21	0	0	21	21	23-Apr-26	21-May-26	11	17	-6	-6	☐
1-SCL-0322	SCL Heat Up Cabinet - 41st & Roosevelt	21	21	0	0	21	21	22-May-26	17-Jul-26	11	17	-6	-6	☐
1-SCL-0323	Remove Old Service Gear - 41st & Roosevelt	1	1	0	0	1	1	20-Jul-26	20-Jul-26	11	17	-6	-6	☐
Roosevelt and Eastlake SDOT Service														
1-SCL-0325	Install Meter Cabinet - Roosevelt & Eastlake	1	1	0	0	1	1	22-Jul-26	22-Jul-26	-15	-9	-6	-6	☐
1-SCL-0326	SDOT Inspection - Roosevelt & Eastlake	5	5	0	0	5	5	23-Jul-26	29-Jul-26	-15	-9	-6	-6	☐
1-SCL-0327	SDCI Inspection - Roosevelt & Eastlake	5	5	0	0	5	5	30-Jul-26	05-Aug-26	-15	-9	-6	-6	☐
1-SCL-0328	SCL Inspection - Roosevelt & Eastlake	21	21	0	0	21	21	06-Aug-26	03-Sep-26	-15	-9	-6	-6	☐
1-SCL-0329	SCL Heat Up Cabinet - Roosevelt & Eastlake	21	21	0	0	21	21	04-Sep-26	05-Oct-26	-15	-9	-6	-6	☐
1-SCL-0330	Remove Old Service Gear - Roosevelt & Eastlake	1	1	0	0	1	1	06-Oct-26	06-Oct-26	-15	-9	-6	-6	☐
SB 41st and Roosevelt KCM Service														
1-SCL-0332	Install Meter Cabinet - SB 41st & Roosevelt	1	1	0	0	1	1	11-May-26	11-May-26	46	52	-6	-6	☐
1-SCL-0333	KCM Inspection - SB 41st & Roosevelt	5	5	0	0	5	5	12-May-26	18-May-26	46	52	-6	-6	☐
1-SCL-0334	SDCI Inspection - SB 41st & Roosevelt	5	5	0	0	5	5	19-May-26	26-May-26	46	52	-6	-6	☐
1-SCL-0335	SCL Inspection - SB 41st & Roosevelt	21	21	0	0	21	21	27-May-26	21-Jul-26	46	52	-6	-6	☐
1-SCL-0336	SCL Heat Up Cabinet - SB 41st & Roosevelt	21	21	0	0	21	21	22-Jul-26	19-Aug-26	46	52	-6	-6	☐
1-SCL-0337	Remove Old Service Gear - SB 41st & Roosevelt	1	1	0	0	1	1	20-Aug-26	20-Aug-26	46	52	-6	-6	☐
NB 41st and Roosevelt KCM Service														
1-SCL-0339	Install Meter Cabinet - NB 41st & Roosevelt	1	1	0	0	1	1	22-Jul-26	22-Jul-26	25	31	-6	-6	☐
1-SCL-0340	KCM Inspection - NB 41st & Roosevelt	5	5	0	0	5	5	23-Jul-26	29-Jul-26	25	31	-6	-6	☐
1-SCL-0341	SDCI Inspection - NB 41st & Roosevelt	5	5	0	0	5	5	30-Jul-26	05-Aug-26	25	31	-6	-6	☐
1-SCL-0342	SCL Inspection - NB 41st & Roosevelt	21	21	0	0	21	21	06-Aug-26	03-Sep-26	25	31	-6	-6	☐
1-SCL-0343	SCL Heat Up Cabinet - NB 41st & Roosevelt	21	21	0	0	21	21	04-Sep-26	05-Oct-26	25	31	-6	-6	☐
1-SCL-0344	Remove Old Service Gear - NB 41st & Roosevelt	1	1	0	0	1	1	06-Oct-26	06-Oct-26	25	31	-6	-6	☐
Signals														
Roosevelt and 43rd														
1-SIG-0347	Install Poles - Roosevelt & 43rd Signal	4	4	0	0	4	4	17-Jul-26	22-Jul-26	-25	-20	-5	-5	☑

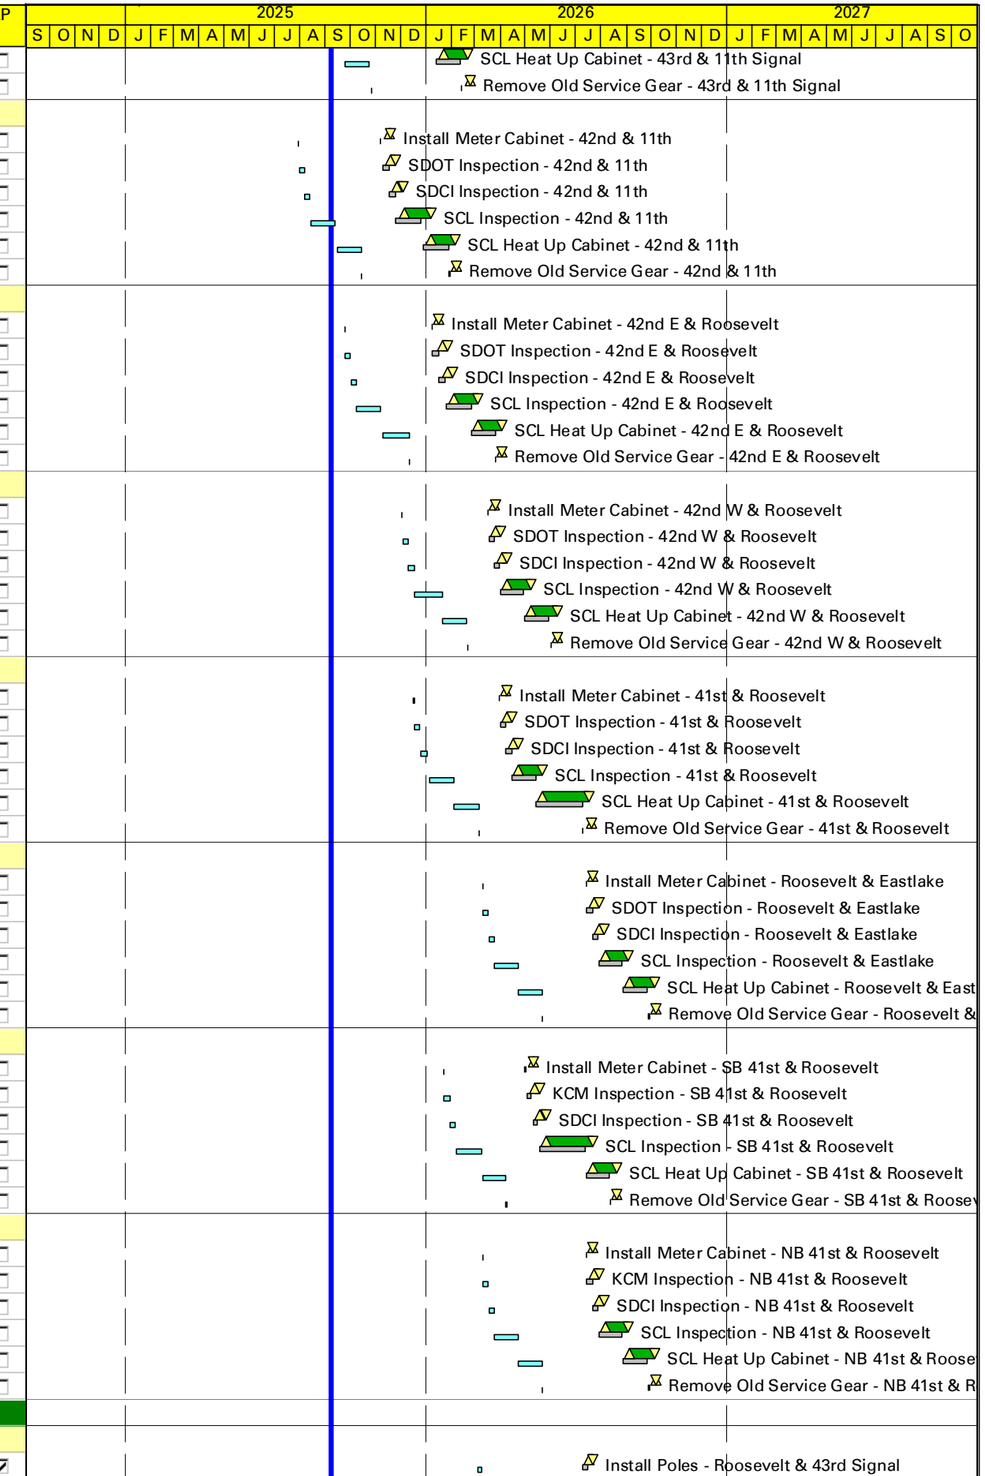

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-SIG-0348	Build Signal - Roosevelt & 43rd Signal	10	10	0	0	10	10	23-Jul-26	05-Aug-26	-25	-20	-5	-5	☑
1-SIG-0349	SDOT Inspection - Roosevelt & 43rd Signal	5	5	0	0	5	5	06-Aug-26	12-Aug-26	-25	-20	-5	-5	☑
1-SIG-0350	SDOT Commission - Roosevelt & 43rd Signal	10	10	0	0	10	10	13-Aug-26	26-Aug-26	-25	-20	-5	-5	☑
1-SIG-0351	Demo Old Signal & Temp Signal - Roosevelt & 43rd Signal	2	2	0	0	2	2	27-Aug-26	28-Aug-26	-25	-20	-5	-5	☑
11th and 43rd														
1-SIG-0353	Install Poles - 11th & 43rd Signal	3	3	0	0	3	3	31-Aug-26	02-Sep-26	-25	-20	-5	-5	☑
1-SIG-0354	Build Signal - 11th & 43rd Signal	12	12	0	0	12	12	03-Sep-26	21-Sep-26	-25	-20	-5	-5	☑
1-SIG-0355	SDOT Inspection - 11th & 43rd Signal	5	5	0	0	5	5	22-Sep-26	28-Sep-26	-25	-20	-5	-5	☑
1-SIG-0356	SDOT Commission - 11th & 43rd Signal	10	10	0	0	10	10	29-Sep-26	13-Oct-26	-25	-20	-5	-5	☑
1-SIG-0357	Demo Old Signal & Temp Signal - 11th & 43rd Signal	4	4	0	0	4	4	14-Oct-26	19-Oct-26	-25	-20	-5	-5	☑
42nd and 11th														
1-SIG-0359	Install Poles - 42nd & 11th Signal	3	3	0	0	3	3	22-Sep-26	24-Sep-26	-15	-10	-5	-5	☐
1-SIG-0360	Build Signal - 42nd & 11th Signal	12	12	0	0	12	12	25-Sep-26	13-Oct-26	-15	-10	-5	-5	☐
1-SIG-0361	SDOT Inspection - 42nd & 11th Signal	5	5	0	0	5	5	14-Oct-26	20-Oct-26	-15	-10	-5	-5	☐
1-SIG-0362	SDOT Commission - 42nd & 11th Signal	10	10	0	0	10	10	21-Oct-26	03-Nov-26	-15	-10	-5	-5	☐
1-SIG-0363	Demo Old Signal & Temp Signal - 42nd & 11th Signal	2	2	0	0	2	2	04-Nov-26	05-Nov-26	-15	-10	-5	-5	☐
42nd and Roosevelt														
1-SIG-0365	Install Poles - 42nd & Roosevelt Signal	2	2	0	0	2	2	10-Jun-26	11-Jun-26	-10	-4	-6	-6	☐
1-SIG-0366	Build Signal - 42nd & Roosevelt Signal	10	10	0	0	10	10	09-Jul-26	22-Jul-26	-10	-4	-6	-6	☐
1-SIG-0367	SDOT Inspection - 42nd & Roosevelt Signal	5	5	0	0	5	5	23-Jul-26	29-Jul-26	-10	-4	-6	-6	☐
1-SIG-0368	SDOT Commission - 42nd & Roosevelt Signal	10	10	0	0	10	10	30-Jul-26	12-Aug-26	-10	-4	-6	-6	☐
1-SIG-0369	Demo Old Signal & Temp Signal - 42nd & Roosevelt Signal	2	2	0	0	2	2	13-Aug-26	14-Aug-26	-10	-4	-6	-6	☐
41st and Roosevelt														
1-SIG-0371	Install Poles - 41st & Roosevelt Signal	2	2	0	0	2	2	17-Aug-26	18-Aug-26	-10	-4	-6	-6	☐
1-SIG-0372	Build Signal - 41st & Roosevelt Signal	10	10	0	0	10	10	19-Aug-26	01-Sep-26	-10	-4	-6	-6	☐
1-SIG-0373	SDOT Inspection - 41st & Roosevelt Signal	5	5	0	0	5	5	02-Sep-26	09-Sep-26	-10	-4	-6	-6	☐
1-SIG-0374	SDOT Commission - 41st & Roosevelt Signal	10	10	0	0	10	10	10-Sep-26	23-Sep-26	-10	-4	-6	-6	☐
1-SIG-0375	Demo Old Signal & Temp Signal - 41st & Roosevelt Signal	2	2	0	0	2	2	24-Sep-26	25-Sep-26	-10	-4	-6	-6	☐
Roosevelt and Eastlake														
1-SIG-0377	Install Poles - Roosevelt & Eastlake Signal	2	2	0	0	2	2	20-Oct-26	21-Oct-26	-25	-20	-5	-5	☑
1-SIG-0378	Build Signal - Roosevelt & Eastlake Signal	10	10	0	0	10	10	22-Oct-26	04-Nov-26	-25	-20	-5	-5	☑
1-SIG-0379	SDOT Inspection - Roosevelt & Eastlake Signal	5	5	0	0	5	5	05-Nov-26	12-Nov-26	-25	-20	-5	-5	☑
1-SIG-0380	SDOT Commission - Roosevelt & Eastlake Signal	10	10	0	0	10	10	13-Nov-26	30-Nov-26	-25	-20	-5	-5	☑
1-SIG-0381	Demo Old Signal & Temp Signal - Roosevelt & Eastlake Signal	2	2	0	0	2	2	01-Dec-26	02-Dec-26	-25	-20	-5	-5	☑
Lighting														
43rd Street Schematic														
1-EL-0384	Build Schematic, Poles, Luminaires Wiring - 43rd Schematic	10	10	0	0	10	10	20-Oct-26	02-Nov-26	-9	-4	-5	-5	☐
1-EL-0385	SCL Final Inspection - 43rd Schematic	10	10	0	0	10	10	03-Nov-26	17-Nov-26	-9	-4	-5	-5	☐
1-EL-0386	SCL Commission Lighting - 43rd Schematic	15	15	0	0	15	15	18-Nov-26	10-Dec-26	-9	-4	-5	-5	☐
1-EL-0387	Demo Old Lighting - 43rd Schematic	2	2	0	0	2	2	11-Dec-26	14-Dec-26	-9	-4	-5	-5	☐
42nd Street Schematic														
1-EL-0399	SCL Service Commissioning - 42nd Schematic	21	21	0	0	21	21	25-Mar-26	22-Apr-26	124	130	-6	-6	☐
1-EL-0389	Build Schematic, Poles, Luminaires Wiring - 42nd Schematic	10	10	0	0	10	10	06-Nov-26	20-Nov-26	-15	-10	-5	-5	☐
1-EL-0390	SCL Final Inspection - 42nd Schematic	10	10	0	0	10	10	23-Nov-26	08-Dec-26	-15	-10	-5	-5	☐
1-EL-0391	SCL Commission Lighting - 42nd Schematic	15	15	0	0	15	15	09-Dec-26	30-Dec-26	-15	-10	-5	-5	☐
1-EL-0392	Demo Old Lighting - 42nd Schematic	2	2	0	0	2	2	31-Dec-26	04-Jan-27	-15	-10	-5	-5	☐
41st and Roosevelt Schematic														
1-EL-0404	SCL Service Commissioning - 41st & Roosevelt Schematic	21	21	0	0	21	21	01-Apr-26	29-Apr-26	125	131	-6	-6	☐
1-EL-0394	Build Schematic, Poles, Luminaires Wiring - 41st & Roosevelt Sch	10	10	0	0	10	10	03-Dec-26	16-Dec-26	-25	-20	-5	-5	☑
1-EL-0395	SCL Final Inspection - 41st & Roosevelt Schematic	10	10	0	0	10	10	17-Dec-26	31-Dec-26	-25	-20	-5	-5	☑
1-EL-0396	SCL Commission Lighting - 41st & Roosevelt Schematic	15	15	0	0	15	15	04-Jan-27	25-Jan-27	-25	-20	-5	-5	☑
1-EL-0397	Demo Old Lighting - 41st & Roosevelt Schematic	2	2	0	0	2	2	26-Jan-27	27-Jan-27	-25	-20	-5	-5	☑
Stations														
SB 41st St.														

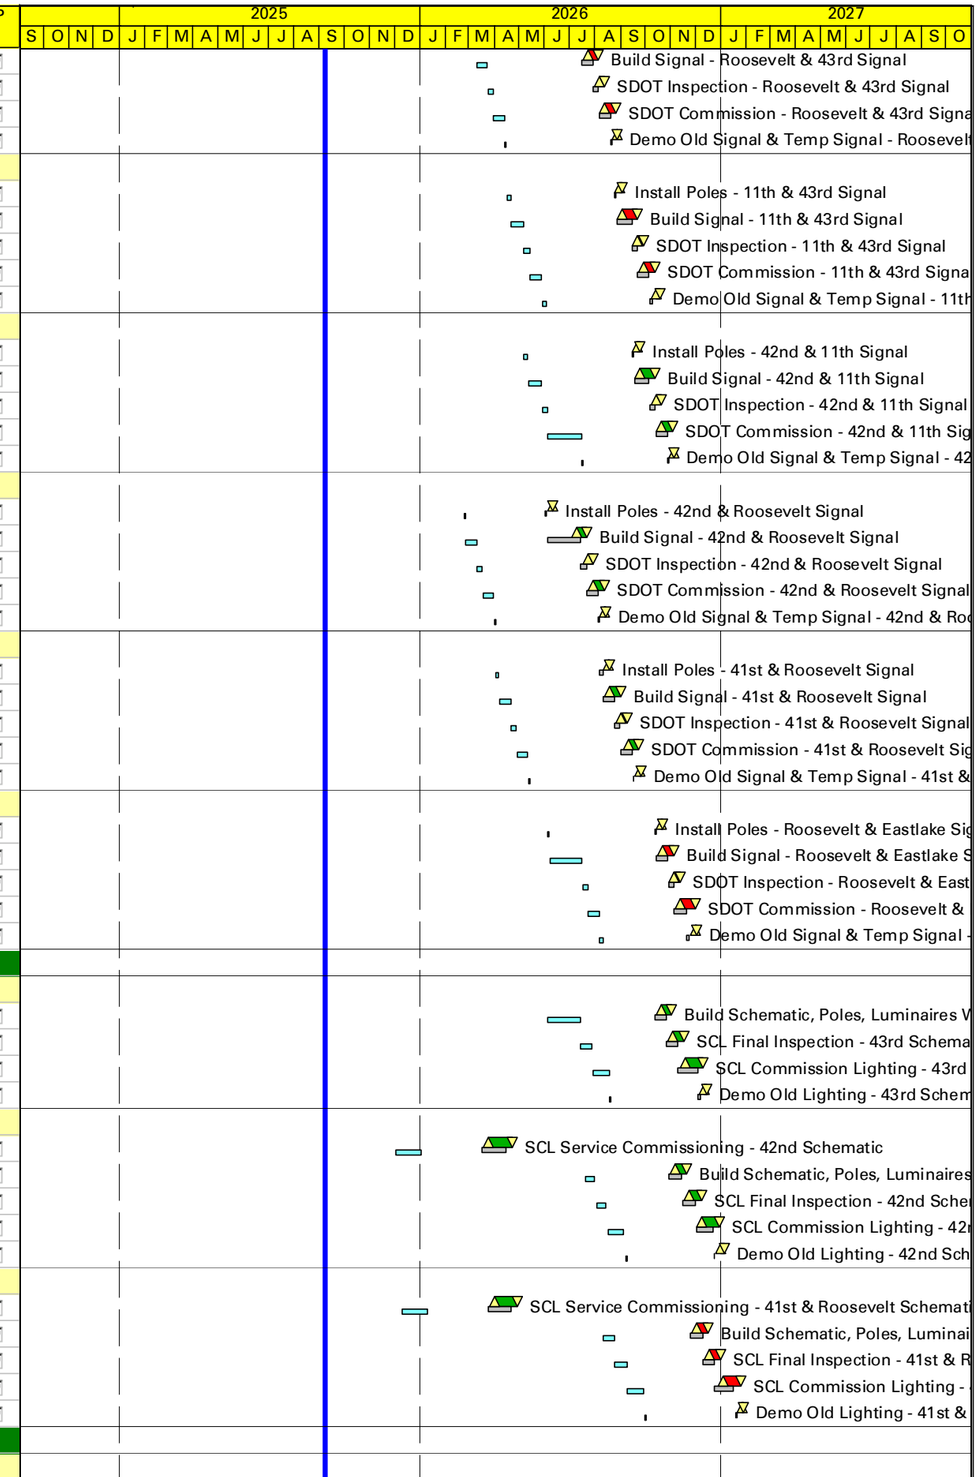

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
1-STN-0400	Install Shelters (2 Each) - SB 41st St. (OFM)	10	10	0	0	10	10	11-May-26	22-May-26	87	93	-6	-6	☐
1-STN-0401	Install Amenities - SB 41st St.	1	1	0	0	1	1	26-May-26	26-May-26	87	93	-6	-6	☐
1-STN-0402	Install Tech Pylon - SB 41st St.	1	1	0	0	1	1	27-May-26	27-May-26	87	93	-6	-6	☐
NB 41st St														
1-STN-0404	Install Shelters (2 Each) - NB 41st St.	10	10	0	0	10	10	28-May-26	10-Jun-26	87	93	-6	-6	☐
1-STN-0405	Install Amenities - NB 41st St.	1	1	0	0	1	1	11-Jun-26	11-Jun-26	87	93	-6	-6	☐
1-STN-0406	Install Tech Pylon - NB 41st St.	1	1	0	0	1	1	09-Jul-26	09-Jul-26	87	93	-6	-6	☐
Station Electrical														
SB 41st Station														
1-SE-0409	Install Electrical - SB 41st St. Station	5	5	0	0	5	5	21-Aug-26	27-Aug-26	46	52	-6	-6	☐
1-SE-0410	KCM Inspection - SB 41st St. Station	5	5	0	0	5	5	28-Aug-26	03-Sep-26	46	52	-6	-6	☐
1-SE-0411	Commission Station Electrical - SB 41st St.	1	1	0	0	1	1	04-Sep-26	04-Sep-26	46	52	-6	-6	☐
NB 41st Station														
1-SE-0413	Install Electrical - NB 41st St. Station	5	5	0	0	5	5	07-Oct-26	14-Oct-26	25	31	-6	-6	☐
1-SE-0414	KCM Inspection - NB 41st St. Station	5	5	0	0	5	5	15-Oct-26	21-Oct-26	25	31	-6	-6	☐
1-SE-0415	Commission Station Electrical - NB 41st St.	1	1	0	0	1	1	22-Oct-26	22-Oct-26	25	31	-6	-6	☐
Hardscapes After Electrical Demo														
43rd														
1-HS-0418	Pour PBL Buffers - 43rd	5	5	0	0	5	5	15-Dec-26	21-Dec-26	-9	-4	-5	-5	☐
11th and 43rd														
1-HS-0420	Demo Foundations - 11th & 43rd	1	1	0	0	1	1	22-Dec-26	22-Dec-26	-9	-4	-5	-5	☐
1-HS-0421	Pour Sidewalks - 11th & 43rd	1	1	0	0	1	1	23-Dec-26	23-Dec-26	-9	-4	-5	-5	☐
11th and 42nd														
1-HS-0423	Demo Foundations - 11th & 42nd	1	1	0	0	1	1	05-Jan-27	05-Jan-27	-15	-10	-5	-5	☐
1-HS-0424	Pour Sidewalks - 11th & 42nd	1	1	0	0	1	1	06-Jan-27	06-Jan-27	-15	-10	-5	-5	☐
42nd West and Roosevelt														
1-HS-0426	Demo Foundations - 42nd W & Roosevelt	1	1	0	0	1	1	07-Jan-27	07-Jan-27	-15	-10	-5	-5	☐
1-HS-0427	Pour Sidewalks - 42nd W & Roosevelt	1	1	0	0	1	1	08-Jan-27	08-Jan-27	-15	-10	-5	-5	☐
42nd and Roosevelt East														
1-HS-0429	Demo Foundations - 42nd & Roosevelt E	1	1	0	0	1	1	11-Jan-27	11-Jan-27	-15	-10	-5	-5	☐
1-HS-0430	Pour Sidewalks - 42nd & Roosevelt E	1	1	0	0	1	1	12-Jan-27	12-Jan-27	-15	-10	-5	-5	☐
42nd and Roosevelt West														
1-HS-0432	Demo Foundations - 42nd & Roosevelt (W)	1	1	0	0	1	1	28-Jan-27	28-Jan-27	-25	-20	-5	-5	☑
1-HS-0433	Pour Sidewalks - 42nd & Roosevelt (W)	1	1	0	0	1	1	29-Jan-27	29-Jan-27	-25	-20	-5	-5	☑
Milling-Paving-Striping														
1-PV-0435	Milling - Zone 1	3	3	0	0	3	3	01-Feb-27	03-Feb-27	-25	-20	-5	-5	☑
1-PBL-0436	PBL Barrier - Zone 1	6	6	0	0	6	6	04-Feb-27	11-Feb-27	-25	-20	-5	-5	☑
1-PV-0437	Asphalt Paving - Zone 1	4	4	0	0	4	4	12-Feb-27	18-Feb-27	-25	-20	-5	-5	☑
1-PV-0438	Asphalt Cure - Zone 1	20	20	0	0	20	20	19-Feb-27	18-Mar-27	-25	-20	-5	-5	☑
1-PM-0439	Channelization - Zone 1	10	10	0	0	10	10	19-Mar-27	01-Apr-27	-25	-20	-5	-5	☑
OCS														
1-SLP-0441	OCS - Install Poles - Zone 1	20	20	0	0	20	20	22-Jul-26	18-Aug-26	96	102	-6	-6	☐
1-OCS-0452	OCS - Temp Supports	2	2	0	0	2	2	19-Aug-26	20-Aug-26	96	102	-6	-6	☐
1-OCS-0472	OCS - Assembly (11th)	5	5	0	0	5	5	21-Aug-26	27-Aug-26	96	102	-6	-6	☐
1-OCS-0492	OCS - Travelers/Pull Wire (11th)	2	2	0	0	2	2	28-Aug-26	31-Aug-26	101	107	-6	-6	☐
1-OCS-0482	OCS - Assembly (Roosevelt)	5	5	0	0	5	5	28-Aug-26	03-Sep-26	96	102	-6	-6	☐
1-OCS-0502	OCS - Travelers/Pull Wire (Roosevelt)	2	2	0	0	2	2	04-Sep-26	08-Sep-26	96	102	-6	-6	☐
1-OCS-0512	OCS - 48 HR Soak	2	2	0	0	2	2	09-Sep-26	10-Sep-26	96	102	-6	-6	☐
1-OCS-0522	OCS - Regulating Clips & Test (11th)	5	5	0	0	5	5	11-Sep-26	17-Sep-26	96	102	-6	-6	☐
1-OCS-0532	OCS - Regulating Clips & Test (Roosevelt)	5	5	0	0	5	5	18-Sep-26	24-Sep-26	96	102	-6	-6	☐
1-OCS-0542	OCS - KCM Inspection	2	2	0	0	2	2	25-Sep-26	28-Sep-26	99	105	-6	-6	☐
Zone 2 - Fuhrman to Lynn														
Pole Foundation Potholing														
2-PH-0445	University Bridge to Louisa St - Pole Foundation Potholing	6	11	0	11	0	11	04-Nov-24 A	19-Nov-24 A			0	0	☑

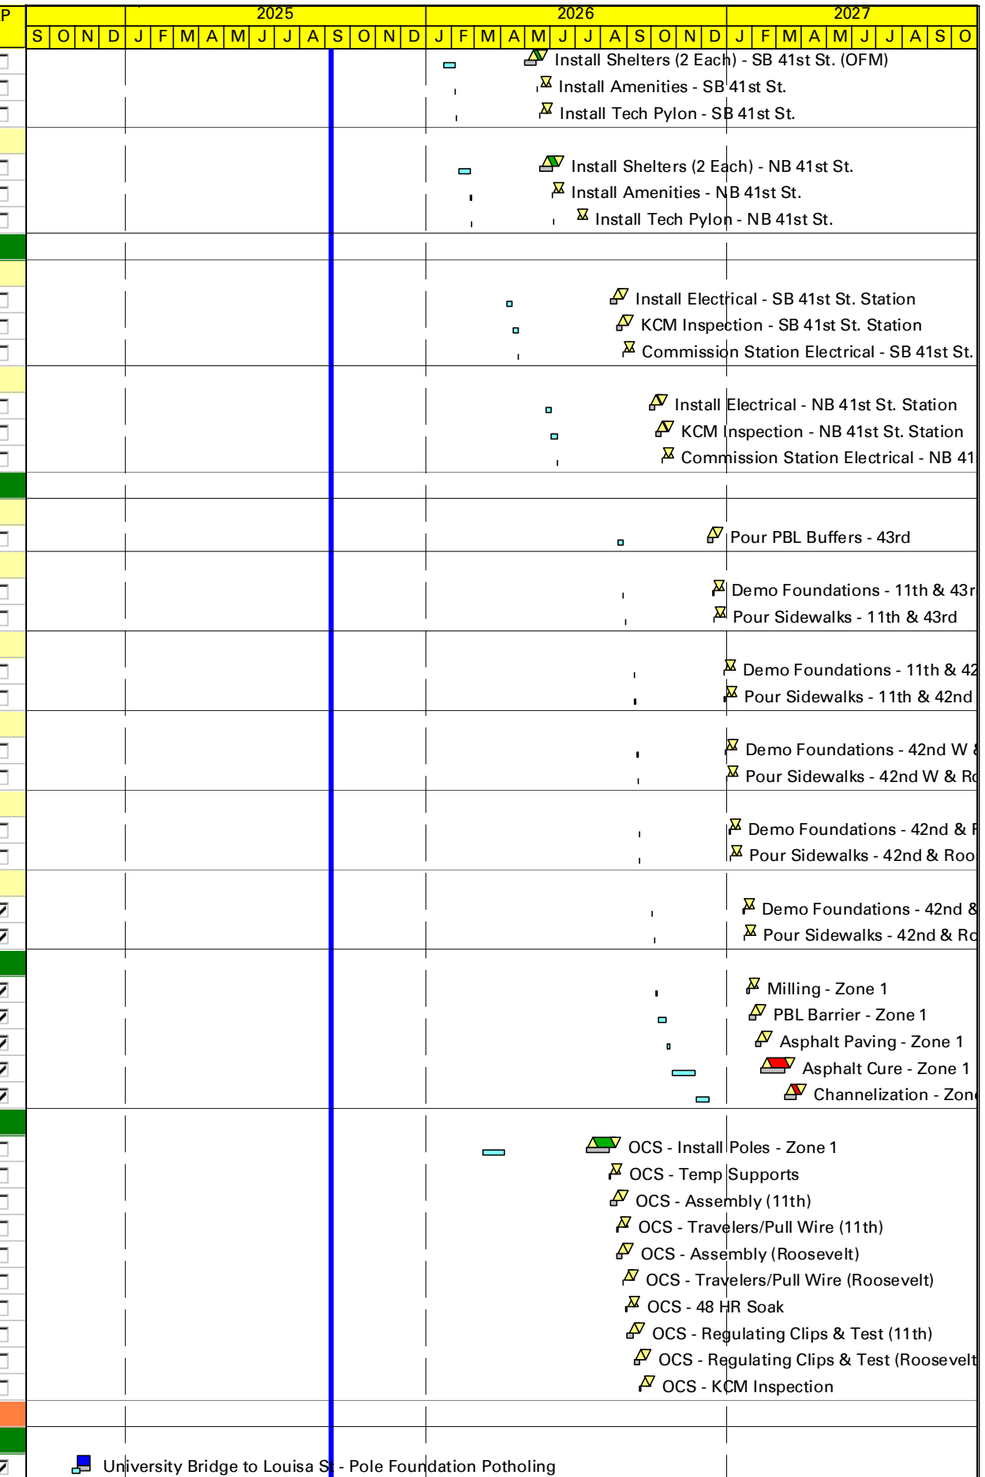

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-031	DSC-031 SWC Harvard Concrete Obstruction for Pothole	1	1	0	1	0	1	14-Nov-24 A	14-Nov-24 A			0	0	☑
DSC-033	DSC-033 Hamlin P2008 Boulder Obstruction	1	1	0	1	0	1	14-Nov-24 A	14-Nov-24 A			0	0	☑
2-PH-0455	Lynn - Complete Pole Foundation Potholing	7	5	0	5	0	5	16-Dec-24 A	20-Dec-24 A			0	0	☑
FM0051-Z2	FM-0051, 0052, 0071 Potholing (Zone 2)	3	25	0	25	0	25	10-Jan-25 A	19-Feb-25 A			0	0	☐
Storm Work														
DSC-019	DSC-019 Fuhrman Vault Conflict w/Inlet Pipe	1	2	0	2	0	2	28-Oct-24 A	29-Oct-24 A			0	0	☑
2-ST-0448	Fuhrman and Eastlake - Storm (ADDED CREW)	3	4	0	4	0	4	28-Oct-24 A	31-Oct-24 A			0	0	☑
DSC-020	DSC-020 SE Corner Fuhrman Unknown Steel Conduit	1	1	0	1	0	1	30-Oct-24 A	30-Oct-24 A			0	0	☑
2-ST-0447	Harvard and Eastlake - Storm	15	15	0	15	0	15	01-Nov-24 A	22-Nov-24 A			0	0	☑
DSC-023	DSC-023 SEC Harvard Unknown Fdn Conflict with CB	1	1	0	1	0	1	05-Nov-24 A	05-Nov-24 A			0	0	☑
DSC-024	DSC-024 SEC Harvard Inlet Conn. Conflict w/Conc. Wall	1	1	0	1	0	1	06-Nov-24 A	06-Nov-24 A			0	0	☑
DSC-027	DSC-027 SEC Harvard CB B1 Utility Conflict	1	1	0	1	0	1	07-Nov-24 A	07-Nov-24 A			0	0	☑
DSC-028	DSC-028 Harvard North Side CB5	1	1	0	1	0	1	08-Nov-24 A	08-Nov-24 A			0	0	☑
2-ST-0449	Allison and Eastlake - Storm (Prior to DSC)	9	6	0	6	0	6	25-Nov-24 A	04-Dec-24 A			0	0	☑
DSC-047	DSC-047 NEC 42nd & 11th Ductank Conflict w/Inlet A7	1	1	0	1	0	1	04-Dec-24 A	04-Dec-24 A			0	0	☑
DSC-049	DSC-049 SWC Allison CB B7 Conflict w/Ductbank	6	7	0	7	0	7	05-Dec-24 A	13-Dec-24 A			0	0	☑
DSC-051	DSC-051 SEC Allison Unknown Unlocated Conduit Conflict w.B7	1	1	0	1	0	1	06-Dec-24 A	06-Dec-24 A			0	0	☑
DSC-052	DSC-052 SEC Allison Unknown Unlocated Steel Line in Conflict w	1	1	0	1	0	1	06-Dec-24 A	06-Dec-24 A			0	0	☑
2-ST-0460	Shelby and Eastlake - Storm (Early Start Mitigation DSC-049)	2	2	0	2	0	2	09-Dec-24 A	10-Dec-24 A			0	0	☑
DSC-056	DSC-056 Shelby East Side BCB B8 Conflict	1	1	0	1	0	1	13-Dec-24 A	13-Dec-24 A			0	0	☑
NCR-001	NCR-001 CB-B07 - 15" PS Line Damaged	1	0	-1	1	0	1	16-Dec-24 A	16-Dec-24 A					☑
2-ST-0459	Allison and Eastlake - Storm (After to DSC-049)	3	14	0	14	0	14	16-Dec-24 A	10-Jan-25 A			0	0	☑
DSC-060	DSC-060 NEC Shelby Granite Slab Conflict w/CB B8	1	1	0	1	0	1	17-Dec-24 A	17-Dec-24 A			0	0	☑
2-ST-0450	Shelby and Eastlake - Storm (After DSC-049)	7	12	0	12	0	12	20-Dec-24 A	14-Jan-25 A			0	0	☑
DSC-064	DSC-064 SEC Shelby CB B9 Conflict w/RCP	3	3	0	3	0	3	23-Dec-24 A	02-Jan-25 A			0	0	☑
DSC-072	DSC-072 SWC Allison CB B7 Conflict w/DB #2	1	1	0	1	0	1	08-Jan-25 A	08-Jan-25 A			0	0	☑
DSC-074	DSC-074 SWC Allison Gas Conflict	1	1	0	1	0	1	10-Jan-25 A	10-Jan-25 A			0	0	☑
DSC-080	DSC-080 NB Shelby Station CB Conflict w/Unknown Pipe	1	1	0	1	0	1	15-Jan-25 A	15-Jan-25 A			0	0	☑
2-ST-0451	NB Shelby Station CB - Storm	7	8	0	8	0	8	15-Jan-25 A	27-Jan-25 A			0	0	☑
NCR-002	NCR-002 CB-B10 - 8" DIP Removed allowing Type 9 in Pipe	1	0	-1	1	0	1	17-Jan-25 A	17-Jan-25 A					☑
DSC-084	DSC-084 NB Shelby Station Unlocated Clay Pipe Conflict CB B10	1	1	0	1	0	1	21-Jan-25 A	21-Jan-25 A			0	0	☑
DSC-088	DSC-088 Hamlin Existing Water Services Leaking	1	1	0	1	0	1	22-Jan-25 A	22-Jan-25 A			0	0	☑
2-ST-0452	Hamlin and Eastlake - Storm	20	31	0	31	0	31	28-Jan-25 A	14-Mar-25 A			0	0	☑
DSC-094	DSC-094 SEC Hamlin Unknown Unlocated Conflict CB B013	2	2	0	2	0	2	30-Jan-25 A	31-Jan-25 A			0	0	☑
DSC-103	DSC-103 Hamlin unknown unlocated utility	1	1	0	1	0	1	10-Feb-25 A	10-Feb-25 A			0	0	☑
DSC-107	DSC-107 Hamlin unknown unlocated utility CB B15	1	1	0	1	0	1	13-Feb-25 A	13-Feb-25 A			0	0	☑
DSC-111	DSC-111 SEC Roanoke Inlet B21 Conflict	1	1	0	1	0	1	18-Feb-25 A	18-Feb-25 A			0	0	☑
2-ST-0464	Roanoke and Eastlake - Storm (partial)	2	2	0	2	0	2	18-Feb-25 A	19-Feb-25 A			0	0	☑
DSC-112	DSC-112 NEC Lynn Inlet B24 Conflict at Ramp	1	1	0	1	0	1	20-Feb-25 A	20-Feb-25 A			0	0	☑
2-ST-0465	Louisa St and Eastlake - Storm (partial)	3	3	0	3	0	3	20-Feb-25 A	24-Feb-25 A			0	0	☑
2-ST-0453	Edgar and Eastlake - Storm	8	11	0	11	0	11	03-Mar-25 A	17-Mar-25 A			0	0	☐
DSC-123	DSC-123 Hamlin CB B14 Conflict w/Gas Main	1	1	0	1	0	1	04-Mar-25 A	04-Mar-25 A			0	0	☑
DSC-128	DSC-128 Edgar Unknown Clay Pipe Inlet B18	2	2	0	2	0	2	13-Mar-25 A	14-Mar-25 A			0	0	☑
DSC-130	DSC-130 Edgar Inlet B18 IE too Low	1	1	0	1	0	1	14-Mar-25 A	14-Mar-25 A			0	0	☑
2-ST-0454	Roanoke and Eastlake - Storm	3	3	0	3	0	3	18-Mar-25 A	20-Mar-25 A			0	0	☐
NCR-005	NCR-005 Earthquake Joint installed into CB-11 beyond 1' limit	1	0	-1	1	0	1	19-Mar-25 A	19-Mar-25 A					☐
DSC-147	DSC-147 Roanoke Inlet B23 Conflict with Ped Pole	1	1	0	1	0	1	20-Mar-25 A	20-Mar-25 A			0	0	☑
2-ST-0455	Louisa St and Eastlake - Storm	6	6	0	6	0	6	21-Mar-25 A	28-Mar-25 A			0	0	☐
DSC-153	DSC-153 Inlet B27 SWC Louisa Existing CB Backed Up	1	1	0	1	0	1	25-Mar-25 A	25-Mar-25 A			0	0	☑
DSC-159	DSC-159 Hamlin to Shelby Sink Hole	1	1	0	1	0	1	28-Mar-25 A	28-Mar-25 A			0	0	☑
DSC-161	DSC-161 Louisa Boulder Conflict with Storm	1	1	0	1	0	1	31-Mar-25 A	31-Mar-25 A			0	0	☑
DSC-227	DSC-227 SEC Lynn CB B22 conflict with Unknown steel pipe	1	1	0	1	0	1	03-Jun-25 A	03-Jun-25 A			0	0	☐
2-ST-0456	Lynn St North Side - Storm	4	4	0	4	0	4	03-Jun-25 A	06-Jun-25 A			0	0	☐
Watermain														

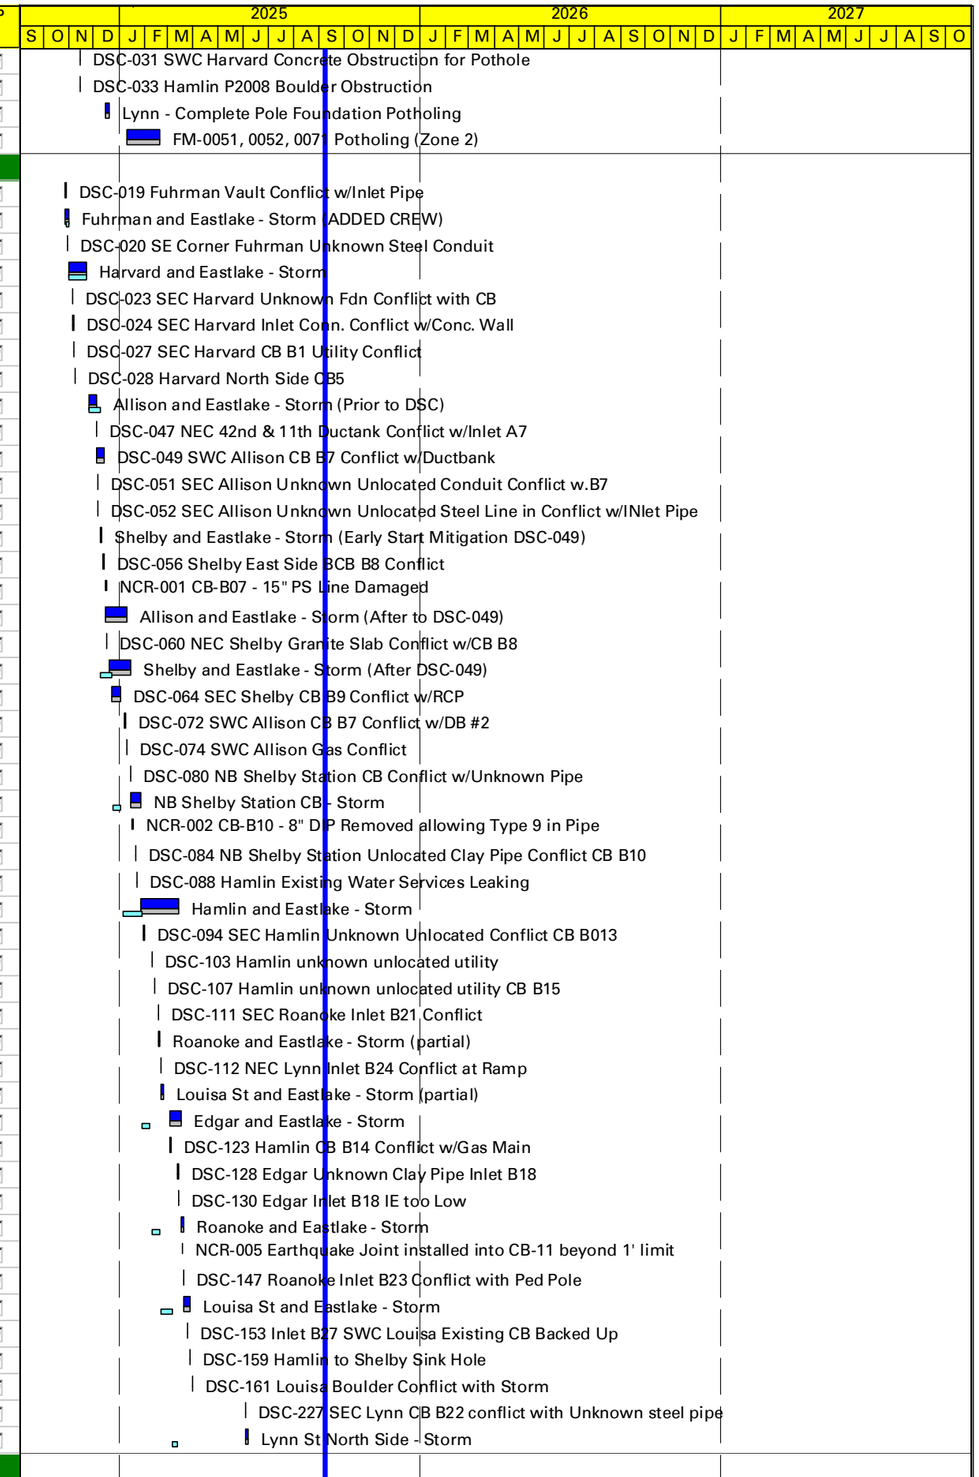

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-W-0599	TROLLEY DEACTIVATION - Fuhrman to Harvard (3/29/25)	0	0	0	0	0	0	31-Mar-25 A				0	0	
2-RW-0602	TROLLEY REACTIVATION Harvard to Fuhrman (8/29/25)	0	0	0	0	0	0		29-Aug-25 A		0	0	0	
Stage 7 Eastlake Fuhrman to Harvard ((1+00 to 6+60)														
SPU Ops Notifications														
2-W-0530	SPU Water Ops Scheduling Notification - Stg 7 (T7.1)	15	15	0	15	0	15	28-Feb-25 A	20-Mar-25 A			0	0	
2-W-0532	SPU Water Ops Scheduling Notification - Stg 7 (CC19 & CC20)	15	15	0	15	0	15	09-May-25 A	30-May-25 A			0	0	
Waterline Installation														
2-W-0476	Temp Main T7.1 - Stg 7 Eastlake/Fuhrman to Harvard	7	8	0	8	0	8	26-Feb-25 A	07-Mar-25 A			0	0	
2-W-0477	Test & Flush Temp Main T7.1 - Stg 7 Eastlake/Fuhrman to Harvard	2	2	0	2	0	2	10-Mar-25 A	11-Mar-25 A			0	0	
2-W-0478	Bact Results - Stg 7 Eastlake/Fuhrman to Harvard	3	3	0	3	0	3	12-Mar-25 A	14-Mar-25 A			0	0	
2-W-0479	SPU Customer Notification - Stg 7 Eastlake/Fuhrman to Harvard (T	5	5	0	5	0	5	17-Mar-25 A	21-Mar-25 A			0	0	
DSC-152	DSC-152 West Side Fuhrman Existing Main at tie 8' deep vs. 4' de	10	10	0	10	0	10	21-Mar-25 A	03-Apr-25 A			0	0	
2-W-0482	SPU Cut/Cap CC18, 19, 20 - Stg 7 Eastlake/Fuhrman to Harvard	2	0	0	0	0	0	22-Mar-25 A	23-Mar-25 A			0	0	
2-W-0481	Connect Temp Main T7.1 - Stg 7 Eastlake/Fuhrman to Harvard	2	0	0	0	0	0	22-Mar-25 A	23-Mar-25 A			0	0	
2-W-0551	Excavate CC18, 19, 20 - Stg 7 Eastlake/Fuhrman to Harvard	2	0	0	0	0	0	22-Mar-25 A	23-Mar-25 A			0	0	
DSC-150	DSC-150 East side Fuhrman Cut and Cap Conflict	2	0	0	0	0	0	22-Mar-25 A	23-Mar-25 A			0	0	
DSC-151	DSC-151 East Side Fuhrman Unmarked Ductbank Conflict with Cu	2	0	0	0	0	0	22-Mar-25 A	23-Mar-25 A			0	0	
2-W-0582	Install Mainline Fuhrman Intersection to Fuhrman Vault	5	5	0	5	0	5	31-Mar-25 A	04-Apr-25 A			0	0	
2-W-0541	SPU Temp Services (5 ea.) - Stg 7 Eastlake/Fuhrman to Harvard	2	2	0	2	0	2	02-Apr-25 A	03-Apr-25 A			0	0	
DSC-168	DSC-168 Stage 7 CDF Conflict	1	1	0	1	0	1	04-Apr-25 A	04-Apr-25 A			0	0	
2-W-0542	Install Monitoring Points - Stg 7 Eastlake/Fuhrman to Harvard	2	2	0	2	0	2	04-Apr-25 A	07-Apr-25 A			0	0	
2-W-0483	Install Fuhrman Vault w/Utility Support - Stg 7 Eastlake/Fuhrman t	5	5	0	5	0	5	07-Apr-25 A	11-Apr-25 A			0	0	
DSC-171	DSC-170 Stage 7 Unknown Steel conduit conflict w/Waterline & Li	1	1	0	1	0	1	08-Apr-25 A	08-Apr-25 A			0	0	
NCR-007	NCR-007 Surveyed 1.81' lower than design	1	0	-1	1	0	1	10-Apr-25 A	10-Apr-25 A					
DSC-173	DSC-173 Phase 7 water CDF Conflict	1	1	0	1	0	1	14-Apr-25 A	14-Apr-25 A			0	0	
2-W-0484	Install Mainline - Stg 7 Eastlake/Fuhrman to Harvard	4	6	0	6	0	6	14-Apr-25 A	21-Apr-25 A			0	0	
DSC-174	DSC-174 Phase 7 Water Unknown Unlocated Steel Utility Conflict	1	1	0	1	0	1	15-Apr-25 A	15-Apr-25 A			0	0	
DSC-176	DSC-176 WM Stage 7 Unknown Water Service	1	1	0	1	0	1	16-Apr-25 A	16-Apr-25 A			0	0	
DSC-177	DSC-177 WM Stage 7 Unknown Gas Line	1	1	0	1	0	1	16-Apr-25 A	16-Apr-25 A			0	0	
DSC-179	DSC-179 Stage 7 Unknown Steel Pipe	1	1	0	1	0	1	17-Apr-25 A	17-Apr-25 A			0	0	
DSC-181	DSC-181 Stage 7 unknown CDF Conflict	1	1	0	1	0	1	18-Apr-25 A	18-Apr-25 A			0	0	
DSC-182	DSC-182 Stage 7 Side Storm Conflict with Mainline	1	1	0	1	0	1	18-Apr-25 A	18-Apr-25 A			0	0	
DSC-185	DSC-185 Stage 7 CDF Conflict	1	1	0	1	0	1	22-Apr-25 A	22-Apr-25 A			0	0	
2-W-0534	Install Mainline Harvard Intersection - Stg 7 Eastlake/Fuhrman to H	5	5	0	5	0	5	22-Apr-25 A	28-Apr-25 A			0	0	
DSC-186	DSC-186 Stage 7 Unknown Unlocated steel line	1	1	0	1	0	1	23-Apr-25 A	23-Apr-25 A			0	0	
PCO-271	Stage 7 Delay Due to Michaels Jetting 48-in	1	1	0	1	0	1	24-Apr-25 A	24-Apr-25 A			0	0	
2-W-0566	Thrust Blocks - Stg 7 Eastlake/Fuhrman to Harvard	2	2	0	2	0	2	29-Apr-25 A	30-Apr-25 A			0	0	
2-W-0586	Install Valve Chamber @ Harvard - Stg 7 Eastlake/Fuhrman to Har	6	6	0	6	0	6	01-May-25 A	08-May-25 A			0	0	
DSC-205	DSC-205 Stage 7, 8-in SS Watermain Conflict	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	
2-W-0596	Complete Mainline Harvard to Sta. 6+60 - Stg 7 Eastlake/Fuhrman	5	5	0	5	0	5	09-May-25 A	15-May-25 A			0	0	
DSC-209	DSC-209 Stage 7 Unknown Steel Line South of Harvard	1	1	0	1	0	1	13-May-25 A	13-May-25 A			0	0	
DSC-210	DSC-210 Stage 7 Abandoned 16in waterline conflict with thrust bl	1	1	0	1	0	1	15-May-25 A	15-May-25 A			0	0	
2-W-0485	Test & Flush Mainline - Stg 7 Eastlake/Fuhrman to Harvard	2	2	0	2	0	2	16-May-25 A	19-May-25 A			0	0	
2-W-0488	Excavate Connections - Stg 7 Eastlake/Fuhrman to Harvard	2	2	0	2	0	2	20-May-25 A	21-May-25 A			0	0	
2-W-0576	Remove Beam & Lag Shoring - Stg 7 Eastlake/Fuhrman to Harvard	2	2	0	2	0	2	20-May-25 A	21-May-25 A			0	0	
2-W-0486	Bact Results - Stg 7 Eastlake/Fuhrman to Harvard	3	3	0	3	0	3	20-May-25 A	22-May-25 A			0	0	
2-W-0489	Excavate Services - Stg 7 Eastlake/Fuhrman to Harvard	1	1	0	1	0	1	22-May-25 A	22-May-25 A			0	0	
2-W-0487	SPU Customer Notification - Stg 7 Eastlake/Fuhrman to Harvard ((	5	5	0	5	0	5	23-May-25 A	30-May-25 A			0	0	
DSC-224	DSC-224 Stage 7 CDF conflict with water service	1	1	0	1	0	1	03-Jun-25 A	03-Jun-25 A			0	0	
2-W-0490	SPU Connection at CC19 and CC20 - Stg 7 Eastlake/Fuhrman to Ha	1	1	0	1	0	1	05-Jun-25 A	05-Jun-25 A			0	0	
2-W-0491	SPU Transfer Services - Stg 7 Eastlake/Fuhrman to Harvard (9 ea.)	1	1	0	1	0	1	06-Jun-25 A	06-Jun-25 A			0	0	
2-W-0492	SPU Temp Jumper Conn Sta. 6+60 to 6+74 - Stg 7 Eastlake/Fuhrm	2	2	0	2	0	2	06-Jun-25 A	09-Jun-25 A			0	0	
2-W-0493	Remove Temp Main - Stg 7 Eastlake/Fuhrman to Harvard	1	1	0	1	0	1	10-Jun-25 A	10-Jun-25 A			0	0	
2-W-0494	Patch Pave - Stg 7 Eastlake/Fuhrman to Harvard	1	1	0	1	0	1	11-Jun-25 A	11-Jun-25 A			0	0	

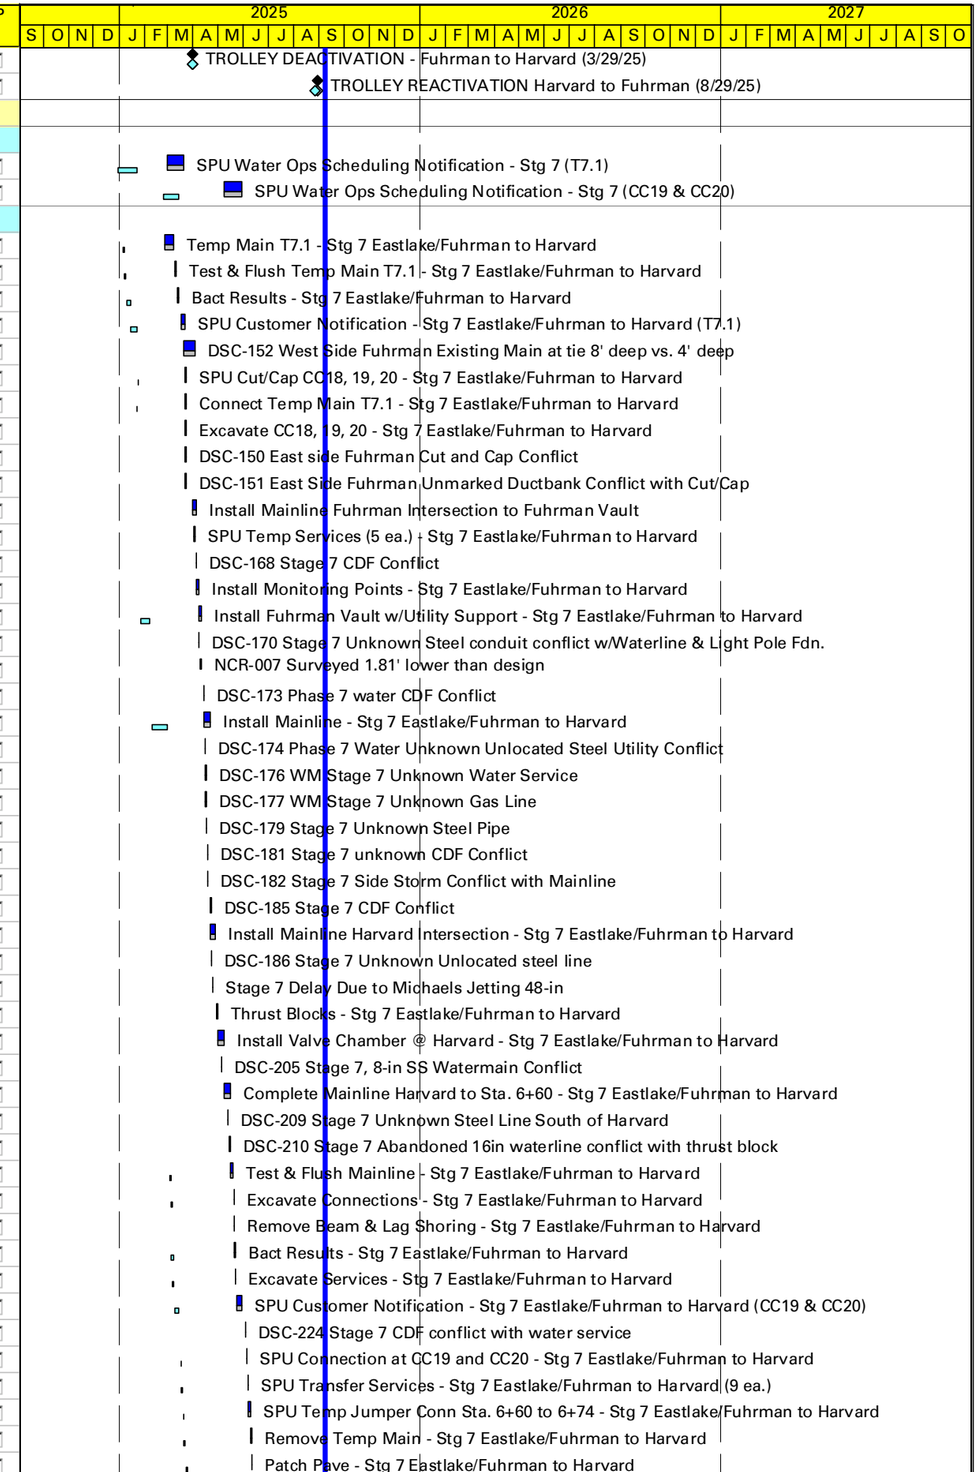

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work | BL1 LOE | Milestone | BL2 LOE | Previous MS | Actual Level of Effort | Previous Bar | Actual Work | Baseline MS | Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-W-0540	Test Stations Watermain Stage 7	5	5	0	5	0	5	12-Jun-25 A	18-Jun-25 A			0	0	☐
Stage 1 Eastlake From Harvard to North of Intersection of Hamlin (6+60 to 21+50)														
SPU Ops Notifications														
2-W-0539	SPU Water Ops Scheduling Notification - Stg 1 (T1.1)	15	15	0	15	0	15	26-Feb-25 A	18-Mar-25 A			0	0	☐
2-W-0529	SPU Water Ops Scheduling Notification - Stg 1 (CC02 & CC03)	15	15	0	15	0	15	15-Jul-25 A	04-Aug-25 A			0	0	☐
Waterline Installation														
2-W-0461	Install Temp Main T1.1 - Stg 1 Harvard to Hamlin	5	6	0	6	0	6	26-Feb-25 A	05-Mar-25 A			0	0	☐
2-W-0609	Test & Flush Temp Main T1.1 - Stg 1 Harvard to Hamlin	2	2	0	2	0	2	10-Mar-25 A	11-Mar-25 A			0	0	☐
2-W-0589	Excavate Hydrant Relocations & Temp Services - Stg 1 Harvard to	3	3	0	3	0	3	12-Mar-25 A	14-Mar-25 A			0	0	☐
2-W-0619	Bact Results Temp Main T1.1 - Stg 1 Harvard to Hamlin	3	3	0	3	0	3	12-Mar-25 A	14-Mar-25 A			0	0	☐
DSC-133	DSC-133 Eastlake, Allison-Hamlin CDF Conflict at Service Jumper	1	1	0	1	0	1	14-Mar-25 A	14-Mar-25 A			0	0	☐
2-W-0629	SPU Customer Notification - Stg 1 Harvard to Hamlin (T1.1)	5	5	0	5	0	5	17-Mar-25 A	21-Mar-25 A			0	0	☐
2-W-0569	SPU Temp Hydrant Relocations (4 ea.) - Stg 1 Harvard to Hamlin	3	3	0	3	0	3	18-Mar-25 A	20-Mar-25 A			0	0	☐
2-W-0579	SPU Temp Service Relocations (5 ea.) - Stg 1 Harvard to Hamlin	2	2	0	2	0	2	20-Mar-25 A	21-Mar-25 A			0	0	☐
2-W-0639	SPU Connect Temp Main T1.1 - Stg 1 Harvard to Hamlin	3	3	0	3	0	3	24-Mar-25 A	26-Mar-25 A			0	0	☐
2-W-0559	Install Mainline Sta. 21+50 to 19+50 - Stg 1 Harvard to Hamlin	8	8	0	8	0	8	02-Apr-25 A	11-Apr-25 A			0	0	☐
NCR-008	NCR-008 Conduits damaged during exposure of CDF duct bank	1	0	-1	1	0	1	10-Apr-25 A	10-Apr-25 A					☐
2-W-0649	Suspend Stage 1 (go to Stage 7)	0	0	0	0	0	0		11-Apr-25 A			0	0	☐
2-W-0463	Install Mainline & Hydrants Sta. 19+50 to 6+60 - Stg 1 Before Stg.	8	8	0	8	0	8	23-May-25 A	04-Jun-25 A			0	0	☐
DSC-216	DSC-216 Eastlake, Harvard-Allison Water Service	1	1	0	1	0	1	27-May-25 A	27-May-25 A			0	0	☐
DSC-219	DSC-219 Eastlake, Unlocated Water Service STA 8+75	1	1	0	1	0	1	28-May-25 A	28-May-25 A			0	0	☐
2-W-0553	Install Mainline & Hydrants Harvard to Allison	9	9	0	9	0	9	10-Jun-25 A	23-Jun-25 A			0	0	☐
2-W-0572	SPU Customer Notification CC01 thru 04	5	5	0	5	0	5	13-Jun-25 A	20-Jun-25 A			0	0	☐
2-W-0552	Excavate for CC01, 02, 03, 04	2	2	0	2	0	2	18-Jun-25 A	20-Jun-25 A			0	0	☐
2-W-0497	Install Mainline Allison to Sta. 21+50	5	9	0	9	0	9	23-Jun-25 A	03-Jul-25 A			0	0	☐
DSC-239	DSC-239 Stage 1 Unknown side sewer sta 18+44	1	1	0	1	0	1	24-Jun-25 A	24-Jun-25 A			0	0	☐
DSC-240	DSC-240 Stage 1 Unknown 6" Water Service STA 17+75	1	1	0	1	0	1	25-Jun-25 A	25-Jun-25 A			0	0	☐
DSC-241	DSC-241 Stage 1 2" Unlocated Steel line	1	1	0	1	0	1	25-Jun-25 A	25-Jun-25 A			0	0	☐
DSC-248	DSC-248 Phase 1 multiple utility conflicts STA 16+10	1	1	0	1	0	1	27-Jun-25 A	27-Jun-25 A			0	0	☐
DSC-251	DSC-251 Stage 1 Unknown unlocated water service	1	1	0	1	0	1	01-Jul-25 A	01-Jul-25 A			0	0	☐
2-W-0592	SPU CUT & CAP DELAY	3	3	0	3	0	3	07-Jul-25 A	09-Jul-25 A			0	0	☐
2-W-0562	SPU Cut and Cap CC01, 02, 03, 04	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	☐
2-W-0462	Install Water Vaults (1 Ea) - Stg 1 Allison	6	6	0	6	0	6	11-Jul-25 A	18-Jul-25 A			0	0	☐
2-W-0464	Install Mainline Allison Lateral Sta. 200+26 to 200+15 - Stg 1 Harva	2	2	0	2	0	2	17-Jul-25 A	18-Jul-25 A			0	0	☐
DSC-269	DSC-269 Stage 1 Waterline CDF conflict STA 14+70	1	1	0	1	0	1	18-Jul-25 A	18-Jul-25 A			0	0	☐
2-W-0475	Mainline Allison Lateral Sta. Sta. 300+00 to 300+31	1	1	0	1	0	1	21-Jul-25 A	21-Jul-25 A			0	0	☐
DSC-271	DSC 271 Stage 1 WM, 2EA unlocated Steel Lines Sta 14+50	1	1	0	1	0	1	21-Jul-25 A	21-Jul-25 A			0	0	☐
2-W-0467	Test & Flush - Stg 1 Harvard to Hamlin	8	8	0	8	0	8	22-Jul-25 A	31-Jul-25 A			0	0	☐
NCR-020	NCR-020 Jansen ruptured a 1 ½" service line	1	0	-1	1	0	1	25-Jul-25 A	25-Jul-25 A					☐
DSC-281	DSC 281 Stage 1, 12+85 Unlocated Conduits & 2in Steel Line	1	1	0	1	0	1	29-Jul-25 A	29-Jul-25 A			0	0	☐
2-W-0470	Excavate Tie-Ins - Stg 1 Harvard to Hamlin	2	2	0	2	0	2	01-Aug-25 A	04-Aug-25 A			0	0	☐
2-W-0468	Bact Results - Stg 1 Harvard to Hamlin	3	3	0	3	0	3	01-Aug-25 A	05-Aug-25 A		1	0	0	☐
DSC-288	DSC 288 Stage 1, 2840 Eastlake Leaking Service behind meter	1	1	0	1	0	1	04-Aug-25 A	04-Aug-25 A			0	0	☐
DSC-293	DSC-293 Stage 1 Sta 19+11 CDF Conflict	1	0	-1	1	0	1	04-Aug-25 A	04-Aug-25 A					☐
DSC-295	DSC-295 Stage 1 WM, WS-301 Root Conflicts	1	0	-1	1	0	1	05-Aug-25 A	05-Aug-25 A					☐
2-W-0471	Excavate Services - Stg 1 Harvard to Hamlin	4	4	0	4	0	4	05-Aug-25 A	08-Aug-25 A		3	0	0	☐
2-W-0469	SPU Customer Notification - Stg 1 Harvard to Hamlin (CC02 & CC(	5	5	0	5	0	5	06-Aug-25 A	12-Aug-25 A		1	0	0	☐
DSC-297	DSC-297 Stage 1 WM, WS-301 CDF Conflict	1	0	-1	1	0	1	07-Aug-25 A	07-Aug-25 A					☐
DSC-298	DSC-298 Stage 1 WM, WS-207 Root Conflicts	1	0	-1	1	0	1	07-Aug-25 A	07-Aug-25 A					☐
DSC-299	DSC-299 Stage 1 WM, WS-205 CDF Conflict	1	0	-1	1	0	1	07-Aug-25 A	07-Aug-25 A					☐
2-W-0472	SPU Connections at CC02 and CC03 - Stg 1 Harvard to Hamlin	1	1	0	1	0	1	13-Aug-25 A	13-Aug-25 A		1	0	0	☐
2-W-0473	SPU Transfer Services - Stg 1 Harvard to Hamlin (21 ea.)	6	6	3	3	0	3	13-Aug-25 A	15-Aug-25 A		1	1	4	☐
2-W-0554	SPU Temp Jumper Conn. Sta. 21+50 - Stg 1 Harvard to Hamlin	2	2	0	2	0	2	18-Aug-25 A	19-Aug-25 A		1	4	4	☐
2-W-0474	Patch Pave - Stg 1 Harvard to Hamlin	1	1	0	1	0	1	20-Aug-25 A	20-Aug-25 A		57	4	4	☐

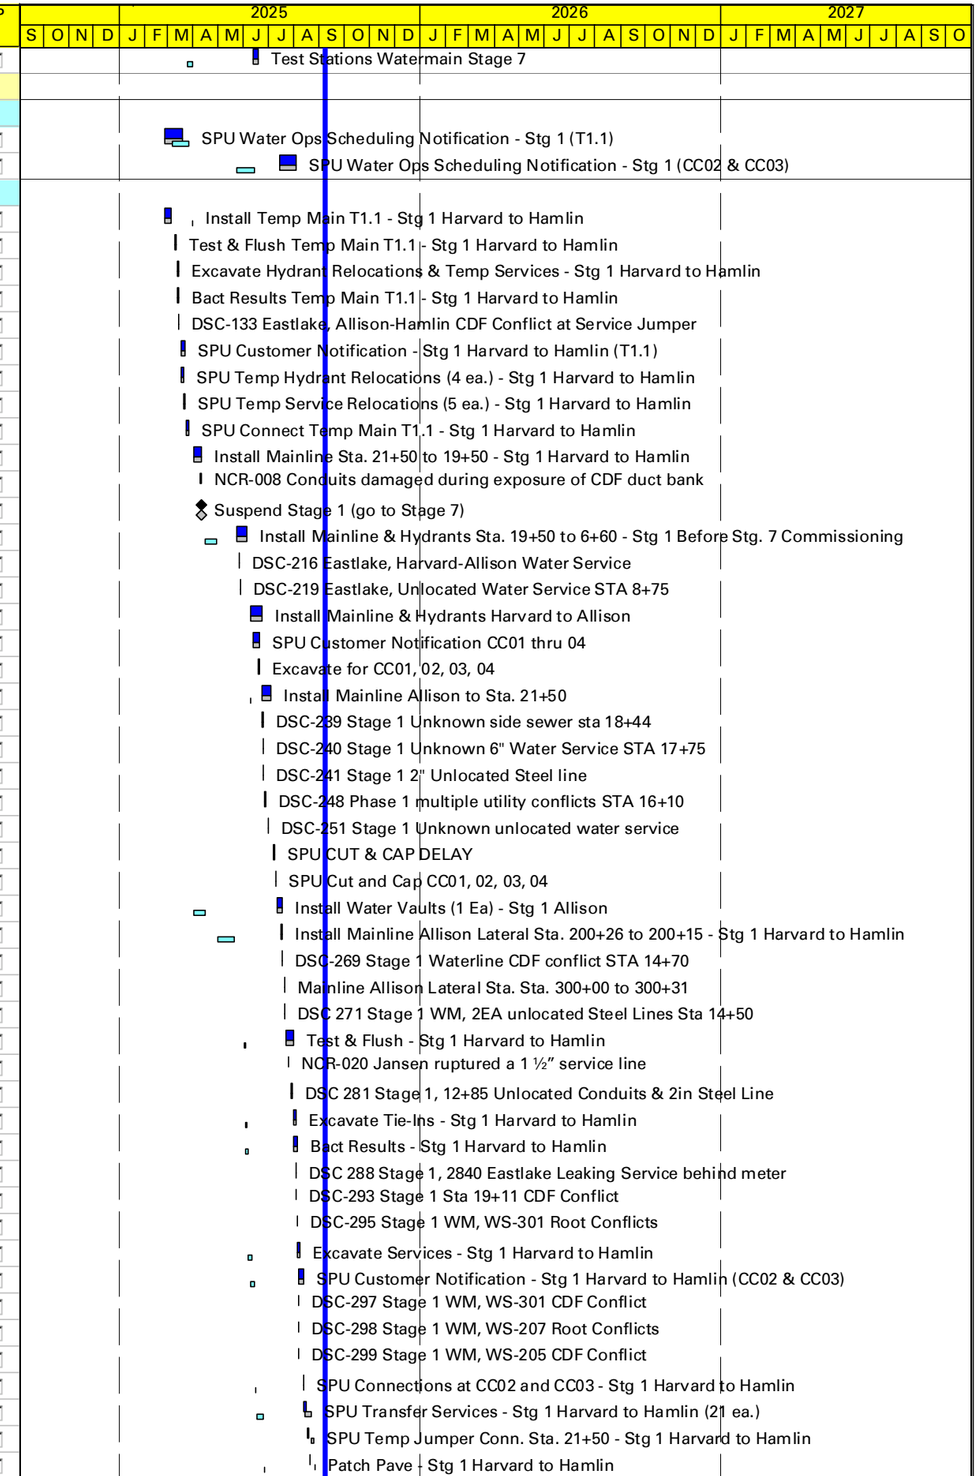

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-W-0549	Test Stations Watermain Stage 1	5	5	4	1	0	1	21-Aug-25 A	21-Aug-25 A		135	4	8	
Stage 2 North of Hamlin to Edgar (21+50 to 33+19)														
SPU Ops Notifications														
2-W-0536	SPU Water Ops Scheduling Notification - Stg 2 (CC05, 06, 07)	15	15	0	15	0	15	15-Aug-25 A	05-Sep-25 A		8	4	4	
2-W-0526	SPU Water Ops Scheduling Notification - Stg 2 (TM2.1 & TM2.2)	15	15	0	13	2	15	20-Aug-25 A	10-Sep-25	8	1	4	4	
2-W-0524	SPU Water Ops Scheduling Notification - Stg 2 (CC05 Tie-in)	15	15	0	0	15	15	26-Sep-25	17-Oct-25	13	8	5	5	
Waterline Installation														
2-W-0606	Install Temp Main TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	5	5	-1	6	0	6	20-Aug-25 A	27-Aug-25 A		1	4	3	
DSC-316	DSC-316 Stage 2 Temp Main unlocated unknown water service cc	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
DSC-320	DSC-320 Stage 2 temp main CDF Encased existing main	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
DSC-321	DSC-321 Unknown Unlocated Water Service STA 28+80 stage 2	1	0	-1	1	0	1	27-Aug-25 A	27-Aug-25 A					
2-W-0616	Test & Flush TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	2	2	-1	3	0	3	28-Aug-25 A	02-Sep-25 A		1	3	2	
DSC-324	DSC-324 Leaking Services at T2.1 Hamlin, WS- 503,504	1	0	-1	1	0	1	29-Aug-25 A	29-Aug-25 A					
2-W-0626	Bact Results TM2.1 & TM2.2 - Stg 2 Hamlin to Edgar	3	3	0	3	0	3	03-Sep-25 A	05-Sep-25 A		1	2	2	
2-W-0519	Install Watermain (prior to temp main commissioning)	8	0	-8	4	4	8	03-Sep-25 A	12-Sep-25	6				
DSC-330	DSC-330 WM Stg 2 Unlocated Steel Pipe STA 27+86	1	0	-1	1	0	1	05-Sep-25 A	05-Sep-25 A					
DSC-331	DSC-331 Stage 2 WM 1IN Copper Line at 27+70	1	0	-1	1	0	1	05-Sep-25 A	05-Sep-25 A					
DSC-332	DSC-332 Stage 2 WM 2EA 2IN Steel Pipes near WS-604	1	0	-1	1	0	1	05-Sep-25 A	05-Sep-25 A					
DSC-338	DSC-338 Stage 2 WM Unknown Utility at STA 26+90	1	0	-1	1	0	1	08-Sep-25 A	08-Sep-25 A					
2-W-0646	SPU Customer Notification - Stg 2 Hamlin to Edgar (TM2.1 & TM2	5	5	0	1	4	5	08-Sep-25 A	12-Sep-25	6	1	2	2	
2-W-0636	SPU Connect Temp Main TM 2.1 & TM 2.2 Including Services & H	1	3	2	0	1	1	15-Sep-25	15-Sep-25	6	1	2	4	
2-W-0656	SPU Install Temp Hydrant & Service Laterals (2 ea.) - Stg 2 Hamlir	1	1	0	0	1	1	16-Sep-25	16-Sep-25	6	1	4	4	
2-W-0499	Install Watermain, Hydrants & Blocking Sta. 21+64 to 33+19 - Stg :	11	12	1	0	11	11	17-Sep-25	01-Oct-25	6	1	5	6	
2-W-0550	Mainline Lateral @ Hamlin - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	02-Oct-25	02-Oct-25	6	1	-7	-7	
2-W-0500	Test & Flush Water Main - Stg 2 Hamlin to Edgar	2	2	0	0	2	2	03-Oct-25	06-Oct-25	6	1	5	5	
2-W-0560	Install Thrust Collar & Cure - Stg 2 Hamlin to Edgar	5	5	0	0	5	5	03-Oct-25	09-Oct-25	22	8	-7	-7	
2-W-0503	Excavate Services and Tie-Ins - Stg 2 Hamlin to Edgar	2	2	0	0	2	2	07-Oct-25	08-Oct-25	6	1	5	5	
2-W-0501	Bact Results - Stg 2 Hamlin to Edgar	3	3	0	0	3	3	07-Oct-25	09-Oct-25	13	8	5	5	
2-W-0502	SPU Customer Notification - Stg 2 Hamlin to Edgar (CC05 Main)	5	5	0	0	5	5	10-Oct-25	17-Oct-25	13	8	5	5	
2-W-0504	SPU Tie-In Watermain at CC05 - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	20-Oct-25	20-Oct-25	13	8	5	5	
2-W-0505	SPU Transfer Water Services - Stg 2 Hamlin to Edgar (12 ea.)	3	3	0	0	3	3	21-Oct-25	23-Oct-25	13	8	5	5	
2-W-0506	SPU Tie-In Main From Stage 1 - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	24-Oct-25	24-Oct-25	13	8	5	5	
2-W-0557	SPU Jumper Conn. Sta. 33+19 - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	27-Oct-25	27-Oct-25	13	8	5	5	
2-W-0567	Remove Temp Mains - Stg 2 Hamlin to Edgar	5	5	0	0	5	5	28-Oct-25	03-Nov-25	13	8	5	5	
2-W-0507	Patch Pave - Stg 2 Hamlin to Edgar	1	1	0	0	1	1	04-Nov-25	04-Nov-25	13	8	5	5	
2-W-0546	Test Stations Watermain Stage 2	5	5	0	0	5	5	05-Nov-25	12-Nov-25	94	89	5	5	
Stage 3 Eastlake Edgar to Louisa (33+19 to 44+50)														
SPU Ops Notifications														
2-W-0527	SPU Water Ops Scheduling Notification - Stg 3 (CC08, 09, 10)	15	15	0	0	15	15	06-Oct-25	27-Oct-25	17	12	5	5	
2-W-0531	SPU Water Ops Scheduling Notification - Stg 3 (CC07 Conn.)	15	15	0	0	15	15	12-Nov-25	04-Dec-25	6	1	5	5	
Waterline Installation														
2-W-0659	Excavate Temp Hydrants & Services - Stg 3 Edgar to Louisa	2	2	0	0	2	2	09-Oct-25	10-Oct-25	6	1	5	5	
2-W-0509	Excavate CC08, 09, 10 - Stg 3 Edgar to Louisa	1	1	0	0	1	1	14-Oct-25	14-Oct-25	21	16	5	5	
2-W-0669	SPU Install Temp Hydrant & Service Laterals - Stg 3 Edgar to Loui	2	2	0	0	2	2	14-Oct-25	15-Oct-25	6	1	5	5	
2-W-0512	Install Watermain & Hydrants From Sta. 33+33 to 44+50 - Stg 3 Ed	20	20	0	0	20	20	16-Oct-25	13-Nov-25	6	1	5	5	
2-W-0533	SPU Customer Notification - Stg 3 Edgar to Louisa (CC08, 09, 10)	5	5	0	0	5	5	21-Oct-25	27-Oct-25	17	12	5	5	
2-W-0511	SPU Cut/Cap CC08, 09, 10 - Stg 3 Edgar to Louisa	1	1	0	0	1	1	28-Oct-25	28-Oct-25	17	12	5	5	
2-W-0543	Lateral Main @ Roanoke Sta. 600+13 to 600+61 - Stg 3 Edgar to Lc	1	1	0	0	1	1	14-Nov-25	14-Nov-25	6	1	5	5	
2-W-0513	Test & Flush Main - Stg 3 Edgar to Louisa	2	2	0	0	2	2	17-Nov-25	18-Nov-25	6	1	5	5	
2-W-0514	Bact Results - Stg 3 Edgar to Louisa	3	3	0	0	3	3	19-Nov-25	21-Nov-25	6	1	5	5	
2-W-0515	SPU Customer Notification - Stg 3 Edgar to Louisa (CC07 Main)	5	5	0	0	5	5	24-Nov-25	02-Dec-25	6	1	5	5	
2-W-0516	Excavate Services and Connections - Stg 3 Edgar to Louisa	2	2	0	0	2	2	03-Dec-25	04-Dec-25	6	1	5	5	
2-W-0517	SPU Connect Main at CC09 & 2 Hydrants - Stg 3 Edgar to Louisa	2	2	0	0	2	2	05-Dec-25	08-Dec-25	6	1	5	5	
2-W-0518	SPU Transfer Services - Stg 3 Edgar to Louisa (30 ea.)	6	6	0	0	6	6	09-Dec-25	16-Dec-25	6	1	5	5	

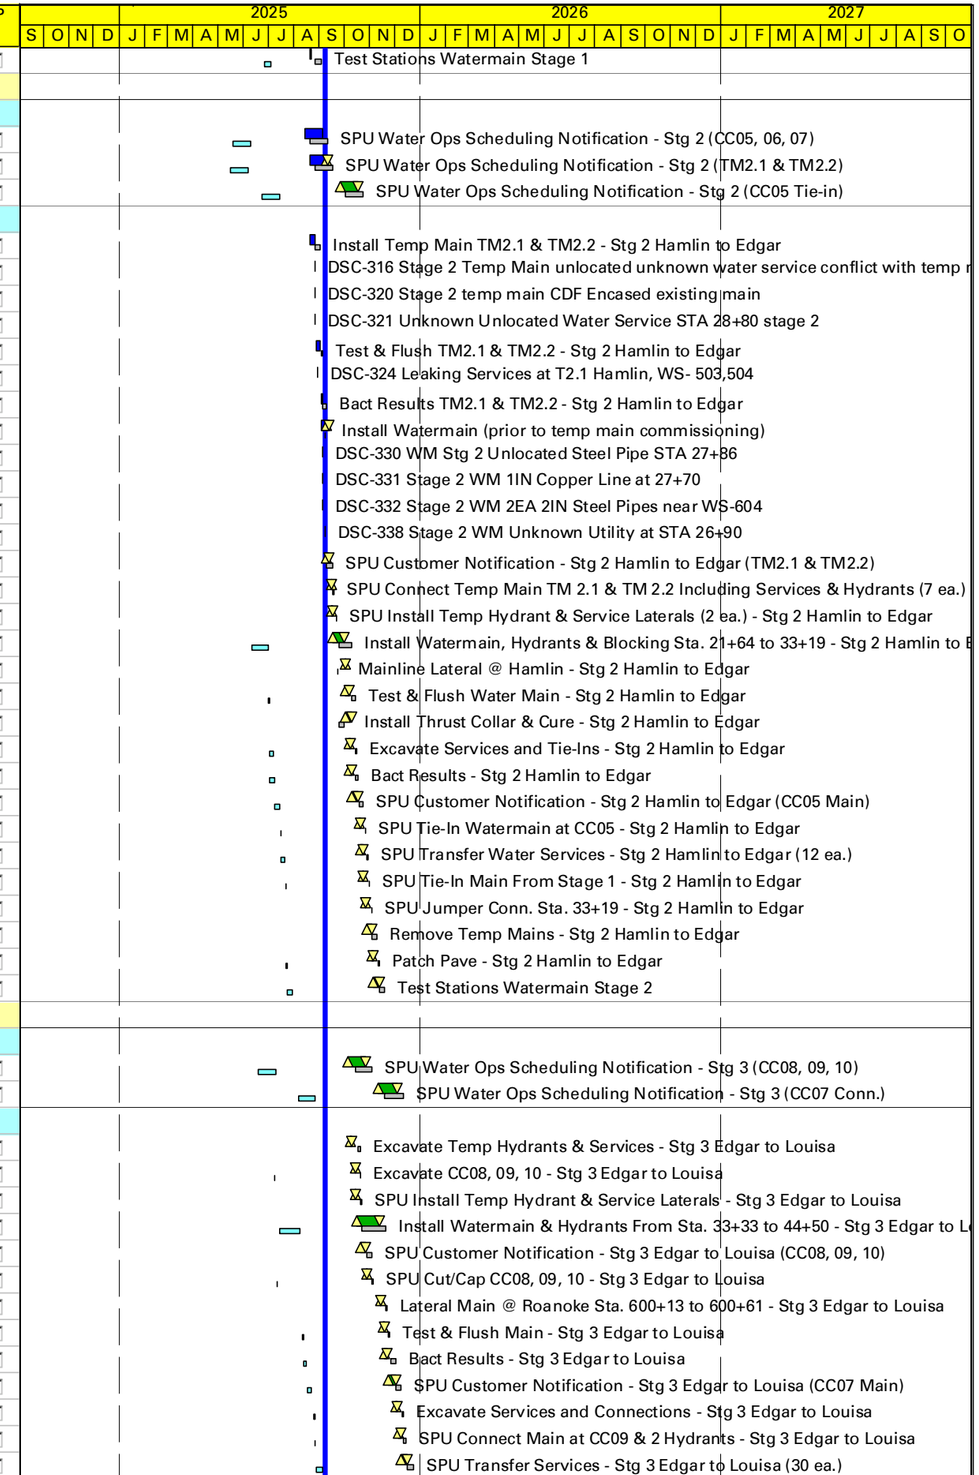

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-W-0520	SPU Tie-In at Sta. 33+19 - Stg 3 Edgar to Louisa	1	1	0	0	1	1	17-Dec-25	17-Dec-25	6	1	5	5	
2-W-0521	SPU Install Temp Jumper Sta. 44+50 - Stg 3 Edgar to Louisa	1	1	0	0	1	1	18-Dec-25	18-Dec-25	6	1	5	5	
2-W-0523	Patch Pave - Stg 3 Edgar to Louisa	1	1	0	0	1	1	19-Dec-25	19-Dec-25	6	1	5	5	
2-W-0547	Test Stations Watermain Stage 3	5	5	0	0	5	5	22-Dec-25	29-Dec-25	67	62	5	5	
Conduit Crossings														
2-CC-0530	Harvard - Conduit Crossings	5	5	0	5	0	5	19-May-25 A	23-May-25 A			0	0	
2-CC-0531	Fuhrman - Conduit Crossings	8	29	0	29	0	29	27-May-25 A	08-Jul-25 A			0	0	
DSC-220	DSC-220 Fuhrman Reinforced Concrete under Roadway	2	17	0	17	0	17	29-May-25 A	23-Jun-25 A			0	0	
DSC-221	DSC-221 Fuhrman conduit crossings multiple unknown unmarkec	2	17	0	17	0	17	29-May-25 A	23-Jun-25 A			0	0	
DSC-223	DSC-223 Fuhrman Eastlake unknown unlocated utilities	3	14	0	14	0	14	03-Jun-25 A	23-Jun-25 A			0	0	
DSC-229	DSC-229 Fuhrman CDF Conflict with Conduit Trench	2	11	0	11	0	11	06-Jun-25 A	23-Jun-25 A			0	0	
DSC-244	DSC-244 Fuhrman conduit crossing conflict with multiple unknow	5	5	0	5	0	5	26-Jun-25 A	02-Jul-25 A			0	0	
2-CC-0529	Allison - Conduit Crossings	4	4	0	0	4	4	15-Sep-25	18-Sep-25	45	57	-12	-12	
2-CC-0527	Louisa - Conduit Crossings	2	2	0	0	2	2	23-Oct-25	24-Oct-25	37	24	13	13	
2-CC-0528	Lynn - Conduit Crossings	6	6	0	0	6	6	27-Oct-25	03-Nov-25	41	28	13	13	
2-CC-0525	Hamlin - Conduit Crossings	7	7	0	0	7	7	05-Nov-25	14-Nov-25	13	8	5	5	
2-CC-0526	Roanoke - Conduit Crossings	4	4	0	0	4	4	22-Dec-25	26-Dec-25	6	1	5	5	
Roadway														
Shelby to Edgar East Side														
2-RW-0614	Complete SCL Pole Relocation 1 ea. (by SCL) - Shelby to Edgar	0	0	0	0	0	0		14-Nov-25	13	8	5	5	
2-RW-0534	Roadway Demo & Exc - Shelby to Edgar (E)	10	10	0	0	10	10	17-Nov-25	02-Dec-25	13	8	5	5	
2-RW-0584	Remove/Abandon Waterline & Appurtances - Shelby to Edgar (E)	10	10	0	0	10	10	17-Nov-25	02-Dec-25	22	17	5	5	
2-RW-0535	Pour Roadway - Shelby to Edgar (E)	6	6	0	0	6	6	03-Dec-25	10-Dec-25	22	17	5	5	
2-RW-0536	Curb - Shelby to Edgar (E)	2	2	0	0	2	2	11-Dec-25	12-Dec-25	22	17	5	5	
2-RW-0537	Patch Pave - Shelby to Edgar (E)	1	1	0	0	1	1	15-Dec-25	15-Dec-25	38	33	5	5	
Edgar to Louisa East Side														
2-RW-0539	Roadway Demo & Exc - Edgar to Louisa (E)	10	10	0	0	10	10	03-Dec-25	16-Dec-25	13	8	5	5	
2-RW-0589	Remove/Abandon Waterline & Appurtances - Edgar to Louisa (E)	10	10	0	0	10	10	03-Dec-25	16-Dec-25	20	15	5	5	
2-RW-0540	Pour Roadway - Edgar to Louisa (E)	6	6	0	0	6	6	17-Dec-25	24-Dec-25	20	15	5	5	
2-RW-0541	Curb - Edgar to Louisa (E)	2	2	0	0	2	2	26-Dec-25	29-Dec-25	29	24	5	5	
2-RW-0542	Patch Pave - Edgar to Louisa (E)	1	1	0	0	1	1	30-Dec-25	30-Dec-25	29	24	5	5	
Louisa to Lynn East Side														
2-RW-0544	Roadway Demo & Exc - Louisa to Lynn (E)	8	8	0	0	8	8	29-Dec-25	08-Jan-26	6	1	5	5	
2-RW-0594	Remove/Abandon Waterline & Appurtances - Louisa to Lynn (E)	8	8	0	0	8	8	29-Dec-25	08-Jan-26	11	6	5	5	
2-RW-0545	Pour Roadway - Louisa to Lynn (E)	3	3	0	0	3	3	09-Jan-26	13-Jan-26	11	6	5	5	
2-RW-0546	Curb - Louisa to Lynn (E)	2	2	0	0	2	2	14-Jan-26	15-Jan-26	11	6	5	5	
2-RW-0547	Patch Pave - Louisa to Lynn (E)	1	1	0	0	1	1	16-Jan-26	16-Jan-26	18	13	5	5	
Shelby to Edgar West Side														
2-RW-0549	Roadway Demo & Exc - Shelby to Edgar (W)	10	10	0	0	10	10	09-Jan-26	23-Jan-26	6	1	5	5	
2-RW-0550	Pour Roadway - Shelby to Edgar (W)	6	6	0	0	6	6	26-Jan-26	02-Feb-26	6	1	5	5	
2-RW-0551	Curb - Shelby to Edgar (W)	2	2	0	0	2	2	03-Feb-26	04-Feb-26	6	1	5	5	
2-RW-0552	Patch Pave - Shelby to Edgar (W)	1	1	0	0	1	1	05-Feb-26	05-Feb-26	6	1	5	5	
Edgar to Louisa West Side														
2-RW-0554	Roadway Demo & Exc - Edgar to Louisa (W)	10	10	0	0	10	10	03-Feb-26	17-Feb-26	14	9	5	5	
2-RW-0555	Pour Roadway - Edgar to Louisa (W)	6	6	0	0	6	6	18-Feb-26	25-Feb-26	14	9	5	5	
2-RW-0556	Curb - Edgar to Louisa (W)	2	2	0	0	2	2	26-Feb-26	27-Feb-26	14	9	5	5	
2-RW-0557	Patch Pave - Edgar to Louisa (W)	1	1	0	0	1	1	02-Mar-26	02-Mar-26	14	9	5	5	
Louisa to Lynn West Side														
2-RW-0559	Roadway Demo & Exc - Louisa to Lynn (W)	8	8	0	0	8	8	18-Feb-26	27-Feb-26	19	14	5	5	
2-RW-0560	Pour Roadway - Louisa to Lynn (W)	3	3	0	0	3	3	02-Mar-26	04-Mar-26	19	14	5	5	
2-RW-0561	Curb - Louisa to Lynn (W)	2	2	0	0	2	2	05-Mar-26	06-Mar-26	19	14	5	5	
2-RW-0562	Patch Pave - Louisa to Lynn (W)	1	1	0	0	1	1	09-Mar-26	09-Mar-26	19	14	5	5	
Harvard to Fuhrman East Side														
2-RW-0569	Roadway Demo & Exc - Harvard to Fuhrman (E)	9	9	0	9	0	9	10-Jun-25 A	23-Jun-25 A			0	0	

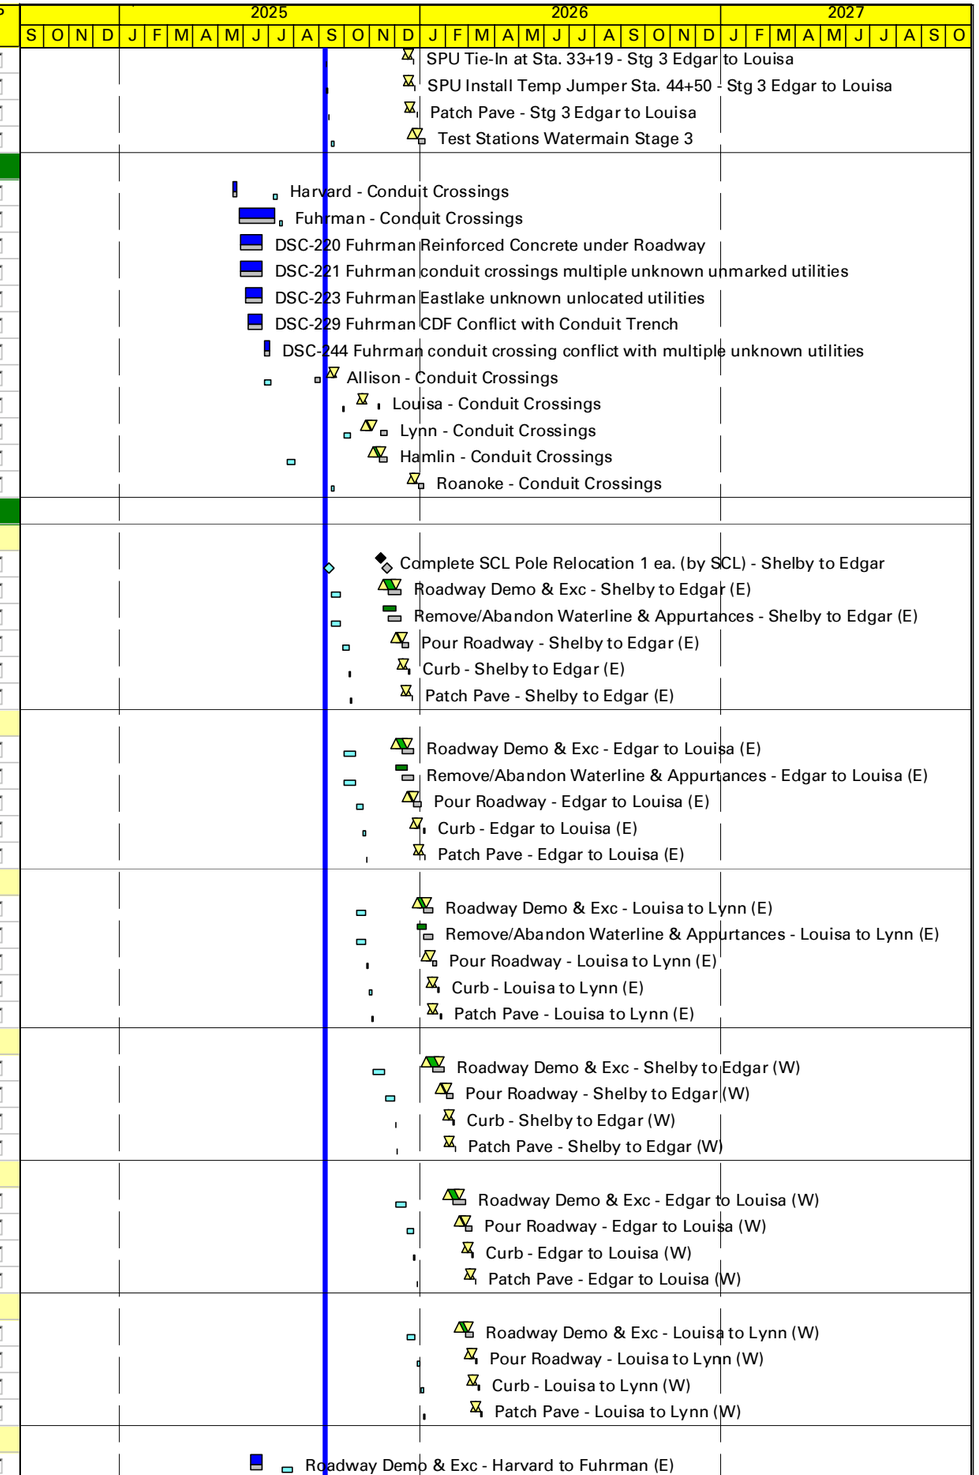

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-RW-0599	Remove/Abandon Waterline & Appurtances - Harvard to Fuhrmar	9	9	0	9	0	9	10-Jun-25 A	23-Jun-25 A			0	0	
2-RW-0570	Pour Roadway - Harvard to Fuhrman (E)	4	4	0	4	0	4	24-Jun-25 A	27-Jun-25 A			0	0	
2-RW-0571	Curb - Harvard to Fuhrman (E) DC-048	3	3	0	3	0	3	30-Jun-25 A	02-Jul-25 A			0	0	
2-RW-0572	Patch Pave - Harvard to Fuhrman (E)	1	1	0	1	0	1	03-Jul-25 A	03-Jul-25 A			0	0	
NCR-018	NCR-018 Saw Cuts for transverse cut are not per approved plan	1	0	-1	1	0	1	01-Jul-25 A	01-Jul-25 A					
Harvard to Fuhrman West Side														
2-RW-0579	Roadway Demo & Exc - Harvard to Fuhrman (W)	9	9	0	9	0	9	07-Jul-25 A	17-Jul-25 A			0	0	
DSC-257	DSC-257 Eastlake west side between Fuhrman and Harvard shallo	1	1	0	1	0	1	09-Jul-25 A	09-Jul-25 A			0	0	
DSC-258	DSC-258 Eastlake west side between Fuhrman and Harvard thick r	1	1	0	1	0	1	09-Jul-25 A	09-Jul-25 A			0	0	
DSC-259	DSC-259 Eastlake west side between Fuhrman and Harvard unknc	1	1	0	1	0	1	09-Jul-25 A	09-Jul-25 A			0	0	
DSC-263	DSC-263 Fuhrman West Side Reinforced pavement	1	1	0	1	0	1	14-Jul-25 A	14-Jul-25 A			0	0	
DSC-273	DSC 273 Harvard & Eastlake Pole Foundation Removal	1	1	0	1	0	1	17-Jul-25 A	17-Jul-25 A			0	0	
DSC-268	DSC-268 Fuhrman CDF conflict with Roadway	1	1	0	1	0	1	18-Jul-25 A	18-Jul-25 A			0	0	
2-RW-0580	Pour Roadway - Harvard to Fuhrman (W)	4	4	0	4	0	4	18-Jul-25 A	23-Jul-25 A			0	0	
2-RW-0581	Curb - Harvard to Fuhrman (W)	2	2	0	2	0	2	24-Jul-25 A	25-Jul-25 A			0	0	
DSC-279	DSC 279 Fuhrman-Harvard West Side RR Ties, Thick Conc	1	1	0	1	0	1	25-Jul-25 A	25-Jul-25 A			0	0	
DSC-280	DSC 280 Fuhrman-Harvard West Side Duct Bank Conflict with Roa	1	1	0	1	0	1	25-Jul-25 A	25-Jul-25 A			0	0	
2-RW-0582	Patch Pave - Harvard to Fuhrman (W)	1	1	0	1	0	1	28-Jul-25 A	28-Jul-25 A			0	0	
Harvard														
Phase-1														
2-RW-694	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.1	6	6	0	6	0	6	29-Jul-25 A	05-Aug-25 A		0	0	0	
2-RW-704	Pour Roadway - Harvard to Fuhrman (W) Ph.1	2	2	-2	4	0	4	06-Aug-25 A	11-Aug-25 A		0	0	-2	
2-RW-724	Patch Pave - Harvard to Fuhrman (W) Ph.1	1	1	-1	2	0	2	12-Aug-25 A	13-Aug-25 A		0	-1	-2	
2-RW-714	Curb - Harvard to Fuhrman (W) Ph.1	1	1	-1	2	0	2	14-Aug-25 A	15-Aug-25 A		0	-4	-5	
DSC-286	DSC 286 Harvard Monitoring Well Conflict	1	1	0	1	0	1	31-Jul-25 A	31-Jul-25 A			0	0	
DSC-292	DSC-292 SWC Fuhrman unknown unlocated duct bank	1	0	-1	1	0	1	04-Aug-25 A	04-Aug-25 A					
Phase-2														
2-RW-654	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.2	3	3	-7	10	0	10	18-Aug-25 A	29-Aug-25 A		0	-4	-11	
2-RW-664	Pour Roadway - Harvard to Fuhrman (W) Ph.2	2	2	-5	5	2	7	02-Sep-25 A	10-Sep-25	74	0	-11	-16	
2-RW-674	Curb - Harvard to Fuhrman (W) Ph.2	1	1	0	0	1	1	11-Sep-25	11-Sep-25	74	0	-16	-16	
2-RW-684	Patch Pave - Harvard to Fuhrman (W) Ph.2	1	1	0	0	1	1	12-Sep-25	12-Sep-25	74	0	-16	-16	
DSC-318	DSC-318 Harvard East side shallow DB in conflict with roadway	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
Phase-3														
2-RW-614	Roadway Demo & Exc - Harvard to Fuhrman (W) Ph.3	3	3	-7	10	0	10	18-Aug-25 A	29-Aug-25 A		0	3	-4	
2-RW-624	Pour Roadway - Harvard to Fuhrman (W) Ph.3	2	2	-5	5	2	7	02-Sep-25 A	10-Sep-25	45	0	-4	-9	
2-RW-634	Curb - Harvard to Fuhrman (W) Ph.3	1	1	0	0	1	1	11-Sep-25	11-Sep-25	45	0	-9	-9	
2-RW-644	Patch Pave - Harvard to Fuhrman (W) Ph.3	1	1	0	0	1	1	12-Sep-25	12-Sep-25	45	0	-9	-9	
Shelby to Harvard East Side														
2-RW-0564	Roadway Demo & Exc - Shelby to Harvard (E)	8	8	-5	5	8	13	02-Sep-25 A	18-Sep-25	74	79	0	-5	
2-RW-0604	Remove/Abandon Waterline & Appurtances - Shelby to Harvard (E)	8	8	-5	5	8	13	02-Sep-25 A	18-Sep-25	74	79	0	-5	
2-RW-0565	Pour Roadway - Shelby to Harvard (E)	4	4	0	0	4	4	19-Sep-25	24-Sep-25	74	79	-5	-5	
2-RW-0566	Curb - Shelby to Harvard (E)	2	2	0	0	2	2	25-Sep-25	26-Sep-25	74	79	-5	-5	
2-RW-0567	Patch Pave - Shelby to Harvard (E)	1	1	0	0	1	1	29-Sep-25	29-Sep-25	74	79	-5	-5	
Shelby to Harvard West Side														
2-SW-0794	Complete SCL Pole Relocation 3 ea. (by SCL) - Harvard SWC	0	0	0	0	0	0		29-Sep-25	74	79	-5	-5	
2-RW-0574	Roadway Demo & Exc - Shelby to Harvard (W)	10	10	0	0	10	10	30-Sep-25	14-Oct-25	74	79	-5	-5	
2-RW-0575	Pour Roadway - Shelby to Harvard (W)	5	5	0	0	5	5	15-Oct-25	21-Oct-25	74	79	-5	-5	
2-RW-0576	Curb - Shelby to Harvard (W)	2	2	0	0	2	2	22-Oct-25	23-Oct-25	74	79	-5	-5	
2-RW-0577	Patch Pave - Shelby to Harvard (W)	1	1	0	0	1	1	24-Oct-25	24-Oct-25	74	79	-5	-5	
Weekend Roadway Work														
Fuhrman West Side														
DSC-284	DSC 284 NWC Fuhrman Reinforced Concrete Slab in SW	1	1	0	1	0	1	30-Jul-25 A	30-Jul-25 A			0	0	
DSC-285	DSC 285 NWC Fuhrman Abandoned Brick CB Structure	1	1	0	1	0	1	30-Jul-25 A	30-Jul-25 A			0	0	
DSC-290	DSC 290 Fuhrman Intersection W, thick concrete and Ties	1	1	0	1	0	1	01-Aug-25 A	01-Aug-25 A			0	0	

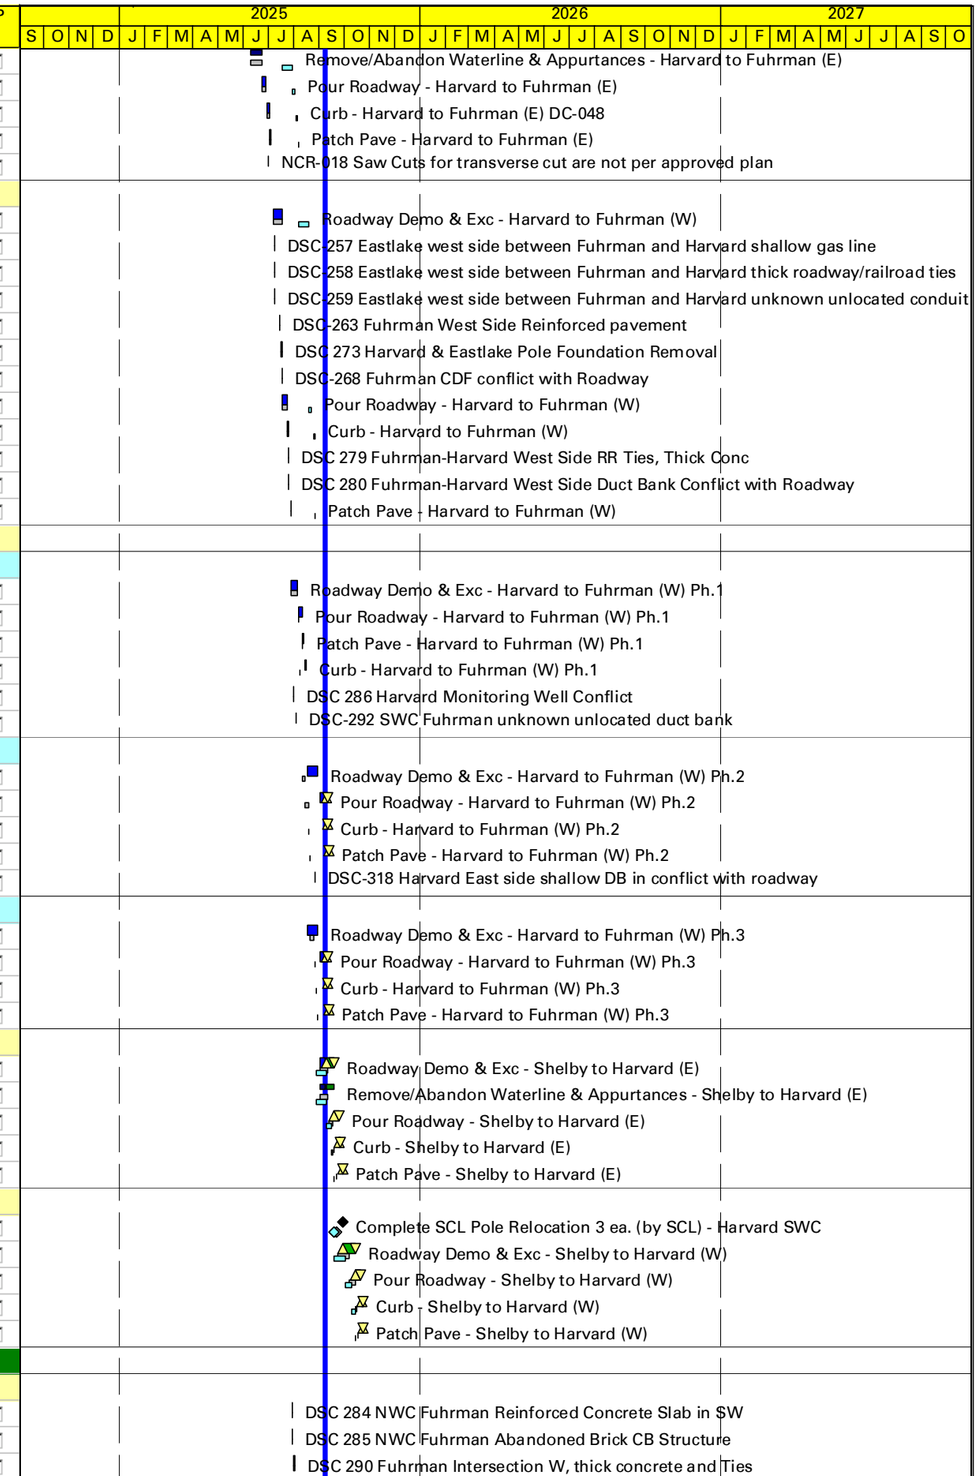

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-291	DSC 291 Fuhrman Intersection W, 2-in Steel line conflict	1	1	0	1	0	1	01-Aug-25 A	01-Aug-25 A			0	0	
2-WE-806	Remove Roadway Type 2 - Fuhrman West Side	1	1	0	1	0	1	02-Aug-25 A	02-Aug-25 A			0	0	
2-WE-816	Pour Roadway - Fuhrman West Side	1	1	0	1	0	1	03-Aug-25 A	03-Aug-25 A			0	0	
Fuhrman NEC														
2-WE-826	Remove Roadway Type 2 - Fuhrman NEC	1	1	0	0	1	1	04-Oct-25	04-Oct-25	38	54	-16	-16	
2-WE-836	Pour Roadway - Fuhrman NEC	1	1	0	0	1	1	05-Oct-25	05-Oct-25	38	54	-16	-16	
Fuhrman SEC														
2-WE-846	Remove Roadway Type 2 - Fuhrman SEC	1	1	0	0	1	1	11-Oct-25	11-Oct-25	38	54	-16	-16	
2-WE-856	Pour Roadway - Fuhrman SEC	1	1	0	0	1	1	12-Oct-25	12-Oct-25	38	54	-16	-16	
Hamlin Phase 1														
2-WE-0585	Remove Roadway Type 2 - Hamlin Ph.1 (WE)	1	1	0	0	1	1	20-Dec-25	20-Dec-25	20	18	2	2	
2-WE-0586	Pour Roadway - Hamlin Ph.1 (WE)	1	1	0	0	1	1	21-Dec-25	21-Dec-25	20	18	2	2	
Hamilin Phase 2														
2-WE-0588	Remove Roadway Type 2 - Hamlin Ph.2 (WE)	1	1	0	0	1	1	27-Dec-25	27-Dec-25	20	18	2	2	
2-WE-0589	Pour Roadway - Hamlin Ph.2 (WE)	1	1	0	0	1	1	28-Dec-25	28-Dec-25	20	18	2	2	
Hamlin Phase 3														
2-WE-0591	Remove Roadway Type 2 - Hamlin Ph.3 (WE)	1	1	0	0	1	1	03-Jan-26	03-Jan-26	20	18	2	2	
2-WE-0592	Pour Roadway - Hamlin Ph.3 (WE)	1	1	0	0	1	1	04-Jan-26	04-Jan-26	20	18	2	2	
Roanoke Phase 1														
2-WE-0594	Remove Roadway Type 2 - Roanoke Ph.1 (WE)	1	1	0	0	1	1	07-Mar-26	07-Mar-26	4	2	2	2	
2-WE-0595	Pour Roadway - Roanoke Ph.1 (WE)	1	1	0	0	1	1	08-Mar-26	08-Mar-26	4	2	2	2	
Roanoke Phase 2														
2-WE-0597	Remove Roadway Type 2 - Roanoke Ph.2 (WE)	1	1	0	0	1	1	14-Mar-26	14-Mar-26	4	2	2	2	
2-WE-0598	Pour Roadway - Roanoke Ph.2 (WE)	1	1	0	0	1	1	15-Mar-26	15-Mar-26	4	2	2	2	
Lynn Phase 1														
2-WE-0600	Remove Roadway Type 2 - Lynn Ph.1 (WE)	1	1	0	0	1	1	21-Mar-26	21-Mar-26	4	2	2	2	
2-WE-0601	Pour Roadway - Lynn Ph.1 (WE)	1	1	0	0	1	1	22-Mar-26	22-Mar-26	4	2	2	2	
Lynn Phase 2														
2-WE-0603	Remove Roadway Type 2 - Lynn Ph.2 (WE)	1	1	0	0	1	1	28-Mar-26	28-Mar-26	4	2	2	2	
2-WE-0604	Pour Roadway - Lynn Ph.2 (WE)	1	1	0	0	1	1	29-Mar-26	29-Mar-26	4	2	2	2	
Pole Foundations														
2-PF-0606	Shelby to Edgar - Pole Foundations (9 ea.)	11	11	0	0	11	11	06-Feb-26	23-Feb-26	6	1	5	5	
2-PF-0608	Shelby to Harvard - Pole Foundations (7 ea.)	9	9	0	0	9	9	24-Feb-26	06-Mar-26	6	1	5	5	
2-PF-0609	Harvard to Fuhrman - Pole Foundations (3 ea.)	5	5	0	0	5	5	09-Mar-26	13-Mar-26	6	1	5	5	
2-PF-0607	Louisa to Lynn (4 Each) - Pole Foundations (4 ea.)	6	6	0	0	6	6	23-Mar-26	30-Mar-26	11	6	5	5	
Sidewalks														
Shelby SWC														
2-SW-0612	Remove Sidewalk - Shelby SWC	1	1	0	0	1	1	16-Mar-26	16-Mar-26	6	1	5	5	
2-SW-0613	Excavate Shelter Foundation - Shelby SWC	1	1	0	0	1	1	17-Mar-26	17-Mar-26	6	1	5	5	
2-SW-0614	Form and Pour Shelter Foundation - Shelby SWC	3	3	0	0	3	3	18-Mar-26	20-Mar-26	6	1	5	5	
2-SW-0615	Grade Sidewalks - Shelby SWC	2	2	0	0	2	2	23-Mar-26	24-Mar-26	6	1	5	5	
2-SW-0616	Pour Sidewalks/Curb Ramps - Shelby SWC	4	4	0	0	4	4	25-Mar-26	30-Mar-26	10	5	5	5	
Hamlin NWC														
2-SW-0618	Remove Sidewalk - Hamlin NWC	1	1	0	0	1	1	25-Mar-26	25-Mar-26	6	1	5	5	
2-SW-0619	Trench Electrical - Hamlin NWC	1	1	0	0	1	1	26-Mar-26	26-Mar-26	6	1	5	5	
2-SW-0620	Electrical - Hamlin NWC	3	3	0	0	3	3	27-Mar-26	31-Mar-26	7	2	5	5	
2-SW-0621	Grade Sidewalks - Hamlin NWC	2	2	0	0	2	2	01-Apr-26	02-Apr-26	7	2	5	5	
2-SW-0622	Pour Sidewalks/Curb Ramps - Hamlin NWC	4	4	0	0	4	4	03-Apr-26	08-Apr-26	7	2	5	5	
Hamlin SWC														
2-SW-0624	Remove Sidewalk - Hamlin SWC	1	1	0	0	1	1	27-Mar-26	27-Mar-26	6	1	5	5	
2-SW-0625	Trench Electrical - Hamlin SWC	1	1	0	0	1	1	30-Mar-26	30-Mar-26	9	4	5	5	
2-SW-0626	Electrical - Hamlin SWC	3	3	0	0	3	3	31-Mar-26	02-Apr-26	9	4	5	5	
2-SW-0627	Grade Sidewalks - Hamlin SWC	2	2	0	0	2	2	03-Apr-26	06-Apr-26	9	4	5	5	
2-SW-0628	Pour Sidewalks/Curb Ramps - Hamlin SWC	4	4	0	0	4	4	09-Apr-26	14-Apr-26	7	2	5	5	

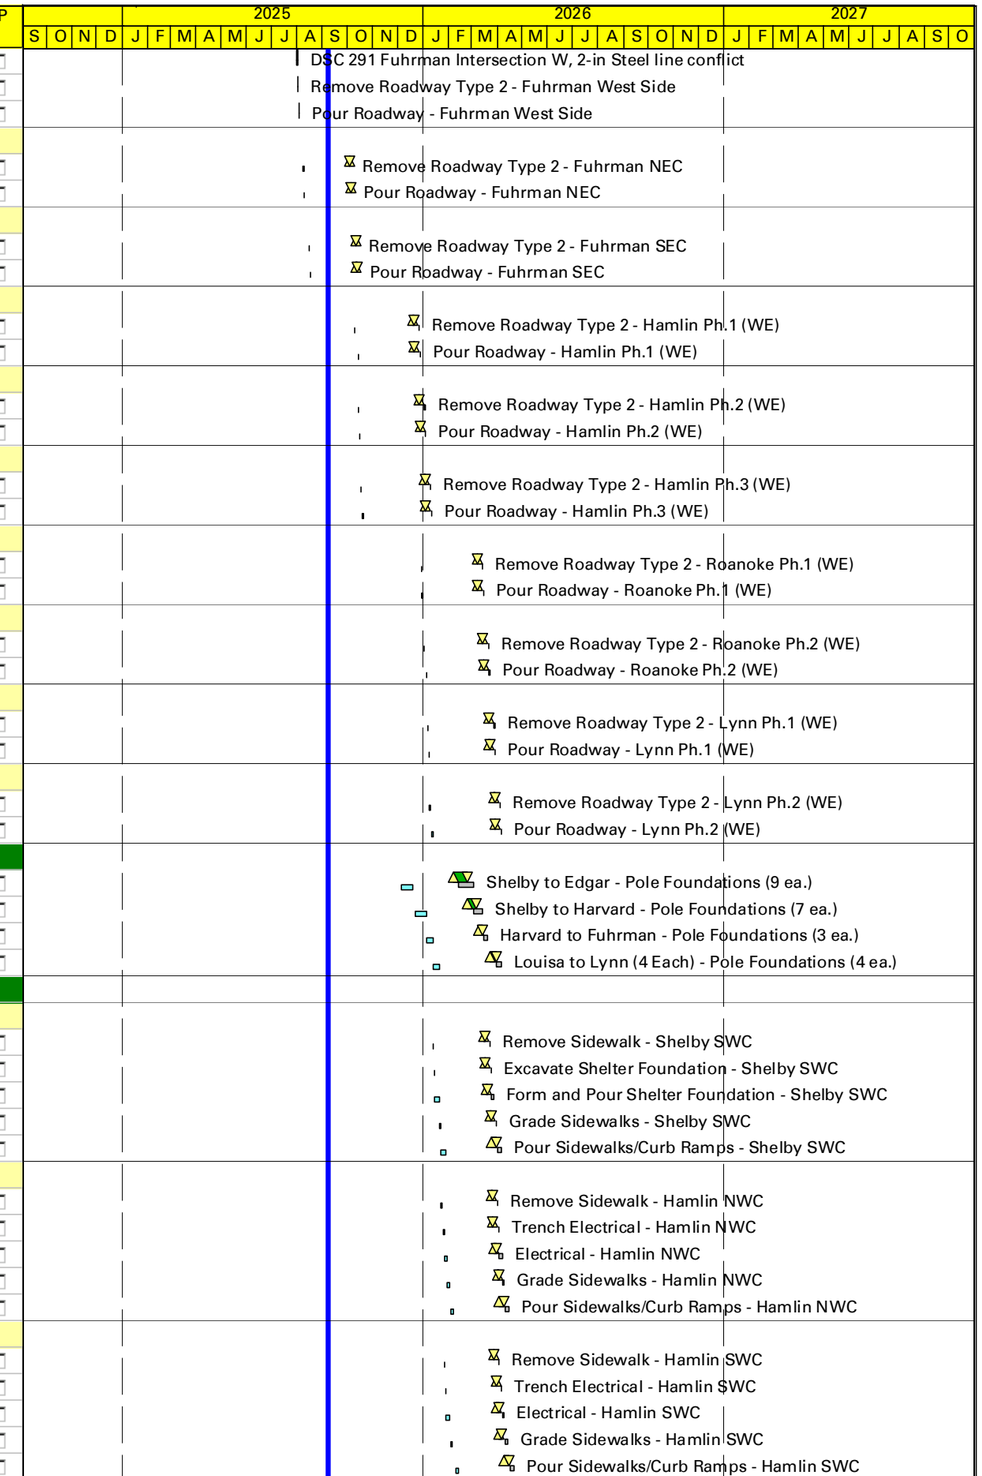

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Edgar NWC														
2-SW-0630	Remove Sidewalk - Edgar NWC	1	1	0	0	1	1	30-Mar-26	30-Mar-26	6	1	5	5	
2-SW-0631	Grade Sidewalks - Edgar NWC	1	1	0	0	1	1	30-Mar-26	30-Mar-26	6	1	5	5	
2-SW-0632	Pour Sidewalks/Curb Ramps - Edgar NWC	1	1	0	0	1	1	09-Apr-26	09-Apr-26	7	2	5	5	
Edgar SWC														
2-SW-0634	Remove Sidewalk - Edgar SWC	1	1	0	0	1	1	31-Mar-26	31-Mar-26	6	1	5	5	
2-SW-0635	Grade Sidewalks - Edgar SWC	1	1	0	0	1	1	31-Mar-26	31-Mar-26	6	1	5	5	
2-SW-0636	Pour Sidewalks/Curb Ramps - Edgar SWC	1	1	0	0	1	1	10-Apr-26	10-Apr-26	7	2	5	5	
Roanoke NWC														
2-SW-0638	Remove Sidewalk - Roanoke NWC	1	1	0	0	1	1	01-Apr-26	01-Apr-26	6	1	5	5	
2-SW-0639	Trench Electrical - Roanoke NWC	1	1	0	0	1	1	02-Apr-26	02-Apr-26	6	1	5	5	
2-SW-0640	Electrical - Roanoke NWC	2	2	0	0	2	2	03-Apr-26	06-Apr-26	10	5	5	5	
2-SW-0641	Grade Sidewalks - Roanoke NWC	1	1	0	0	1	1	07-Apr-26	07-Apr-26	10	5	5	5	
2-SW-0642	Pour Sidewalks/Curb Ramps - Roanoke NWC	3	3	0	0	3	3	13-Apr-26	15-Apr-26	7	2	5	5	
Roanoke SWC														
2-SW-0644	Remove Sidewalk - Roanoke SWC	1	1	0	0	1	1	03-Apr-26	03-Apr-26	6	1	5	5	
2-SW-0645	Trench Electrical - Roanoke SWC	1	1	0	0	1	1	06-Apr-26	06-Apr-26	6	1	5	5	
2-SW-0646	Electrical - Roanoke SWC	2	2	0	0	2	2	07-Apr-26	08-Apr-26	11	6	5	5	
2-SW-0647	Grade Sidewalks - Roanoke SWC	1	1	0	0	1	1	09-Apr-26	09-Apr-26	11	6	5	5	
2-SW-0648	Pour Sidewalks/Curb Ramps - Roanoke SWC	3	3	0	0	3	3	16-Apr-26	20-Apr-26	7	2	5	5	
Louisa NWC														
2-SW-0650	Remove Sidewalk - Louisa NWC	1	1	0	0	1	1	07-Apr-26	07-Apr-26	6	1	5	5	
2-SW-0651	Trench Electrical - Louisa NWC	1	1	0	0	1	1	08-Apr-26	08-Apr-26	6	1	5	5	
2-SW-0652	Electrical - Louisa NWC	2	2	0	0	2	2	09-Apr-26	10-Apr-26	12	7	5	5	
2-SW-0653	Grade Sidewalks - Louisa NWC	1	1	0	0	1	1	13-Apr-26	13-Apr-26	12	7	5	5	
2-SW-0654	Pour Sidewalks/Curb Ramps - Louisa NWC	3	3	0	0	3	3	21-Apr-26	23-Apr-26	7	2	5	5	
Louisa SWC														
2-SW-0656	Remove Sidewalk - Louisa SWC	1	1	0	0	1	1	09-Apr-26	09-Apr-26	6	1	5	5	
2-SW-0657	Grade Sidewalks - Louisa SWC	1	1	0	0	1	1	10-Apr-26	10-Apr-26	6	1	5	5	
2-SW-0658	Pour Sidewalks/Curb Ramps - Louisa SWC	1	1	0	0	1	1	24-Apr-26	24-Apr-26	7	2	5	5	
Shelby SEC														
2-SW-0660	Remove Sidewalk - Shelby SEC	2	2	0	0	2	2	13-Apr-26	14-Apr-26	6	1	5	5	
2-SW-0661	Grade Sidewalks - Shelby SEC	1	1	0	0	1	1	15-Apr-26	15-Apr-26	6	1	5	5	
2-SW-0662	Pour Sidewalks/Curb Ramps - Shelby SEC	3	3	0	0	3	3	27-Apr-26	29-Apr-26	7	2	5	5	
Hamlin NEC														
2-SW-0664	Remove Sidewalk - Hamlin NEC	2	2	0	0	2	2	16-Apr-26	17-Apr-26	6	1	5	5	
2-SW-0665	Trench Electrical - Hamlin NEC	2	2	0	0	2	2	20-Apr-26	21-Apr-26	6	1	5	5	
2-SW-0666	Electrical - Hamlin NEC	5	5	0	0	5	5	22-Apr-26	28-Apr-26	7	2	5	5	
2-SW-0667	Excavate Shelter Foundations - Hamlin NEC	1	1	0	0	1	1	29-Apr-26	29-Apr-26	7	2	5	5	
2-SW-0668	Form Pour Shelter Foundations - Hamlin NEC	4	4	0	0	4	4	30-Apr-26	05-May-26	7	2	5	5	
2-SW-0669	Grade Sidewalks - Hamlin NEC	1	1	0	0	1	1	06-May-26	06-May-26	7	2	5	5	
2-SW-0670	Pour Sidewalks/Curb Ramps - Hamlin NEC	4	4	0	0	4	4	07-May-26	12-May-26	7	2	5	5	
Hamlin SEC														
2-SW-0672	Remove Sidewalk - Hamlin SEC	1	1	0	0	1	1	22-Apr-26	22-Apr-26	6	1	5	5	
2-SW-0673	Trench Electrical - Hamlin SEC	1	1	0	0	1	1	23-Apr-26	23-Apr-26	6	1	5	5	
2-SW-0674	Electrical - Hamlin SEC	5	5	0	0	5	5	24-Apr-26	30-Apr-26	14	9	5	5	
2-SW-0675	Grade Sidewalks - Hamlin SEC	1	1	0	0	1	1	07-May-26	07-May-26	10	5	5	5	
2-SW-0676	Pour Sidewalks/Curb Ramps - Hamlin SEC	4	4	0	0	4	4	13-May-26	18-May-26	7	2	5	5	
Edgar NEC														
2-SW-0678	Remove Sidewalk - Edgar NEC	1	1	0	0	1	1	24-Apr-26	24-Apr-26	6	1	5	5	
2-SW-0679	Grade Sidewalks - Edgar NEC	1	1	0	0	1	1	27-Apr-26	27-Apr-26	6	1	5	5	
2-SW-0680	Pour Sidewalks/Curb Ramps - Edgar NEC	1	1	0	0	1	1	28-Apr-26	28-Apr-26	35	30	5	5	
Edgar SEC														
2-SW-0682	Remove Sidewalk - Edgar SEC	1	1	0	0	1	1	28-Apr-26	28-Apr-26	6	1	5	5	

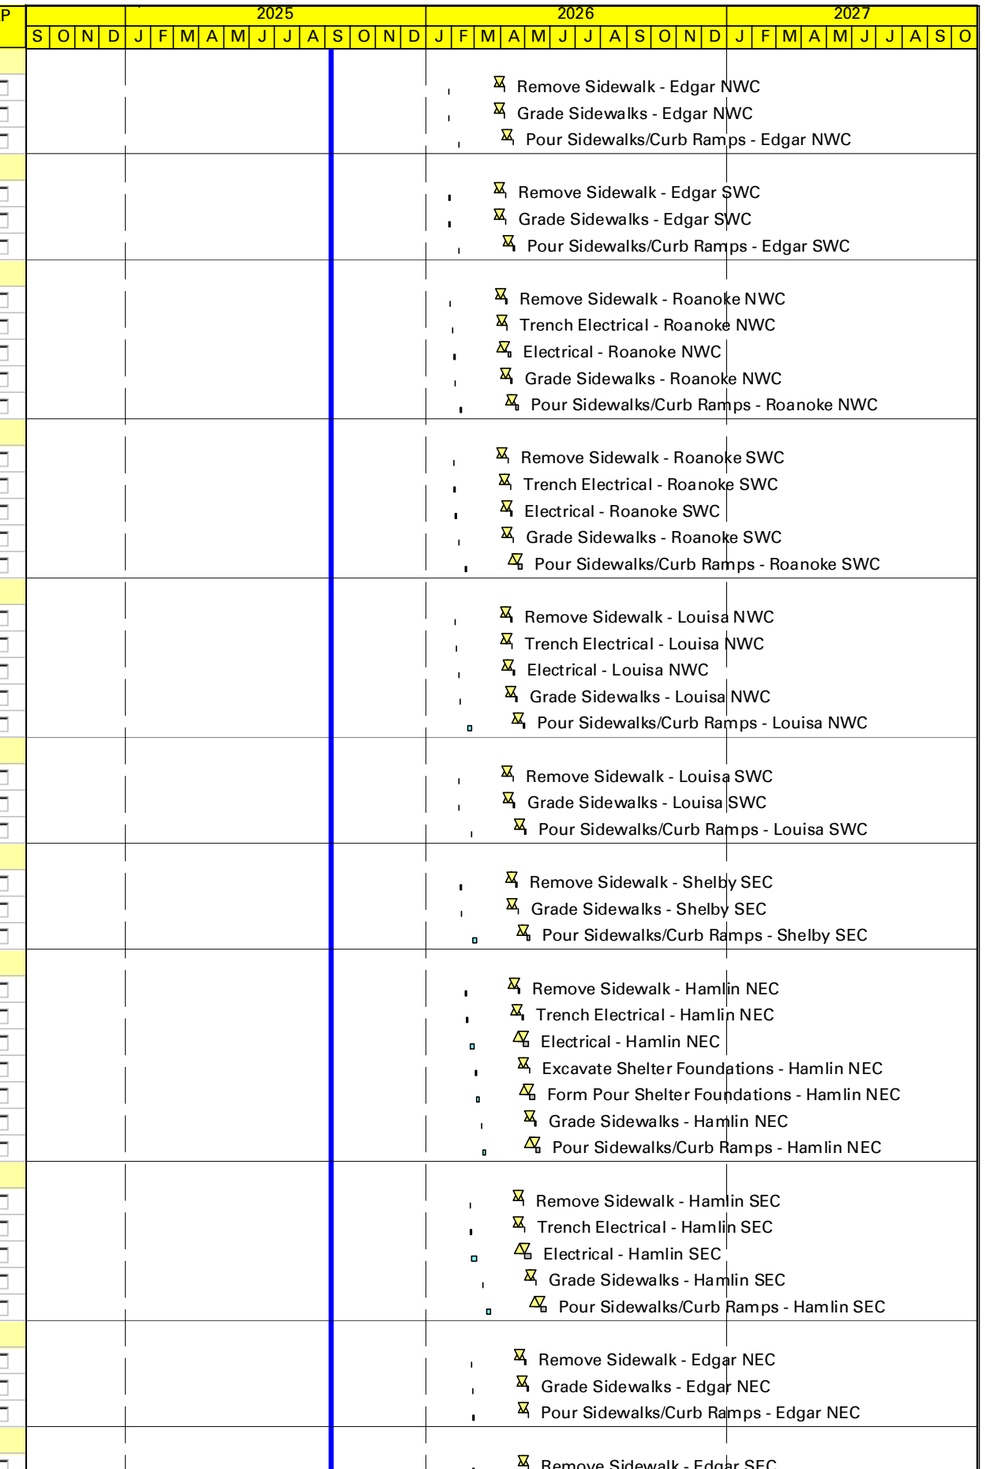

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-SW-0683	Grade Sidewalks - Edgar SEC	1	1	0	0	1	1	29-Apr-26	29-Apr-26	6	1	5	5	☐
2-SW-0684	Pour Sidewalks/Curb Ramps - Edgar SEC	1	1	0	0	1	1	30-Apr-26	30-Apr-26	34	29	5	5	☐
Roanoke NEC														
2-SW-0686	Remove Sidewalk - Roanoke NEC	1	1	0	0	1	1	30-Apr-26	30-Apr-26	6	1	5	5	☐
2-SW-0687	Trench Electrical - Roanoke NEC	1	1	0	0	1	1	01-May-26	01-May-26	6	1	5	5	☐
2-SW-0688	Electrical - Roanoke NEC	3	3	0	0	3	3	04-May-26	06-May-26	29	24	5	5	☐
2-SW-0689	Grade Sidewalks - Roanoke NEC	1	1	0	0	1	1	07-May-26	07-May-26	29	24	5	5	☐
2-SW-0690	Pour Sidewalks/Curb Ramps - Roanoke NEC	3	3	0	0	3	3	08-May-26	12-May-26	29	24	5	5	☐
Roanoke SEC														
2-SW-0692	Remove Sidewalk - Roanoke SEC	1	1	0	0	1	1	04-May-26	04-May-26	6	1	5	5	☐
2-SW-0693	Trench Electrical - Roanoke SEC	2	2	0	0	2	2	05-May-26	06-May-26	6	1	5	5	☐
2-SW-0694	Electrical - Roanoke SEC	6	6	0	0	6	6	07-May-26	14-May-26	6	1	5	5	☐
2-SW-0695	Grade Sidewalks - Roanoke SEC	1	1	0	0	1	1	15-May-26	15-May-26	6	1	5	5	☐
2-SW-0696	Pour Sidewalks/Curb Ramps - Roanoke SEC	3	3	0	0	3	3	18-May-26	20-May-26	26	21	5	5	☐
Louisa NEC														
2-SW-0698	Remove Sidewalk - Louisa NEC	1	1	0	0	1	1	07-May-26	07-May-26	6	1	5	5	☐
2-SW-0699	Trench Electrical - Louisa NEC	1	1	0	0	1	1	08-May-26	08-May-26	6	1	5	5	☐
2-SW-0700	Electrical - Louisa NEC	5	5	0	0	5	5	11-May-26	15-May-26	6	1	5	5	☐
2-SW-0701	Grade Sidewalks - Louisa NEC	1	1	0	0	1	1	18-May-26	18-May-26	6	1	5	5	☐
2-SW-0702	Pour Sidewalks/Curb Ramps - Louisa NEC	2	2	0	0	2	2	19-May-26	20-May-26	6	1	5	5	☐
Louisa SEC														
2-SW-0704	Remove Sidewalk - Louisa SEC	1	1	0	0	1	1	21-May-26	21-May-26	6	1	5	5	☐
2-SW-0705	Grade Sidewalks - Louisa SEC	1	1	0	0	1	1	22-May-26	22-May-26	6	1	5	5	☐
2-SW-0706	Pour Sidewalks/Curb Ramps - Louisa SEC	1	1	0	0	1	1	26-May-26	26-May-26	6	1	5	5	☐
Shelby NWC														
2-SW-0708	Remove Sidewalk - Shelby NWC	1	1	0	0	1	1	27-May-26	27-May-26	6	1	5	5	☐
2-SW-0709	Grade Sidewalks - Shelby NWC	1	1	0	0	1	1	28-May-26	28-May-26	6	1	5	5	☐
2-SW-0710	Pour Sidewalks/Curb Ramps - Shelby NWC	1	1	0	0	1	1	29-May-26	29-May-26	25	20	5	5	☐
Allison SWC														
2-SW-0712	Remove Sidewalk - Allison SWC	1	1	0	0	1	1	29-May-26	29-May-26	6	1	5	5	☐
2-SW-0713	Trench Electrical - Allison SWC	2	2	0	0	2	2	01-Jun-26	02-Jun-26	6	1	5	5	☐
2-SW-0714	Electrical - Allison SWC	4	4	0	0	4	4	03-Jun-26	08-Jun-26	6	1	5	5	☐
2-SW-0715	Grade Sidewalks - Allison SWC	2	2	0	0	2	2	09-Jun-26	10-Jun-26	6	1	5	5	☐
2-SW-0716	Pour Sidewalks/Curb Ramps - Allison SWC	4	4	0	0	4	4	11-Jun-26	13-Jul-26	6	1	5	5	☐
Allison NWC														
2-SW-0718	Remove Sidewalk - Allison NWC	1	1	0	0	1	1	14-Jul-26	14-Jul-26	6	1	5	5	☐
2-SW-0719	Trench Electrical - Allison NWC	1	1	0	0	1	1	15-Jul-26	15-Jul-26	6	1	5	5	☐
2-SW-0720	Electrical - Allison NWC	3	3	0	0	3	3	16-Jul-26	20-Jul-26	6	1	5	5	☐
2-SW-0721	Grade Sidewalks - Allison NWC	2	2	0	0	2	2	21-Jul-26	22-Jul-26	6	1	5	5	☐
2-SW-0722	Pour Sidewalks/Curb Ramps - Allison NWC	3	3	0	0	3	3	23-Jul-26	27-Jul-26	6	1	5	5	☐
Harvard SWC														
2-SW-0724	Remove Sidewalk - Harvard SWC	2	2	0	0	2	2	16-Mar-26	17-Mar-26	27	14	5	5	☐
2-SW-0725	Trench Electrical - Harvard SWC	1	1	0	0	1	1	18-Mar-26	18-Mar-26	27	14	5	5	☐
2-SW-0726	Electrical - Harvard SWC	5	5	0	0	5	5	19-Mar-26	25-Mar-26	27	14	5	5	☐
2-SW-0727	Excavate Shelter Foundations - Harvard SWC	1	1	0	0	1	1	26-Mar-26	26-Mar-26	27	14	5	5	☐
2-SW-0728	Form Pour Shelter Foundations - Harvard SWC	4	4	0	0	4	4	27-Mar-26	01-Apr-26	27	14	5	5	☐
2-SW-0729	Grade Sidewalks - Harvard SWC	2	2	0	0	2	2	02-Apr-26	03-Apr-26	27	14	5	5	☐
2-SW-0730	Pour Sidewalks/Curb Ramps - Harvard SWC	4	4	0	0	4	4	06-Apr-26	09-Apr-26	31	22	5	5	☐
Harvard NWC														
2-SW-0732	Remove Sidewalk - Harvard NWC	2	2	0	0	2	2	06-Apr-26	07-Apr-26	27	14	5	5	☐
2-SW-0733	Trench Electrical - Harvard NWC	1	1	0	0	1	1	08-Apr-26	08-Apr-26	27	14	5	5	☐
2-SW-0734	Electrical - Harvard NWC	3	3	0	0	3	3	09-Apr-26	13-Apr-26	27	14	5	5	☐
2-SW-0735	Grade Sidewalks - Harvard NWC	2	2	0	0	2	2	14-Apr-26	15-Apr-26	27	14	5	5	☐
2-SW-0736	Pour Sidewalks/Curb Ramps - Harvard NWC	4	4	0	0	4	4	16-Apr-26	21-Apr-26	27	18	5	5	☐

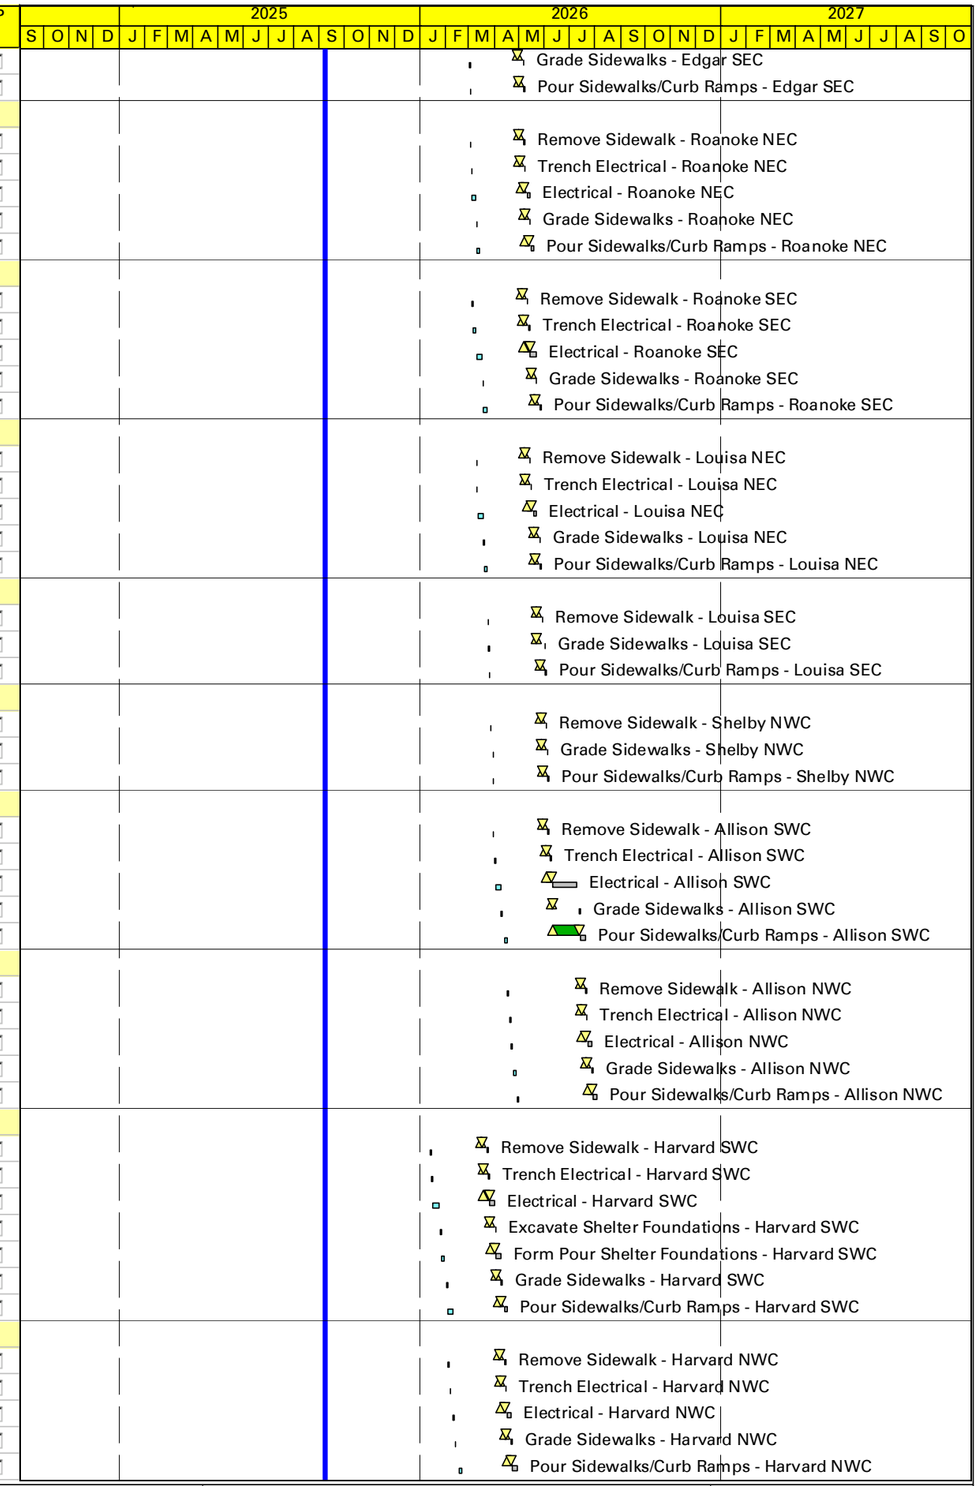

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Fuhrman NWC														
2-SW-0744	Remove Sidewalk - Fuhrman NWC	1	1	0	1	0	1	28-Jul-25 A	28-Jul-25 A		39	196	196	☐
2-SW-0745	Trench Electrical - Fuhrman NWC	1	1	0	1	0	1	29-Jul-25 A	29-Jul-25 A		39	196	196	☐
2-SW-0746	Electrical - Fuhrman NWC	2	2	-29	28	3	31	30-Jul-25 A	11-Sep-25	173	39	196	167	☐
DSC-308	DSC-308 NWC Fuhrman, Shallow Fiber Conduit Conflict	11	0	-19	16	3	19	15-Aug-25 A	11-Sep-25	173				☐
2-SW-0747	Grade Sidewalks - Fuhrman NWC	1	1	0	0	1	1	12-Sep-25	12-Sep-25	173	39	167	167	☐
2-SW-0748	Pour Sidewalks/Curb Ramps - Fuhrman NWC	3	3	0	0	3	3	15-Sep-25	17-Sep-25	173	103	167	167	☐
Fuhrman SWC														
2-SW-0738	Remove Sidewalk - Fuhrman SWC	2	2	-1	3	0	3	04-Aug-25 A	06-Aug-25 A		14	179	178	☐
2-SW-0739	Trench Electrical - Fuhrman SWC	1	1	-1	2	0	2	07-Aug-25 A	08-Aug-25 A		14	178	177	☐
2-SW-0740	Electrical - Fuhrman SWC	3	3	1	2	0	2	11-Aug-25 A	12-Aug-25 A		14	177	178	☐
DSC-304	DSC-304 Fuhrman SWC, conduits in conflict with handhole	1	0	-1	1	0	1	12-Aug-25 A	12-Aug-25 A					☐
DSC-305	DSC-305 Fuhrman SWC wooden pole utilities	1	0	-1	1	0	1	12-Aug-25 A	12-Aug-25 A					☐
DSC-306	DSC-306 Fuhrman SWC PPB in middle of ramp	1	0	-1	1	0	1	12-Aug-25 A	12-Aug-25 A					☐
2-SW-0741	Grade Sidewalks - Fuhrman SWC	2	2	0	2	0	2	13-Aug-25 A	14-Aug-25 A		14	178	178	☐
2-SW-0742	Pour Sidewalks/Curb Ramps - Fuhrman SWC	3	4	1	0	3	3	15-Sep-25	17-Sep-25	173	14	158	159	☐
Shelby NEC														
2-SW-0750	Remove Sidewalk - Shelby NEC	1	1	0	0	1	1	28-Jul-26	28-Jul-26	6	1	5	5	☐
2-SW-0751	Grade Sidewalks - Shelby NEC	1	1	0	0	1	1	29-Jul-26	29-Jul-26	6	1	5	5	☐
2-SW-0752	Pour Sidewalks/Curb Ramps - Shelby NEC	2	2	0	0	2	2	30-Jul-26	31-Jul-26	7	2	5	5	☐
Allison SEC														
2-SW-0754	Remove Sidewalk - Allison SEC	1	1	0	0	1	1	30-Jul-26	30-Jul-26	6	1	5	5	☐
2-SW-0755	Grade Sidewalks - Allison SEC	1	1	0	0	1	1	31-Jul-26	31-Jul-26	6	1	5	5	☐
2-SW-0756	Pour Sidewalks/Curb Ramps - Allison SEC	2	2	0	0	2	2	03-Aug-26	04-Aug-26	7	2	5	5	☐
Allison NEC														
2-SW-0758	Excavate Wall - Allison NEC	3	3	0	0	3	3	03-Aug-26	05-Aug-26	6	1	5	5	☐
2-SW-0759	Form Wall - Allison NEC	4	4	0	0	4	4	06-Aug-26	11-Aug-26	6	1	5	5	☐
2-SW-0760	Rebar Wall - Allison NEC	3	3	0	0	3	3	12-Aug-26	14-Aug-26	6	1	5	5	☐
2-SW-0761	Pour Wall - Allison NEC	3	3	0	0	3	3	17-Aug-26	19-Aug-26	6	1	5	5	☐
2-SW-0762	Strip Wall - Allison NEC	1	1	0	0	1	1	20-Aug-26	20-Aug-26	6	1	5	5	☐
2-SW-0763	Remove Sidewalk - Allison NEC	2	2	0	0	2	2	21-Aug-26	24-Aug-26	6	1	5	5	☐
2-SW-0764	Trench Electrical - Allison NEC	2	2	0	0	2	2	25-Aug-26	26-Aug-26	6	1	5	5	☐
2-SW-0765	Electrical - Allison NEC	5	5	0	0	5	5	27-Aug-26	02-Sep-26	6	1	5	5	☐
2-SW-0766	Grade Sidewalks - Allison NEC	2	2	0	0	2	2	03-Sep-26	04-Sep-26	6	1	5	5	☐
2-SW-0767	Pour Sidewalks/Curb Ramps - Allison NEC	4	4	0	0	4	4	08-Sep-26	11-Sep-26	6	1	5	5	☐
Harvard SEC														
2-SW-0769	Remove Sidewalk - Harvard SEC	2	2	0	0	2	2	08-Sep-26	09-Sep-26	11	6	5	5	☐
2-SW-0770	Trench Electrical - Harvard SEC	2	2	0	0	2	2	10-Sep-26	11-Sep-26	11	6	5	5	☐
2-SW-0771	Electrical - Harvard SEC	5	5	0	0	5	5	14-Sep-26	18-Sep-26	11	6	5	5	☐
2-SW-0772	Excavate Shelter Foundation - Harvard SEC	1	1	0	0	1	1	21-Sep-26	21-Sep-26	11	6	5	5	☐
2-SW-0773	Form Pour Shelter Foundation - Harvard SEC	4	4	0	0	4	4	22-Sep-26	25-Sep-26	11	6	5	5	☐
2-SW-0774	Grade Sidewalks - Harvard SEC	1	1	0	0	1	1	28-Sep-26	28-Sep-26	11	6	5	5	☐
2-SW-0775	Pour Sidewalks/Curb Ramps - Harvard SEC	5	5	0	0	5	5	29-Sep-26	05-Oct-26	11	6	5	5	☐
Harvard NEC														
2-SW-0777	Remove Sidewalk - Harvard NEC	2	2	0	0	2	2	06-Oct-26	07-Oct-26	20	15	5	5	☐
2-SW-0778	Trench Electrical - Harvard NEC	2	2	0	0	2	2	08-Oct-26	09-Oct-26	20	15	5	5	☐
2-SW-0779	Electrical - Harvard NEC	5	5	0	0	5	5	13-Oct-26	19-Oct-26	20	15	5	5	☐
2-SW-0780	Grade Sidewalks - Harvard NEC	1	1	0	0	1	1	20-Oct-26	20-Oct-26	20	15	5	5	☐
2-SW-0781	Pour Sidewalks/Curb Ramps - Harvard NEC	4	4	0	0	4	4	21-Oct-26	26-Oct-26	20	15	5	5	☐
Fuhrman SEC														
2-SW-0783	Remove Sidewalk - Fuhrman SEC	2	2	0	0	2	2	13-Oct-26	14-Oct-26	22	17	5	5	☐
2-SW-0784	Trench Electrical - Fuhrman SEC	2	2	0	0	2	2	15-Oct-26	16-Oct-26	22	17	5	5	☐
2-SW-0785	Electrical - Fuhrman SEC	3	3	0	0	3	3	19-Oct-26	21-Oct-26	22	17	5	5	☐
2-SW-0786	Grade Sidewalks - Fuhrman SEC	1	1	0	0	1	1	22-Oct-26	22-Oct-26	22	17	5	5	☐

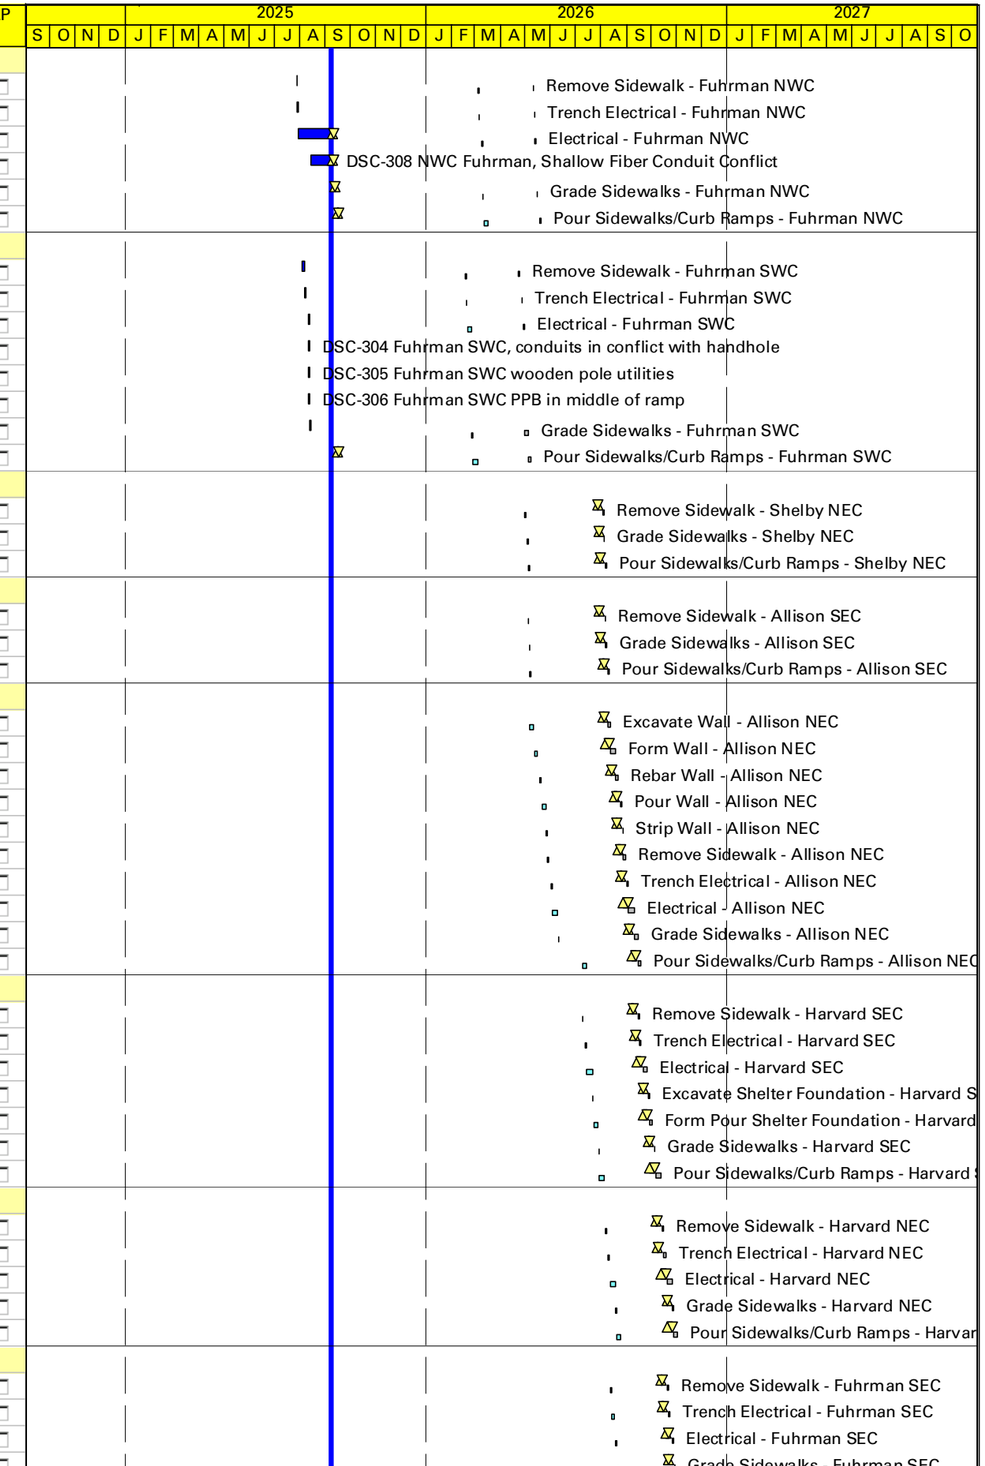

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work | BL1 LOE | Milestone | BL2 LOE | Previous MS | Actual Level of Effort | Previous Bar | Actual Work | Baseline MS | Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-SW-0787	Pour Sidewalks/Curb Ramps - Fuhrman SEC	4	4	0	0	4	4	27-Oct-26	30-Oct-26	20	15	5	5	
Fuhrman NEC														
2-SW-0789	Remove Sidewalk - Fuhrman NEC	1	1	0	0	1	1	02-Nov-26	02-Nov-26	26	21	5	5	
2-SW-0790	Trench Electrical - Fuhrman NEC	1	1	0	0	1	1	03-Nov-26	03-Nov-26	26	21	5	5	
2-SW-0791	Electrical - Fuhrman NEC	5	5	0	0	5	5	04-Nov-26	10-Nov-26	26	21	5	5	
2-SW-0792	Grade Sidewalks - Fuhrman NEC	1	1	0	0	1	1	12-Nov-26	12-Nov-26	26	21	5	5	
2-SW-0793	Pour Sidewalks/Curb Ramps - Fuhrman NEC	3	3	0	0	3	3	13-Nov-26	17-Nov-26	26	21	5	5	
Weekend Driveways														
Shelby to Hamlin West Side (1 Each)														
2-WE-0796	Remove Driveway - Shelby to Hamlin (W)	1	1	0	0	1	1	01-Aug-26	01-Aug-26	36	34	2	2	
2-WE-0797	Pour Driveway - Shelby to Hamlin (W)	1	1	0	0	1	1	02-Aug-26	02-Aug-26	36	34	2	2	
Hamlin to Edgar West Side (1 Each)														
2-WE-0799	Remove Driveway - Hamlin to Edgar (W)	1	1	0	0	1	1	08-Aug-26	08-Aug-26	36	34	2	2	
2-WE-0800	Pour Driveway - Hamlin to Edgar (W)	1	1	0	0	1	1	09-Aug-26	09-Aug-26	36	34	2	2	
Edgar to Roadoke West Side (1 Each)														
2-WE-0802	Remove Driveway - Edgar to Roanoke (W)	1	1	0	0	1	1	15-Aug-26	15-Aug-26	36	34	2	2	
2-WE-0803	Pour Driveway - Edgar to Roanoke (W)	1	1	0	0	1	1	16-Aug-26	16-Aug-26	36	34	2	2	
Louisa to Lynn West Side (3 Each)														
2-WE-0805	Remove Driveway - Louisa to Lynn (W)	1	1	0	0	1	1	22-Aug-26	22-Aug-26	36	34	2	2	
2-WE-0806	Pour Driveway - Louisa to Lynn (W)	1	1	0	0	1	1	23-Aug-26	23-Aug-26	36	34	2	2	
Landscaping														
2-LS-0809	Install Irrigation - Zone 2	10	10	0	0	10	10	18-Nov-26	03-Dec-26	36	31	5	5	
2-LS-0810	Trees and Shrubs - Zone 2	20	20	0	0	20	20	04-Dec-26	04-Jan-27	36	31	5	5	
SCL Services														
Hamlin SDOT Service														
2-SCL-0813	Install Meter Cabinet - Hamlin	1	1	0	0	1	1	19-May-26	19-May-26	7	2	5	5	
2-SCL-0814	SDOT Inspection - Hamlin	5	5	0	0	5	5	20-May-26	27-May-26	7	2	5	5	
2-SCL-0815	SDCI Inspection - Hamlin	5	5	0	0	5	5	28-May-26	03-Jun-26	7	2	5	5	
2-SCL-0816	SCL Inspection - Hamlin	21	21	0	0	21	21	04-Jun-26	29-Jul-26	7	2	5	5	
2-SCL-0817	SCL Heat Up Cabinet - Hamlin	21	21	0	0	21	21	30-Jul-26	27-Aug-26	7	2	5	5	
2-SCL-0818	Remove Old Service Gear - Hamlin	1	1	0	0	1	1	28-Aug-26	28-Aug-26	7	2	5	5	
Roanoke SDOT Service														
2-SCL-0820	Install Meter Cabinet - Roanoke	1	1	0	0	1	1	21-May-26	21-May-26	26	21	5	5	
2-SCL-0821	SDOT Inspection - Roanoke	5	5	0	0	5	5	22-May-26	29-May-26	26	21	5	5	
2-SCL-0822	SDCI Inspection - Roanoke	5	5	0	0	5	5	01-Jun-26	05-Jun-26	26	21	5	5	
2-SCL-0823	SCL Inspection - Roanoke	21	21	0	0	21	21	08-Jun-26	31-Jul-26	26	21	5	5	
2-SCL-0824	SCL Heat Up Cabinet - Roanoke	21	21	0	0	21	21	03-Aug-26	31-Aug-26	26	21	5	5	
2-SCL-0825	Remove Old Service Gear - Roanoke	1	1	0	0	1	1	01-Sep-26	01-Sep-26	26	21	5	5	
Louisa SDOT Service														
2-SCL-870	Install Meter Cabinet - Louisa	1	1	0	0	1	1	21-May-26	21-May-26	99	94	5	5	
2-SCL-880	SDOT Inspection - Louisa	5	5	0	0	5	5	22-May-26	29-May-26	99	94	5	5	
2-SCL-890	SDCI Inspection - Louisa	5	5	0	0	5	5	01-Jun-26	05-Jun-26	99	94	5	5	
2-SCL-900	SCL Inspection - Louisa	21	21	0	0	21	21	08-Jun-26	31-Jul-26	99	94	5	5	
2-SCL-910	SCL Heat Up Cabinet - Louisa	21	21	0	0	21	21	03-Aug-26	31-Aug-26	99	94	5	5	
2-SCL-920	Remove Old Service Gear - Louisa	1	1	0	0	1	1	01-Sep-26	01-Sep-26	108	103	5	5	
Allison SDOT Service														
2-SCL-0827	Install Meter Cabinet - Allison	1	1	0	0	1	1	14-Sep-26	14-Sep-26	6	1	5	5	
2-SCL-0828	SDOT Inspection - Allison	5	5	0	0	5	5	15-Sep-26	21-Sep-26	6	1	5	5	
2-SCL-0829	SDCI Inspection - Allison	5	5	0	0	5	5	22-Sep-26	28-Sep-26	6	1	5	5	
2-SCL-0830	SCL Inspection - Allison	21	21	0	0	21	21	29-Sep-26	28-Oct-26	6	1	5	5	
2-SCL-0831	SCL Heat Up Cabinet - Allison	21	21	0	0	21	21	29-Oct-26	01-Dec-26	6	1	5	5	
2-SCL-0832	Remove Old Service Gear - Allison	1	1	0	0	1	1	02-Dec-26	02-Dec-26	6	1	5	5	
Harvard SDOT Service														
2-SCL-0834	Install Meter Cabinet - Harvard	1	1	0	0	1	1	06-Oct-26	06-Oct-26	11	6	5	5	

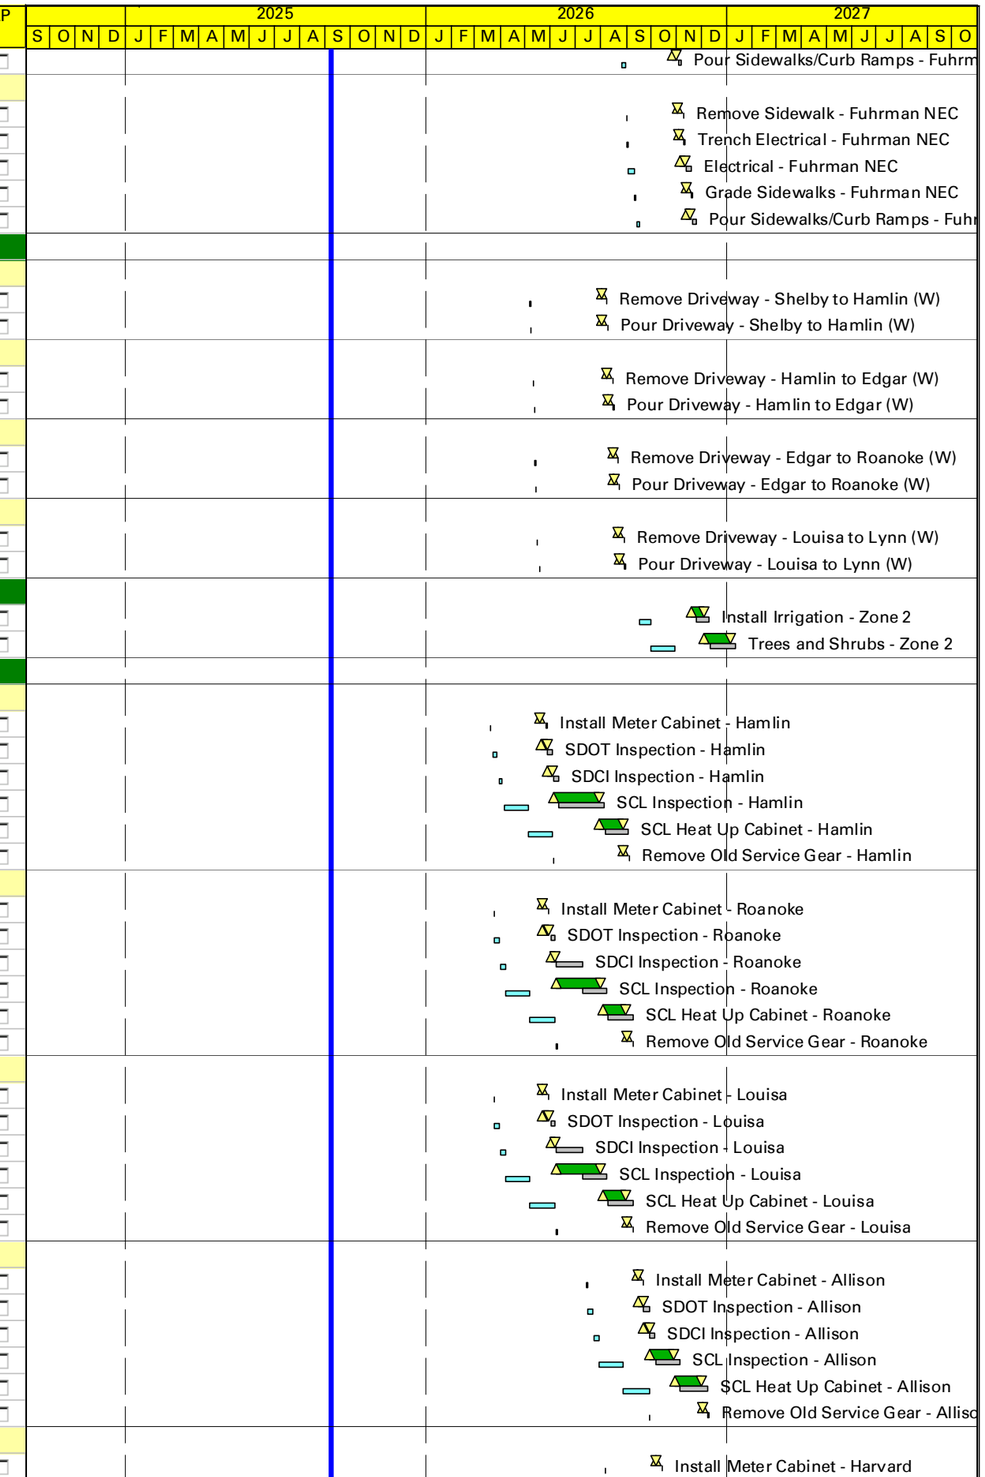

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort; Critical Remaining Work; BL1 LOE; Milestone; BL2 LOE; Previous MS; Actual Level of Effort; Previous Bar; Actual Work; Baseline MS; Remaining Work; Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-SCL-0835	SDOT Inspection - Harvard	5	5	0	0	5	5	07-Oct-26	14-Oct-26	11	6	5	5	☐
2-SCL-0836	SDCI Inspection - Harvard	5	5	0	0	5	5	15-Oct-26	21-Oct-26	11	6	5	5	☐
2-SCL-0837	SCL Inspection - Harvard	21	21	0	0	21	21	22-Oct-26	20-Nov-26	11	6	5	5	☐
2-SCL-0838	SCL Heat Up Cabinet - Harvard	21	21	0	0	21	21	23-Nov-26	23-Dec-26	11	6	5	5	☐
2-SCL-0839	Remove Old Service Gear - Harvard	1	1	0	0	1	1	24-Dec-26	24-Dec-26	11	6	5	5	☐
Fuhrman SDOT Service														
2-SCL-0841	Install Meter Cabinet - Fuhrman	1	1	0	0	1	1	02-Nov-26	02-Nov-26	20	15	5	5	☐
2-SCL-0842	SDOT Inspection - Fuhrman	5	5	0	0	5	5	03-Nov-26	09-Nov-26	20	15	5	5	☐
2-SCL-0843	SDCI Inspection - Fuhrman	5	5	0	0	5	5	10-Nov-26	17-Nov-26	20	15	5	5	☐
2-SCL-0844	SCL Inspection - Fuhrman	21	21	0	0	21	21	18-Nov-26	18-Dec-26	20	15	5	5	☐
2-SCL-0845	SCL Heat Up Cabinet - Fuhrman	21	21	0	0	21	21	21-Dec-26	21-Jan-27	20	15	5	5	☐
2-SCL-0846	Remove Old Service Gear - Fuhrman	1	1	0	0	1	1	22-Jan-27	22-Jan-27	20	15	5	5	☐
Hamlin SB Station KCM Service														
2-SCL-0848	Install Meter Cabinet - Hamlin SB Station	1	1	0	0	1	1	15-Apr-26	15-Apr-26	128	123	5	5	☐
2-SCL-0849	SDOT Inspection - Hamlin SB Station	5	5	0	0	5	5	16-Apr-26	22-Apr-26	128	123	5	5	☐
2-SCL-0850	SDCI Inspection - Hamlin SB Station	5	5	0	0	5	5	23-Apr-26	29-Apr-26	128	123	5	5	☐
2-SCL-0851	SCL Inspection - Hamlin SB Station	21	21	0	0	21	21	30-Apr-26	29-May-26	128	123	5	5	☐
2-SCL-0852	SCL Heat Up Cabinet - Hamlin SB Station	21	21	0	0	21	21	01-Jun-26	24-Jul-26	128	123	5	5	☐
Hamlin NB Station KCM Service														
2-SCL-0854	Install Meter Cabinet - Hamlin NB Station	1	1	0	0	1	1	13-May-26	13-May-26	105	100	5	5	☐
2-SCL-0855	SDOT Inspection - Hamlin NB Station	5	5	0	0	5	5	14-May-26	20-May-26	105	100	5	5	☐
2-SCL-0856	SDCI Inspection - Hamlin NB Station	5	5	0	0	5	5	21-May-26	28-May-26	105	100	5	5	☐
2-SCL-0857	SCL Inspection - Hamlin NB Station	21	21	0	0	21	21	29-May-26	23-Jul-26	105	100	5	5	☐
2-SCL-0858	SCL Heat Up Cabinet - Hamlin NB Station	21	21	0	0	21	21	24-Jul-26	21-Aug-26	105	100	5	5	☐
Harvard SB Station KCM Service														
2-SCL-0860	Install Meter Cabinet - Harvard SB Station	1	1	0	0	1	1	10-Apr-26	10-Apr-26	142	113	29	29	☐
2-SCL-0861	SDOT Inspection - Harvard SB Station	5	5	0	0	5	5	13-Apr-26	17-Apr-26	142	113	29	29	☐
2-SCL-0862	SDCI Inspection - Harvard SB Station	5	5	0	0	5	5	20-Apr-26	24-Apr-26	142	113	29	29	☐
2-SCL-0863	SCL Inspection - Harvard SB Station	21	21	0	0	21	21	27-Apr-26	26-May-26	142	113	29	29	☐
2-SCL-0864	SCL Heat Up Cabinet - Harvard SB Station	21	21	0	0	21	21	27-May-26	21-Jul-26	142	113	29	29	☐
Harvard NB Station KCM Service														
2-SCL-0866	Install Meter Cabinet - Harvard NB Station	1	1	0	0	1	1	22-Apr-26	22-Apr-26	27	14	13	13	☐
2-SCL-0867	SDOT Inspection - Harvard NB Station	5	5	0	0	5	5	23-Apr-26	29-Apr-26	27	14	13	13	☐
2-SCL-0868	SDCI Inspection - Harvard NB Station	5	5	0	0	5	5	30-Apr-26	06-May-26	27	14	13	13	☐
2-SCL-0869	SCL Inspection - Harvard NB Station	21	21	0	0	21	21	07-May-26	05-Jun-26	27	14	13	13	☐
2-SCL-0870	SCL Heat Up Cabinet - Harvard NB Station	21	21	0	0	21	21	08-Jun-26	31-Jul-26	27	14	13	13	☐
Signals														
Hamlin														
2-SIG-0873	Install Poles - Hamlin	4	4	0	0	4	4	31-Aug-26	03-Sep-26	7	2	5	5	☐
2-SIG-0874	Build Signal - Hamlin	12	12	0	0	12	12	04-Sep-26	22-Sep-26	7	2	5	5	☐
2-SIG-0875	SDOT Inspection - Hamlin	5	5	0	0	5	5	23-Sep-26	29-Sep-26	7	2	5	5	☐
2-SIG-0876	SDOT Commission - Hamlin	10	10	0	0	10	10	30-Sep-26	14-Oct-26	80	75	5	5	☐
2-SIG-0877	Demo Old Signal & Temp Signal - Hamlin	2	2	0	0	2	2	15-Oct-26	16-Oct-26	80	75	5	5	☐
Roanoke														
2-SIG-0879	Install Poles - Roanoke	2	2	0	0	2	2	30-Sep-26	01-Oct-26	7	2	5	5	☐
2-SIG-0880	Build Signal - Roanoke	10	10	0	0	10	10	02-Oct-26	16-Oct-26	7	2	5	5	☐
2-SIG-0881	SDOT Inspection - Roanoke	5	5	0	0	5	5	19-Oct-26	23-Oct-26	7	2	5	5	☐
2-SIG-0882	SDOT Commission - Roanoke	10	10	0	0	10	10	26-Oct-26	06-Nov-26	7	2	5	5	☐
2-SIG-0883	Demo Old Signal & Temp Signal - Roanoke	2	2	0	0	2	2	09-Nov-26	10-Nov-26	7	2	5	5	☐
Louisa														
2-SIG-901	Install Poles - Louisa	4	4	0	0	4	4	02-Oct-26	07-Oct-26	18	13	5	5	☐
2-SIG-911	Build Signal - Louisa	12	12	0	0	12	12	08-Oct-26	26-Oct-26	18	13	5	5	☐
2-SIG-921	SDOT Inspection - Louisa	5	5	0	0	5	5	27-Oct-26	02-Nov-26	56	51	5	5	☐
2-SIG-931	SDOT Commission - Louisa	10	10	0	0	10	10	03-Nov-26	17-Nov-26	56	51	5	5	☐

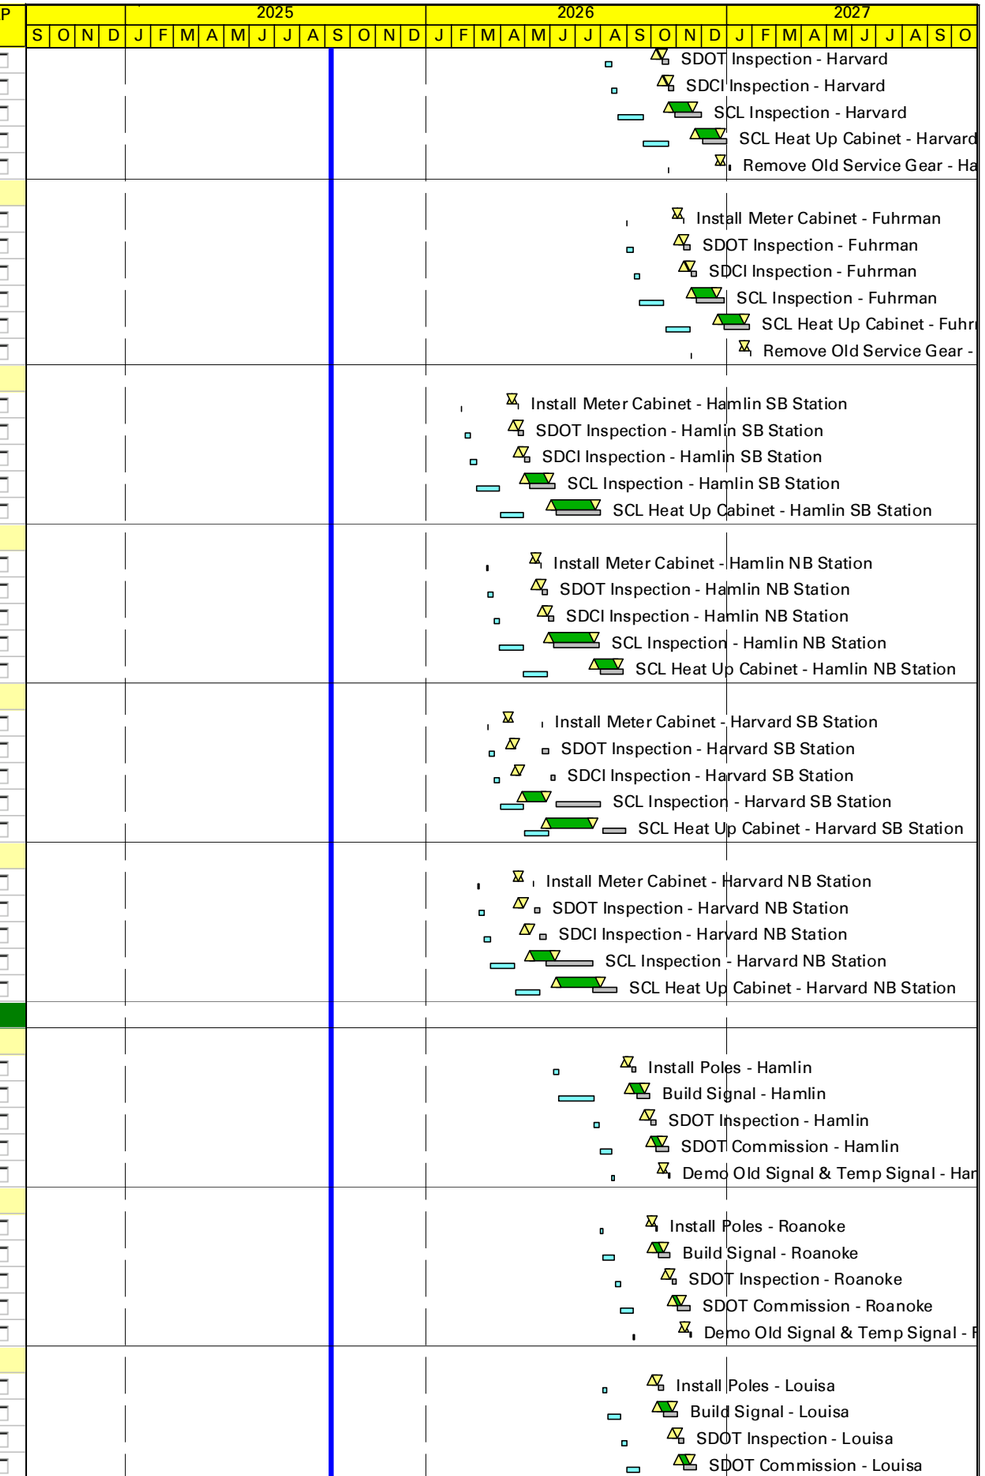

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-SIG-941	Demo Old Signal & Temp Signal - Louisa	2	2	0	0	2	2	18-Nov-26	19-Nov-26	56	51	5	5	☐
Allison														
2-SIG-0885	Install Poles - Allison	2	2	0	0	2	2	12-Nov-26	13-Nov-26	7	2	5	5	☐
2-SIG-0886	Build Signal - Allison	10	10	0	0	10	10	16-Nov-26	01-Dec-26	7	2	5	5	☐
2-SIG-0887	SDOT Inspection - Allison	5	5	0	0	5	5	02-Dec-26	08-Dec-26	36	31	5	5	☐
2-SIG-0888	SDOT Commission - Allison	10	10	0	0	10	10	09-Dec-26	22-Dec-26	36	31	5	5	☐
2-SIG-0889	Demo Old Signal & Temp Signal - Allison	2	2	0	0	2	2	23-Dec-26	24-Dec-26	36	31	5	5	☐
Harvard														
2-SIG-0891	Install Poles - Harvard	2	2	0	0	2	2	03-Dec-26	04-Dec-26	6	1	5	5	☐
2-SIG-0892	Build Signal - Harvard	8	8	0	0	8	8	07-Dec-26	16-Dec-26	6	1	5	5	☐
2-SIG-0893	SDOT Inspection - Harvard	5	5	0	0	5	5	17-Dec-26	23-Dec-26	26	21	5	5	☐
2-SIG-0894	SDOT Commission - Harvard	10	10	0	0	10	10	24-Dec-26	08-Jan-27	26	21	5	5	☐
2-SIG-0895	Demo Old Signal & Temp Signal - Harvard	2	2	0	0	2	2	11-Jan-27	12-Jan-27	26	21	5	5	☐
Fuhrman														
2-SIG-0897	Install Poles - Fuhrman	2	2	0	0	2	2	28-Dec-26	29-Dec-26	11	6	5	5	☐
2-SIG-0898	Build Signal - Fuhrman	8	8	0	0	8	8	30-Dec-26	11-Jan-27	11	6	5	5	☐
2-SIG-0899	SDOT Inspection - Fuhrman	5	5	0	0	5	5	12-Jan-27	19-Jan-27	11	6	5	5	☐
2-SIG-0900	SDOT Commission - Fuhrman	10	10	0	0	10	10	20-Jan-27	02-Feb-27	11	6	5	5	☐
2-SIG-0901	Demo Old Signal & Temp Signal - Fuhrman	2	2	0	0	2	2	03-Feb-27	04-Feb-27	11	6	5	5	☐
Lighting														
Hamlin Schematic														
2-EL-0904	Build Schematic, Poles, Luminaires Wiring - Hamlin Schematic	10	10	0	0	10	10	23-Sep-26	06-Oct-26	61	56	5	5	☐
2-EL-0905	SCL Final Inspection - Hamlin Schematic	10	10	0	0	10	10	07-Oct-26	21-Oct-26	61	56	5	5	☐
2-EL-0906	SCL Commission Lighting - Hamlin Schematic	15	15	0	0	15	15	22-Oct-26	12-Nov-26	61	56	5	5	☐
2-EL-0907	Demo Old Lighting - Hamlin Schematic	2	2	0	0	2	2	13-Nov-26	16-Nov-26	61	56	5	5	☐
Allison Schematic														
2-EL-0909	Build Schematic, Poles, Luminaires Wiring - Allison Schematic	5	5	0	0	5	5	02-Dec-26	08-Dec-26	22	17	5	5	☐
2-EL-0910	SCL Final Inspection - Allison Schematic	10	10	0	0	10	10	09-Dec-26	22-Dec-26	22	17	5	5	☐
2-EL-0911	SCL Commission Lighting - Allison Schematic	15	15	0	0	15	15	23-Dec-26	14-Jan-27	22	17	5	5	☐
2-EL-0912	Demo Old Lighting - Allison Schematic	2	2	0	0	2	2	15-Jan-27	19-Jan-27	22	17	5	5	☐
Harvard Schematic														
2-EL-0934	SCL Service Commissioning - Harvard Schematic	21	21	0	0	21	21	22-Apr-26	20-May-26	153	148	5	5	☐
2-EL-0914	Build Schematic, Poles, Luminaires Wiring - Harvard Schematic	10	10	0	0	10	10	17-Dec-26	31-Dec-26	6	1	5	5	☐
2-EL-0915	SCL Final Inspection - Harvard Schematic	10	10	0	0	10	10	04-Jan-27	15-Jan-27	8	3	5	5	☐
2-EL-0916	SCL Commission Lighting - Harvard Schematic	15	15	0	0	15	15	19-Jan-27	08-Feb-27	8	3	5	5	☐
2-EL-0917	Demo Old Lighting - Harvard Schematic	2	2	0	0	2	2	09-Feb-27	10-Feb-27	8	3	5	5	☐
Fuhrman Schematic														
2-EL-0919	Build Schematic, Poles, Luminaires Wiring - Fuhrman Schematic	2	2	0	0	2	2	04-Jan-27	05-Jan-27	6	1	5	5	☐
2-EL-0920	SCL Final Inspection - Fuhrman Schematic	10	10	0	0	10	10	06-Jan-27	20-Jan-27	8	3	5	5	☐
2-EL-0921	SCL Commission Lighting - Fuhrman Schematic	15	15	0	0	15	15	21-Jan-27	10-Feb-27	8	3	5	5	☐
2-EL-0922	Demo Old Lighting - Fuhrman Schematic	2	2	0	0	2	2	11-Feb-27	12-Feb-27	8	3	5	5	☐
Roanoke Schematic														
2-EL-0924	Build Schematic, Poles, Luminaires Wiring - Roanoke Schematic	1	1	0	0	1	1	06-Jan-27	06-Jan-27	6	1	5	5	☐
2-EL-0925	SCL Final Inspection - Roanoke Schematic	10	10	0	0	10	10	07-Jan-27	21-Jan-27	8	3	5	5	☐
2-EL-0926	SCL Commission Lighting - Roanoke Schematic	15	15	0	0	15	15	22-Jan-27	11-Feb-27	8	3	5	5	☐
2-EL-0927	Demo Old Lighting - Roanoke Schematic	1	1	0	0	1	1	12-Feb-27	12-Feb-27	8	3	5	5	☐
Louisa Schematic														
2-EL-0929	Build Schematic, Poles, Luminaires Wiring - Louisa Schematic	2	2	0	0	2	2	07-Jan-27	08-Jan-27	6	1	5	5	☐
2-EL-0930	SCL Final Inspection - Louisa Schematic	10	10	0	0	10	10	11-Jan-27	25-Jan-27	6	1	5	5	☐
2-EL-0931	SCL Commission Lighting - Louisa Schematic	15	15	0	0	15	15	26-Jan-27	16-Feb-27	6	1	5	5	☐
2-EL-0932	Demo Old Lighting - Louisa Schematic	1	1	0	0	1	1	17-Feb-27	17-Feb-27	6	1	5	5	☐
Stations														
Hamlin SB Station														
2-STN-0935	Install Shelters (2 Each) - Hamlin SB Station (OFM)	10	10	0	0	10	10	15-Apr-26	28-Apr-26	169	164	5	5	☐

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
2-STN-0936	Install Amenities - Hamlin SB Station	1	1	0	0	1	1	29-Apr-26	29-Apr-26	169	164	5	5	☐
2-STN-0937	Install Tech Pylon - Hamlin SB Station	1	1	0	0	1	1	30-Apr-26	30-Apr-26	169	164	5	5	☐
Hamlin NB Station														
2-STN-0939	Install Shelters (2 Each) - Hamlin NB Station	10	10	0	0	10	10	13-May-26	27-May-26	146	141	5	5	☐
2-STN-0940	Install Amenities - Hamlin NB Station	1	1	0	0	1	1	28-May-26	28-May-26	146	141	5	5	☐
2-STN-0941	Install Tech Pylon - Hamlin NB Station	1	1	0	0	1	1	29-May-26	29-May-26	146	141	5	5	☐
Harvard SB Station														
2-STN-0943	Install Shelters (2 Each) - Harvard SB Station (OFM)	10	10	0	0	10	10	10-Apr-26	23-Apr-26	184	179	5	5	☐
2-STN-0944	Install Amenities - Harvard SB Station	1	1	0	0	1	1	24-Apr-26	24-Apr-26	184	179	5	5	☐
2-STN-0945	Install Tech Pylon - Harvard SB Station	1	1	0	0	1	1	27-Apr-26	27-Apr-26	184	179	5	5	☐
Harvard NB Station														
2-STN-0947	Install Shelters (2 Each) - Harvard NB Station	10	10	0	0	10	10	22-Apr-26	05-May-26	177	164	13	13	☐
2-STN-0948	Install Amenities - Harvard NB Station	1	1	0	0	1	1	06-May-26	06-May-26	177	164	13	13	☐
2-STN-0949	Install Tech Pylon - Harvard NB Station	1	1	0	0	1	1	07-May-26	07-May-26	177	164	13	13	☐
Station Electrical														
Hamlin SB														
2-SE-0952	Install Electrical - Hamlin SB Station	5	5	0	0	5	5	27-Jul-26	31-Jul-26	128	123	5	5	☐
2-SE-0953	KCM Inspection - Hamlin SB Station	5	5	0	0	5	5	03-Aug-26	07-Aug-26	128	123	5	5	☐
2-SE-0954	Commission Station Electrical - Hamlin SB Station	1	1	0	0	1	1	10-Aug-26	10-Aug-26	128	123	5	5	☐
Hamlin NB														
2-SE-0956	Install Electrical - Hamlin NB Station	5	5	0	0	5	5	24-Aug-26	28-Aug-26	105	100	5	5	☐
2-SE-0957	KCM Inspection - Hamlin NB Station	5	5	0	0	5	5	31-Aug-26	04-Sep-26	109	104	5	5	☐
2-SE-0958	Commission Station Electrical - Hamlin NB Station	1	1	0	0	1	1	08-Sep-26	08-Sep-26	109	104	5	5	☐
Harvard SB														
2-SE-0960	Install Electrical - Harvard SB Station	5	5	0	0	5	5	31-Aug-26	04-Sep-26	105	100	5	5	☐
2-SE-0961	KCM Inspection - Harvard SB Station	5	5	0	0	5	5	08-Sep-26	14-Sep-26	105	100	5	5	☐
2-SE-0962	Commission Station Electrical - Harvard SB Station	1	1	0	0	1	1	15-Sep-26	15-Sep-26	105	100	5	5	☐
Hardscapes After Electrical Demo														
Hamlin														
2-HS-0965	Remove Foundations - Hamlin	1	1	0	0	1	1	19-Oct-26	19-Oct-26	80	75	5	5	☐
2-HS-0966	Prep Sidewalks - Hamlin	1	1	0	0	1	1	20-Oct-26	20-Oct-26	80	75	5	5	☐
2-HS-0967	Pour Sidewalks - Hamlin	1	1	0	0	1	1	21-Oct-26	21-Oct-26	80	75	5	5	☐
Roanoke														
2-HS-0969	Remove Foundations - Roanoke	1	1	0	0	1	1	12-Nov-26	12-Nov-26	64	59	5	5	☐
2-HS-0970	Prep Sidewalks - Roanoke	1	1	0	0	1	1	13-Nov-26	13-Nov-26	64	59	5	5	☐
2-HS-0971	Pour Sidewalks - Roanoke	1	1	0	0	1	1	16-Nov-26	16-Nov-26	64	59	5	5	☐
Louisa														
2-HS-983	Remove Foundations - Louisa	1	1	0	0	1	1	20-Nov-26	20-Nov-26	56	51	5	5	☐
2-HS-993	Prep Sidewalks - Louisa	1	1	0	0	1	1	23-Nov-26	23-Nov-26	56	51	5	5	☐
2-HS-1003	Pour Sidewalks - Louisa	1	1	0	0	1	1	24-Nov-26	24-Nov-26	56	51	5	5	☐
Allison														
2-HS-0973	Remove Foundations - Allison	1	1	0	0	1	1	28-Dec-26	28-Dec-26	36	31	5	5	☐
2-HS-0974	Prep Sidewalks - Allison	1	1	0	0	1	1	29-Dec-26	29-Dec-26	36	31	5	5	☐
2-HS-0975	Pour Sidewalks - Allison	1	1	0	0	1	1	30-Dec-26	30-Dec-26	36	31	5	5	☐
Harvard														
2-HS-0977	Remove Foundations - Harvard	1	1	0	0	1	1	13-Jan-27	13-Jan-27	26	21	5	5	☐
2-HS-0978	Prep Sidewalks - Harvard	1	1	0	0	1	1	14-Jan-27	14-Jan-27	26	21	5	5	☐
2-HS-0979	Pour Sidewalks - Harvard	1	1	0	0	1	1	15-Jan-27	15-Jan-27	26	21	5	5	☐
Fuhrman														
2-HS-0981	Remove Foundations - Fuhrman	1	1	0	0	1	1	05-Feb-27	05-Feb-27	11	6	5	5	☐
2-HS-0982	Prep Sidewalks - Fuhrman	1	1	0	0	1	1	08-Feb-27	08-Feb-27	11	6	5	5	☐
2-HS-0983	Pour Sidewalks - Fuhrman	1	1	0	0	1	1	09-Feb-27	09-Feb-27	11	6	5	5	☐
PBL Buffers														
2-PBL-0985	Pour PBL Buffers - Zone 2	20	20	0	0	20	20	18-Nov-26	17-Dec-26	26	21	5	5	☐

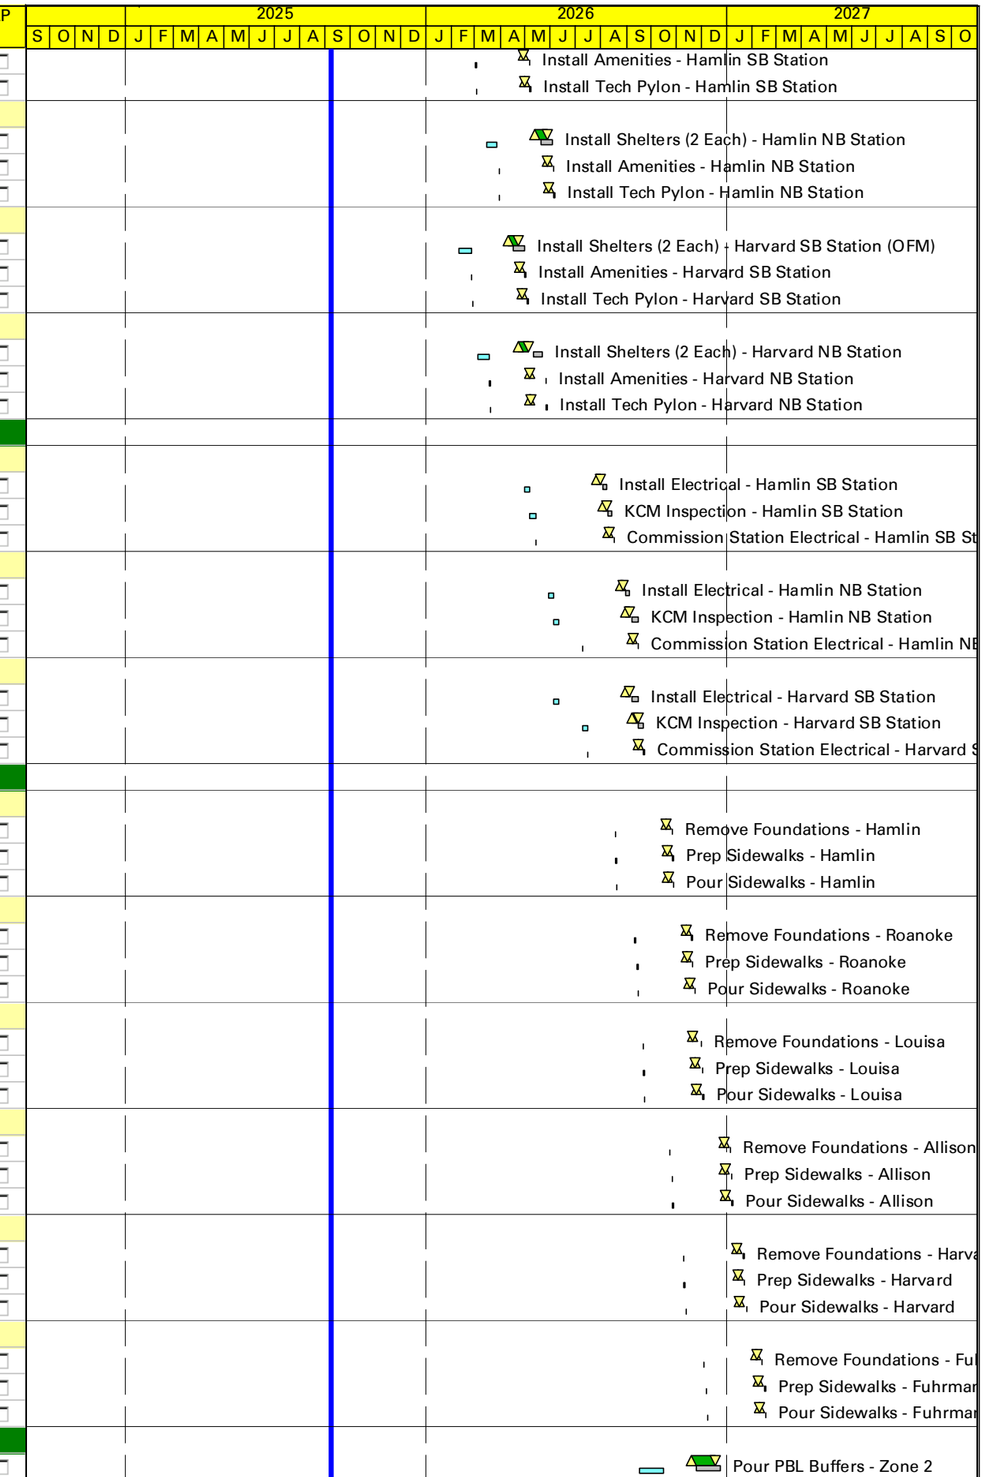

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© Primavera Systems, Inc.

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Chanalization														
2-PM-0987	Channelization - Zone 2	20	20	0	0	20	20	18-Dec-26	19-Jan-27	26	21	5	5	☐
OCS														
2-OCS-0989	OCS - Material Handover - Zone 2	1	1	0	0	1	1	19-Aug-26	19-Aug-26	126	132	-6	-6	☐
Zone 3 - Lynn to Galer														
Pole Foundation Potholing														
3-PH-0992	Lynn to Galer (4 Each) - Pole Foundation Potholing	0	0	0	0	0	0	20-Nov-24 A	20-Nov-24 A			0	0	☑
Storm Work														
Mainline														
3-ST-0996	Mh 25 to 26 (Garfield) 110 Lf - Storm	8	8	0	8	0	8	17-Oct-24 A	28-Oct-24 A			0	0	☐
DSC-014	DSC-014 Garfield & Eastlake Gas Line Conflict MH-B25	1	1	0	1	0	1	24-Oct-24 A	24-Oct-24 A			0	0	☐
DSC-015	DSC-015 NW Corner Garfield Unknown/Unlocated Side Sewer	1	1	0	1	0	1	25-Oct-24 A	25-Oct-24 A			0	0	☐
DSC-010	DSC-010 Garfield 48-inch Sewer / Exc. Around Sewer	1	2	0	2	0	2	25-Oct-24 A	28-Oct-24 A			0	0	☐
DSC-018	DSC-018 CDF Encased Sewer Pipe Conflict w/Storm	2	2	0	2	0	2	25-Oct-24 A	28-Oct-24 A			0	0	☐
3-ST-0995A	Mh 25 to 27 (Garfield to Galer) - (Prior to Vib. Mon. Shutdown)	2	2	0	2	0	2	29-Oct-24 A	30-Oct-24 A			0	0	☐
DSC-021	DSC-021 Abandoned Gas Line Conflict	1	1	0	1	0	1	30-Oct-24 A	30-Oct-24 A			0	0	☐
3-ST-0995B	Mh 25 to 27 (Garfield to Galer) - VIB. MON. RESOLUTION (TBD)	7	11	0	11	0	11	31-Oct-24 A	15-Nov-24 A			0	0	☐
3-ST-0997	Mh 25 to 23 (Garfield to Blaine) 336 Lf - Storm	8	10	0	10	0	10	01-Nov-24 A	15-Nov-24 A			0	0	☐
DSC-025	DSC-025 NWC Garfield Water Service Loop	1	1	0	1	0	1	06-Nov-24 A	06-Nov-24 A			0	0	☐
DSC-026	DSC-026 Garfield to Blaine Timbers in Excavation	1	1	0	1	0	1	07-Nov-24 A	07-Nov-24 A			0	0	☐
DSC-029	DSC-029 Garfield NW Mid-Block Unknown Water Service	1	1	0	1	0	1	08-Nov-24 A	08-Nov-24 A			0	0	☐
DSC-030	DSC-030 Garfield to Blaine West CDF in Conflict with Storm	1	1	0	1	0	1	13-Nov-24 A	13-Nov-24 A			0	0	☐
3-ST-0995	Mh 25 to 27 (Garfield to Galer) 307 Lf - Storm	5	5	0	5	0	5	18-Nov-24 A	22-Nov-24 A			0	0	☐
DSC-035	DSC-035 Garfield to Galer Side Sewer Conflict	5	5	0	5	0	5	18-Nov-24 A	22-Nov-24 A			0	0	☐
DSC-038	DSC-038 Blaine to Howe Gas Conflict w/Storm	1	1	0	1	0	1	21-Nov-24 A	21-Nov-24 A			0	0	☐
DSC-042	DSC-042 Blaine MH B23 Conflict with Gas	2	2	0	2	0	2	25-Nov-24 A	26-Nov-24 A			0	0	☐
3-ST-0998	Mh 23 to 20 (Blaine to Howe) 403 Lf - Storm (DSC's 042 & 043)	14	16	0	16	0	16	25-Nov-24 A	18-Dec-24 A			0	0	☐
DSC-043	DSC-043 Blaine CDF Conflict w/MH	1	1	0	1	0	1	27-Nov-24 A	27-Nov-24 A			0	0	☐
DSC-050	DSC-050 Blaine Mainline Storm Conflict w/Side Sewer	1	1	0	1	0	1	06-Dec-24 A	06-Dec-24 A			0	0	☐
DSC-053	DSC-053 Blaine to Howe Stump in Conflict with Storm Main	1	1	0	1	0	1	09-Dec-24 A	09-Dec-24 A			0	0	☐
DSC-057	DSC-057 Blaine to Howe Unknown Unlocated Steel Line	1	1	0	1	0	1	16-Dec-24 A	16-Dec-24 A			0	0	☐
DSC-059	DSC-059 Blaine to Howe Tieback Conflict w/Mainline	1	1	0	1	0	1	18-Dec-24 A	18-Dec-24 A			0	0	☐
DSC-061	DSC-061 Howe Gas Service Conflicts	1	1	0	1	0	1	18-Dec-24 A	18-Dec-24 A			0	0	☐
DSC-062	DSC-062 Gas Line Howe North	5	8	0	8	0	8	20-Dec-24 A	08-Jan-25 A			0	0	☐
DSC-067	DSC-067 Howe Unknown Waterline	1	1	0	1	0	1	02-Jan-25 A	02-Jan-25 A			0	0	☐
DSC-068	DSC-068 Howe CDF Obstruction	1	1	0	1	0	1	02-Jan-25 A	02-Jan-25 A			0	0	☐
DSC-069	DSC-069 Howe Sewer Maintenance Hole Conflict	2	2	0	2	0	2	03-Jan-25 A	06-Jan-25 A			0	0	☐
3-ST-0999	Mh 20 to Mh 19 (Howe to Newton) 326 Lf - Storm	9	11	0	11	0	11	09-Jan-25 A	24-Jan-25 A			0	0	☐
DSC-075	DSC-075 Howe to Newton Leaking Water Service (disputed)	1	1	0	1	0	1	13-Jan-25 A	13-Jan-25 A			0	0	☐
DSC-078	DSC-078 Howe to Newton CDF Conflict with Mainline	1	1	0	1	0	1	15-Jan-25 A	15-Jan-25 A			0	0	☐
DSC-079	DSC-079 Howe to Newton Unknown Unlocated Copper Line	1	1	0	1	0	1	15-Jan-25 A	15-Jan-25 A			0	0	☐
DSC-081	DSC-081 Howe to Newton Wood in Trench	1	1	0	1	0	1	15-Jan-25 A	15-Jan-25 A			0	0	☐
DSC-086	DSC-086 Newton MH 19 Conflict with Cast Iron Pipe	1	1	0	1	0	1	22-Jan-25 A	22-Jan-25 A			0	0	☐
DSC-087	DSC-087 Newton MH 19 Conflict with Another Pipe	1	1	0	1	0	1	22-Jan-25 A	22-Jan-25 A			0	0	☐
DSC-089	DSC-089 Newton CDF Encased Gas Line Conflict with MH 19A	1	1	0	1	0	1	24-Jan-25 A	24-Jan-25 A			0	0	☐
3-ST-1000	Mh 19 to 17 (Newton to Boston) 325 Lf - Storm (DC-023)	10	18	0	18	0	18	27-Jan-25 A	24-Feb-25 A			0	0	☐
DSC-093	DSC-093 Newton to Boston Storm - Unknown Steel Pipes	1	1	0	1	0	1	30-Jan-25 A	30-Jan-25 A			0	0	☐
DSC-096	DSC-096 Newton to Boston Storm - Side Sewer Above Mainline	1	1	0	1	0	1	31-Jan-25 A	31-Jan-25 A			0	0	☐
DSC-097	DSC-097 Newton to Boston CDF Unknown Location of Gas Line	2	2	0	2	0	2	03-Feb-25 A	04-Feb-25 A			0	0	☐
DSC-098	DSC-098 Newton to Boston CDF Unknown Location of Mainline	2	2	0	2	0	2	03-Feb-25 A	04-Feb-25 A			0	0	☐
DSC-102	DSC-102 Newton to Boston Side Sewer Conflict with Mainline	1	1	0	1	0	1	11-Feb-25 A	11-Feb-25 A			0	0	☐
DSC-106	DSC-106 Newton to Boston Unknown Water Service	1	1	0	1	0	1	13-Feb-25 A	13-Feb-25 A			0	0	☐
DSC-109	DSC-109 Newton to Boston Unknown Unlocated Side Sewer 2031	1	1	0	1	0	1	13-Feb-25 A	13-Feb-25 A			0	0	☐
DSC-108	DSC-108 Newton to Boston leaking water service	2	2	0	2	0	2	13-Feb-25 A	14-Feb-25 A			0	0	☐

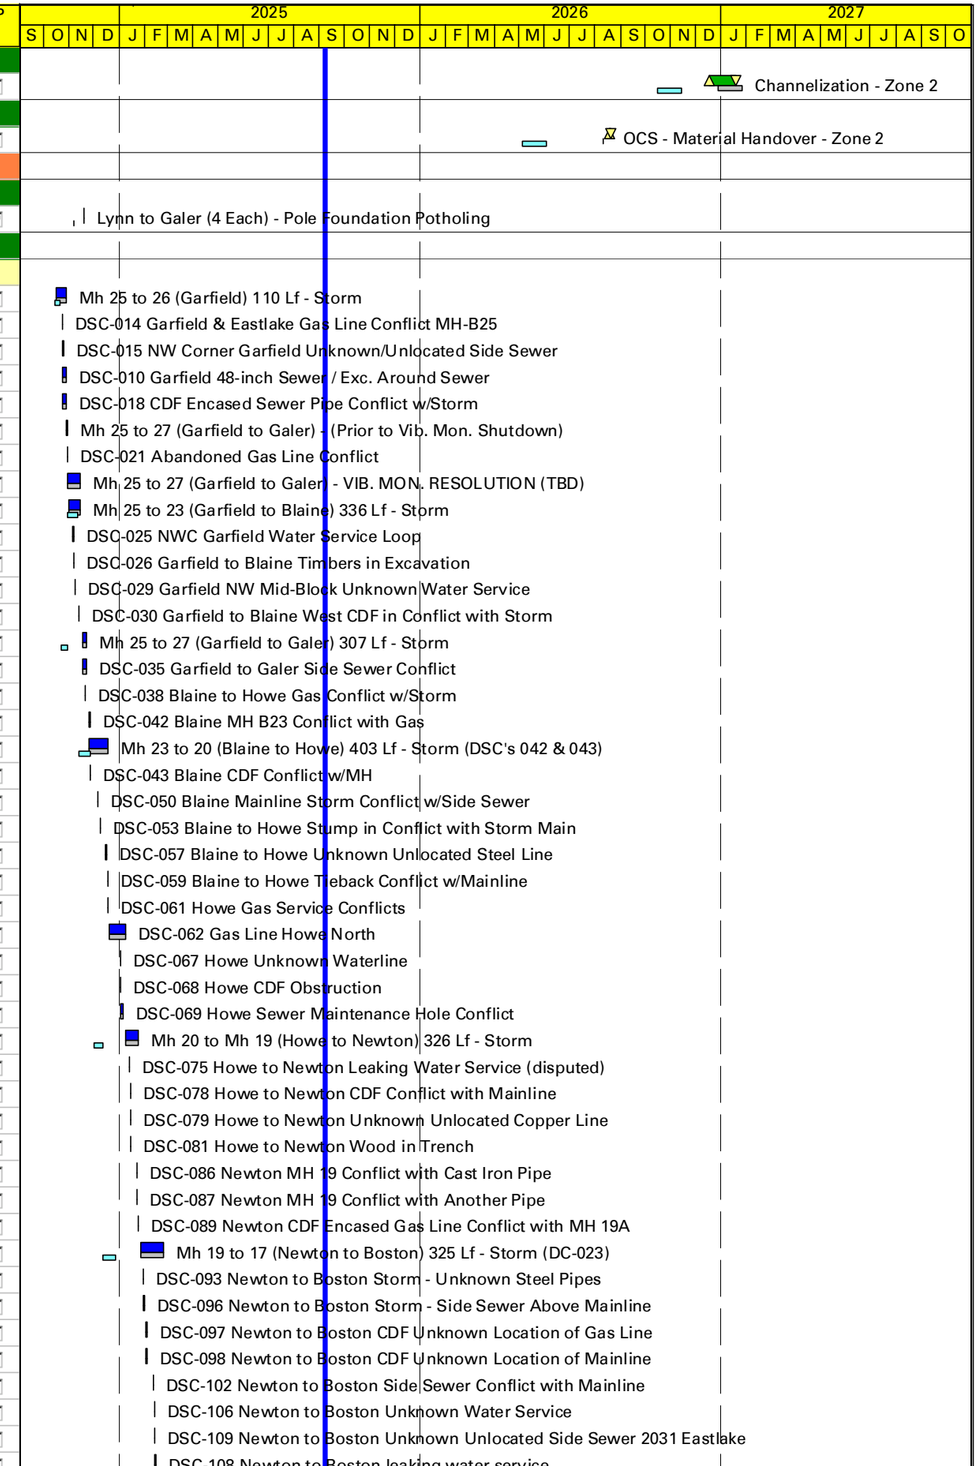

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-ST-1001	Mh 17 to Mh 16 (Boston to Lynn) 308 Lf - Storm (DC-023)	12	12	0	12	0	12	25-Feb-25 A	12-Mar-25 A			0	0	
DSC-121	DSC-121 Eastlake-Boston-Lynn Side Sewer Storm Conflict	2	2	0	2	0	2	03-Mar-25 A	04-Mar-25 A			0	0	
DSC-125	DSC-125 Boston to Lynn Unknown Comm Line	1	1	0	1	0	1	07-Mar-25 A	07-Mar-25 A			0	0	
DSC-126	DSC-126 Boston to Lynn Unknown Water Service	1	1	0	1	0	1	11-Mar-25 A	11-Mar-25 A			0	0	
DSC-127	DSC-127 Boston to Lynn Boulder Conflict	1	1	0	1	0	1	12-Mar-25 A	12-Mar-25 A			0	0	
DSC-129	DSC-129 Boston to Lynn Water Service Conflict With MH	1	1	0	1	0	1	13-Mar-25 A	13-Mar-25 A			0	0	
DSC-132	DSC-132 Boston to Lynn Unknown Steel Line Mainline Storm	1	1	0	1	0	1	13-Mar-25 A	13-Mar-25 A			0	0	
DSC-136	DSC-136 Boston to Lynn Unknown Steel Line Mainline Storm	1	1	0	1	0	1	14-Mar-25 A	14-Mar-25 A			0	0	
DSC-138	DSC-138 Boston to Lynn Unknown Side Sewer Conflict w/Mainline	2	2	0	2	0	2	14-Mar-25 A	17-Mar-25 A			0	0	
DSC-134	DSC-134 Eastlake, Lynn-Boston 1.5in Steel Line Storm Conflict	2	2	0	2	0	2	14-Mar-25 A	17-Mar-25 A			0	0	
Side Storm (WQV, CB's and Inlets)														
3-ST-1005	Garfield to Blaine - Side Storm (DC-013) WEST SIDE	8	8	0	8	0	8	18-Nov-24 A	27-Nov-24 A			0	0	
DSC-041	DSC-041 Garfield to Blaine CB33 Pipe Conflict	1	1	0	1	0	1	25-Nov-24 A	25-Nov-24 A			0	0	
3-ST-1025	Galer to Garfield - Side Storm (DC-013) WEST SIDE	14	15	0	15	0	15	02-Dec-24 A	20-Dec-24 A			0	0	
DSC-046	DSC-046 Garfield to Galer West Side WQV B120 Conflict w/DB	1	1	0	1	0	1	03-Dec-24 A	03-Dec-24 A			0	0	
DSC-048	DSC-048 Garfield to Galer CB B31 Conflict w/Conc. Structure	1	1	0	1	0	1	05-Dec-24 A	05-Dec-24 A			0	0	
3-ST-1004	Patch Pave Galer to Garfield - Side Storm (west side)	2	2	0	2	0	2	23-Dec-24 A	24-Dec-24 A			0	0	
3-ST-1006	Patch Pave Garfield to Blaine - Side Storm (west side)	3	3	0	3	0	3	02-Jan-25 A	06-Jan-25 A			0	0	
3-ST-1017	Blaine to Howe St - Side Storm WEST SIDE (partial)	5	5	0	5	0	5	02-Jan-25 A	08-Jan-25 A			0	0	
3-ST-1003	Galer to Garfield - Side Storm (DC-013) EAST SIDE	9	10	0	10	0	10	06-Jan-25 A	17-Jan-25 A			0	0	
DSC-071	DSC-071 NEC Galer Water Vault Conflict With Inlet	1	1	0	1	0	1	07-Jan-25 A	07-Jan-25 A			0	0	
3-ST-1008	Patch Pave Blaine to Howe - Side Storm (west side)	2	2	0	2	0	2	09-Jan-25 A	10-Jan-25 A			0	0	
DSC-077	DSC-077 Galer to Garfield CB B36 Ductbank Conflict	1	1	0	1	0	1	14-Jan-25 A	14-Jan-25 A			0	0	
3-ST-1027	Blaine to Howe St - Side Storm WEST SIDE (complete)	5	5	0	5	0	5	21-Jan-25 A	27-Jan-25 A			0	0	
DSC-091	DSC-091 SWV Howe Unknown Utility @ CB-B24 Excavation	1	1	0	1	0	1	27-Jan-25 A	27-Jan-25 A			0	0	
3-ST-1010	Patch Pave Howe to Newton - Side Storm	2	2	0	2	0	2	28-Jan-25 A	29-Jan-25 A			0	0	
3-ST-1035	Garfield to Blaine - Side Storm (DC-013) EAST SIDE	10	10	0	10	0	10	30-Jan-25 A	14-Feb-25 A			0	0	
DSC-100	DSC-100 Blaine Existing Storm IE Too High	1	1	0	1	0	1	03-Feb-25 A	03-Feb-25 A			0	0	
NCR-003	NCR-003 CB-B30 - 20" PS Line Damaged	1	0	-1	1	0	1	04-Feb-25 A	04-Feb-25 A					
DSC-104	DSC-104 NEC Blaine Timber obstruction CB B33	1	1	0	1	0	1	10-Feb-25 A	10-Feb-25 A			0	0	
DSC-116	DSC-116 Garfield-Blaine WQ-B1124 Conduit Conflict	5	1	0	1	0	1	13-Feb-25 A	13-Feb-25 A			0	0	
3-ST-1009	Newton - Side Storm (WEST SIDE)	4	11	0	11	0	11	19-Feb-25 A	05-Mar-25 A			0	0	
3-ST-1012	Patch Pave Newton to Boston - Side Storm	2	2	0	2	0	2	06-Mar-25 A	07-Mar-25 A			0	0	
3-ST-1037	Testing & CCTV Galer to Blaine	4	4	0	4	0	4	10-Mar-25 A	13-Mar-25 A			0	0	
3-ST-1039	Blaine (EAST SIDE)	5	8	0	8	0	8	14-Mar-25 A	25-Mar-25 A			0	0	
DSC-139	DSC-139 Blaine East Side WQV B-112 Conflicts	1	1	0	1	0	1	17-Mar-25 A	17-Mar-25 A			0	0	
RFI-059	RFI 059 WQ B117 and B113 grade change	31	31	0	31	0	31	18-Mar-25 A	29-Apr-25 A			0	0	
3-ST-1029	Boston Side Storm (WEST SIDE)	8	8	0	8	0	8	26-Mar-25 A	04-Apr-25 A			0	0	
3-ST-1013	Lynn St. South Side - Side Storm (WEST SIDE)	3	3	0	3	0	3	07-Apr-25 A	09-Apr-25 A			0	0	
3-ST-1014	Patch Pave Boston to Lynn - Side Storm	5	5	0	5	0	5	10-Apr-25 A	16-Apr-25 A			0	0	
3-ST-1047	Blaine - Side Storm (EAST SIDE) (DC-023)	10	10	0	10	0	10	17-Apr-25 A	30-Apr-25 A			0	0	
DSC-180	DSC-180 Blaine NEC Comm Ductbank Conflict	1	1	0	1	0	1	18-Apr-25 A	18-Apr-25 A			0	0	
3-ST-1057	FM to Pothole Ductbank on Fairview	2	2	0	2	0	2	18-Apr-25 A	21-Apr-25 A			0	0	
DSC-187	DSC-187 CB B26 Conflict with side sewer	1	1	0	1	0	1	23-Apr-25 A	23-Apr-25 A			0	0	
DSC-192	DSC-192 Blaine East Side Gas Line Conflict with Storm	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	
DSC-193	DSC-193 Blaine to Lynn East side WQV B101 Comm Conflict	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	
3-ST-1007	Howe St - Side Storm EAST SIDE (DC-023)	9	9	0	9	0	9	01-May-25 A	13-May-25 A			0	0	
3-ST-1019	Newton - Side Storm (EAST SIDE) (DC-023)	5	5	0	5	0	5	14-May-25 A	20-May-25 A			0	0	
3-ST-1011	Boston - Side Storm (EAST SIDE) (DC-023)	8	8	0	8	0	8	21-May-25 A	02-Jun-25 A			0	0	
Water Main														
Stage 4 Galer to South of Blaine (65+21 to 75+63)														
SPU Ops Notifications														
3-W-1074	SPU Water Ops Scheduling Notification - Stg 4 (TM4)	15	15	0	15	0	15	18-Mar-25 A	07-Apr-25 A			0	0	
3-W-1072	SPU Water Ops Scheduling Notification - Stg 4 (Hyd/Lateral)	15	15	0	15	0	15	19-Mar-25 A	08-Apr-25 A			0	0	

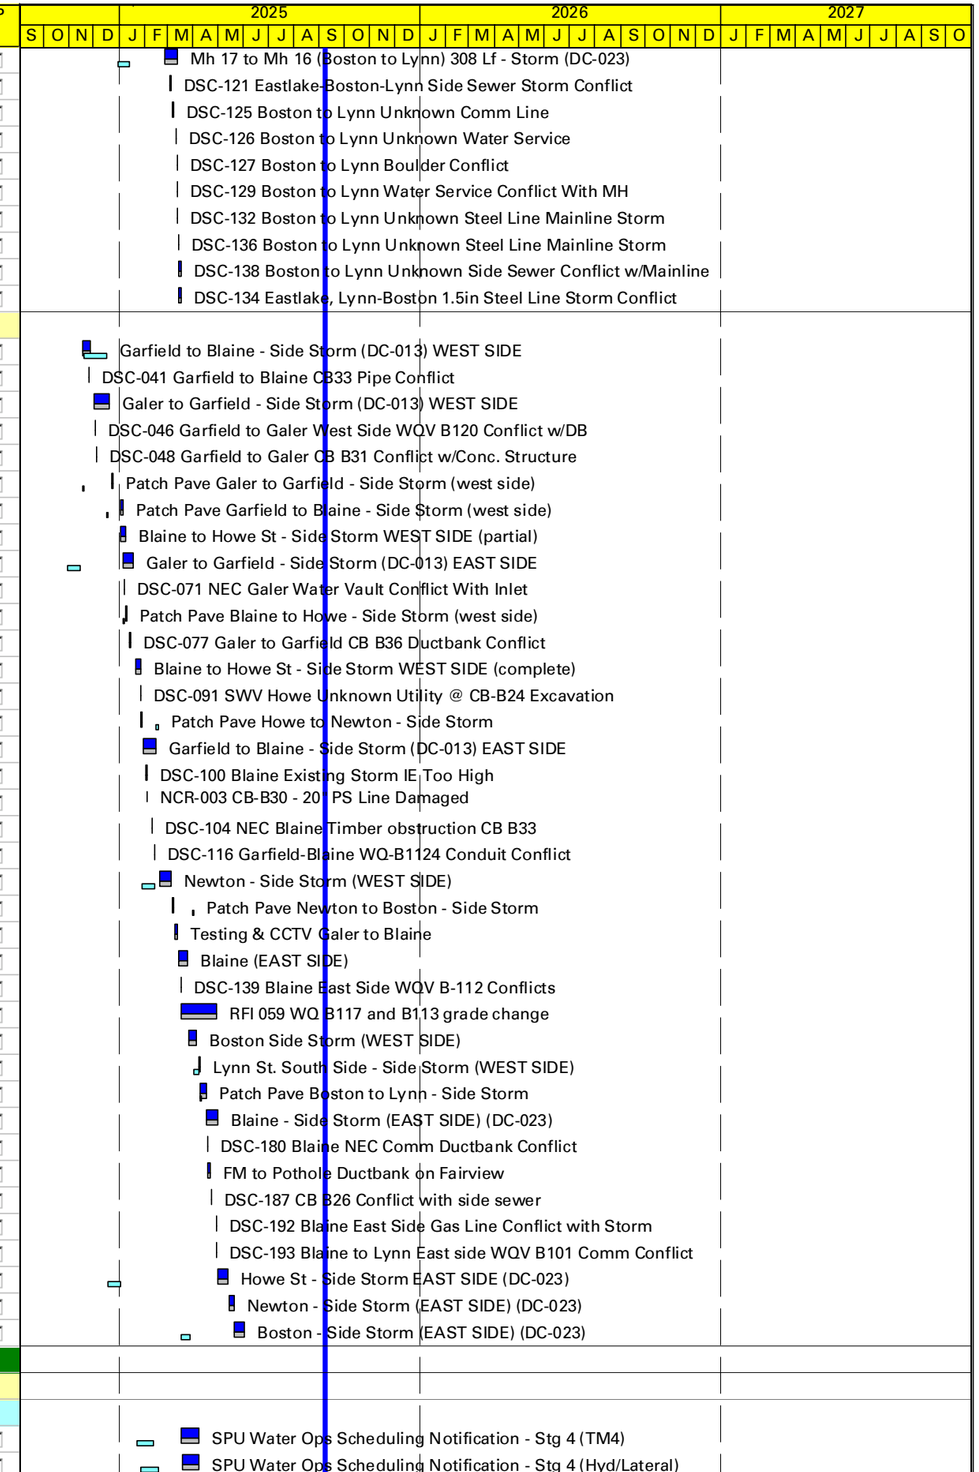

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-W-1064	SPU Water Ops Scheduling Notification - Stg 4 (Conn.)	15	15	0	15	0	15	27-May-25 A	16-Jun-25 A			0	0	
3-W-1070	SPU Water Ops Scheduling Notification - Stg 4 (Temp Jumper)	15	15	0	15	0	15	29-May-25 A	18-Jun-25 A			0	0	
Waterline Installation														
3-W-1017	Build Temp Main TM4 - Stg 4 Galer to Blaine	3	3	0	3	0	3	19-Mar-25 A	21-Mar-25 A			0	0	
DSC-149	DSC-149 Garfield Unlocated Cooper Service Conflict with Temp M	2	2	0	2	0	2	20-Mar-25 A	21-Mar-25 A			0	0	
3-W-1018	Test & Flush Temp Mains TM4 - Stg 4 Galer to Blaine	2	2	0	2	0	2	24-Mar-25 A	25-Mar-25 A			0	0	
DSC-154	DSC-154 Stage 4 service Jumper Conflict with CDF	1	1	0	1	0	1	26-Mar-25 A	26-Mar-25 A			0	0	
3-W-1065	Excavate CC12, 13,14 - Stg 4 Galer to Blaine	2	2	0	2	0	2	26-Mar-25 A	27-Mar-25 A			0	0	
3-W-1019	Bact Results - Stg 4 Galer to Blaine (TM4)	3	3	0	3	0	3	26-Mar-25 A	28-Mar-25 A			0	0	
DSC-155	DSC-155 Stage 4 service Jumper Conflict with CDF #2	1	1	0	1	0	1	27-Mar-25 A	27-Mar-25 A			0	0	
DSC-156	DSC-156 Stage 4 Existing Watermain Leaking	1	1	0	1	0	1	27-Mar-25 A	27-Mar-25 A			0	0	
DSC-157	DSC-157 Water Stage 4 Unknown Ductbank North of Galer	1	1	0	1	0	1	28-Mar-25 A	28-Mar-25 A			0	0	
3-W-1020	SPU Customer Notification - Stg 4 Galer to Blaine (TM4)	5	5	0	5	0	5	31-Mar-25 A	04-Apr-25 A			0	0	
DSC-167	DSC-167 Stage 4 Watermain Existing Hydrant Without Restraint tc	1	1	0	1	0	1	04-Apr-25 A	04-Apr-25 A			0	0	
3-W-1022	SPU Connect Temp Main TM4 - Stg 4 Galer to Blaine	1	1	0	1	0	1	08-Apr-25 A	08-Apr-25 A			0	0	
3-W-1023	SPU Transfer Services to Temp Main - Stg 4 Galer to Blaine	1	1	0	1	0	1	08-Apr-25 A	08-Apr-25 A			0	0	
3-W-1024	SPU Hydrant/Lateral Relocation 3 ea. - Stg 4 Galer to Blaine	1	1	0	1	0	1	08-Apr-25 A	08-Apr-25 A			0	0	
3-W-1035	SPU Service Lateral Relocations 6 ea. - Stg 4 Galer to Blaine	1	1	0	1	0	1	09-Apr-25 A	09-Apr-25 A			0	0	
3-W-1095	SPU DELAY CUT & CAPS	2	2	0	2	0	2	10-Apr-25 A	11-Apr-25 A			0	0	
3-W-1045	SPU Cut/Cap CC12, 13,14 - Stg 4 Galer to Blaine	1	1	0	1	0	1	14-Apr-25 A	14-Apr-25 A			0	0	
3-W-1025	Install Mainline & Hydrants Sta. 75+40 to 65+21 - Stg 4 Galer to Bl	19	19	0	19	0	19	15-Apr-25 A	09-May-25 A			0	0	
DSC-183	DSC-183 Stage 4 Watermain side sewer conflict with mainline	1	1	0	1	0	1	21-Apr-25 A	21-Apr-25 A			0	0	
DSC-184	DSC-184 Stage 4 Unknown Unlocated steel Line	1	1	0	1	0	1	22-Apr-25 A	22-Apr-25 A			0	0	
DSC-188	DSC-188 Stage 4 Duct Bank Conflict with Watermain	1	1	0	1	0	1	23-Apr-25 A	23-Apr-25 A			0	0	
DSC-189	DSC-189 Stage 4 Side Sewer DSO Map incorrect	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	
DSC-194	DSC-194 Stage 4 Watermain Conflict with Gas Line	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	
DSC-196	DSC-196 Stage 4 Watermain Side Sewer Conflict with Mainline at	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	
DSC-198	DSC-198 Stage 4 Test station Concrete obstruction under sidewalk	1	1	0	1	0	1	01-May-25 A	01-May-25 A			0	0	
DSC-199	DSC-199 Stage 4 Water unmarked Storm Line at Garfield	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	
DSC-204	DSC-204 Eastlake & Garfield, CDF in Watermain Trench	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	
NCR-011	NCR-011 Damaged a known 8" WM - broke existing corp valve	1	0	-1	1	0	1	05-May-25 A	05-May-25 A					
DSC-208	DSC-208 Stage 4 Thrust Collar conflict with Gas Line	1	1	0	1	0	1	12-May-25 A	12-May-25 A			0	0	
3-W-1085	Install & Cure Thrust Collars - Stg 4 Galer to Blaine	10	10	0	10	0	10	12-May-25 A	23-May-25 A			0	0	
DSC-211	DSC-211 Stage 4 Thrust Collar Excavation STA 69+11 conflict with	1	1	0	1	0	1	15-May-25 A	15-May-25 A			0	0	
NCR-017	NCR-017 Utility Strike	1	0	-1	1	0	1	15-May-25 A	15-May-25 A					
3-W-1075	Install Main Lateral @ Galer Sta. 900+05 to 900+20 - Stg 4 Galer tc	1	1	0	1	0	1	19-May-25 A	19-May-25 A			0	0	
3-W-1087	Install Main Lateral @ Fairview Sta. 901+65 to 901+11 - Stg 4 Gale	1	1	0	1	0	1	20-May-25 A	20-May-25 A			0	0	
DSC-218	DSC-218 Galer Thrust Collar & 18"PS Conflict	5	5	0	5	0	5	27-May-25 A	02-Jun-25 A			0	0	
3-W-1026	Test & Flush Main Line - Stg 4 Galer to Blaine	1	1	0	1	0	1	03-Jun-25 A	03-Jun-25 A			0	0	
DSC-225	DSC-225 Stage 4 unknown unlocated Cast Iron pipe	1	1	0	1	0	1	03-Jun-25 A	03-Jun-25 A			0	0	
3-W-1027	Bact Results - Stg 4 Galer to Blaine (Main)	3	3	0	3	0	3	04-Jun-25 A	06-Jun-25 A			0	0	
3-W-1029	Excavate Services - Stg 4 Galer to Blaine	3	3	0	3	0	3	04-Jun-25 A	06-Jun-25 A			0	0	
3-W-1028	SPU Customer Notification - Stg 4 Galer to Blaine (CC13 Main)	5	5	0	5	0	5	09-Jun-25 A	13-Jun-25 A			0	0	
3-W-1091	SPU Resource Availability	8	11	0	11	0	11	10-Jun-25 A	25-Jun-25 A			0	0	
3-W-1049	SPU Water Main Connection @ CC13 & Hydrant @ 74+26 - Stg 4 (	1	1	0	1	0	1	17-Jun-25 A	17-Jun-25 A			0	0	
DSC-234	DSC-234 Stage 4 Watermain 1505 Service is 8" not 4"	1	1	0	1	0	1	17-Jun-25 A	17-Jun-25 A			0	0	
DSC-249	DSC-249 Stage 4 CDF conflict at WS at 1503 & 1502 Eastlake	1	1	0	1	0	1	17-Jun-25 A	17-Jun-25 A			0	0	
DSC-235	DSC-235 Stage 4 Watermain Ductbank Conflict w/SCL Power	1	1	0	1	0	1	18-Jun-25 A	18-Jun-25 A			0	0	
DSC-247	DSC-247 Phase 4 water service leak	1	1	0	1	0	1	27-Jun-25 A	27-Jun-25 A			0	0	
3-W-1031	SPU Transfer Services - Stg 4 Galer to Blaine (17 ea.)	1	1	0	1	0	1	02-Jul-25 A	02-Jul-25 A			0	0	
3-W-1032	SPU Connect at Sta. 75+63 & 901+00 - Stg 4 Galer to Blaine	1	1	0	1	0	1	03-Jul-25 A	03-Jul-25 A			0	0	
3-W-1073	Exc. Temp Jumper Conn. Sta. 65+21 - Stg 4 Galer to Blaine	1	1	0	1	0	1	07-Jul-25 A	07-Jul-25 A			0	0	
3-W-1101	SPU Resource Delay	1	1	0	1	0	1	07-Jul-25 A	07-Jul-25 A			0	0	
3-W-1033	SPU Temp Jumper Conn. Sta. 65+21 - Stg 4 Galer to Blaine	1	1	0	1	0	1	08-Jul-25 A	08-Jul-25 A			0	0	

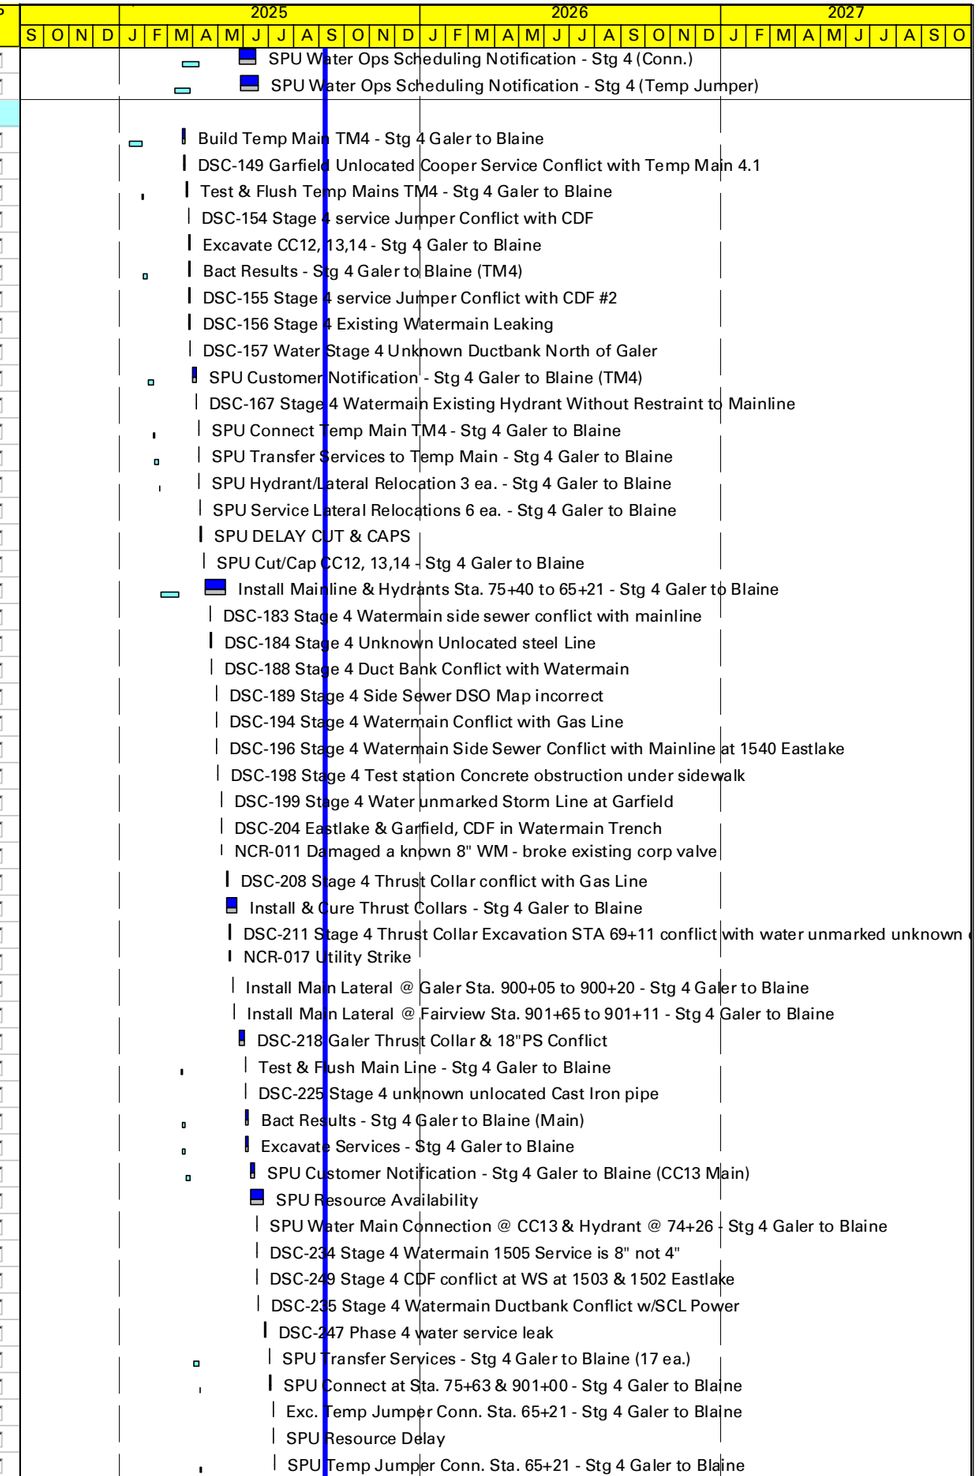

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-W-1034	Patch Pave - Stg 4 Galer to Blaine	1	1	0	1	0	1	09-Jul-25 A	09-Jul-25 A			0	0	
DSC-083	DSC-083 Garfield NEC Water Vault 118 Pipe Conflict w/Waterline	1	1	0	1	0	1	09-Jul-25 A	09-Jul-25 A			0	0	
3-W-1077	Test Stations Watermain Stage 4	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	
Stage 5 South of Blaine to Boston (55+00 to 65+21)														
SPU Ops Notifications														
3-W-1067	SPU Water Ops Scheduling Notification - Stg 5 (CC15)	15	15	0	15	0	15	16-Jul-25 A	05-Aug-25 A		22	0	0	
3-W-1066	SPU Water Ops Scheduling Notification - Stg 5 (Conn.)	12	12	0	12	0	12	23-Jul-25 A	07-Aug-25 A		22	0	0	
3-W-1063	SPU Water Ops Scheduling Notification - Stg 5 (Jumper)	11	11	0	11	0	11	25-Jul-25 A	08-Aug-25 A		22	0	0	
Waterline Installation														
DSC-228	DSC-228 Stage 5 Service Jumper conflict with unknown conduits	1	1	0	1	0	1	04-Jun-25 A	04-Jun-25 A			0	0	
3-W-1106	Excavate Hydrant & Service Relocations - Stg 5 Blaine to Boston	3	3	0	3	0	3	04-Jun-25 A	06-Jun-25 A			0	0	
3-W-1086	SPU Hydrant Lateral Relocations (2 ea.) - Stg 5 Blaine to Boston	1	1	0	1	0	1	09-Jun-25 A	09-Jun-25 A			0	0	
3-W-1096	SPU Service Service Relocations (5 ea.) - Stg 5 Blaine to Boston	1	1	0	1	0	1	09-Jun-25 A	09-Jun-25 A			0	0	
3-W-1116	8" Gate Valve on Yale Lateral - Stg 5 Blaine to Boston	1	1	0	1	0	1	09-Jun-25 A	09-Jun-25 A			0	0	
3-W-1156	Install Stg. 5 Mainline Prior to Stg. 4 Commissioning	4	15	0	15	0	15	10-Jun-25 A	01-Jul-25 A			0	0	
DSC-238	DSC-238 Stage 5 Gas Line locates incorrect	1	1	0	1	0	1	24-Jun-25 A	24-Jun-25 A			0	0	
DSC-242	DSC-242 Stage 5 1302 Eastlake leaking water service	1	1	0	1	0	1	25-Jun-25 A	25-Jun-25 A			0	0	
DSC-243	DSC-243 OCS Line Heights	1	1	0	1	0	1	26-Jun-25 A	26-Jun-25 A			0	0	
DSC-261	DSC-261 Stage 5 Unknown Steel Pipe 60+39 (1914 Eastlake)	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	
3-W-1036	Install Mainline, Hydrants & Blocking Sta. 65+07 to 55+00 - Stg 5 E	9	9	0	9	0	9	10-Jul-25 A	22-Jul-25 A			0	0	
DSC-264	DSC-264 Stage 5 unknown steel pipe STA 58+29	1	1	0	1	0	1	16-Jul-25 A	16-Jul-25 A			0	0	
DSC-265	DSC-265 Stage 5 CDF Conflict	1	1	0	1	0	1	16-Jul-25 A	16-Jul-25 A			0	0	
NCR-019	NCR-019 12X4 tees that were installed were the incorrect size per	1	0	-1	1	0	1	17-Jul-25 A	17-Jul-25 A					
DSC-272	DSC 272 Stage 5 unknown unlocated steel line	1	1	0	1	0	1	21-Jul-25 A	21-Jul-25 A			0	0	
DSC-274	DSC 274 Unknown unlocated water service 55+85	1	1	0	1	0	1	22-Jul-25 A	22-Jul-25 A			0	0	
3-W-1039	Test & Flush - Stg 5 Blaine to Boston	2	2	0	2	0	2	23-Jul-25 A	24-Jul-25 A			0	0	
3-W-1040	Bact Results - Stg 5 Blaine to Boston (Main)	2	2	0	2	0	2	25-Jul-25 A	28-Jul-25 A			0	0	
3-W-1042	Excavate Tie-Ins and Services - Stg 5 Blaine to Boston	6	6	0	6	0	6	25-Jul-25 A	01-Aug-25 A			0	0	
3-W-1041	SPU Customer Notification - Stg 5 Blaine to Boston	5	5	0	5	0	5	29-Jul-25 A	04-Aug-25 A			0	0	
DSC-294	DSC-294 Stage 5 WM, WS-1211 & WS-1210 Sizes	1	0	-1	1	0	1	05-Aug-25 A	05-Aug-25 A					
3-W-1037	Install Mainline Lateral @ Newton Sta. 700+63 to 700+13 - Stg 5 B	1	1	0	1	0	1	06-Aug-25 A	06-Aug-25 A		23	0	0	
3-W-1043	SPU Connect CC15 - Stg 5 Blaine to Boston	1	1	0	1	0	1	06-Aug-25 A	06-Aug-25 A		22	0	0	
3-W-1044	SPU Transfer Services In Stage 5 - Stg 5 Blaine to Boston	1	1	0	1	0	1	07-Aug-25 A	07-Aug-25 A		22	0	0	
3-W-1083	Install Thrust Collar Sta. 700+02 - Stg 5 Blaine to Boston	2	2	0	2	0	2	07-Aug-25 A	08-Aug-25 A		23	0	0	
3-W-1047	SPU Temp Jumper Conn. @ Sta. 65+00 - Stg 5 Blaine to Boston	1	1	0	1	0	1	08-Aug-25 A	08-Aug-25 A		22	0	0	
DSC-300	DSC-300 Stage 5 Unknown unmarked water service	7	0	-8	8	0	8	08-Aug-25 A	19-Aug-25 A					
3-W-1097	Remove Temp Jumper Sta. 65+21 - Stg 5 Blaine to Boston	1	1	0	1	0	1	11-Aug-25 A	11-Aug-25 A		22	0	0	
3-W-1048	Patch Pave - Stg 5 Blaine to Boston	2	2	0	2	0	2	12-Aug-25 A	13-Aug-25 A		22	0	0	
3-W-1076	Test Stations Watermain Stage 5	5	5	4	1	0	1	14-Aug-25 A	14-Aug-25 A		156	0	4	
3-W-1046	SPU Connection Sta. 65+21 Yale Pl. - Stg 5 Blaine to Boston	1	1	0	1	0	1	20-Aug-25 A	20-Aug-25 A		22	-8	-8	
Stage 6 Boston to Louisa (44+50 to 55+00)														
SPU Ops Notifications														
3-W-1080	SPU Water Ops Scheduling Notification - Stg 6 (Temp Services)	15	15	0	15	0	15	01-Aug-25 A	21-Aug-25 A		13	0	0	
3-W-1068	SPU Water Ops Scheduling Notification - Stg 6 (Conn.)	15	15	0	0	15	15	15-Sep-25	03-Oct-25	26	13	13	13	
3-W-1071	SPU Water Ops Scheduling Notification - Stg 6 (Conn.)	15	15	0	0	15	15	24-Sep-25	15-Oct-25	26	13	13	13	
Waterline Installation														
DSC-282	DSC 282 Stage 6, New 6in Fire Service Not in Plans	1	1	0	1	0	1	29-Jul-25 A	29-Jul-25 A			0	0	
DSC-283	DSC 283 Stage 6, WS-1302 leaking repair sleeve	1	1	0	1	0	1	29-Jul-25 A	29-Jul-25 A			0	0	
3-W-1100	Install TM 6.1 - Stg 6 Boston to Louisa	3	3	0	3	0	3	29-Jul-25 A	31-Jul-25 A			0	0	
DSC-287	DSC 287 Stage 6, 2EA Steel line conflict STA 49+75	1	1	0	1	0	1	31-Jul-25 A	31-Jul-25 A			0	0	
3-W-1110	Test & Flush TM 6.1 - Stg 6 Boston to Louisa	3	3	2	1	0	1	01-Aug-25 A	01-Aug-25 A		13	0	2	
DSC-289	DSC 289 Stage 6, WS-1010 Pinched EX Shallow Service	1	1	0	1	0	1	01-Aug-25 A	01-Aug-25 A			0	0	
3-W-1120	Bact Results TM 6.1 - Stg 6 Boston to Louisa	3	3	0	3	0	3	06-Aug-25 A	08-Aug-25 A		13	0	0	
3-W-1130	SPU Customer Notification TM 6.1 - Stg 6 Boston to Louisa	5	5	0	5	0	5	11-Aug-25 A	15-Aug-25 A		13	0	0	

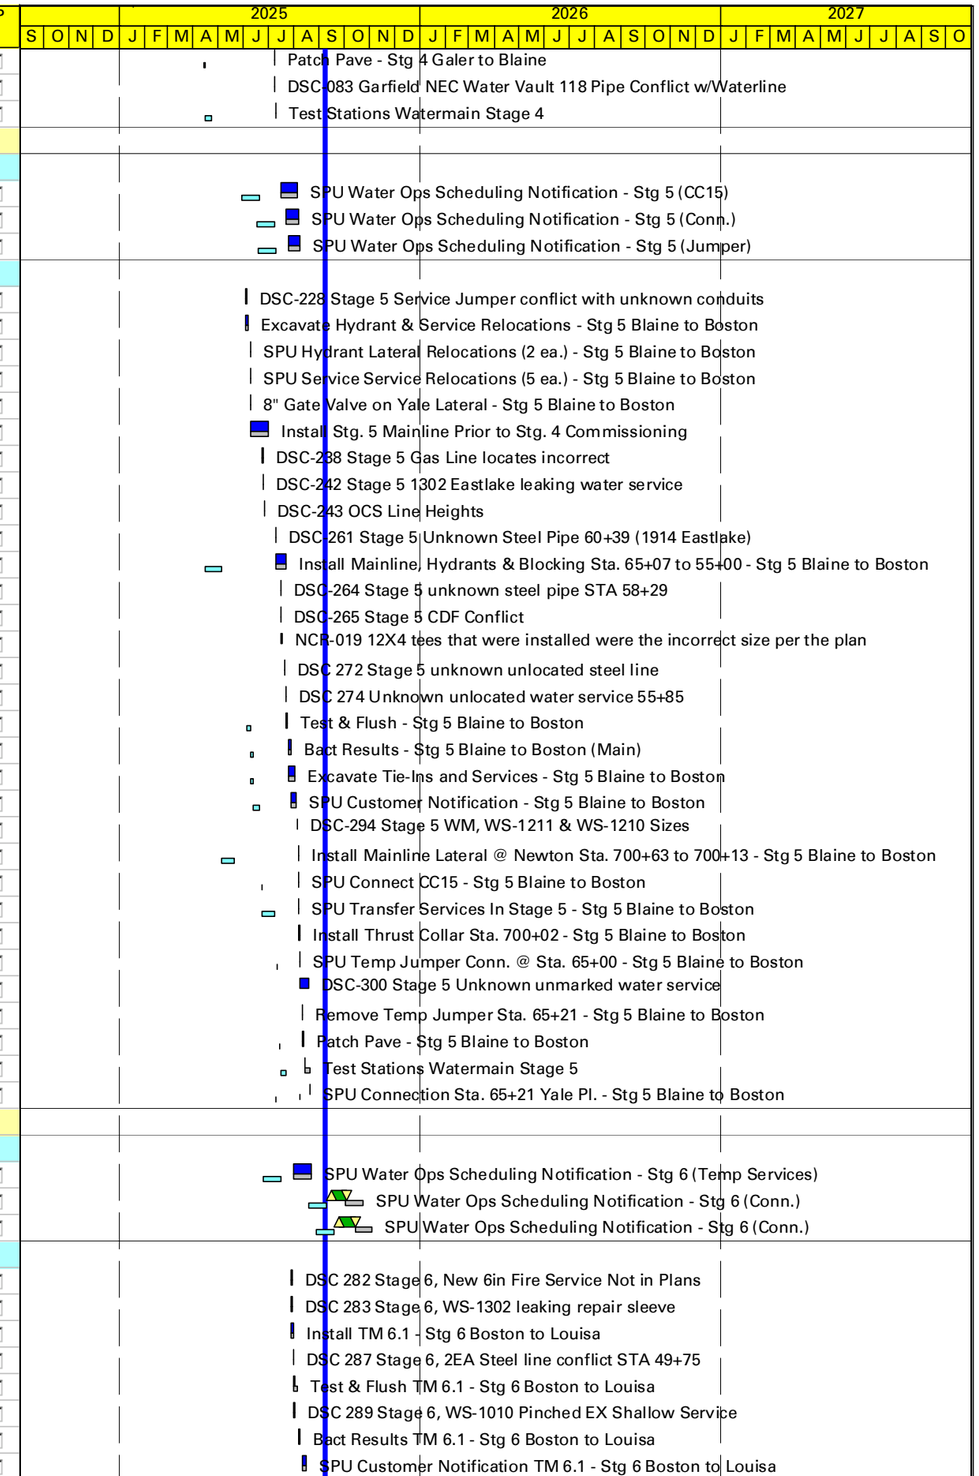

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-W-1140	SPU Connect TM 6.1 - Stg 6 Boston to Louisa	1	1	0	1	0	1	18-Aug-25 A	18-Aug-25 A		13	0	0	
3-W-1050	Transfer Services to TM 6.1 (7 ea.) - Stg 6 Boston to Louisa	3	3	2	1	0	1	19-Aug-25 A	19-Aug-25 A		13	0	2	
3-W-1051	SPU Temp Service Laterals (5 ea.) - Stg 6 Boston to Louisa	2	2	1	1	0	1	20-Aug-25 A	20-Aug-25 A		13	2	3	
3-W-1081	SPU Temp Hydrant Laterals (2 ea.) - Stg 6 Boston to Louisa	1	1	0	1	0	1	21-Aug-25 A	21-Aug-25 A		13	3	3	
3-W-1052	Install Mainline & Hydrants Sta. 44+64 to 50+00 - Stg 6 Boston to	15	15	6	9	0	9	22-Aug-25 A	04-Sep-25 A		13	3	9	
DSC-322	DSC-322 Stage 6 miss-marked water services	1	0	-1	1	0	1	27-Aug-25 A	27-Aug-25 A					
DSC-326	DSC-326 Stage 6 existing storm in conflict with watermain at Bost	1	0	-1	1	0	1	03-Sep-25 A	03-Sep-25 A					
3-W-1053	Install Mainline & Hydrants Sta. 50+00 to 54+86 - Stg 6 Boston to	11	15	4	2	9	11	05-Sep-25 A	19-Sep-25	26	13	9	13	
DSC-337	DSC-337 Stage 6 WM, Power Conflict at 50+79	1	0	-1	1	0	1	08-Sep-25 A	08-Sep-25 A					
3-W-1054	Test & Flush - Stg 6 Boston to Louisa	2	2	0	0	2	2	22-Sep-25	23-Sep-25	26	13	13	13	
3-W-1055	Bact Results - Stg 6 Boston to Louisa	3	3	0	0	3	3	24-Sep-25	26-Sep-25	26	13	13	13	
3-W-1057	Excavate Connections and Services - Stg 6 Boston to Louisa	3	3	0	0	3	3	24-Sep-25	26-Sep-25	31	18	13	13	
3-W-1056	SPU Customer Notification - Stg 6 Boston to Louisa	5	5	0	0	5	5	29-Sep-25	03-Oct-25	26	13	13	13	
3-W-1058	Connection at Sta. 55+00 - Stg 6 Boston to Louisa	1	1	0	0	1	1	06-Oct-25	06-Oct-25	26	13	13	13	
3-W-1059	SPU Transfer Services - Stg 6 Boston to Louisa (22 ea.)	6	6	0	0	6	6	07-Oct-25	15-Oct-25	26	13	13	13	
3-W-1060	SPU Connection at Sta. 44+00 - Stg 6 Boston to Louisa	1	1	0	0	1	1	16-Oct-25	16-Oct-25	26	13	13	13	
3-W-1061	Remove Temp Main - Stg 6 Boston to Louisa	2	2	0	0	2	2	17-Oct-25	20-Oct-25	26	13	13	13	
3-W-1062	Patch Pave - Stg 6 Boston to Louisa	2	2	0	0	2	2	21-Oct-25	22-Oct-25	26	13	13	13	
3-W-1090	Test Stations Watermain Stage 6	5	5	0	0	5	5	23-Oct-25	29-Oct-25	142	129	13	13	
Conduit Crossings														
3-CC-1064	Galer - Conduit Crossings	13	13	0	13	0	13	26-Jun-25 A	15-Jul-25 A			0	0	
3-CC-1065	Garfield - Conduit Crossings	10	10	0	10	0	10	07-Jul-25 A	18-Jul-25 A			0	0	
DSC-256	DSC-256 Unknown Conduits NEC Galer	1	1	0	1	0	1	09-Jul-25 A	09-Jul-25 A			0	0	
3-CC-1066	Lynn - Conduit Crossings	5	5	0	0	5	5	23-Oct-25	29-Oct-25	26	13	13	13	
Roadway														
Galer to Garfield East Side														
3-RW-1139	Complete SCL Pole Relocation 1 ea. (by SCL) - Galer to Garfield	0	0	0	0	0	0		18-Jul-25 A			0	0	
3-RW-1069	Roadway Demo & Exc - Galer to Garfield (E)	7	7	0	7	0	7	21-Jul-25 A	29-Jul-25 A			0	0	
3-RW-1109	Remove/Abandon Waterline & Appurtances - Galer to Garfield (E)	7	7	0	7	0	7	21-Jul-25 A	29-Jul-25 A			0	0	
DSC-276	DSC 276 Galer-Garfield Demolition, Red CDF Conflict	1	1	0	1	0	1	23-Jul-25 A	23-Jul-25 A			0	0	
DSC-277	DSC 277 Galer-Garfield Irrigation line cast in existing roadway	1	1	0	1	0	1	24-Jul-25 A	24-Jul-25 A			0	0	
DSC-278	DSC 278 Galer Eastside Gasline in conflict with the roadway	1	1	0	1	0	1	24-Jul-25 A	24-Jul-25 A			0	0	
3-RW-1070	Pour Roadway - Galer to Garfield (E)	10	10	-1	11	0	11	04-Aug-25 A	18-Aug-25 A		-5	0	-1	
NCR-023	NCR-023 Electrical loop not installed	1	0	-1	1	0	1	07-Aug-25 A	07-Aug-25 A					
3-RW-1071	Curb - Galer to Garfield (E)	2	2	1	1	0	1	27-Aug-25 A	27-Aug-25 A		-5	-7	-6	
3-RW-1072	Patch Pave - Galer to Garfield (E)	1	1	0	1	0	1	27-Aug-25 A	27-Aug-25 A		-5	-5	-5	
Garfield to Howe East Side														
3-RW-1114	Remove/Abandon Waterline & Appurtances - Garfield to Howe (E)	10	10	-4	14	0	14	14-Aug-25 A	04-Sep-25 A		-5	5	1	
3-RW-1074	Roadway Demo & Exc - Garfield to Howe (E)	10	10	-7	17	0	17	14-Aug-25 A	08-Sep-25 A		-5	5	-2	
DSC-307	DSC-307 Garfield WQ-B117 Unknown Unlocated Conduit	1	0	-1	1	0	1	15-Aug-25 A	15-Aug-25 A					
DSC-309	DSC-309 Garfield East Side WQV B117 Conflict with Gas line	1	0	-17	15	2	17	18-Aug-25 A	10-Sep-25	-8				
DSC-317	DSC-317 Howe East side pavement thickness 18"	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
DSC-319	DSC-319 Garfield WQV B117 to CB B34 will not work per plan	1	0	-1	1	0	1	26-Aug-25 A	26-Aug-25 A					
3-RW-1075	Pour Roadway - Garfield to Howe (E)	5	5	-4	3	6	9	04-Sep-25 A	16-Sep-25	-8	-5	1	-3	
DSC-340	DSC-340 NEC Garfield Ex. MH Elevation Conflict	1	0	-1	1	0	1	08-Sep-25 A	08-Sep-25 A					
3-RW-1076	Curb - Garfield to Howe (E)	2	2	0	0	2	2	17-Sep-25	18-Sep-25	-5	0	-3	-3	
RFI-069	Install WQ B117 and B113 after RFI-059	8	8	0	0	8	8	17-Sep-25	26-Sep-25	-8	-5	-3	-3	
3-RW-1116	Mid-Block Sidewalk Galer to Howe	2	0	-2	0	2	2	19-Sep-25	22-Sep-25	-5				
3-RW-1077	Patch Pave - Garfield to Howe (E)	1	1	0	0	1	1	23-Sep-25	23-Sep-25	-5	0	-5	-5	
Galer to Garfield West Side														
3-RW-1079	Roadway Demo & Exc - Galer to Garfield (W)	10	10	0	0	10	10	29-Sep-25	10-Oct-25	-8	-5	-3	-3	
3-RW-1080	Pour Roadway - Galer to Garfield (W)	6	6	0	0	6	6	14-Oct-25	21-Oct-25	9	12	-3	-3	
3-RW-1081	Curb - Galer to Garfield (W)	2	2	0	0	2	2	22-Oct-25	23-Oct-25	9	12	-3	-3	
3-RW-1082	Patch Pave - Galer to Garfield (W)	1	1	0	0	1	1	24-Oct-25	24-Oct-25	9	12	-3	-3	

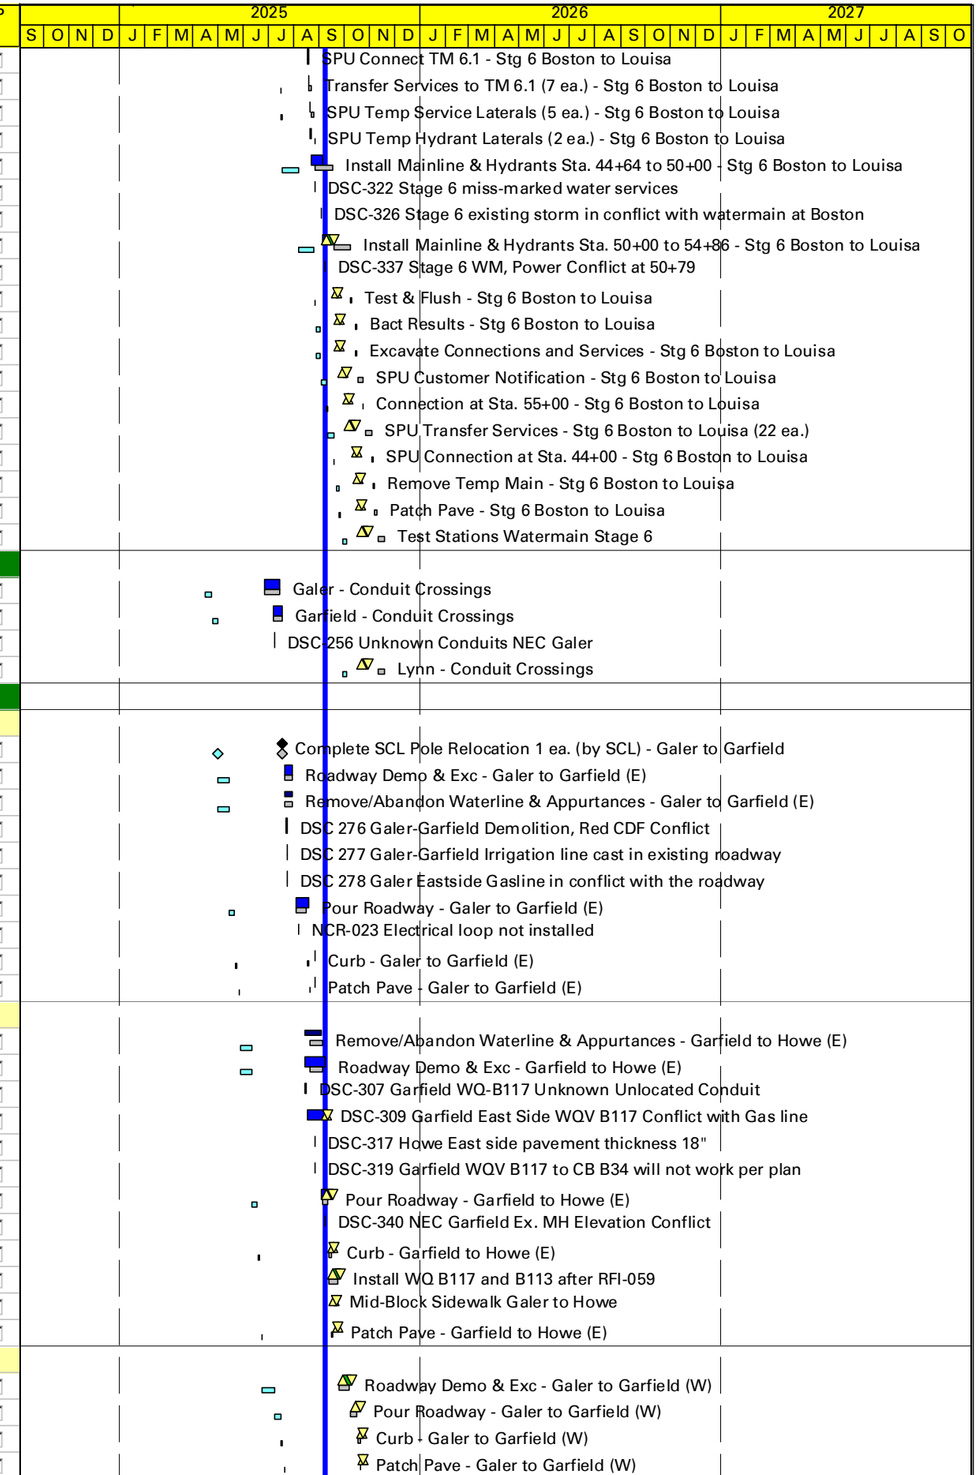

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Garfield to Howe West Side														
3-RW-1084	Roadway Demo & Exc - Garfield to Howe (W)	10	10	0	0	10	10	14-Oct-25	27-Oct-25	-8	-5	-3	-3	
3-RW-1085	Pour Roadway - Garfield to Howe (W)	5	5	0	0	5	5	28-Oct-25	03-Nov-25	1	4	-3	-3	
3-RW-1086	Curb - Garfield to Howe (W)	2	2	0	0	2	2	04-Nov-25	05-Nov-25	1	4	-3	-3	
3-RW-1087	Patch Pave - Garfield to Howe (W)	1	1	0	0	1	1	06-Nov-25	06-Nov-25	1	4	-3	-3	
Howe to Boston East Side														
3-RW-1089	Roadway Demo & Exc - Howe to Boston (E)	10	10	0	0	10	10	28-Oct-25	10-Nov-25	-8	-5	-3	-3	
3-RW-1119	Remove/Abandon Waterline & Appurtances - Howe to Boston (E)	10	10	0	0	10	10	28-Oct-25	10-Nov-25	-8	-5	-3	-3	
3-RW-1090	Pour Roadway - Howe to Boston (E)	5	5	0	0	5	5	12-Nov-25	18-Nov-25	-8	-5	-3	-3	
3-RW-1091	Curb - Howe to Boston (E)	2	2	0	0	2	2	19-Nov-25	20-Nov-25	-8	-5	-3	-3	
3-RW-1092	Patch Pave - Howe to Boston (E)	1	1	0	0	1	1	21-Nov-25	21-Nov-25	-8	-5	-3	-3	
Howe to Boston West Side														
3-RW-1094	Roadway Demo & Exc - Howe to Boston (W)	5	5	0	0	5	5	24-Nov-25	02-Dec-25	-8	-5	-3	-3	
3-RW-1095	Pour Roadway - Howe to Boston (W)	10	10	0	0	10	10	03-Dec-25	16-Dec-25	-8	-5	-3	-3	
3-RW-1096	Curb - Howe to Boston (W)	2	2	0	0	2	2	17-Dec-25	18-Dec-25	-8	-5	-3	-3	
3-RW-1097	Patch Pave - Howe to Boston (W)	1	1	0	0	1	1	19-Dec-25	19-Dec-25	-8	-5	-3	-3	
Boston to Lynn East Side														
3-RW-1099	Roadway Demo & Exc - Boston to Lynn (E)	8	8	0	0	8	8	22-Dec-25	02-Jan-26	-8	-5	-3	-3	
3-RW-1129	Remove/Abandon Waterline & Appurtances -Boston to Lynn (E)	8	8	0	0	8	8	22-Dec-25	02-Jan-26	-8	-5	-3	-3	
3-RW-1100	Pour Roadway - Boston to Lynn (E)	3	3	0	0	3	3	05-Jan-26	07-Jan-26	-8	-5	-3	-3	
3-RW-1101	Curb - Boston to Lynn (E)	1	1	0	0	1	1	08-Jan-26	08-Jan-26	-8	-5	-3	-3	
3-RW-1102	Patch Pave - Boston to Lynn (E)	1	1	0	0	1	1	09-Jan-26	09-Jan-26	-8	-5	-3	-3	
Boston to Lynn West Side														
3-RW-1104	Roadway Demo & Exc - Boston to Lynn (W)	8	8	0	0	8	8	12-Jan-26	22-Jan-26	-8	-5	-3	-3	
3-RW-1105	Pour Roadway - Boston to Lynn (W)	3	3	0	0	3	3	23-Jan-26	27-Jan-26	-8	-5	-3	-3	
3-RW-1106	Curb - Boston to Lynn (W)	1	1	0	0	1	1	28-Jan-26	28-Jan-26	-8	-5	-3	-3	
3-RW-1107	Patch Pave - Boston to Lynn (W)	1	1	0	0	1	1	29-Jan-26	29-Jan-26	-8	-5	-3	-3	
Weekend Roadway Work														
Galer East Side Phase 1														
3-WE-1110	Remove Roadway Type 2 - Galer (E) Ph.1	1	1	0	1	0	1	06-Sep-25 A	06-Sep-25 A		26	14	14	
3-WE-1111	Pour Roadway - Galer (E) Ph.1	1	1	0	1	0	1	07-Sep-25 A	07-Sep-25 A		26	14	14	
Galer East Side Phase 2														
3-WE-1113	Remove Roadway Type 2 - Garfield - Howe (E) Ph.2	1	1	0	0	1	1	13-Sep-25	13-Sep-25	40	26	14	14	
3-WE-1114	Pour Roadway - Garfield - Howe (E) Ph.2	1	1	0	0	1	1	14-Sep-25	14-Sep-25	40	26	14	14	
Fairview West Side Phase 1														
3-WE-1116	Remove Roadway Type 2 - Fairview (W) Ph.1	1	1	0	0	1	1	20-Sep-25	20-Sep-25	40	26	14	14	
3-WE-1117	Pour Roadway - Fairview (W) Ph.1	1	1	0	0	1	1	21-Sep-25	21-Sep-25	40	26	14	14	
Fairview West Side Phase 2														
3-WE-1119	Remove Roadway Type 2 - Fairview (W) Ph.2	1	1	0	0	1	1	27-Sep-25	27-Sep-25	40	26	14	14	
3-WE-1120	Pour Roadway - Fairview (W) Ph.2	1	1	0	0	1	1	28-Sep-25	28-Sep-25	40	26	14	14	
Lynn East Side														
3-WE-1122	Remove Roadway Type 2 - Lynn (E)	1	1	0	0	1	1	31-Jan-26	31-Jan-26	-4	-4	0	0	
3-WE-1123	Pour Roadway - Lynn (E)	1	1	0	0	1	1	01-Feb-26	01-Feb-26	-4	-4	0	0	
Lynn West Side														
3-WE-1125	Remove Roadway Type 2 - Lynn (W)	1	1	0	0	1	1	07-Feb-26	07-Feb-26	-4	-4	0	0	
3-WE-1126	Pour Roadway - Lynn (W)	1	1	0	0	1	1	08-Feb-26	08-Feb-26	-4	-4	0	0	
Pole Foundations														
3-PF-1128	Lynn to Galer - Pole Foundations (8 ea.)	13	13	0	0	13	13	09-Feb-26	26-Feb-26	-7	-7	0	0	
Sidewalks														
Galer SEC														
3-SW-1131	Remove Sidewalk - Galer SEC	1	1	0	0	1	1	27-Feb-26	27-Feb-26	-7	-7	0	0	
3-SW-1132	Trench Electrical - Galer SEC	2	2	0	0	2	2	02-Mar-26	03-Mar-26	-7	-7	0	0	
3-SW-1133	Electrical - Galer SEC	4	4	0	0	4	4	04-Mar-26	09-Mar-26	-7	-7	0	0	
3-SW-1134	Grade Sidewalks - Galer SEC	2	2	0	0	2	2	10-Mar-26	11-Mar-26	-7	-7	0	0	

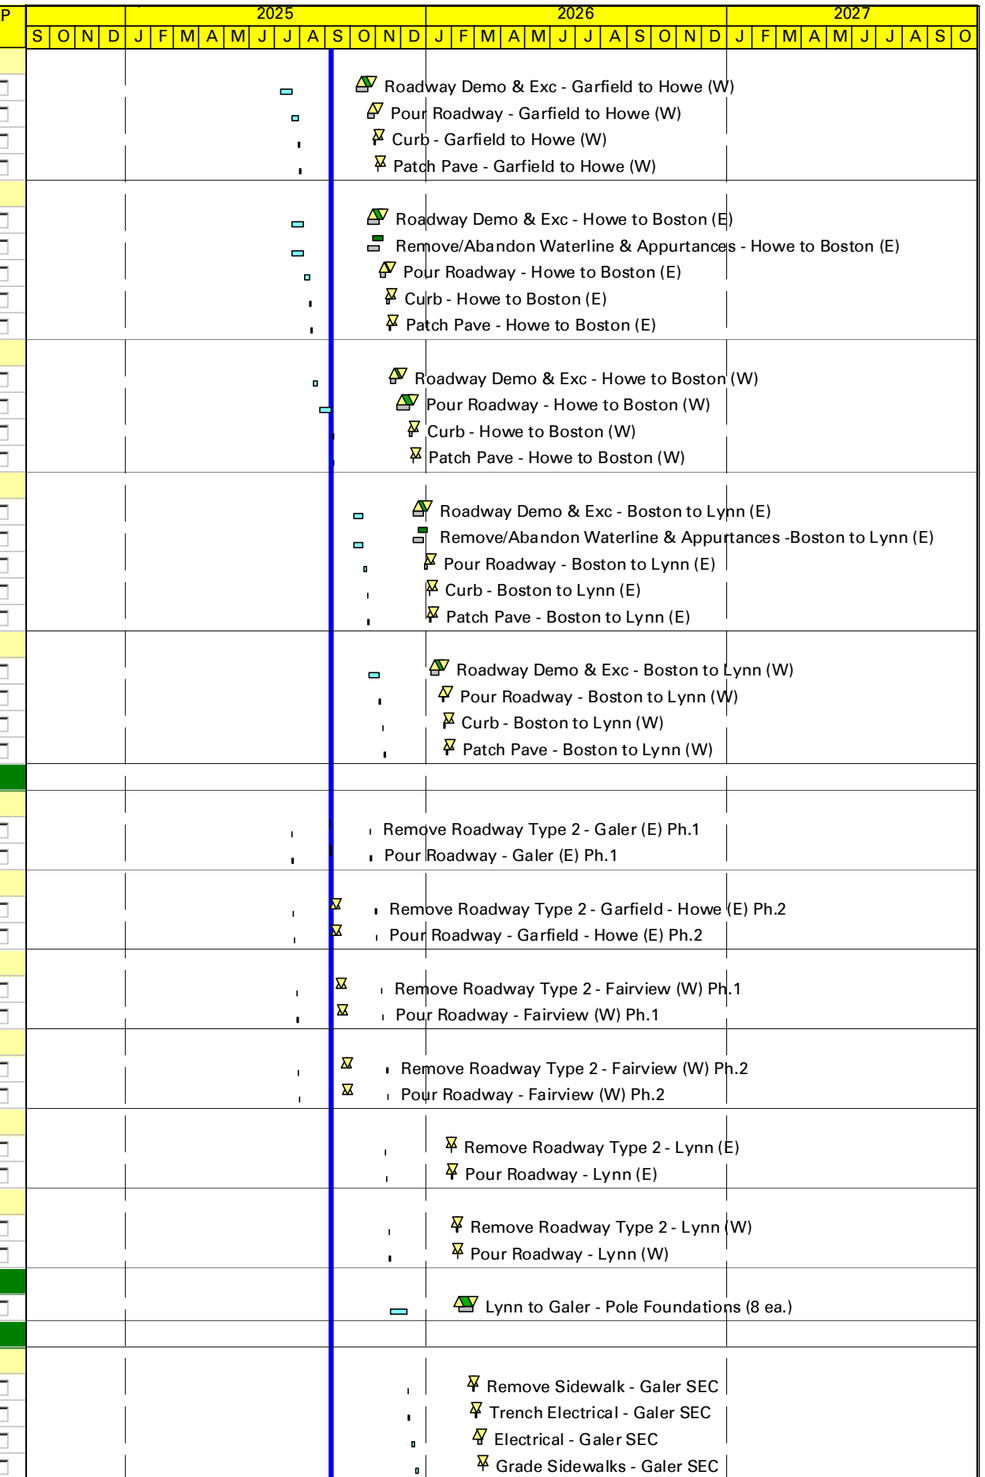

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work
BL1 LOE | Milestone
BL2 LOE | Previous MS
Actual Level of Effort | Previous Bar
Actual Work | Baseline MS
Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-SW-1135	Pour Sidewalks/Curb Ramps - Galer SEC	3	3	0	0	3	3	12-Mar-26	16-Mar-26	-7	-7	0	0	
Galer NEC														
3-SW-1137	Remove Sidewalk - Galer NEC	2	2	0	0	2	2	17-Mar-26	18-Mar-26	-7	-7	0	0	
3-SW-1138	Trench Electrical - Galer NEC	2	2	0	0	2	2	19-Mar-26	20-Mar-26	-7	-7	0	0	
3-SW-1139	Electrical - Galer NEC	4	4	0	0	4	4	23-Mar-26	26-Mar-26	5	5	0	0	
3-SW-1140	Grade Sidewalks - Galer NEC	2	2	0	0	2	2	27-Mar-26	30-Mar-26	5	5	0	0	
3-SW-1141	Pour Sidewalks/Curb Ramps - Galer NEC	4	4	0	0	4	4	31-Mar-26	03-Apr-26	5	5	0	0	
Garfield SEC														
3-SW-1143	Remove Sidewalk - Garfield SEC	2	2	0	0	2	2	23-Mar-26	24-Mar-26	-7	-7	0	0	
3-SW-1144	Trench Electrical - Garfield SEC	2	2	0	0	2	2	25-Mar-26	26-Mar-26	-7	-7	0	0	
3-SW-1145	Electrical - Garfield SEC	4	4	0	0	4	4	27-Mar-26	01-Apr-26	5	5	0	0	
3-SW-1146	Grade Sidewalks - Garfield SEC	2	2	0	0	2	2	02-Apr-26	03-Apr-26	5	5	0	0	
3-SW-1147	Pour Sidewalks/Curb Ramps - Garfield SEC	4	4	0	0	4	4	06-Apr-26	09-Apr-26	5	5	0	0	
Garfield NEC														
3-SW-1149	Remove Sidewalk - Garfield NEC	1	1	0	0	1	1	27-Mar-26	27-Mar-26	-7	-7	0	0	
3-SW-1150	Trench Electrical - Garfield NEC	2	2	0	0	2	2	30-Mar-26	31-Mar-26	-7	-7	0	0	
3-SW-1151	Electrical - Garfield NEC	6	6	0	0	6	6	01-Apr-26	08-Apr-26	-7	-7	0	0	
3-SW-1152	Excavate Shelter Foundation - Garfield NEC	1	1	0	0	1	1	09-Apr-26	09-Apr-26	-7	-7	0	0	
3-SW-1153	Form Pour Shelter Foundation - Garfield NEC	4	4	0	0	4	4	10-Apr-26	15-Apr-26	-7	-7	0	0	
3-SW-1154	Grade Sidewalks - Garfield NEC	2	2	0	0	2	2	16-Apr-26	17-Apr-26	-7	-7	0	0	
3-SW-1155	Pour Sidewalks/Curb Ramps - Garfield NEC	4	4	0	0	4	4	20-Apr-26	23-Apr-26	-1	-1	0	0	
Blaine SEC														
3-SW-1157	Remove Sidewalk - Blaine SEC	1	1	0	0	1	1	20-Apr-26	20-Apr-26	-7	-7	0	0	
3-SW-1158	Grade Sidewalks - Blaine SEC	2	2	0	0	2	2	21-Apr-26	22-Apr-26	-7	-7	0	0	
3-SW-1159	Pour Sidewalks/Curb Ramps - Blaine SEC	3	3	0	0	3	3	23-Apr-26	27-Apr-26	-7	-7	0	0	
Blaine NEC														
3-SW-1161	Remove Sidewalk - Blaine NEC	1	1	0	0	1	1	28-Apr-26	28-Apr-26	-7	-7	0	0	
3-SW-1162	Grade Sidewalks - Blaine NEC	1	1	0	0	1	1	29-Apr-26	29-Apr-26	-7	-7	0	0	
3-SW-1163	Pour Sidewalks/Curb Ramps - Blaine NEC	4	4	0	0	4	4	30-Apr-26	05-May-26	-7	-7	0	0	
Howe SEC														
3-SW-1165	Remove Sidewalk - Howe SEC	1	1	0	0	1	1	06-May-26	06-May-26	-7	-7	0	0	
3-SW-1166	Grade Sidewalks - Howe SEC	2	2	0	0	2	2	07-May-26	08-May-26	-7	-7	0	0	
3-SW-1167	Pour Sidewalks/Curb Ramps - Howe SEC	4	4	0	0	4	4	11-May-26	14-May-26	-7	-7	0	0	
Howe NEC														
3-SW-1169	Remove Sidewalk - Howe NEC	1	1	0	0	1	1	15-May-26	15-May-26	-7	-7	0	0	
3-SW-1170	Grade Sidewalks - Howe NEC	2	2	0	0	2	2	18-May-26	19-May-26	-7	-7	0	0	
3-SW-1171	Pour Sidewalks/Curb Ramps - Howe NEC	4	4	0	0	4	4	20-May-26	26-May-26	-7	-7	0	0	
Newton SEC														
3-SW-1173	Remove Sidewalk - Newton SEC	1	1	0	0	1	1	27-May-26	27-May-26	-7	-7	0	0	
3-SW-1174	Grade Sidewalks - Newton SEC	1	1	0	0	1	1	28-May-26	28-May-26	-7	-7	0	0	
3-SW-1175	Pour Sidewalks/Curb Ramps - Newton SEC	2	2	0	0	2	2	29-May-26	01-Jun-26	-7	-7	0	0	
Newton NEC														
3-SW-1177	Remove Sidewalk - Newton NEC	1	1	0	0	1	1	02-Jun-26	02-Jun-26	-7	-7	0	0	
3-SW-1178	Grade Sidewalks - Newton NEC	1	1	0	0	1	1	03-Jun-26	03-Jun-26	-7	-7	0	0	
3-SW-1179	Pour Sidewalks/Curb Ramps - Newton NEC	2	2	0	0	2	2	04-Jun-26	05-Jun-26	-7	-7	0	0	
Boston SEC														
3-SW-1181	Remove Sidewalk - Boston SEC	1	1	0	0	1	1	08-Jun-26	08-Jun-26	-7	-7	0	0	
3-SW-1182	Grade Sidewalks - Boston SEC	2	2	0	0	2	2	09-Jun-26	10-Jun-26	-7	-7	0	0	
3-SW-1183	Pour Sidewalks/Curb Ramps - Boston SEC	4	4	0	0	4	4	11-Jun-26	13-Jul-26	-7	-7	0	0	
Boston NEC														
3-SW-1185	Remove Sidewalk - Boston NEC	2	2	0	0	2	2	14-Jul-26	15-Jul-26	-7	-7	0	0	
3-SW-1186	Trench Electrical - Boston NEC	2	2	0	0	2	2	16-Jul-26	17-Jul-26	-7	-7	0	0	
3-SW-1187	Electrical - Boston NEC	6	6	0	0	6	6	20-Jul-26	27-Jul-26	-7	-7	0	0	
3-SW-1188	Grade Sidewalks - Boston NEC	1	1	0	0	1	1	28-Jul-26	28-Jul-26	-7	-7	0	0	

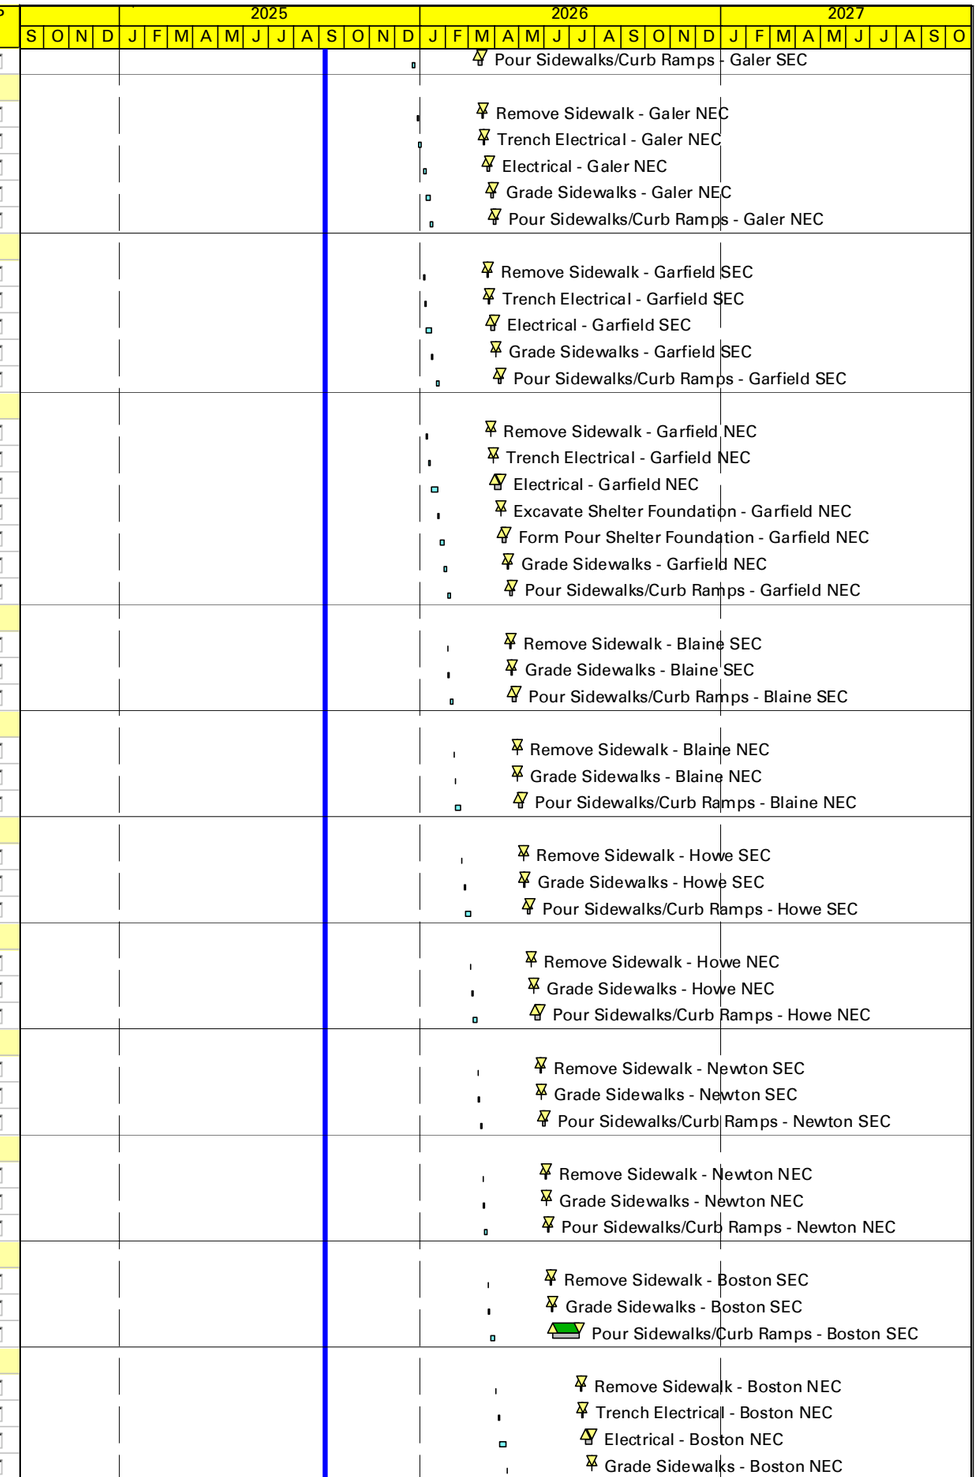

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort; BL1 LOE; BL2 LOE; Actual Level of Effort; Actual Work; Remaining Work; Critical Remaining Work; Milestone; Previous MS; Previous Bar; Baseline MS; Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-SW-1189	Pour Sidewalks/Curb Ramps - Boston NEC	4	4	0	0	4	4	29-Jul-26	03-Aug-26	-7	-7	0	0	
Lynn SEC														
3-SW-1191	Remove Sidewalk - Lynn SEC	2	2	0	0	2	2	27-Feb-26	02-Mar-26	5	5	0	0	
3-SW-1192	Trench Electrical - Lynn SEC	3	3	0	0	3	3	03-Mar-26	05-Mar-26	5	5	0	0	
3-SW-1193	Electrical - Lynn SEC	5	5	0	0	5	5	06-Mar-26	12-Mar-26	5	5	0	0	
3-SW-1194	Grade Sidewalks - Lynn SEC	2	2	0	0	2	2	13-Mar-26	16-Mar-26	5	5	0	0	
3-SW-1195	Pour Sidewalks/Curb Ramps - Lynn SEC	7	7	0	0	7	7	17-Mar-26	25-Mar-26	5	5	0	0	
Lynn NEC														
3-SW-1197	Remove Sidewalk - Lynn NEC	2	2	0	0	2	2	26-Mar-26	27-Mar-26	5	5	0	0	
3-SW-1198	Trench Electrical - Lynn NEC	2	2	0	0	2	2	30-Mar-26	31-Mar-26	5	5	0	0	
3-SW-1199	Electrical - Lynn NEC	4	4	0	0	4	4	01-Apr-26	06-Apr-26	5	5	0	0	
3-SW-1200	Grade Sidewalks - Lynn NEC	2	2	0	0	2	2	07-Apr-26	08-Apr-26	5	5	0	0	
3-SW-1201	Pour Sidewalks/Curb Ramps - Lynn NEC	3	3	0	0	3	3	09-Apr-26	13-Apr-26	15	15	0	0	
Galer SWC														
3-SW-1203	Remove Sidewalk - Galer SWC	1	1	0	0	1	1	09-Apr-26	09-Apr-26	5	5	0	0	
3-SW-1204	Trench Electrical - Galer SWC	2	2	0	0	2	2	10-Apr-26	13-Apr-26	5	5	0	0	
3-SW-1205	Electrical - Galer SWC	4	4	0	0	4	4	14-Apr-26	17-Apr-26	5	5	0	0	
3-SW-1206	Grade Sidewalks - Galer SWC	2	2	0	0	2	2	20-Apr-26	21-Apr-26	5	5	0	0	
3-SW-1207	Pour Sidewalks/Curb Ramps - Galer SWC	3	3	0	0	3	3	22-Apr-26	24-Apr-26	9	9	0	0	
Galer NWC														
3-SW-1209	Remove Sidewalk - Galer NWC	1	1	0	0	1	1	22-Apr-26	22-Apr-26	5	5	0	0	
3-SW-1210	Trench Electrical - Galer NWC	1	1	0	0	1	1	23-Apr-26	23-Apr-26	5	5	0	0	
3-SW-1211	Electrical - Galer NWC	4	4	0	0	4	4	24-Apr-26	29-Apr-26	5	5	0	0	
3-SW-1212	Grade Sidewalks - Galer NWC	1	1	0	0	1	1	30-Apr-26	30-Apr-26	5	5	0	0	
3-SW-1213	Pour Sidewalks/Curb Ramps - Galer NWC	1	1	0	0	1	1	01-May-26	01-May-26	5	5	0	0	
Garfield SWC														
3-SW-1215	Remove Sidewalk - Garfield SWC	2	2	0	0	2	2	24-Apr-26	27-Apr-26	-1	-1	0	0	
3-SW-1216	Trench Electrical - Garfield SWC	3	3	0	0	3	3	28-Apr-26	30-Apr-26	-1	-1	0	0	
3-SW-1217	Electrical - Garfield SWC	6	6	0	0	6	6	01-May-26	08-May-26	-1	-1	0	0	
3-SW-1218	Excavate Shelter Foundation - Garfield SWC	1	1	0	0	1	1	11-May-26	11-May-26	-1	-1	0	0	
3-SW-1219	Form Pour Shelter Foundation - Garfield SWC	4	4	0	0	4	4	12-May-26	15-May-26	-1	-1	0	0	
3-SW-1220	Grade Sidewalks - Garfield SWC	3	3	0	0	3	3	18-May-26	20-May-26	-1	-1	0	0	
3-SW-1221	Pour Sidewalks/Curb Ramps - Garfield SWC	6	6	0	0	6	6	21-May-26	29-May-26	32	32	0	0	
Garfield NWC														
3-SW-1223	Remove Sidewalk - Garfield NWC	1	1	0	0	1	1	21-May-26	21-May-26	-1	-1	0	0	
3-SW-1224	Trench Electrical - Garfield NWC	1	1	0	0	1	1	22-May-26	22-May-26	-1	-1	0	0	
3-SW-1225	Electrical - Garfield NWC	7	7	0	0	7	7	26-May-26	03-Jun-26	-1	-1	0	0	
3-SW-1226	Grade Sidewalks - Garfield NWC	1	1	0	0	1	1	04-Jun-26	04-Jun-26	-1	-1	0	0	
3-SW-1227	Pour Sidewalks/Curb Ramps - Garfield NWC	3	3	0	0	3	3	05-Jun-26	09-Jun-26	15	15	0	0	
Blaine SWC														
3-SW-1229	Remove Sidewalk - Blaine SWC	1	1	0	0	1	1	05-Jun-26	05-Jun-26	-1	-1	0	0	
3-SW-1230	Grade Sidewalks - Blaine SWC	1	1	0	0	1	1	08-Jun-26	08-Jun-26	-1	-1	0	0	
3-SW-1231	Pour Sidewalks/Curb Ramps - Blaine SWC	3	3	0	0	3	3	09-Jun-26	11-Jun-26	-1	-1	0	0	
Blaine NWC														
3-SW-1233	Remove Sidewalk - Blaine NWC	1	1	0	0	1	1	09-Jun-26	09-Jun-26	0	0	0	0	
3-SW-1234	Grade Sidewalks - Blaine NWC	1	1	0	0	1	1	10-Jun-26	10-Jun-26	0	0	0	0	
3-SW-1235	Pour Sidewalks/Curb Ramps - Blaine NWC	2	2	0	0	2	2	09-Jul-26	10-Jul-26	-1	-1	0	0	
Howe SWC														
3-SW-1237	Remove Sidewalk - Howe SEC	1	1	0	0	1	1	11-Jun-26	11-Jun-26	0	0	0	0	
3-SW-1238	Grade Sidewalks - Howe SEC	1	1	0	0	1	1	09-Jul-26	09-Jul-26	0	0	0	0	
3-SW-1239	Pour Sidewalks/Curb Ramps - Howe SEC	3	3	0	0	3	3	13-Jul-26	15-Jul-26	-1	-1	0	0	
Howe NWC														
3-SW-1241	Remove Sidewalk - Howe NEC	2	2	0	0	2	2	10-Jul-26	13-Jul-26	0	0	0	0	
3-SW-1242	Grade Sidewalks - Howe NEC	1	1	0	0	1	1	14-Jul-26	14-Jul-26	0	0	0	0	

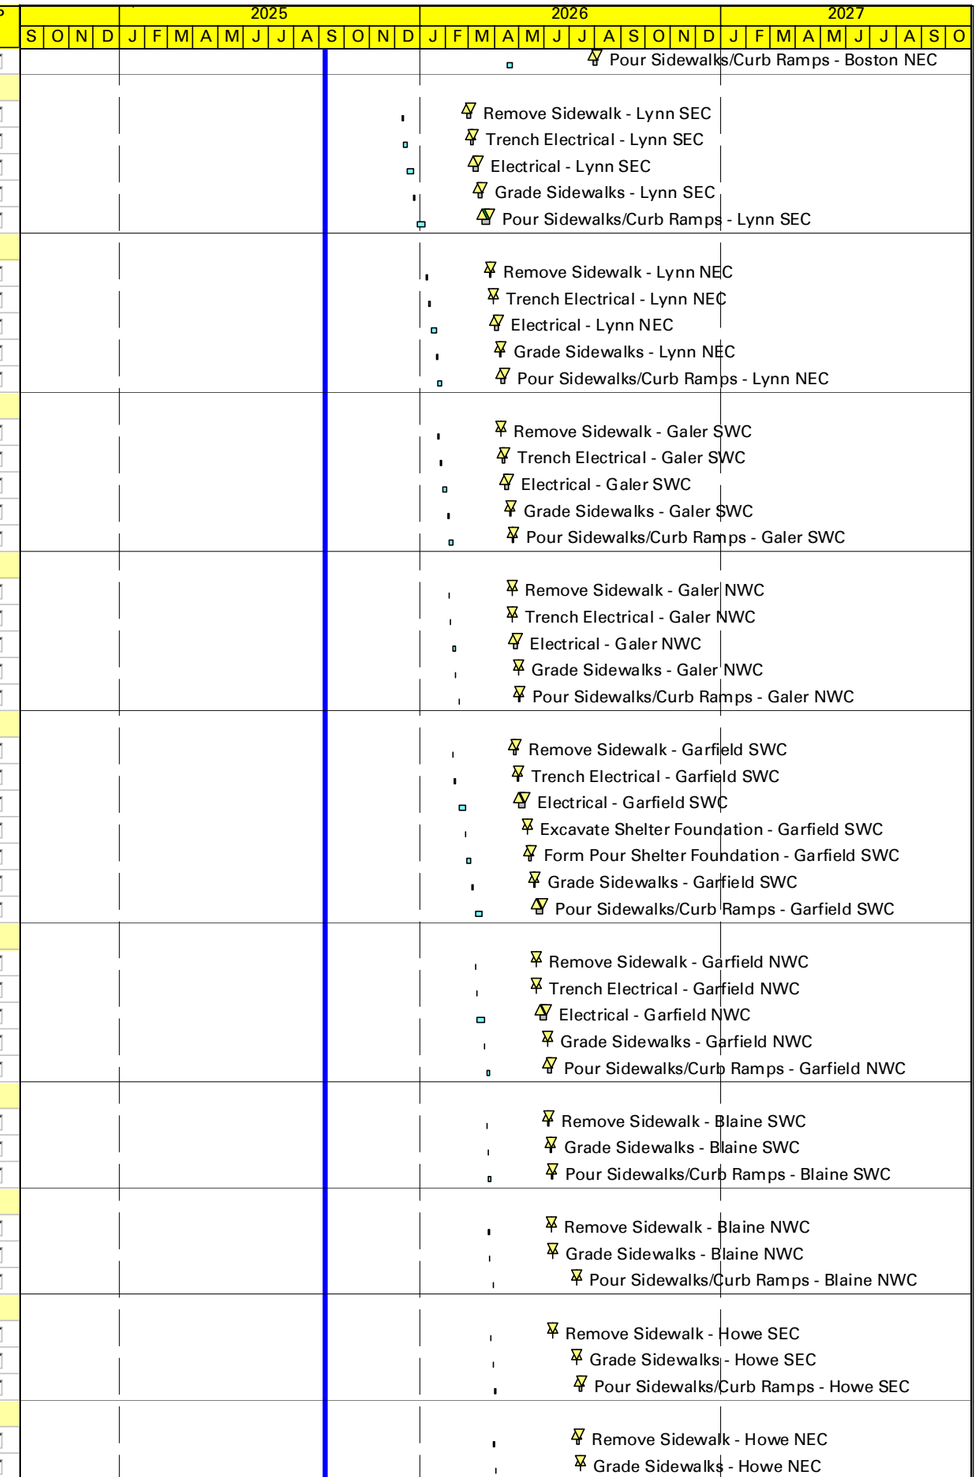

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-SW-1243	Pour Sidewalks/Curb Ramps - Howe NEC	4	4	0	0	4	4	16-Jul-26	21-Jul-26	-1	-1	0	0	
Newton SWC														
3-SW-1245	Remove Sidewalk - Newton SEC	2	2	0	0	2	2	15-Jul-26	16-Jul-26	0	0	0	0	
3-SW-1246	Grade Sidewalks - Newton SEC	1	1	0	0	1	1	17-Jul-26	17-Jul-26	0	0	0	0	
3-SW-1247	Pour Sidewalks/Curb Ramps - Newton SEC	4	4	0	0	4	4	22-Jul-26	27-Jul-26	-1	-1	0	0	
Newton NWC														
3-SW-1249	Remove Sidewalk - Newton NWC	1	1	0	0	1	1	20-Jul-26	20-Jul-26	0	0	0	0	
3-SW-1250	Grade Sidewalks - Newton NWC	1	1	0	0	1	1	21-Jul-26	21-Jul-26	0	0	0	0	
3-SW-1251	Pour Sidewalks/Curb Ramps - Newton NWC	2	2	0	0	2	2	28-Jul-26	29-Jul-26	-1	-1	0	0	
Boston SWC														
3-SW-1253	Remove Sidewalk - Boston SWC	1	1	0	0	1	1	22-Jul-26	22-Jul-26	0	0	0	0	
3-SW-1254	Grade Sidewalks - Boston SWC	1	1	0	0	1	1	23-Jul-26	23-Jul-26	0	0	0	0	
3-SW-1255	Pour Sidewalks/Curb Ramps - Boston SWC	3	3	0	0	3	3	30-Jul-26	03-Aug-26	-1	-1	0	0	
Boston NWC														
3-SW-1257	Remove Sidewalk - Boston NWC	2	2	0	0	2	2	24-Jul-26	27-Jul-26	0	0	0	0	
3-SW-1258	Grade Sidewalks - Boston NWC	1	1	0	0	1	1	28-Jul-26	28-Jul-26	0	0	0	0	
3-SW-1259	Pour Sidewalks/Curb Ramps - Boston NWC	3	3	0	0	3	3	04-Aug-26	06-Aug-26	-1	-1	0	0	
Lynn SWC														
3-SW-1261	Remove Sidewalk - Lynn SWC	3	3	0	0	3	3	29-Jul-26	31-Jul-26	0	0	0	0	
3-SW-1262	Trench Electrical - Lynn SWC	3	3	0	0	3	3	03-Aug-26	05-Aug-26	0	0	0	0	
3-SW-1263	Electrical - Lynn SWC	6	6	0	0	6	6	06-Aug-26	13-Aug-26	0	0	0	0	
3-SW-1264	Excavate Shelter Foundation - Lynn SWC	1	1	0	0	1	1	14-Aug-26	14-Aug-26	0	0	0	0	
3-SW-1265	Form Pour Shelter Foundation - Lynn SWC	4	4	0	0	4	4	17-Aug-26	20-Aug-26	0	0	0	0	
3-SW-1266	Grade Sidewalks - Lynn SWC	1	1	0	0	1	1	21-Aug-26	21-Aug-26	0	0	0	0	
3-SW-1267	Pour Sidewalks/Curb Ramps - Lynn SWC	3	3	0	0	3	3	24-Aug-26	26-Aug-26	0	0	0	0	
Lynn NWC														
3-SW-1269	Remove Sidewalk - Lynn NWC	2	2	0	0	2	2	27-Aug-26	28-Aug-26	27	27	0	0	
3-SW-1270	Trench Electrical - Lynn NWC	1	1	0	0	1	1	31-Aug-26	31-Aug-26	27	27	0	0	
3-SW-1271	Electrical - Lynn NWC	4	4	0	0	4	4	01-Sep-26	04-Sep-26	27	27	0	0	
3-SW-1272	Grade Sidewalks - Lynn NWC	1	1	0	0	1	1	08-Sep-26	08-Sep-26	27	27	0	0	
3-SW-1273	Pour Sidewalks/Curb Ramps - Lynn NWC	3	3	0	0	3	3	09-Sep-26	11-Sep-26	27	27	0	0	
Weekend Driveways														
Galer to Garfield East Side														
3-WE-1276	Remove Driveway - Galer to Garfield (E)	1	1	0	0	1	1	11-Apr-26	11-Apr-26	34	34	0	0	
3-WE-1277	Pour Driveway - Galer to Garfield (E)	1	1	0	0	1	1	12-Apr-26	12-Apr-26	34	34	0	0	
Garfield to Blaine East Side														
3-WE-1279	Remove Driveway - Garfield to Blaine (E)	1	1	0	0	1	1	02-May-26	02-May-26	30	30	0	0	
3-WE-1280	Pour Driveway - Garfield to Blaine (E)	1	1	0	0	1	1	03-May-26	03-May-26	30	30	0	0	
Blaine to Howe East Side														
3-WE-1282	Remove Driveway - Blaine to Howe (E)	1	1	0	0	1	1	16-May-26	16-May-26	28	28	0	0	
3-WE-1283	Pour Driveway - Blaine to Howe (E)	1	1	0	0	1	1	17-May-26	17-May-26	28	28	0	0	
Howe to Newton East Side														
3-WE-1285	Remove Driveway - Howe to Newton (E)	1	1	0	0	1	1	06-Jun-26	06-Jun-26	24	24	0	0	
3-WE-1286	Pour Driveway - Howe to Newton (E)	1	1	0	0	1	1	07-Jun-26	07-Jun-26	24	24	0	0	
Galer to Garfield West Side														
3-WE-1288	Remove Driveway - Galer to Garfield (W)	1	1	0	0	1	1	13-Jun-26	13-Jun-26	24	24	0	0	
3-WE-1289	Pour Driveway - Galer to Garfield (W)	1	1	0	0	1	1	14-Jun-26	14-Jun-26	24	24	0	0	
Garfield to Blaine West Side														
3-WE-1291	Remove Driveway - Garfield to Blaine (W)	1	1	0	0	1	1	20-Jun-26	20-Jun-26	24	24	0	0	
3-WE-1292	Pour Driveway - Garfield to Blaine (W)	1	1	0	0	1	1	21-Jun-26	21-Jun-26	24	24	0	0	
Howe to Newton West Side														
3-WE-1294	Remove Driveway - Howe to Newton (W)	1	1	0	0	1	1	01-Aug-26	01-Aug-26	14	14	0	0	
3-WE-1295	Pour Driveway - Howe to Newton (W)	1	1	0	0	1	1	02-Aug-26	02-Aug-26	14	14	0	0	
Newton to Boston West Side														

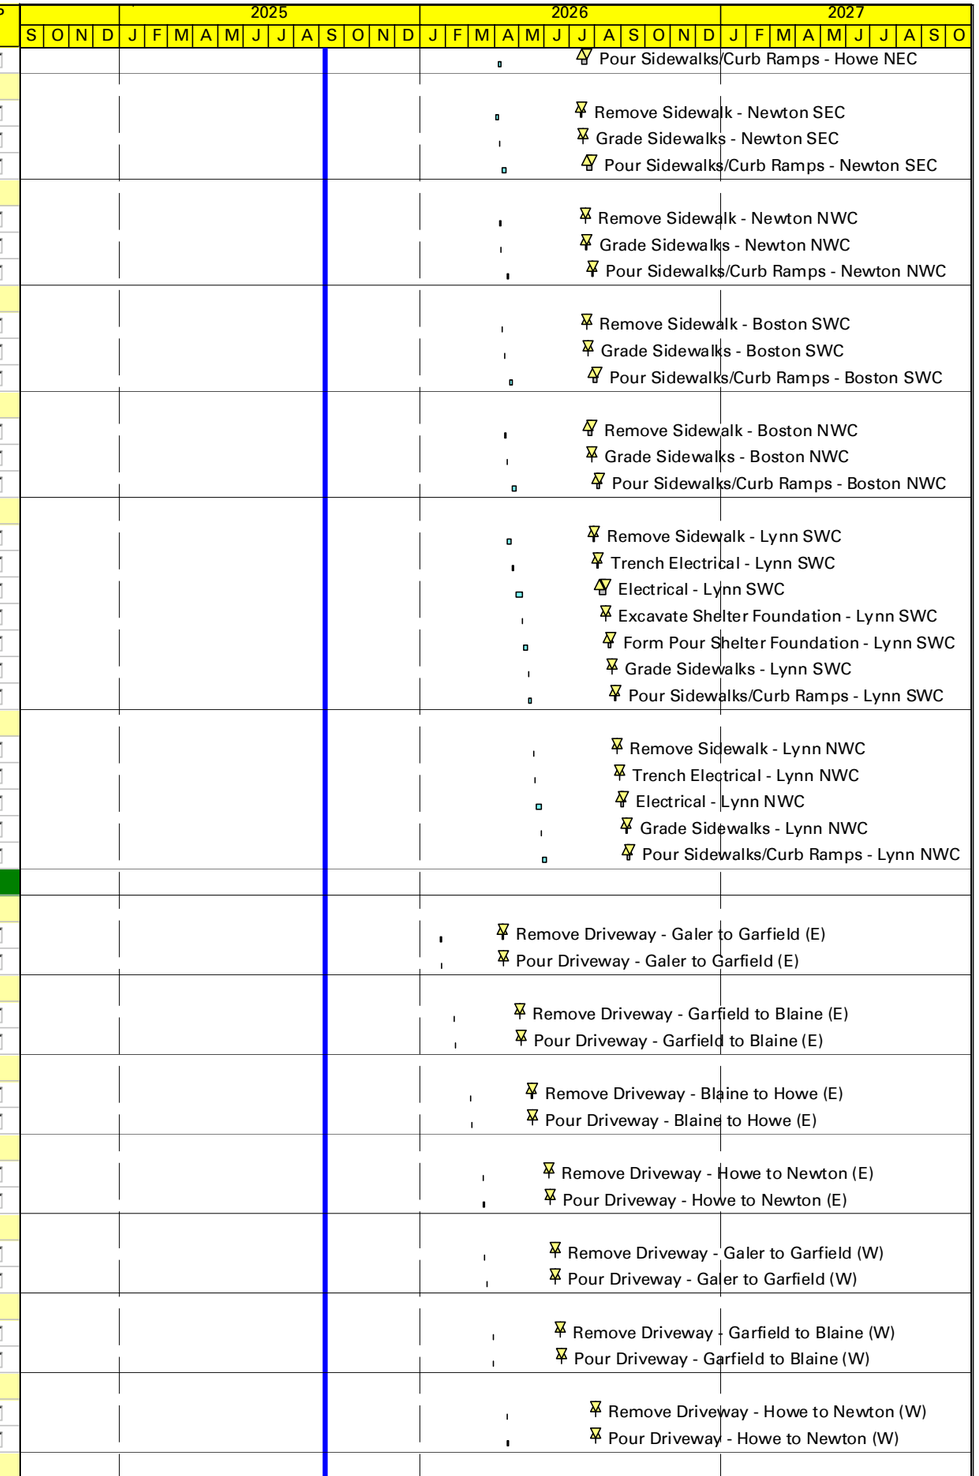

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-WE-1297	Remove Driveway - Newton to Boston (W)	1	1	0	0	1	1	08-Aug-26	08-Aug-26	14	14	0	0	
3-WE-1298	Pour Driveway - Newton to Boston (W)	1	1	0	0	1	1	09-Aug-26	09-Aug-26	14	14	0	0	
Boston to Lynn West Side														
3-WE-1300	Remove Driveway - Boston to Lynn (W)	1	1	0	0	1	1	29-Aug-26	29-Aug-26	10	10	0	0	
3-WE-1301	Pour Driveway - Boston to Lynn (W)	1	1	0	0	1	1	30-Aug-26	30-Aug-26	10	10	0	0	
Landscaping														
3-LS-1304	Install Irrigation - Zone 3	10	10	0	0	10	10	14-Sep-26	25-Sep-26	81	81	0	0	
3-LS-1305	Trees and Shrubs - Zone 3	20	20	0	0	20	20	01-Oct-26	29-Oct-26	78	78	0	0	
SCL Services														
Galer/Fairview SDOT Service														
3-SCL-1308	Install Meter Cabinet - Galer	1	1	0	0	1	1	10-Jun-26	10-Jun-26	15	15	0	0	
3-SCL-1309	SDOT Inspection - Galer	5	5	0	0	5	5	11-Jun-26	14-Jul-26	15	15	0	0	
3-SCL-1310	SDCI Inspection - Galer	5	5	0	0	5	5	15-Jul-26	21-Jul-26	15	15	0	0	
3-SCL-1311	SCL Inspection - Galer	21	21	0	0	21	21	22-Jul-26	19-Aug-26	15	15	0	0	
3-SCL-1312	SCL Heat Up Cabinet - Galer	21	21	0	0	21	21	20-Aug-26	18-Sep-26	15	15	0	0	
Garfield SDOT Service														
3-SCL-1314	Install Meter Cabinet - Garfield	1	1	0	0	1	1	24-Apr-26	24-Apr-26	52	52	0	0	
3-SCL-1315	SDOT Inspection - Garfield	5	5	0	0	5	5	27-Apr-26	01-May-26	52	52	0	0	
3-SCL-1316	SDCI Inspection - Garfield	5	5	0	0	5	5	04-May-26	08-May-26	52	52	0	0	
3-SCL-1317	SCL Inspection - Garfield	21	21	0	0	21	21	11-May-26	09-Jun-26	52	52	0	0	
3-SCL-1318	SCL Heat Up Cabinet - Garfield	21	21	0	0	21	21	10-Jun-26	04-Aug-26	52	52	0	0	
Boston SDOT Service														
3-SCL-1320	Install Meter Cabinet - Boston	1	1	0	0	1	1	04-Aug-26	04-Aug-26	-7	-7	0	0	
3-SCL-1321	SDOT Inspection - Boston	5	5	0	0	5	5	05-Aug-26	11-Aug-26	-7	-7	0	0	
3-SCL-1322	SDCI Inspection - Boston	5	5	0	0	5	5	12-Aug-26	18-Aug-26	-7	-7	0	0	
3-SCL-1323	SCL Inspection - Boston	21	21	0	0	21	21	19-Aug-26	17-Sep-26	-7	-7	0	0	
3-SCL-1324	SCL Heat Up Cabinet - Boston	21	21	0	0	21	21	18-Sep-26	19-Oct-26	-7	-7	0	0	
Lynn SDOT Service														
3-SCL-1326	Install Meter Cabinet - Lynn	1	1	0	0	1	1	07-Aug-26	07-Aug-26	-1	-1	0	0	
3-SCL-1327	SDOT Inspection - Lynn	5	5	0	0	5	5	10-Aug-26	14-Aug-26	-1	-1	0	0	
3-SCL-1328	SDCI Inspection - Lynn	5	5	0	0	5	5	17-Aug-26	21-Aug-26	-1	-1	0	0	
3-SCL-1329	SCL Inspection - Lynn	21	21	0	0	21	21	24-Aug-26	22-Sep-26	-1	-1	0	0	
3-SCL-1330	SCL Heat Up Cabinet - Lynn	21	21	0	0	21	21	23-Sep-26	22-Oct-26	-1	-1	0	0	
SB Garfield KCM Service														
3-SCL-1332	Install Meter Cabinet - SB Garfield	1	1	0	0	1	1	01-Jun-26	01-Jun-26	32	32	0	0	
3-SCL-1333	KCM Inspections - SB Garfield	5	5	0	0	5	5	02-Jun-26	08-Jun-26	32	32	0	0	
3-SCL-1334	SDCI Inspection - SB Garfield	5	5	0	0	5	5	09-Jun-26	10-Jul-26	32	32	0	0	
3-SCL-1335	SCL Inspection - SB Garfield	21	21	0	0	21	21	13-Jul-26	10-Aug-26	32	32	0	0	
3-SCL-1336	SCL Heat Up Cabinet - SB Garfield	21	21	0	0	21	21	11-Aug-26	09-Sep-26	32	32	0	0	
NB Garfield KCM Service														
3-SCL-1338	Install Meter Cabinet - NB Garfield	1	1	0	0	1	1	24-Apr-26	24-Apr-26	68	68	0	0	
3-SCL-1339	KCM Inspections - NB Garfield	5	5	0	0	5	5	27-Apr-26	01-May-26	68	68	0	0	
3-SCL-1340	SDCI Inspection - NB Garfield	5	5	0	0	5	5	04-May-26	08-May-26	68	68	0	0	
3-SCL-1341	SCL Inspection - NB Garfield	21	21	0	0	21	21	11-May-26	09-Jun-26	68	68	0	0	
3-SCL-1342	SCL Heat Up Cabinet - NB Garfield	21	21	0	0	21	21	10-Jun-26	04-Aug-26	68	68	0	0	
SB Lynn KCM Service														
3-SCL-1344	Install Meter Cabinet - SB Lynn	1	1	0	0	1	1	27-Aug-26	27-Aug-26	0	0	0	0	
3-SCL-1345	KCM Inspections - SB Lynn	5	5	0	0	5	5	28-Aug-26	03-Sep-26	0	0	0	0	
3-SCL-1346	SDCI Inspection - SB Lynn	5	5	0	0	5	5	04-Sep-26	11-Sep-26	0	0	0	0	
3-SCL-1347	SCL Inspection - SB Lynn	21	21	0	0	21	21	14-Sep-26	13-Oct-26	0	0	0	0	
3-SCL-1348	SCL Heat Up Cabinet - SB Lynn	21	21	0	0	21	21	14-Oct-26	12-Nov-26	0	0	0	0	
NB Lynn KCM Service														
3-SCL-1350	Install Meter Cabinet - NB Lynn	1	1	0	0	1	1	28-Aug-26	28-Aug-26	10	10	0	0	
3-SCL-1351	KCM Inspections - NB Lynn	5	5	0	0	5	5	31-Aug-26	04-Sep-26	10	10	0	0	

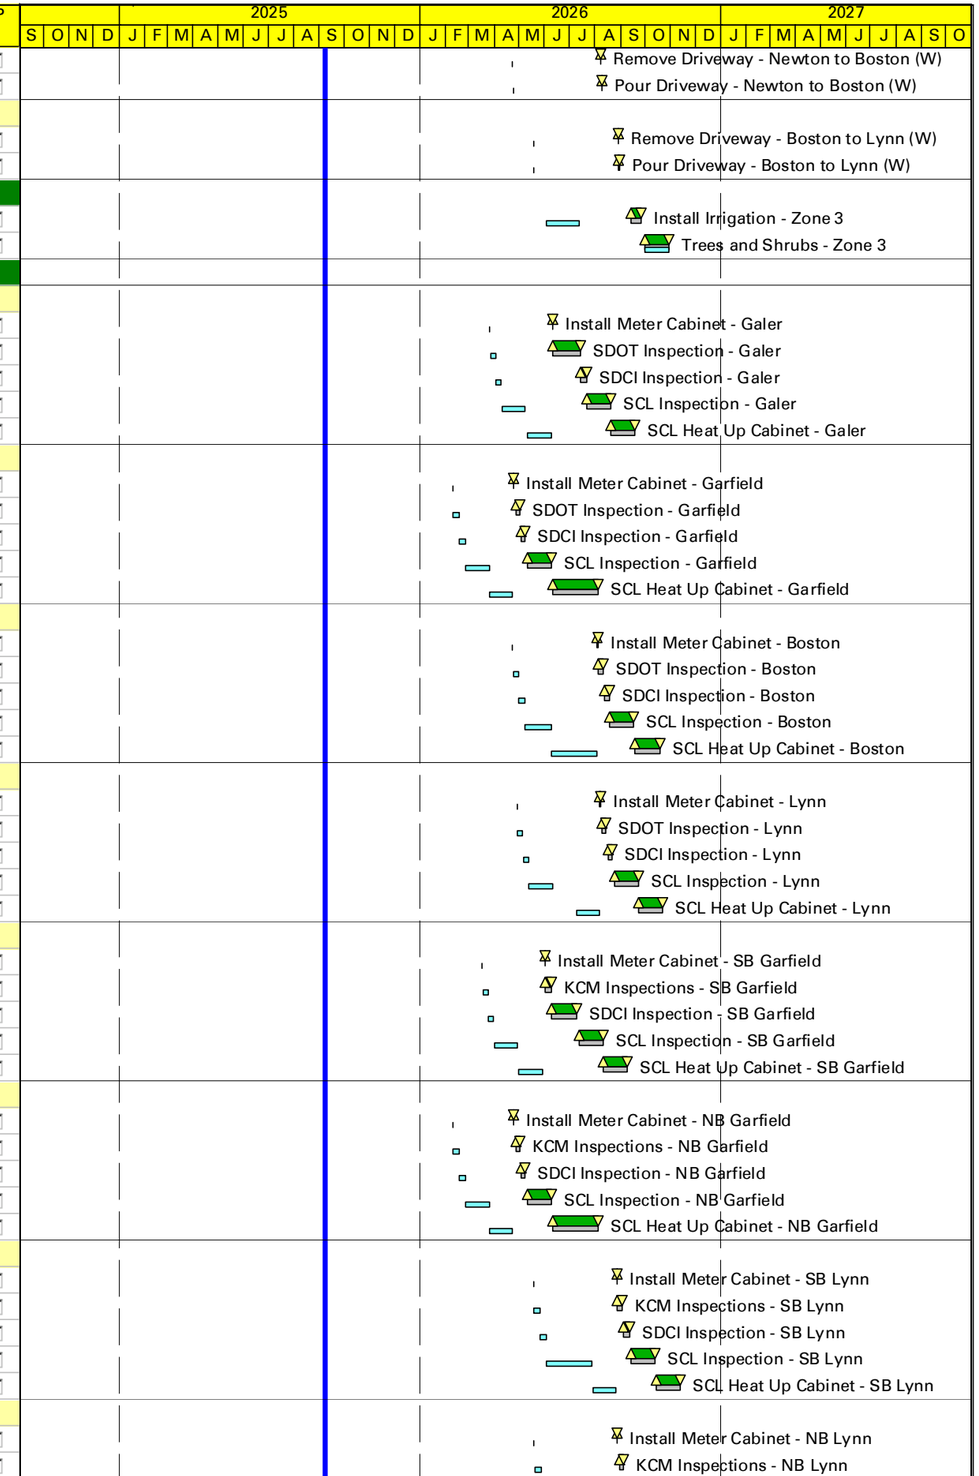

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-SCL-1352	SDCI Inspection - NB Lynn	5	5	0	0	5	5	08-Sep-26	14-Sep-26	10	10	0	0	☐
3-SCL-1353	SCL Inspection - NB Lynn	21	21	0	0	21	21	15-Sep-26	14-Oct-26	10	10	0	0	☐
3-SCL-1354	SCL Heat Up Cabinet - NB Lynn	21	21	0	0	21	21	15-Oct-26	13-Nov-26	10	10	0	0	☐
Signals														
Galer/Fairview														
3-SIG-1357	Install Poles - Galer	2	2	0	0	2	2	21-Sep-26	22-Sep-26	15	15	0	0	☐
3-SIG-1358	Build Signal - Galer	10	10	0	0	10	10	23-Sep-26	06-Oct-26	15	15	0	0	☐
3-SIG-1359	SDOT Inspection - Galer	5	5	0	0	5	5	07-Oct-26	14-Oct-26	30	30	0	0	☐
3-SIG-1360	SDOT Commission - Galer	10	10	0	0	10	10	15-Oct-26	28-Oct-26	30	30	0	0	☐
3-SIG-1361	Demo Old Signal & Temp Signal - Galer	2	2	0	0	2	2	29-Oct-26	30-Oct-26	30	30	0	0	☐
Garfield														
3-SIG-1363	Install Poles - Garfield	2	2	0	0	2	2	05-Aug-26	06-Aug-26	52	52	0	0	☐
3-SIG-1364	Build Signal - Garfield	10	10	0	0	10	10	07-Aug-26	20-Aug-26	52	52	0	0	☐
3-SIG-1365	SDOT Inspection - Garfield	5	5	0	0	5	5	21-Aug-26	27-Aug-26	65	65	0	0	☐
3-SIG-1366	SDOT Commission - Garfield	10	10	0	0	10	10	28-Aug-26	11-Sep-26	65	65	0	0	☐
3-SIG-1367	Demo Old Signal & Temp Signal - Garfield	2	2	0	0	2	2	14-Sep-26	15-Sep-26	65	65	0	0	☐
Boston														
3-SIG-1369	Install Poles - Boston	2	2	0	0	2	2	20-Oct-26	21-Oct-26	-7	-7	0	0	☐
3-SIG-1370	Build Signal - Boston	7	7	0	0	7	7	22-Oct-26	30-Oct-26	-7	-7	0	0	☐
3-SIG-1371	SDOT Inspection - Boston	5	5	0	0	5	5	02-Nov-26	06-Nov-26	19	19	0	0	☐
3-SIG-1372	SDOT Commission - Boston	10	10	0	0	10	10	09-Nov-26	23-Nov-26	19	19	0	0	☐
3-SIG-1373	Demo Old Signal & Temp Signal - Boston	2	2	0	0	2	2	24-Nov-26	25-Nov-26	19	19	0	0	☐
Lynn														
3-SIG-1375	Install Poles - Lynn	2	2	0	0	2	2	02-Nov-26	03-Nov-26	-7	-7	0	0	☐
3-SIG-1376	Build Signal - Lynn	7	7	0	0	7	7	04-Nov-26	13-Nov-26	-7	-7	0	0	☐
3-SIG-1377	SDOT Inspection - Lynn	5	5	0	0	5	5	16-Nov-26	20-Nov-26	13	13	0	0	☐
3-SIG-1378	SDOT Commission - Lynn	10	10	0	0	10	10	23-Nov-26	08-Dec-26	13	13	0	0	☐
3-SIG-1379	Demo Old Signal & Temp Signal - Lynn	2	2	0	0	2	2	09-Dec-26	10-Dec-26	13	13	0	0	☐
Lighting														
Eastlake/Fairfiew Schematic														
3-EL-1382	Build Schematic, Poles, Luminaires Wiring - Eastlake/Fairview Sch	5	5	0	0	5	5	07-Oct-26	14-Oct-26	15	15	0	0	☐
3-EL-1383	SCL Final Inspection - Eastlake/Fairview Schematic	10	10	0	0	10	10	15-Oct-26	28-Oct-26	15	15	0	0	☐
3-EL-1384	SCL Commission Lighting - Eastlake/Fairview Schematic	15	15	0	0	15	15	29-Oct-26	19-Nov-26	15	15	0	0	☐
3-EL-1385	Demo Old Lighting - Eastlake/Fairview Schematic	2	2	0	0	2	2	20-Nov-26	23-Nov-26	15	15	0	0	☐
Garfield Schematic														
3-EL-1387	Build Schematic, Poles, Luminaires Wiring - Garfield Schematic	5	5	0	0	5	5	21-Aug-26	27-Aug-26	52	52	0	0	☐
3-EL-1388	SCL Final Inspection - Garfield Schematic	10	10	0	0	10	10	28-Aug-26	11-Sep-26	52	52	0	0	☐
3-EL-1389	SCL Commission Lighting - Garfield Schematic	15	15	0	0	15	15	14-Sep-26	02-Oct-26	52	52	0	0	☐
3-EL-1390	Demo Old Lighting - Garfield Schematic	2	2	0	0	2	2	05-Oct-26	06-Oct-26	52	52	0	0	☐
Boston Schematic														
3-EL-1402	SCL Service Commissioning - Boston Schematic	21	21	0	0	21	21	07-Aug-26	04-Sep-26	58	58	0	0	☐
3-EL-1392	Build Schematic, Poles, Luminaires Wiring - Boston Schematic	5	5	0	0	5	5	02-Nov-26	06-Nov-26	5	5	0	0	☐
3-EL-1393	SCL Final Inspection - Boston Schematic	10	10	0	0	10	10	09-Nov-26	23-Nov-26	5	5	0	0	☐
3-EL-1394	SCL Commission Lighting - Boston Schematic	15	15	0	0	15	15	24-Nov-26	16-Dec-26	5	5	0	0	☐
3-EL-1395	Demo Old Lighting - Boston Schematic	2	2	0	0	2	2	17-Dec-26	18-Dec-26	5	5	0	0	☐
Lynn Schematic														
3-EL-1407	SCL Service Commissioning - Lynn Schematic	21	21	0	0	21	21	14-Sep-26	13-Oct-26	35	35	0	0	☐
3-EL-1397	Build Schematic, Poles, Luminaires Wiring - Lynn Schematic	10	10	0	0	10	10	16-Nov-26	01-Dec-26	-7	-7	0	0	☐
3-EL-1398	SCL Final Inspection - Lynn Schematic	10	10	0	0	10	10	02-Dec-26	15-Dec-26	-7	-7	0	0	☐
3-EL-1399	SCL Commission Lighting - Lynn Schematic	15	15	0	0	15	15	16-Dec-26	07-Jan-27	-7	-7	0	0	☐
3-EL-1400	Demo Old Lighting - Lynn Schematic	2	2	0	0	2	2	08-Jan-27	11-Jan-27	-7	-7	0	0	☐
Stations														
SB Garfield														
3-STN-1403	Install Shelters (2 Each) - Garfield SB Station	10	10	0	0	10	10	01-Jun-26	09-Jul-26	37	37	0	0	☐

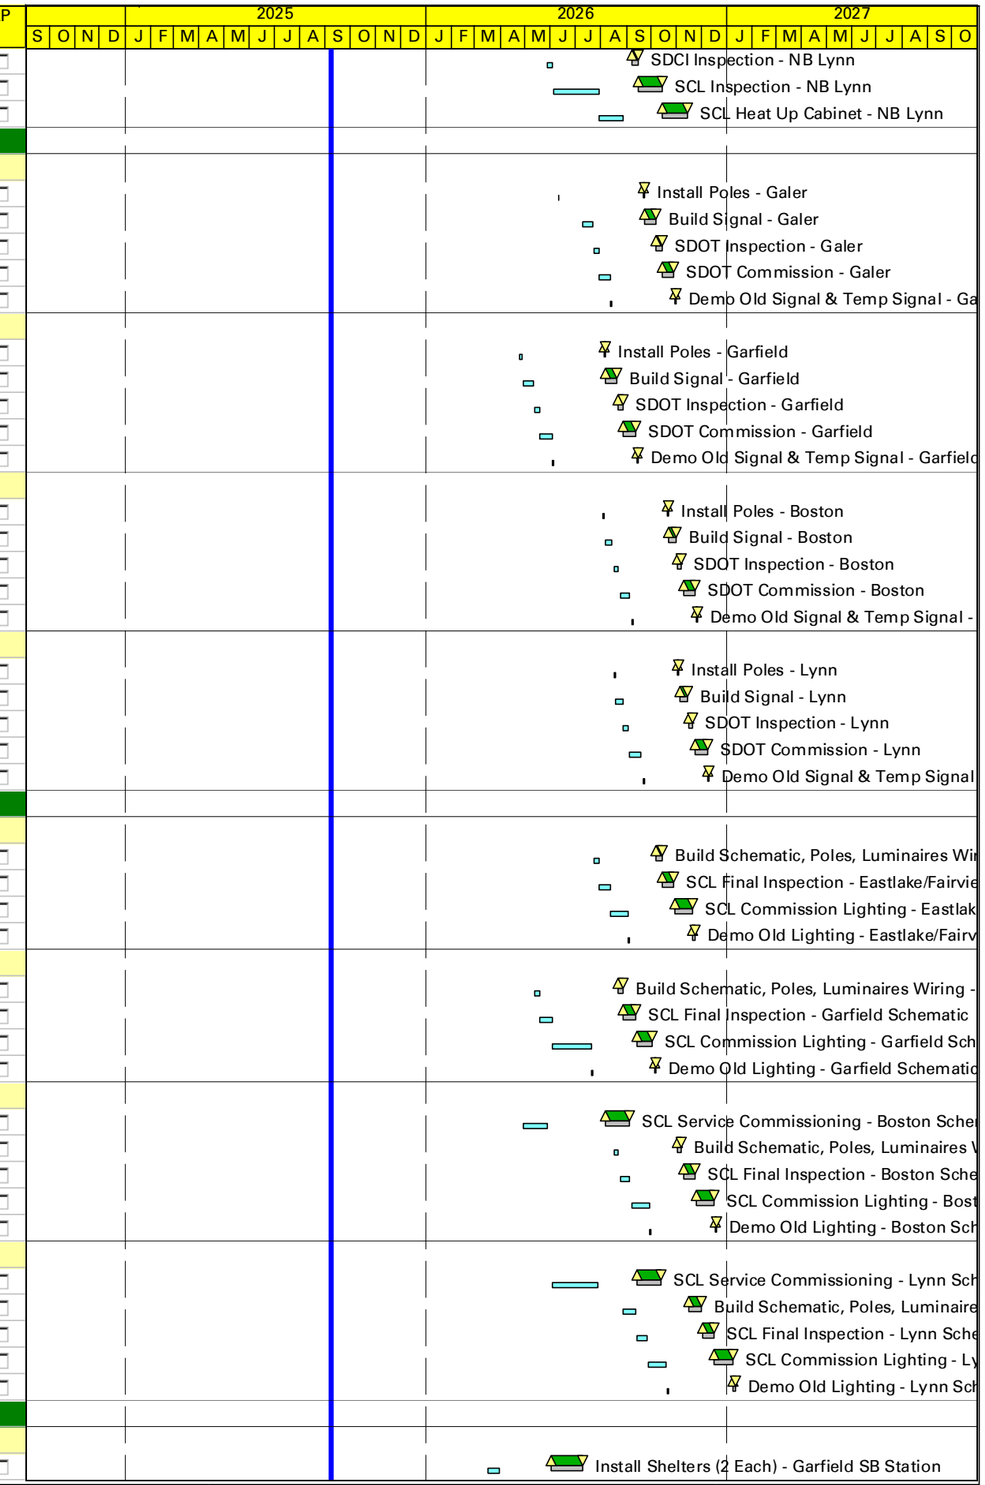

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-STN-1404	Install Amenities - Garfield SB Station	1	1	0	0	1	1	10-Jul-26	10-Jul-26	37	37	0	0	
3-STN-1405	Install Tech Pylon - Garfield SB Station	1	1	0	0	1	1	13-Jul-26	13-Jul-26	37	37	0	0	
NB Garfield Station														
3-STN-1407	Install Shelters (2 Each) - Garfield NB Station	10	10	0	0	10	10	14-Jul-26	27-Jul-26	37	37	0	0	
3-STN-1408	Install Amenities - Garfield NB Station	1	1	0	0	1	1	28-Jul-26	28-Jul-26	37	37	0	0	
3-STN-1409	Install Tech Pylon - Garfield NB Station	1	1	0	0	1	1	29-Jul-26	29-Jul-26	37	37	0	0	
SB Lynn Station														
3-STN-1411	Install Shelters (2 Each) - Lynn SB Station	10	10	0	0	10	10	27-Aug-26	10-Sep-26	17	17	0	0	
3-STN-1412	Install Amenities - Lynn SB Station	1	1	0	0	1	1	11-Sep-26	11-Sep-26	17	17	0	0	
3-STN-1413	Install Tech Pylon - Lynn SB Station	1	1	0	0	1	1	14-Sep-26	14-Sep-26	17	17	0	0	
NB Lynn Station														
3-STN-1415	Install Shelters (2 Each) - NB Lynn Station	10	10	0	0	10	10	15-Sep-26	28-Sep-26	17	17	0	0	
3-STN-1416	Install Amenities - NB Lynn Station	1	1	0	0	1	1	29-Sep-26	29-Sep-26	17	17	0	0	
3-STN-1417	Install Tech Pylon - NB Lynn Station	1	1	0	0	1	1	30-Sep-26	30-Sep-26	17	17	0	0	
Station Electrical														
SB Garfield Station Electrical														
3-SE-1420	Install Electrical - Garfield SB Station	5	5	0	0	5	5	01-Oct-26	07-Oct-26	17	17	0	0	
3-SE-1421	KCM Inspection - Garfield SB Station	5	5	0	0	5	5	08-Oct-26	15-Oct-26	17	17	0	0	
3-SE-1422	Commission Station Electrical - Garfield SB Station	1	1	0	0	1	1	16-Oct-26	16-Oct-26	17	17	0	0	
NB Garfield Station Electrical														
3-SE-1424	Install Electrical - Garfield NB Station	5	5	0	0	5	5	19-Oct-26	23-Oct-26	17	17	0	0	
3-SE-1425	KCM Inspection - Garfield NB Station	5	5	0	0	5	5	26-Oct-26	30-Oct-26	17	17	0	0	
3-SE-1426	Commission Station Electrical - Garfield NB Station	1	1	0	0	1	1	02-Nov-26	02-Nov-26	17	17	0	0	
SB Lynn Station Electrical														
3-SE-1428	Install Electrical - Lynn SB Station	5	5	0	0	5	5	13-Nov-26	19-Nov-26	0	0	0	0	
3-SE-1429	KCM Inspection - Lynn SB Station	5	5	0	0	5	5	20-Nov-26	30-Nov-26	0	0	0	0	
3-SE-1430	Commission Station Electrical - Lynn SB Station	1	1	0	0	1	1	01-Dec-26	01-Dec-26	0	0	0	0	
NB Lynn Station Electrical														
3-SE-1432	Install Electrical - Lynn NB Station	5	5	0	0	5	5	02-Dec-26	08-Dec-26	0	0	0	0	
3-SE-1433	KCM Inspection - Lynn NB Station	5	5	0	0	5	5	09-Dec-26	15-Dec-26	0	0	0	0	
3-SE-1434	Commission Station Electrical - Lynn NB Station	1	1	0	0	1	1	16-Dec-26	16-Dec-26	0	0	0	0	
Hardscapes After Electrical Demo														
Galer														
3-HS-1437	Remove Foundations - Galer	1	1	0	0	1	1	17-Dec-26	17-Dec-26	0	0	0	0	
3-HS-1438	Prep Sidewalks - Galer	1	1	0	0	1	1	18-Dec-26	18-Dec-26	0	0	0	0	
3-HS-1439	Pour Sidewalks - Galer	1	1	0	0	1	1	21-Dec-26	21-Dec-26	0	0	0	0	
Garfield														
3-HS-1441	Remove Foundations - Garfield	1	1	0	0	1	1	22-Dec-26	22-Dec-26	0	0	0	0	
3-HS-1442	Prep Sidewalks - Garfield	1	1	0	0	1	1	23-Dec-26	23-Dec-26	0	0	0	0	
3-HS-1443	Pour Sidewalks - Garfield	1	1	0	0	1	1	24-Dec-26	24-Dec-26	0	0	0	0	
Boston														
3-HS-1445	Remove Foundations - Boston	1	1	0	0	1	1	28-Dec-26	28-Dec-26	0	0	0	0	
3-HS-1446	Prep Sidewalks - Boston	1	1	0	0	1	1	29-Dec-26	29-Dec-26	0	0	0	0	
3-HS-1447	Pour Sidewalks - Boston	1	1	0	0	1	1	30-Dec-26	30-Dec-26	0	0	0	0	
Lynn														
3-HS-1449	Remove Foundations - Lynn	1	1	0	0	1	1	12-Jan-27	12-Jan-27	-7	-7	0	0	
3-HS-1450	Prep Sidewalks - Lynn	1	1	0	0	1	1	13-Jan-27	13-Jan-27	-7	-7	0	0	
3-HS-1451	Pour Sidewalks - Lynn	1	1	0	0	1	1	14-Jan-27	14-Jan-27	-7	-7	0	0	
PBL Buffers														
3-PBL-1453	Pour PBL Buffers - Zone 3	20	20	0	0	20	20	15-Jan-27	12-Feb-27	-7	-7	0	0	
Channalization														
3-PM-1455	Channelization - Zone 3	15	15	0	0	15	15	16-Feb-27	08-Mar-27	-7	-7	0	0	
OCS														
3-OCS-1477	OCS - Feeder Work & Disconnect Switch T-225-01	5	5	0	0	5	5	11-Dec-26	17-Dec-26	45	45	0	0	

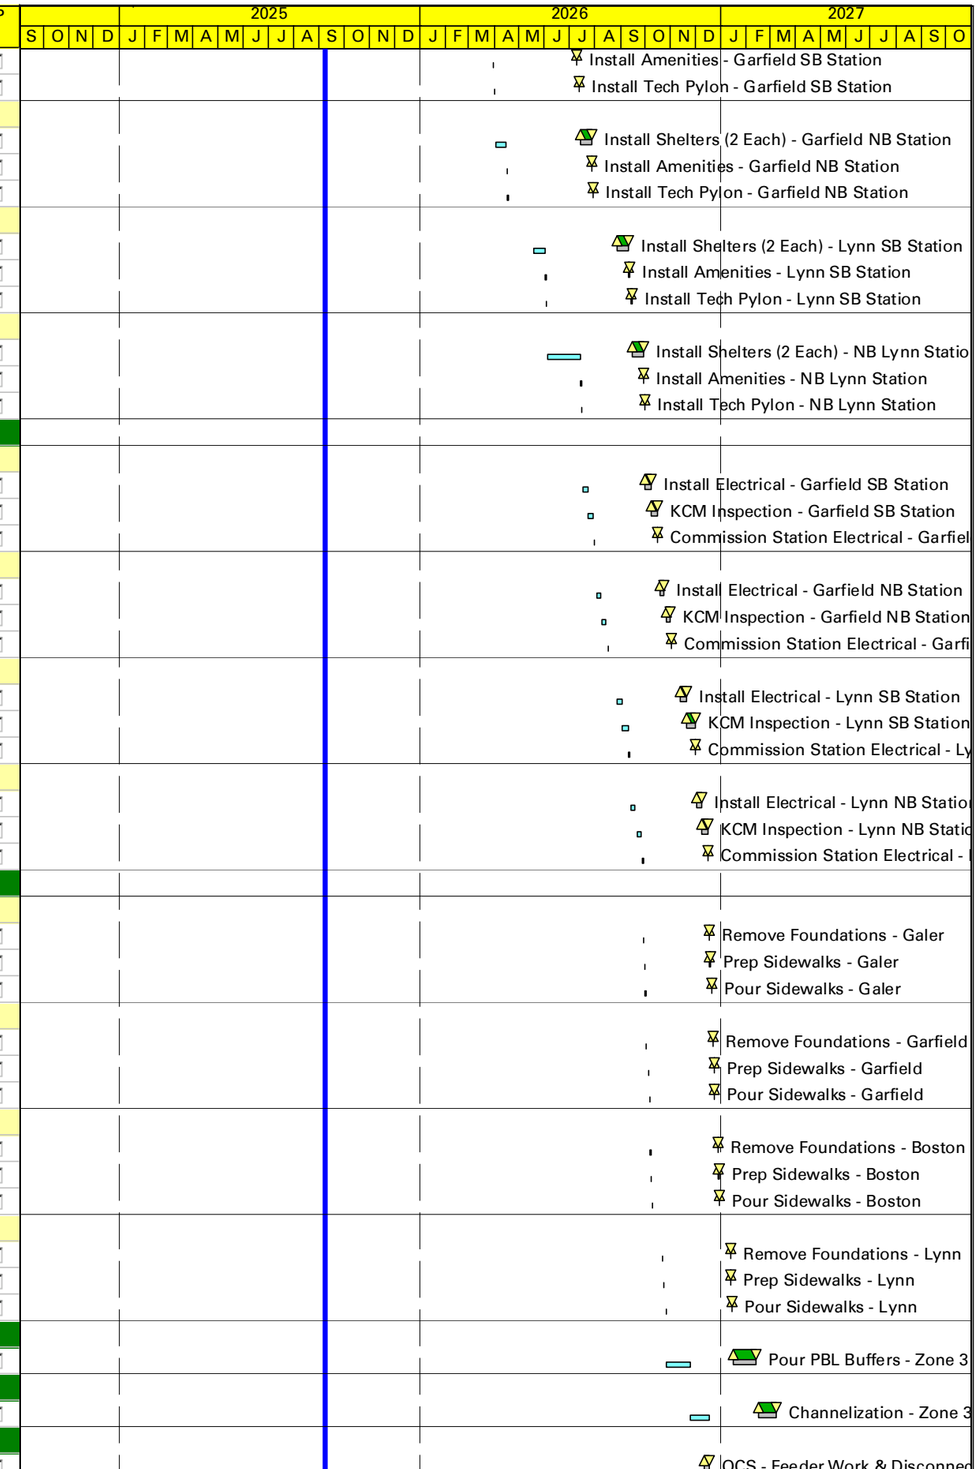

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
3-OCS-1457	OCS - Material Handover - Zone 3	1	1	0	0	1	1	18-Dec-26	18-Dec-26	45	45	0	0	☐
Zone 4 - Galer to 3rd														
Pole Foundation Potholing														
4-PH-1460A	Eastlake to Harrison - Pole Foundation Potholing (PARTIAL)	1	1	0	1	0	1	20-Nov-24 A	20-Nov-24 A			0	0	☑
DSC-034	DSC-034 / FM-0017 Additional Ductbank Verification	5	5	0	5	0	5	21-Nov-24 A	27-Nov-24 A			0	0	☑
4-PH-1460	Eastlake to Harrison - Pole Foundation Potholing	6	4	0	4	0	4	23-Dec-24 A	03-Jan-25 A			0	0	☑
FM0051-Z4	FM-0051 Potholing (Zone 4)	7	4	0	4	0	4	06-Jan-25 A	09-Jan-25 A			0	0	☐
DSC-070	DSC-070 SEC Ward Unstable Soils for Pole Foundation Pothole	1	1	0	1	0	1	07-Jan-25 A	07-Jan-25 A			0	0	☐
DSC-073	DSC-073 P2901 Pothole Contaminated Soil Material	1	1	0	1	0	1	08-Jan-25 A	08-Jan-25 A			0	0	☐
FM-078	PCO 156 / FM 078 Remove Water Valve Vault	1	1	0	1	0	1	31-Jan-25 A	31-Jan-25 A			0	0	☐
FM-071	FM-0071 Additional Potholing (Zone 4)	5	5	0	5	0	5	31-Jan-25 A	10-Feb-25 A			0	0	☐
Storm														
DSC-082	DSC-082 SWC Yale Unknown Unlocated Copper Line	3	3	0	3	0	3	16-Jan-25 A	21-Jan-25 A			0	0	☑
4-ST-1462	Eastlake to Yale - Storm (partial w/FM070)	2	15	0	15	0	15	16-Jan-25 A	10-Feb-25 A			0	0	☑
DSC-085	DSC-085 SWC Yale CB C14 Corrugated Pipe Conflict	1	1	0	1	0	1	21-Jan-25 A	21-Jan-25 A			0	0	☑
DSC-090	DSC-090 North of Yale CB C01 Conflict with Existing Pipe	1	1	0	1	0	1	27-Jan-25 A	27-Jan-25 A			0	0	☑
DSC-092	DSC-092 North of Aloha CB C03 Conflict With Ductbank	4	4	0	4	0	4	29-Jan-25 A	03-Feb-25 A			0	0	☑
DSC-095	DSC-095 NWC Yale & Fairview Unknown Ductbank	1	1	0	1	0	1	31-Jan-25 A	31-Jan-25 A			0	0	☑
DSC-101	DSC-101 NWC Yale Unknown Steel Line CB C02	2	2	0	2	0	2	07-Feb-25 A	10-Feb-25 A			0	0	☑
DSC-105	DSC-105 Yale Fairview WQV 101 core tap conflicts	1	1	0	1	0	1	13-Feb-25 A	13-Feb-25 A			0	0	☑
4-ST-1463	Yale to Aloha - Storm (partial w/FM070)	22	11	0	11	0	11	14-Feb-25 A	03-Mar-25 A			0	0	☑
DSC-110	DSC-110 Yale to Aloha WQV C101 Ductbank Conflict	3	3	0	3	0	3	18-Feb-25 A	20-Feb-25 A			0	0	☑
DSC-114	DSC-114 Ward & Fairview CB-C4 Ductbank Conflict	2	2	0	2	0	2	24-Feb-25 A	25-Feb-25 A			0	0	☑
DSC-117	DSC-117 Yale to Aloha CB C5 Conflict Comm Line	1	1	0	1	0	1	26-Feb-25 A	26-Feb-25 A			0	0	☑
DSC-119	DSC-119 Fairview & Ward CB C5 Conduit Conflict	1	1	0	1	0	1	28-Feb-25 A	28-Feb-25 A			0	0	☑
FM0059.2	Eastlake to Yale - Storm After Re-Design (FM-0059)	4	4	0	4	0	4	04-Mar-25 A	07-Mar-25 A			0	0	☑
DSC-076	DSC-076 Eastlake to Yale CB C001 Conflict w/Comm	5	17	0	17	0	17	13-Jan-25 A	07-Feb-25 A			0	0	☑
FM0059.1	FM-0059 Stop Work - SDOT Redesign Storm (partial w/FM070)	15	31	0	31	0	31	14-Jan-25 A	03-Mar-25 A			0	0	☑
FM0059.4	STOP WORK - SDOT RE-DESIGN (FM-0059 & FM-0124)	3	22	0	22	0	22	03-Mar-25 A	01-Apr-25 A			0	0	☑
FM0059.22	SCL Hot Watch Notification (Change Order 006)	10	9	0	9	0	9	04-Mar-25 A	14-Mar-25 A			0	0	☑
4-ST-1466	Metro Notification	1	10	0	10	0	10	11-Mar-25 A	24-Mar-25 A			0	0	☑
DSC-131	DSC-131 Valley and Fairview Ductbank Conflict w/Storm	1	1	0	1	0	1	13-Mar-25 A	13-Mar-25 A			0	0	☑
DSC-135	DSC-135 Valley and Fairview Unknown Comm Conflict w/Storm	1	1	0	1	0	1	14-Mar-25 A	14-Mar-25 A			0	0	☑
DSC-137	DSC-137 Valley and Fairview 3' Thick Roadway	1	1	0	1	0	1	14-Mar-25 A	14-Mar-25 A			0	0	☑
FM0059.12	Aloha to Valley (not affected by Stop Work Order) - Storm	5	6	0	6	0	6	14-Mar-25 A	21-Mar-25 A			0	0	☑
DSC-140	DSC-140 Valley and Fairview ECO block Conflict with CB C11	1	1	0	1	0	1	17-Mar-25 A	17-Mar-25 A			0	0	☑
DSC-141	DSC-141 Valley and Fairview Conduit Conflicts with CB C11	2	2	0	2	0	2	17-Mar-25 A	18-Mar-25 A			0	0	☑
DSC-143	DSC-143 Valley and Fairview Unmarked Conduits CB 11	1	1	0	1	0	1	18-Mar-25 A	18-Mar-25 A			0	0	☑
DSC-144	DSC-144 Valley and Fairview Concrete Mixed Backfill CB 11	2	2	0	2	0	2	18-Mar-25 A	19-Mar-25 A			0	0	☑
DSC-148	DSC-148 Valley and Fairview Inlet C-30 Conflict	1	1	0	1	0	1	20-Mar-25 A	20-Mar-25 A			0	0	☑
4-ST-1465	Westlake and Virginia - Storm	6	6	0	6	0	6	25-Mar-25 A	01-Apr-25 A			0	0	☑
4-ST-1463.1	Yale to Aloha - Storm (AFTER RE-DESIGN) 3 WD per added CB C21	20	18	0	18	0	18	02-Apr-25 A	25-Apr-25 A			0	0	☑
4-ST-1464	Aloha to Valley - Storm (AFTER RE-DESIGN / FM-0059 & FM-0124)	10	10	0	10	0	10	28-Apr-25 A	09-May-25 A			0	0	☐
DSC-191	DSC-191 Aloha to Valley CB C9 conduit conflict	1	1	0	1	0	1	29-Apr-25 A	29-Apr-25 A			0	0	☐
DSC-200	DSC-200 Aloha to Valley CB C10 Duct Bank Conflict	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	☐
DSC-203	DSC-203 Fairview, Aloha-Valley CB-C10 Unlocated DB	1	1	0	1	0	1	05-May-25 A	05-May-25 A			0	0	☐
DSC-207	DSC-207 Fairview CB C13 unknown unlocated conduit conflicts	1	1	0	1	0	1	09-May-25 A	09-May-25 A			0	0	☐
NCR-009	NCR-009 SCL Conduits damaged	1	0	-1	1	0	1	18-Mar-25 A	18-Mar-25 A					☑
DSC-158	DSC-158 Westlake unknown Storm Line	1	1	0	1	0	1	28-Mar-25 A	28-Mar-25 A			0	0	☑
DSC-160	DSC-160 Westlake unknown Conduit	1	1	0	1	0	1	28-Mar-25 A	28-Mar-25 A			0	0	☑
DSC-164	DSC-164 PCO0240.01 Yale to Aloha CB C6 Conflict w/Ductbank	1	1	0	1	0	1	02-Apr-25 A	02-Apr-25 A			0	0	☑
DSC-165	DSC-165 Yale to Aloha WQV C102 Sewer Cleanout conflict	1	1	0	1	0	1	04-Apr-25 A	04-Apr-25 A			0	0	☑
DSC-166	DSC-166 Yale to Aloha WQC C102 unknown Ductbank	1	1	0	1	0	1	04-Apr-25 A	04-Apr-25 A			0	0	☑
DSC-169	DSC-169 Ward Inlet C3 unknown conduit conflict	1	1	0	1	0	1	07-Apr-25 A	07-Apr-25 A			0	0	☑

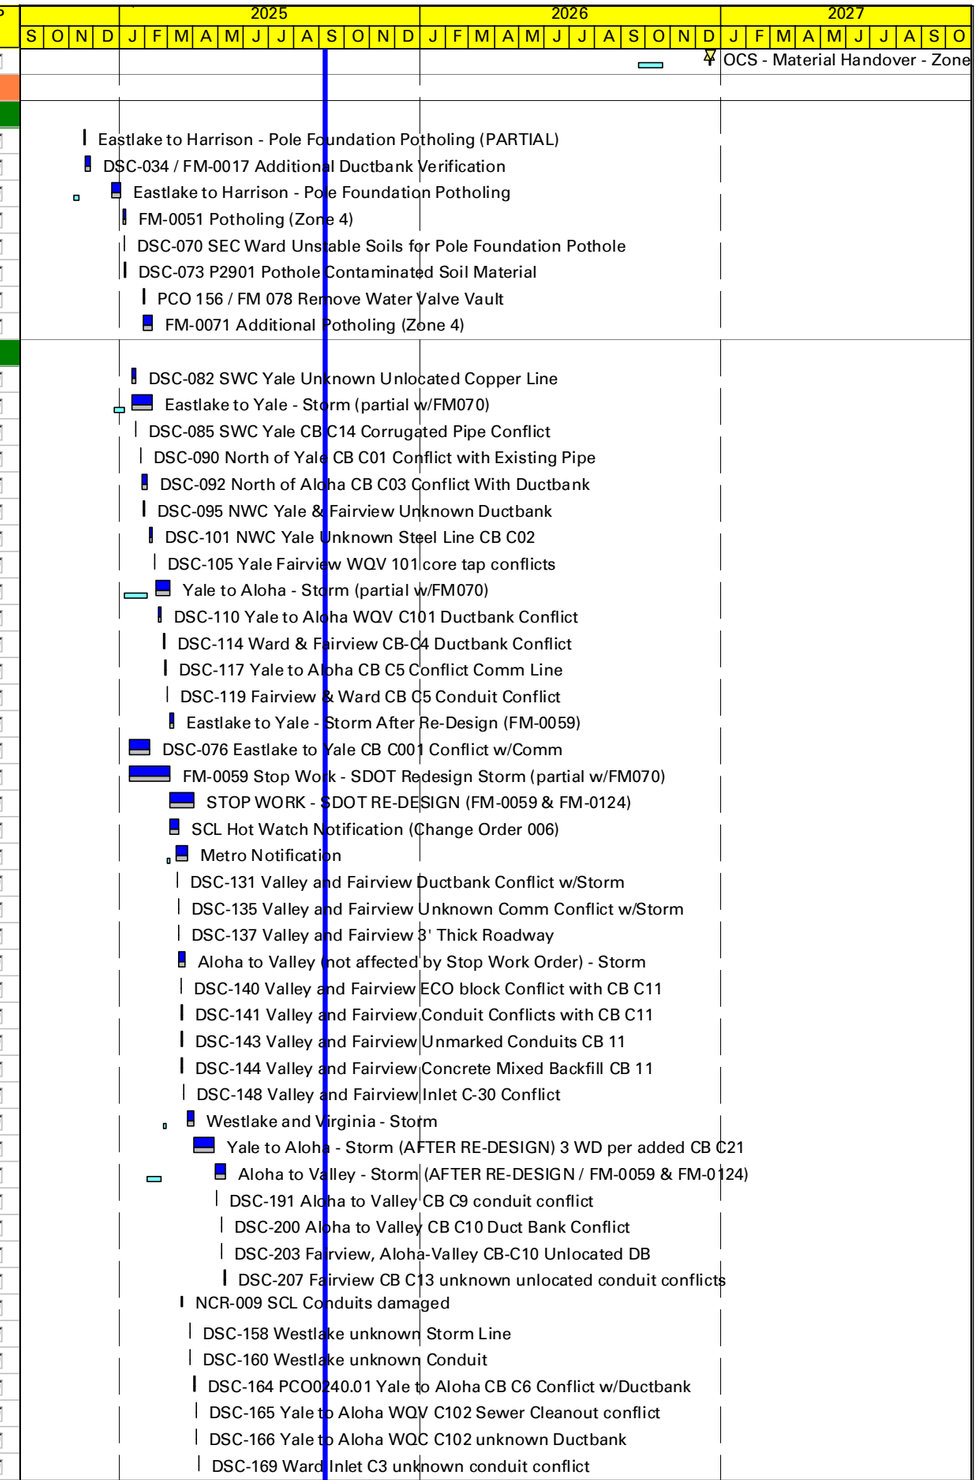

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort; BL1 LOE; BL2 LOE; Actual Level of Effort; Actual Work; Remaining Work; Critical Remaining Work; Milestone; Previous MS; Previous Bar; Baseline MS; Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-170	DSC-170 Ward Inlet C3 Unknown Conduit Conflict #2	1	1	0	1	0	1	08-Apr-25 A	08-Apr-25 A			0	0	☑
DSC-178	DSC-178 Ward CB B3 core tap conflict with Ductbank	1	1	0	1	0	1	17-Apr-25 A	17-Apr-25 A			0	0	☑
DSC-175	DSC-175 NWC Ward CB C-4 Conflict with Ductbank	20	19	0	19	0	19	15-Apr-25 A	09-May-25 A			0	0	☑
DSC-175A	Complete CB C4 after DSC-175	2	2	0	2	0	2	12-May-25 A	13-May-25 A			0	0	☐
4-ST-1474	Install Curb Drain Structure (DC-053)	3	3	0	3	0	3	14-May-25 A	16-May-25 A			0	0	☐
FM-152	FM 152 Stop Work Fairview	17	99	0	83	16	99	09-May-25 A	30-Sep-25	-24	-24	0	0	☐
FM-152A	Fairview Comm Ductbank Resolution / Mobilize	12	99	0	83	16	99	09-May-25 A	30-Sep-25	-24	-24	0	0	☐
4-DB-1000	FM 152 ADDED DUCTBANK SCOPE (Definition & Duration TBD)	0	0	0	0	0	0	01-Oct-25	01-Oct-25	-24	-24	0	0	☐
4-ST-1484	Aloha to Valley - Storm (AFTER FM 152)	5	5	0	0	5	5	01-Oct-25	07-Oct-25	-24	-24	0	0	☐
Conduit Crossings														
4-CC-1468	Yale - Conduit Crossings (SDOT direction to re-sequence includes	5	5	0	5	0	5	14-May-25 A	20-May-25 A			0	0	☐
4-CC-1469	Ward & Aloha - Conduit Crossings	12	32	0	32	0	32	15-May-25 A	01-Jul-25 A			0	0	☐
DSC-213	DSC-213 Aloha unknown clay pipe conflict with conduits	13	13	0	13	0	13	20-May-25 A	06-Jun-25 A			0	0	☐
DSC-214	DSC-214 Ward Undercrossing Conduit Conflicts	11	21	0	21	0	21	22-May-25 A	23-Jun-25 A			0	0	☐
DSC-215	DSC-215 Aloha Undercrossing Conduit Conflicts	10	20	0	20	0	20	23-May-25 A	23-Jun-25 A			0	0	☐
DSC-217	DSC-217 Aloha Undercrossing NB DI Pipe Conflict	9	19	0	19	0	19	27-May-25 A	23-Jun-25 A			0	0	☐
4-CC-1471	Harrison - Conduit Crossings	5	10	0	10	0	10	09-Jun-25 A	23-Jun-25 A			0	0	☐
DSC-230	DSC-230 Fairview & Harrison, unlocated water service	1	1	0	1	0	1	10-Jun-25 A	10-Jun-25 A			0	0	☐
DSC-231	DSC-231 Fairview & Harrison, Cast Iron Pipe Conflict	1	1	0	1	0	1	10-Jun-25 A	10-Jun-25 A			0	0	☐
DSC-232	DSC-232 Fairview & Harrison, 20-in Thick Concrete Paving	1	1	0	1	0	1	10-Jun-25 A	10-Jun-25 A			0	0	☐
NCR-016	NCR-016 6" gas main was struck and damaged	1	0	-1	1	0	1	10-Jun-25 A	10-Jun-25 A					☐
DSC-233	DSC-233 Fairview & Harrison, Unlocated Ductbank	1	1	0	1	0	1	11-Jun-25 A	11-Jun-25 A			0	0	☐
DSC-236	DSC-236 Fairview Undercrossing Unknown duct bank	1	1	0	1	0	1	24-Jun-25 A	24-Jun-25 A			0	0	☐
4-CC-1470	Valley - Conduit Crossings	0	0	0	0	0	0	02-Jul-25 A	02-Jul-25 A			0	0	☐
DSC-252	DSC-252 Fairview and Harrison Undercrossing Thick Concrete	1	1	0	1	0	1	07-Jul-25 A	07-Jul-25 A			0	0	☐
4-CC-1481	Harrison Undercrossing	17	17	0	17	0	17	07-Jul-25 A	29-Jul-25 A			0	0	☐
DSC-253	DSC-253 Fairview and Harrison Undercrossing Waterline Conflict	1	1	0	1	0	1	08-Jul-25 A	08-Jul-25 A			0	0	☐
DSC-254	DSC-254 Unknown Concrete Harrison Undercrossing	1	1	0	1	0	1	09-Jul-25 A	09-Jul-25 A			0	0	☐
DSC-255	DSC-255 Fairview and Harrison Abandoned Gas Line in Conflict	1	1	0	1	0	1	09-Jul-25 A	09-Jul-25 A			0	0	☐
DSC-260	DSC-260 Harrison undercrossing unknown 6" clay	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	☐
DSC-262	DSC-262 Harrison 5R Conduit Conflict	1	1	0	1	0	1	10-Jul-25 A	10-Jul-25 A			0	0	☐
DSC-267	DSC-267 Fairview & Harrison, Re-dig Trench for SCL Core	1	1	0	1	0	1	17-Jul-25 A	17-Jul-25 A			0	0	☐
4-CC-1478	Yale - Complete Conduit Crossings After Ductbank Relocation	3	3	0	0	3	3	08-Oct-25	10-Oct-25	-24	-24	0	0	☐
4-CC-1479	Aloha - Complete Conduit Crossings After Ductbank Relocation	3	3	0	0	3	3	14-Oct-25	16-Oct-25	-24	-24	0	0	☐
Roadway														
Eastlake to Valley West Side														
4-RW-1474	Demo, Common Ex, Type 2 - Eastlake to Valley (W)	16	16	0	0	16	16	17-Oct-25	07-Nov-25	-24	-24	0	0	☐
4-RW-1475	Pour Roadway - Eastlake to Valley (W)	6	6	0	0	6	6	10-Nov-25	18-Nov-25	-24	-24	0	0	☐
4-RW-1476	Curb - Eastlake to Valley (W)	3	3	0	0	3	3	19-Nov-25	21-Nov-25	-24	-24	0	0	☐
Weekend Paving														
Yale Phase 1														
4-WE-1499	COMPLETE CONDUIT YALE EAST SIDE	5	5	1	4	0	4	14-Aug-25 A	19-Aug-25 A		18	3	4	☐
DSC-310	DSC-310 Yale East Side Unknown CB and Ductbank	1	0	-1	1	0	1	18-Aug-25 A	18-Aug-25 A					☐
4-WE-1479	Remove Roadway Type 2 - Yale Ph.1 (WE)	1	1	0	1	0	1	23-Aug-25 A	23-Aug-25 A		6	2	2	☐
4-WE-1480	Pour Roadway - Yale Ph.1 (WE)	1	1	0	1	0	1	24-Aug-25 A	24-Aug-25 A		6	2	2	☐
Yale Phase 2														
4-WE-1482	Remove Roadway Type 2 - Yale Ph.2 (WE)	1	1	0	0	1	1	22-Nov-25	22-Nov-25	-10	-10	0	0	☐
4-WE-1483	Pour Roadway - Yale Ph.2 (WE)	1	1	0	0	1	1	23-Nov-25	23-Nov-25	-10	-10	0	0	☐
Yale Phase 3														
4-WE-1485	Remove Roadway Type 2 - Yale Ph.3 (WE)	1	1	0	0	1	1	29-Nov-25	29-Nov-25	-10	-10	0	0	☐
4-WE-1486	Pour Roadway - Yale Ph.3 (WE)	1	1	0	0	1	1	30-Nov-25	30-Nov-25	-10	-10	0	0	☐
Aloha Phase 1														
DSC-312	DSC-312 NEC Aloha unknown unmarked conduits	1	0	-1	1	0	1	20-Aug-25 A	20-Aug-25 A					☐
DSC-313	DSC-313 Aloha unknown unlocated Fiber line	1	0	-1	1	0	1	20-Aug-25 A	20-Aug-25 A					☐

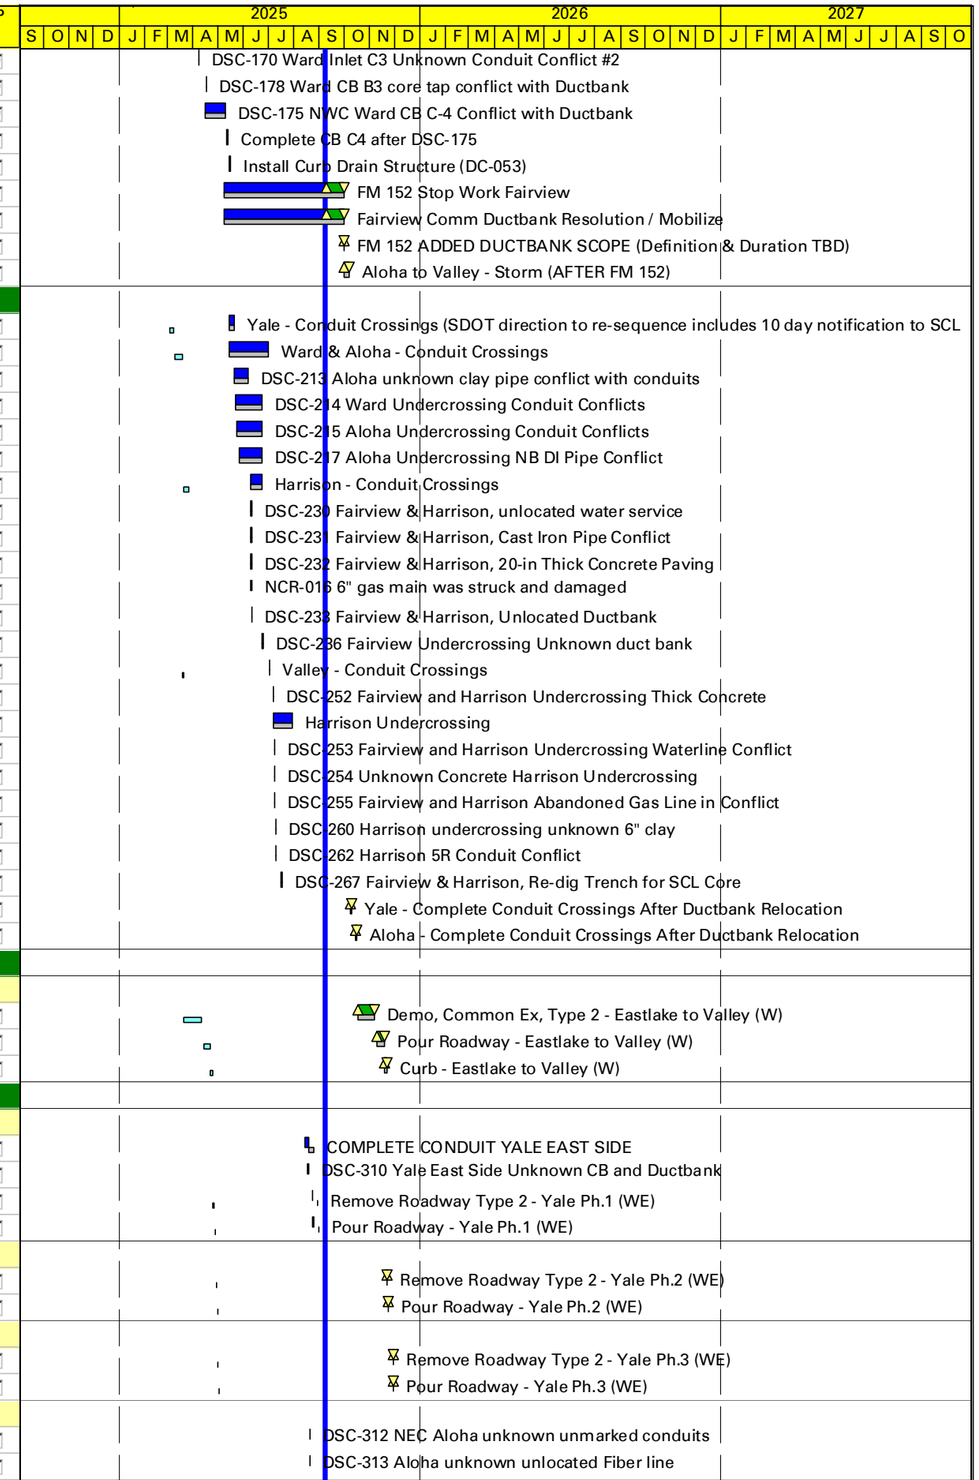

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-314	DSC-314 Aloha Unknown unlocated conduit	1	0	-1	1	0	1	20-Aug-25 A	20-Aug-25 A					
4-WE-1508	COMPLETE CONDUIT ALOHA EAST SIDE	5	5	0	5	0	5	20-Aug-25 A	26-Aug-25 A		18	4	4	
DSC-315	DSC-315 Aloha East Contaminated Soils	1	0	-1	1	0	1	21-Aug-25 A	21-Aug-25 A					
4-WE-1518	BOAT SHOW - CANNOT CLOSE ALOHA	2	0	-2	2	0	2	30-Aug-25 A	31-Aug-25 A					
DSC-334	DSC-334 SEC Fairview & Aloha Plugged Inlet	5	0	-5	2	3	5	05-Sep-25 A	11-Sep-25	25				
DSC-335	DSC-335 SEC Fairview & Aloha Comm Conduit Conflict	5	0	-5	2	3	5	05-Sep-25 A	11-Sep-25	25				
DSC-336	DSC-336 Fairview & Aloha Ex. Pole Foundation in Grade	5	0	-5	2	3	5	05-Sep-25 A	11-Sep-25	-1				
4-WE-1488	Remove Roadway Type 2 - Aloha Ph.1 (WE)	1	1	0	1	0	1	06-Sep-25 A	06-Sep-25 A		6	0	0	
4-WE-1489	Pour Roadway - Aloha Ph.1 (WE)	1	1	0	1	0	1	07-Sep-25 A	07-Sep-25 A		6	0	0	
4-WE-1519	Pour Roadway - Aloha / After DCS's 334, 335, 336	2	0	-2	0	2	2	12-Sep-25	15-Sep-25	25				
Aloha Phase 2														
4-WE-1491	Remove Roadway Type 2 - Aloha Ph.2 (WE)	1	1	0	0	1	1	06-Dec-25	06-Dec-25	-10	-10	0	0	
4-WE-1492	Pour Roadway - Aloha Ph.2 (WE)	1	1	0	0	1	1	07-Dec-25	07-Dec-25	-10	-10	0	0	
Valley to Roy Phase 1														
4-WE-1494	Remove Roadway Type 2 - Valley to Roy Ph.1 (WE)	1	1	0	0	1	1	13-Sep-25	13-Sep-25	14	6	0	0	
4-WE-1495	Pour Roadway - Valley to Roy Ph.1 (WE)	1	1	0	0	1	1	14-Sep-25	14-Sep-25	14	6	0	0	
Valley to Roy Phase 2														
4-WE-1497	Remove Roadway Type 2 - Valley to Roy Ph.2 (WE)	1	1	0	0	1	1	13-Dec-25	13-Dec-25	-10	-10	0	0	
4-WE-1498	Pour Roadway - Valley to Roy Ph.2 (WE)	1	1	0	0	1	1	14-Dec-25	14-Dec-25	-10	-10	0	0	
Harrison Phase 1														
4-WE-1500	Remove Roadway Type 2 - Harrison Ph.1 (WE)	1	1	0	0	1	1	20-Dec-25	20-Dec-25	-10	-10	0	0	
4-WE-1501	Pour Roadway - Harrison Ph.1 (WE)	1	1	0	0	1	1	21-Dec-25	21-Dec-25	-10	-10	0	0	
Harrison Phase 2														
4-WE-1503	Remove Roadway Type 2 - Harrison Ph.2 (WE)	1	1	0	0	1	1	27-Dec-25	27-Dec-25	-10	-10	0	0	
4-WE-1504	Pour Roadway - Harrison Ph.2 (WE)	1	1	0	0	1	1	28-Dec-25	28-Dec-25	-10	-10	0	0	
Virginia and Boren														
4-WE-1506	Remove Roadway Type 2 - Virginia & Boren (WE)	1	1	0	0	1	1	03-Jan-26	03-Jan-26	60	60	0	0	
4-WE-1507	Pour Roadway - Virginia & Boren (WE)	1	1	0	0	1	1	04-Jan-26	04-Jan-26	60	60	0	0	
Virginia Terry to 9th														
4-WE-1509	Remove Roadway Type 2 - Virginia / Terry to 9th (WE)	1	1	0	0	1	1	10-Jan-26	10-Jan-26	60	60	0	0	
4-WE-1510	Pour Roadway - Virginia / Terry to 9th (WE)	1	1	0	0	1	1	11-Jan-26	11-Jan-26	60	60	0	0	
Virginia Westlake to 6th														
4-WE-1512	Remove Roadway Type 2 - Virginia / Westlake to 6th (WE)	1	1	0	0	1	1	17-Jan-26	17-Jan-26	60	60	0	0	
4-WE-1513	Pour Roadway - Virginia / Westlake to 6th (WE)	1	1	0	0	1	1	18-Jan-26	18-Jan-26	60	60	0	0	
Pole Foundations														
DSC-339	DSC-339 Aloha P2904 Ground Water at 13'	1	0	-1	1	0	1	08-Sep-25 A	08-Sep-25 A					
4-PF-1526	YALE TO ALOHA - EAST SIDE - POLE FOUNDATIONS (3 ea.)	4	4	-1	1	4	5	08-Sep-25 A	12-Sep-25	-5	15	0	-1	
4-PF-1536	ALOHA - EAST SIDE Pole Foundations (2 ea,)	3	3	-2	1	4	5	08-Sep-25 A	12-Sep-25	-5	15	4	2	
4-PF-1529	VALLEY - EAST SIDE Pole Foundations (2 ea.)	2	2	0	0	2	2	15-Sep-25	16-Sep-25	57	15	2	2	
4-PF-1515	Yale - Pole Foundations (4 ea.)	6	6	0	0	6	6	01-Dec-25	08-Dec-25	5	5	0	0	
4-PF-1516	Yale to Aloha - WEST SIDE Pole Foundations (3 ea.)	4	4	0	0	4	4	09-Dec-25	12-Dec-25	5	5	0	0	
4-PF-1517	Aloha - WEST SIDE Pole Foundations (6 ea,)	9	9	0	0	9	9	15-Dec-25	26-Dec-25	5	5	0	0	
4-PF-1518	Aloha to Valley - Pole Foundations (3 ea.)	5	5	0	0	5	5	29-Dec-25	05-Jan-26	5	5	0	0	
4-PF-1519	Valley - WEST SIDE Pole Foundations (1 ea.)	2	2	0	0	2	2	06-Jan-26	07-Jan-26	5	5	0	0	
Sidewalks														
Yale NEC														
4-SW-1567	Remove Sidewalk - Yale NEC	1	1	0	0	1	1	15-Sep-25	15-Sep-25	22	15	4	4	
4-SW-1568	Trench Electrical - Yale NEC	2	2	0	0	2	2	16-Sep-25	17-Sep-25	22	15	4	4	
4-SW-1569	Electrical - Yale NEC	4	4	0	0	4	4	18-Sep-25	23-Sep-25	22	15	4	4	
4-SW-1570	Grade Sidewalks - Yale NEC	1	1	0	0	1	1	24-Sep-25	24-Sep-25	22	15	4	4	
4-SW-1571	Pour Sidewalks/Curb Ramps - Yale NEC	3	3	0	0	3	3	25-Sep-25	29-Sep-25	22	15	4	4	
Yale SEC														
4-SW-1573	Remove Sidewalk - Yale SEC	1	1	0	1	0	1	26-Aug-25 A	26-Aug-25 A		17	20	20	
4-SW-1574	Trench Electrical - Yale SEC	1	1	0	1	0	1	27-Aug-25 A	27-Aug-25 A		17	20	20	

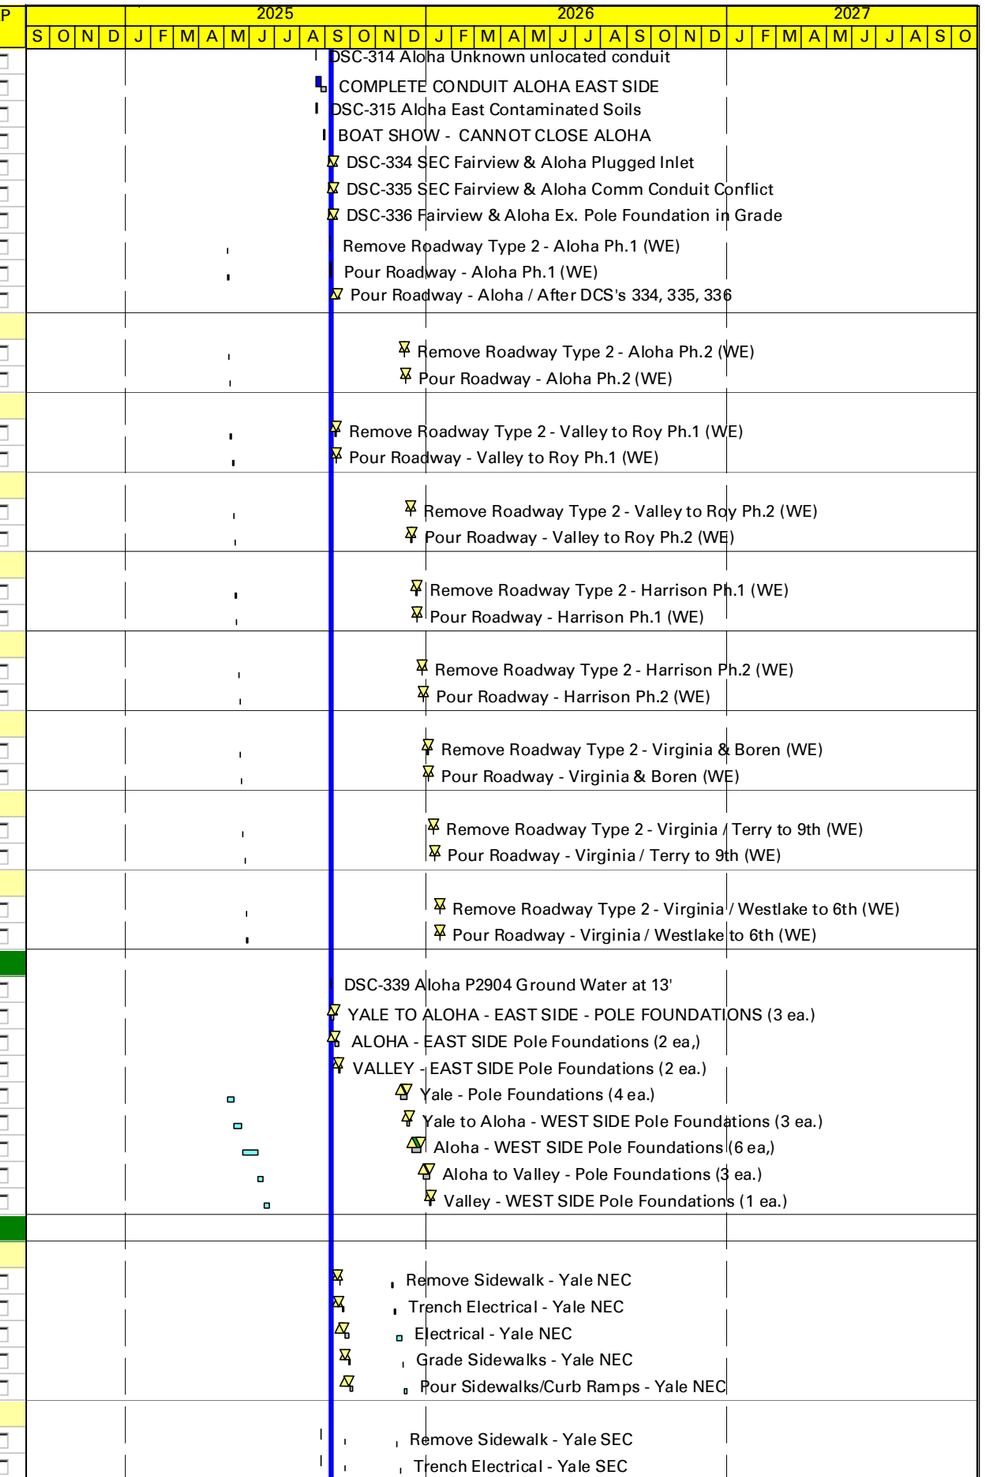

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work | BL1 LOE | Milestone | BL2 LOE | Previous MS | Actual Level of Effort | Previous Bar | Actual Work | Baseline MS | Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
DSC-323	DSC-323 SWC Yale & Fairview 8in Sidewalk	1	0	-1	1	0	1	28-Aug-25 A	28-Aug-25 A					
4-SW-1575	Electrical - Yale SEC	3	3	-1	4	0	4	28-Aug-25 A	03-Sep-25 A		17	20	19	
DSC-325	DSC-325 SEC Yale & Fairview Unlocated Utility	1	0	-1	1	0	1	29-Aug-25 A	29-Aug-25 A					
4-SW-1576	Grade Sidewalks - Yale SEC	1	1	0	1	0	1	04-Sep-25 A	04-Sep-25 A		17	19	19	
4-SW-1577	Pour Sidewalks/Curb Ramps - Yale SEC	2	2	0	0	2	2	25-Sep-25	26-Sep-25	22	15	7	7	
Aloha NEC														
4-SW-1579	Remove Sidewalk - Aloha NEC	2	2	0	0	2	2	24-Nov-25	25-Nov-25	-22	-22	0	0	
4-SW-1580	Trench Electrical - Aloha NEC	3	3	0	0	3	3	26-Nov-25	02-Dec-25	-22	-22	0	0	
4-SW-1581	Excavate Shelter Foundations - Aloha NEC	1	1	0	0	1	1	03-Dec-25	03-Dec-25	-22	-22	0	0	
4-SW-1582	Form Pour Shelter Foundations - Aloha NEC	3	3	0	0	3	3	04-Dec-25	08-Dec-25	-22	-22	0	0	
4-SW-1583	Electrical - Aloha NEC	5	5	0	0	5	5	09-Dec-25	15-Dec-25	-22	-22	0	0	
4-SW-1584	Grade Sidewalks - Aloha NEC	2	2	0	0	2	2	16-Dec-25	17-Dec-25	-22	-22	0	0	
4-SW-1585	Pour Sidewalks/Curb Ramps - Aloha NEC	5	5	0	0	5	5	18-Dec-25	24-Dec-25	-22	-22	0	0	
Aloha SEC														
4-SW-1587	Remove Sidewalk - Aloha SEC	1	1	0	0	1	1	26-Dec-25	26-Dec-25	-22	-22	0	0	
4-SW-1588	Trench Electrical - Aloha SEC	2	2	0	0	2	2	29-Dec-25	30-Dec-25	-22	-22	0	0	
4-SW-1589	Electrical - Aloha SEC	4	4	0	0	4	4	31-Dec-25	06-Jan-26	-21	-21	0	0	
4-SW-1590	Grade Sidewalks - Aloha SEC	1	1	0	0	1	1	08-Jan-26	08-Jan-26	-22	-22	0	0	
4-SW-1591	Pour Sidewalks/Curb Ramps - Aloha SEC	3	3	0	0	3	3	09-Jan-26	13-Jan-26	-22	-22	0	0	
Harrison NEC														
4-SW-1613	Remove Sidewalk Harrison NEC	2	2	0	0	2	2	31-Dec-25	02-Jan-26	-22	-22	0	0	
4-SW-1614	Trench Electrical Harrison NEC	2	2	0	0	2	2	05-Jan-26	06-Jan-26	-22	-22	0	0	
4-SW-1615	Excavate Shelter Foundations Harrison NEC	1	1	0	0	1	1	07-Jan-26	07-Jan-26	-22	-22	0	0	
4-SW-1616	Form Pour Shelter Foundations Harrison NEC	4	4	0	0	4	4	08-Jan-26	13-Jan-26	103	103	0	0	
4-SW-1617	Electrical Harrison NEC	6	6	0	0	6	6	14-Jan-26	22-Jan-26	103	103	0	0	
4-SW-1618	Grade Sidewalks Harrison NEC	1	1	0	0	1	1	23-Jan-26	23-Jan-26	103	103	0	0	
4-SW-1619	Pour Sidewalks/Curb Ramps - Harrison NEC	4	4	0	0	4	4	26-Jan-26	29-Jan-26	103	103	0	0	
Valley NEC														
4-SW-1593	Remove Sidewalk - Valley NEC	1	1	0	0	1	1	14-Jan-26	14-Jan-26	-22	-22	0	0	
4-SW-1594	Trench Electrical - Valley NEC	2	2	0	0	2	2	15-Jan-26	16-Jan-26	-22	-22	0	0	
4-SW-1595	Electrical - Valley NEC	4	4	0	0	4	4	20-Jan-26	23-Jan-26	-22	-22	0	0	
4-SW-1596	Grade Sidewalks - Valley NEC	1	1	0	0	1	1	26-Jan-26	26-Jan-26	-22	-22	0	0	
4-SW-1597	Pour Sidewalks/Curb Ramps - Valley NEC	3	3	0	0	3	3	27-Jan-26	29-Jan-26	-22	-22	0	0	
Valley SEC to Mercer														
4-SW-1599	Remove Sidewalk Valley SEC to Mercer	1	1	0	0	1	1	30-Jan-26	30-Jan-26	-22	-22	0	0	
4-SW-1600	Trench Electrical Valley SEC to Mercer	2	2	0	0	2	2	02-Feb-26	03-Feb-26	-22	-22	0	0	
4-SW-1601	Electrical Valley SEC to Mercer	4	4	0	0	4	4	04-Feb-26	09-Feb-26	-22	-22	0	0	
4-SW-1602	Grade Sidewalks Valley SEC to Mercer	1	1	0	0	1	1	10-Feb-26	10-Feb-26	-22	-22	0	0	
4-SW-1603	Pour Sidewalks/Curb Ramps - Valley SEC to Mercer	4	4	0	0	4	4	11-Feb-26	17-Feb-26	-22	-22	0	0	
Yale NWC														
4-SW-1522	Remove Sidewalk - Yale NWC	1	1	0	0	1	1	18-Feb-26	18-Feb-26	-22	-22	0	0	
4-SW-1523	Trench Electrical - Yale NWC	2	2	0	0	2	2	19-Feb-26	20-Feb-26	-22	-22	0	0	
4-SW-1524	Electrical - Yale NWC	11	11	0	0	11	11	23-Feb-26	09-Mar-26	29	29	0	0	
4-SW-1525	Grade Sidewalks - Yale NWC	1	1	0	0	1	1	10-Mar-26	10-Mar-26	29	29	0	0	
4-SW-1526	Pour Sidewalks/Curb Ramps - Yale NWC	3	3	0	0	3	3	11-Mar-26	13-Mar-26	29	29	0	0	
Yale SWC														
4-SW-1528	Remove Sidewalk - Yale SWC	3	3	0	0	3	3	23-Feb-26	25-Feb-26	-22	-22	0	0	
4-SW-1529	Trench Electrical - Yale SWC	3	3	0	0	3	3	26-Feb-26	02-Mar-26	-22	-22	0	0	
4-SW-1530	Electrical - Yale SWC	8	8	0	0	8	8	03-Mar-26	12-Mar-26	27	27	0	0	
4-SW-1531	Grade Sidewalks - Yale SWC	3	3	0	0	3	3	13-Mar-26	17-Mar-26	27	27	0	0	
4-SW-1532	Pour Sidewalks/Curb Ramps - Yale SWC	6	6	0	0	6	6	18-Mar-26	25-Mar-26	27	27	0	0	
Ward West Side														
4-SW-1534	Remove Sidewalk - Ward (W)	3	3	0	0	3	3	03-Mar-26	05-Mar-26	-22	-22	0	0	
4-SW-1535	Trench Electrical - Ward (W)	3	3	0	0	3	3	06-Mar-26	10-Mar-26	-22	-22	0	0	

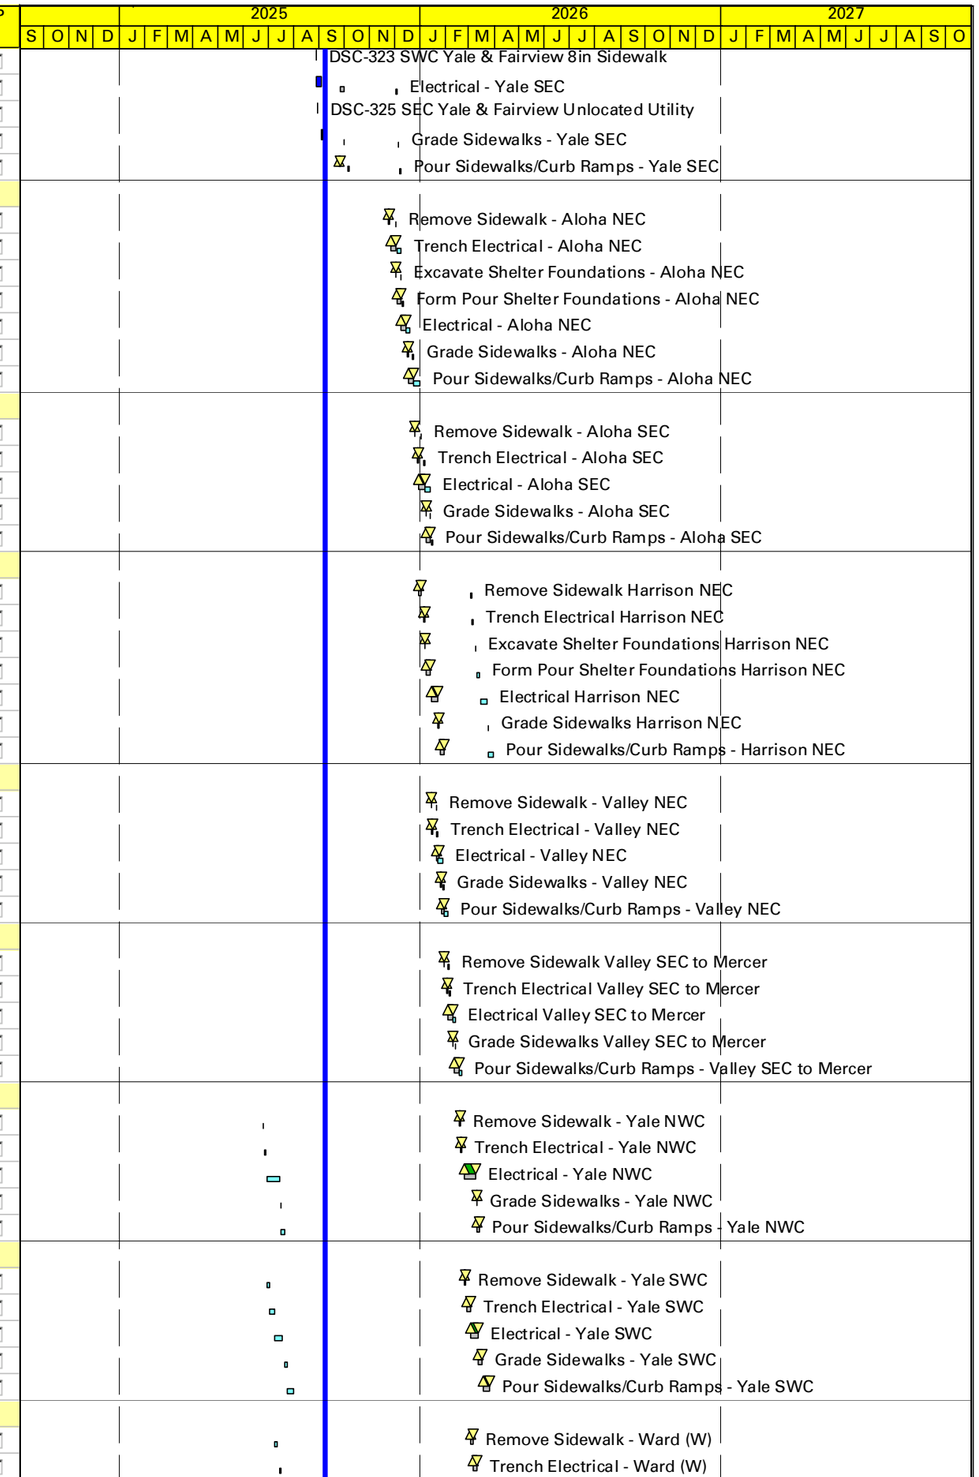

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
4-SW-1536	Electrical - Ward (W)	5	5	0	0	5	5	11-Mar-26	17-Mar-26	-22	-22	0	0	☐
4-SW-1537	Grade Sidewalks - Ward (W)	1	1	0	0	1	1	18-Mar-26	18-Mar-26	-22	-22	0	0	☐
4-SW-1538	Pour Sidewalks/Curb Ramps - Ward (W)	4	4	0	0	4	4	19-Mar-26	24-Mar-26	28	28	0	0	☐
Aloha NWC														
4-SW-1540	Remove Sidewalk - Aloha NWC	3	3	0	0	3	3	19-Mar-26	23-Mar-26	-22	-22	0	0	☐
4-SW-1541	Trench Electrical - Aloha NWC	3	3	0	0	3	3	24-Mar-26	26-Mar-26	-22	-22	0	0	☐
4-SW-1542	Electrical - Aloha NWC	18	18	0	0	18	18	27-Mar-26	21-Apr-26	-22	-22	0	0	☐
4-SW-1543	Grade Sidewalks - Aloha NWC	3	3	0	0	3	3	22-Apr-26	24-Apr-26	-22	-22	0	0	☐
4-SW-1544	Pour Sidewalks/Curb Ramps - Aloha NWC	6	6	0	0	6	6	27-Apr-26	04-May-26	5	5	0	0	☐
Aloha SWC														
4-SW-1546	Remove Sidewalk - Aloha SWC	3	3	0	0	3	3	27-Apr-26	29-Apr-26	-22	-22	0	0	☐
4-SW-1547	Trench Electrical - Aloha SWC	3	3	0	0	3	3	30-Apr-26	04-May-26	-22	-22	0	0	☐
4-SW-1548	Electrical - Aloha SWC	8	8	0	0	8	8	05-May-26	14-May-26	-22	-22	0	0	☐
4-SW-1549	Grade Sidewalks - Aloha SWC	3	3	0	0	3	3	15-May-26	19-May-26	-22	-22	0	0	☐
4-SW-1550	Pour Sidewalks/Curb Ramps - Aloha SWC	6	6	0	0	6	6	20-May-26	28-May-26	-6	-6	0	0	☐
Fairview Place NWC														
4-SW-1552	Remove Sidewalk Fairview Pl. NWC	3	3	0	0	3	3	20-May-26	22-May-26	-22	-22	0	0	☐
4-SW-1553	Trench Electrical Fairview Pl. NWC	3	3	0	0	3	3	26-May-26	28-May-26	-22	-22	0	0	☐
4-SW-1554	Electrical Fairview Pl. NWC	8	8	0	0	8	8	29-May-26	09-Jun-26	-22	-22	0	0	☐
4-SW-1555	Grade Sidewalks Fairview Pl. NWC	3	3	0	0	3	3	10-Jun-26	09-Jul-26	-22	-22	0	0	☐
4-SW-1556	Pour Sidewalks/Curb Ramps - Fairview Pl. NWC	6	6	0	0	6	6	10-Jul-26	17-Jul-26	-17	-17	0	0	☐
Fairview Place to Valley														
4-SW-1558	Remove Sidewalk Fairview Pl. to Valley	2	2	0	0	2	2	10-Jul-26	13-Jul-26	-22	-22	0	0	☐
4-SW-1559	Trench Electrical Fairview Pl. to Valley	2	2	0	0	2	2	14-Jul-26	15-Jul-26	-22	-22	0	0	☐
4-SW-1560	Electrical Fairview Pl. to Valley	5	5	0	0	5	5	16-Jul-26	22-Jul-26	-22	-22	0	0	☐
4-SW-1561	Grade Sidewalks Fairview Pl. to Valley	2	2	0	0	2	2	23-Jul-26	24-Jul-26	-22	-22	0	0	☐
4-SW-1562	Pour Sidewalks/Curb Ramps - Fairview Pl. to Valley	4	4	0	0	4	4	27-Jul-26	30-Jul-26	-22	-22	0	0	☐
Asphalt Pave Bike Lane Yale to Valley														
4-SW-1564	Prep For Asphalt - Bike Lane Yale to Valley	3	3	0	0	3	3	31-Jul-26	04-Aug-26	60	60	0	0	☐
4-SW-1565	Asphalt Pave - Bike Lane Yale to Valley	3	3	0	0	3	3	05-Aug-26	07-Aug-26	60	60	0	0	☐
Aloha Center Median														
4-SW-1605	Remove Sidewalk - Aloha Center Median	2	2	0	0	2	2	31-Jul-26	03-Aug-26	-22	-22	0	0	☐
4-SW-1606	Trench Electrical - Aloha Center Median	3	3	0	0	3	3	04-Aug-26	06-Aug-26	-22	-22	0	0	☐
4-SW-1607	Excavate Shelter Foundations - Aloha Center Median	1	1	0	0	1	1	07-Aug-26	07-Aug-26	-22	-22	0	0	☐
4-SW-1608	Form Pour Shelter Foundations - Aloha Center Median	3	3	0	0	3	3	10-Aug-26	12-Aug-26	-22	-22	0	0	☐
4-SW-1609	Electrical - Aloha Center Median	5	5	0	0	5	5	13-Aug-26	19-Aug-26	-22	-22	0	0	☐
4-SW-1610	Grade Sidewalks - Aloha Center Median	2	2	0	0	2	2	20-Aug-26	21-Aug-26	-22	-22	0	0	☐
4-SW-1611	Pour Sidewalks/Curb Ramps - Aloha Center Median	5	5	0	0	5	5	24-Aug-26	28-Aug-26	7	7	0	0	☐
Harrison SEC														
4-SW-1621	Remove Sidewalk - Harrison SEC	1	1	0	0	1	1	24-Aug-26	24-Aug-26	-22	-22	0	0	☐
4-SW-1622	Pour Sidewalks/Curb Ramps - Harrison SEC	2	2	0	0	2	2	25-Aug-26	26-Aug-26	-22	-22	0	0	☐
Harrison SWC														
4-SW-1624	Remove Sidewalk - Harrison SWC	2	2	0	0	2	2	27-Aug-26	28-Aug-26	-22	-22	0	0	☐
4-SW-1625	Trench Electrical - Harrison SWC	2	2	0	0	2	2	31-Aug-26	01-Sep-26	-22	-22	0	0	☐
4-SW-1626	Excavate Shelter Foundations - Harrison SWC	1	1	0	0	1	1	02-Sep-26	02-Sep-26	-22	-22	0	0	☐
4-SW-1627	Form Pour Shelter Foundations - Harrison SWC	4	4	0	0	4	4	03-Sep-26	09-Sep-26	-6	-6	0	0	☐
4-SW-1628	Electrical - Harrison SWC	6	6	0	0	6	6	10-Sep-26	17-Sep-26	-6	-6	0	0	☐
4-SW-1629	Grade Sidewalks - Harrison SWC	1	1	0	0	1	1	18-Sep-26	18-Sep-26	-6	-6	0	0	☐
4-SW-1630	Pour Sidewalks/Curb Ramps - Harrison SWC	4	4	0	0	4	4	21-Sep-26	24-Sep-26	-6	-6	0	0	☐
Virginia and Boren SEC														
4-SW-1632	Remove Sidewalk - Virginia & Boren SEC	2	2	0	0	2	2	03-Sep-26	04-Sep-26	-22	-22	0	0	☐
4-SW-1633	Trench Electrical - Virginia & Boren SEC	2	2	0	0	2	2	08-Sep-26	09-Sep-26	-22	-22	0	0	☐
4-SW-1634	Excavate Shelter Foundations - Virginia & Boren SEC	1	1	0	0	1	1	10-Sep-26	10-Sep-26	-22	-22	0	0	☐
4-SW-1635	Form Pour Shelter Foundations - Virginia & Boren SEC	4	4	0	0	4	4	11-Sep-26	16-Sep-26	-8	-8	0	0	☐

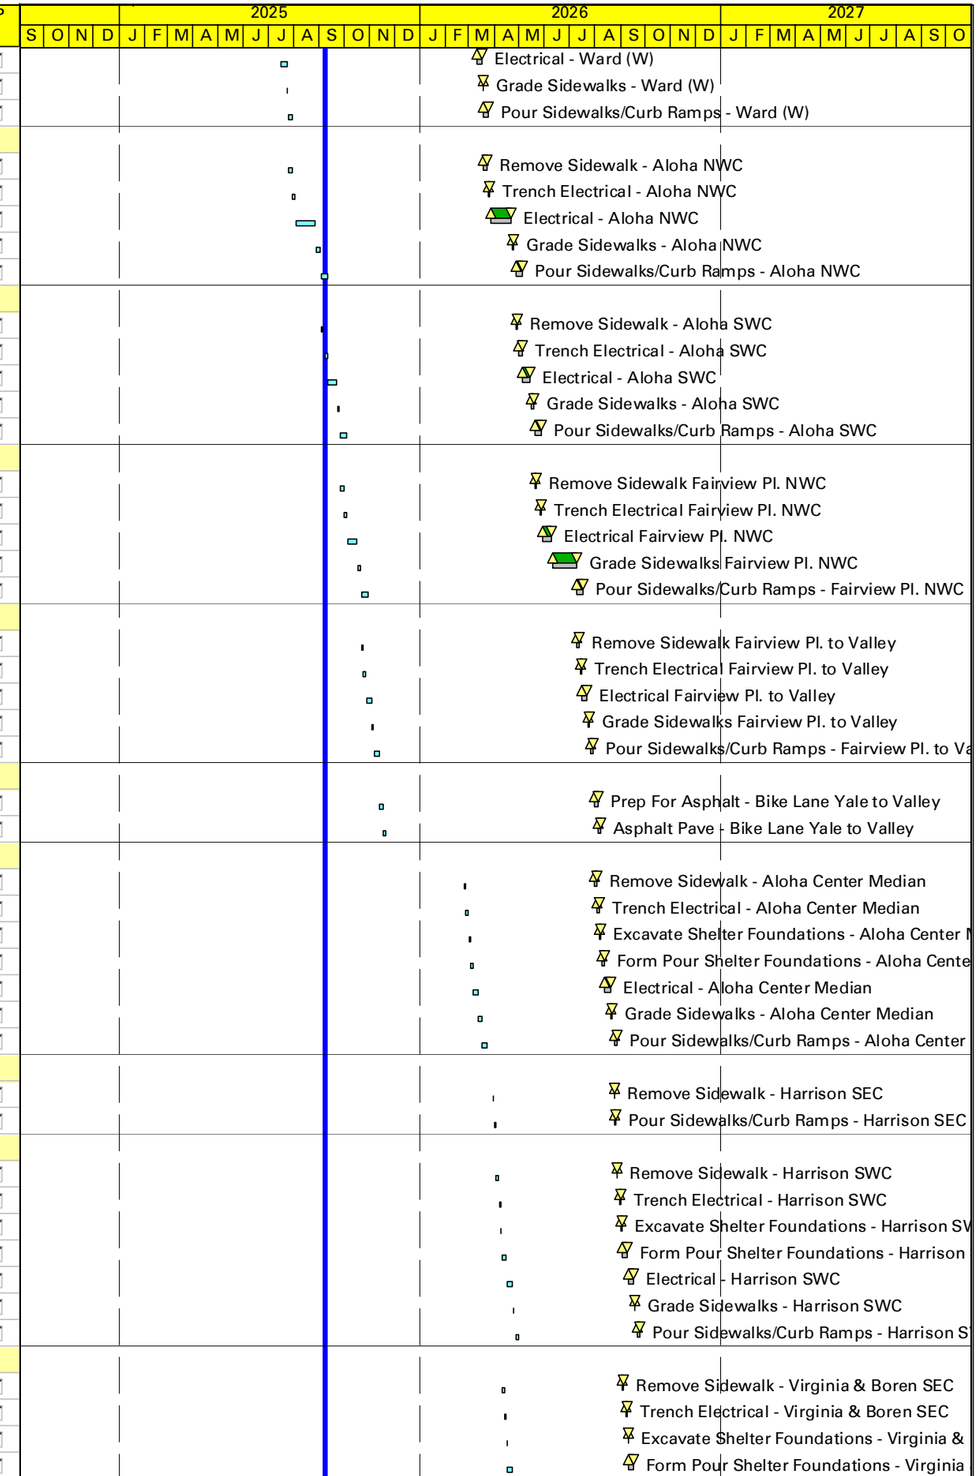

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
4-SW-1636	Electrical - Virginia & Boren SEC	6	6	0	0	6	6	17-Sep-26	24-Sep-26	-8	-8	0	0	
4-SW-1637	Grade Sidewalks - Virginia & Boren SEC	1	1	0	0	1	1	25-Sep-26	25-Sep-26	-8	-8	0	0	
4-SW-1638	Pour Sidewalks/Curb Ramps - Virginia & Boren SEC	6	6	0	0	6	6	28-Sep-26	05-Oct-26	-8	-8	0	0	
Virgina and Terry SEC														
4-SW-1640	Remove Sidewalk - Virginia & Terry SEC	2	2	0	0	2	2	11-Sep-26	14-Sep-26	-22	-22	0	0	
4-SW-1641	Trench Electrical - Virginia & Terry SEC	2	2	0	0	2	2	15-Sep-26	16-Sep-26	-22	-22	0	0	
4-SW-1642	Excavate Shelter Foundations - Virginia & Terry SEC	1	1	0	0	1	1	17-Sep-26	17-Sep-26	-22	-22	0	0	
4-SW-1643	Form Pour Shelter Foundations - Virginia & Terry SEC	4	4	0	0	4	4	18-Sep-26	23-Sep-26	-7	-7	0	0	
4-SW-1644	Electrical - Virginia & Terry SEC	6	6	0	0	6	6	24-Sep-26	01-Oct-26	-7	-7	0	0	
4-SW-1645	Grade Sidewalks - Virginia & Terry SEC	1	1	0	0	1	1	02-Oct-26	02-Oct-26	-7	-7	0	0	
4-SW-1646	Pour Sidewalks/Curb Ramps - Virginia & Terry SEC	6	6	0	0	6	6	06-Oct-26	14-Oct-26	-8	-8	0	0	
Virginia and Westlake SEC														
4-SW-1648	Remove Sidewalk - Virginia & Westlake SEC	1	1	0	0	1	1	18-Sep-26	18-Sep-26	-22	-22	0	0	
4-SW-1649	Trench Electrical - Virginia & Westlake SEC	2	2	0	0	2	2	21-Sep-26	22-Sep-26	-22	-22	0	0	
4-SW-1650	Electrical - Virginia & Westlake SEC	4	4	0	0	4	4	23-Sep-26	28-Sep-26	-1	-1	0	0	
4-SW-1651	Grade Sidewalks - Virginia & Westlake SEC	1	1	0	0	1	1	29-Sep-26	29-Sep-26	-1	-1	0	0	
4-SW-1652	Pour Sidewalks/Curb Ramps - Virginia & Westlake SEC	4	4	0	0	4	4	30-Sep-26	05-Oct-26	-1	-1	0	0	
Virginia and 6th NEC														
4-SW-1654	Remove Sidewalk - Virginia & 6th NEC	2	2	0	0	2	2	23-Sep-26	24-Sep-26	-22	-22	0	0	
4-SW-1655	Trench Electrical - Virginia & 6th NEC	2	2	0	0	2	2	25-Sep-26	28-Sep-26	-22	-22	0	0	
4-SW-1656	Excavate Shelter Foundations - Virginia & 6th NEC	1	1	0	0	1	1	29-Sep-26	29-Sep-26	-22	-22	0	0	
4-SW-1657	Form Pour Shelter Foundations - Virginia & 6th NEC	4	4	0	0	4	4	30-Sep-26	05-Oct-26	-17	-17	0	0	
4-SW-1658	Electrical - Virginia & 6th NEC	6	6	0	0	6	6	06-Oct-26	14-Oct-26	-17	-17	0	0	
4-SW-1659	Grade Sidewalks - Virginia & 6th NEC	1	1	0	0	1	1	15-Oct-26	15-Oct-26	-17	-17	0	0	
4-SW-1660	Pour Sidewalks/Curb Ramps - Virginia & 6th NEC	5	5	0	0	5	5	16-Oct-26	22-Oct-26	-17	-17	0	0	
Stewert and 7th NWC														
4-SW-1662	Remove Sidewalk - Stewart & 7th NWC	2	2	0	0	2	2	30-Sep-26	01-Oct-26	-22	-22	0	0	
4-SW-1663	Trench Electrical - Stewart & 7th NWC	2	2	0	0	2	2	02-Oct-26	05-Oct-26	-22	-22	0	0	
4-SW-1664	Excavate Shelter Foundations - Stewart & 7th NWC	1	1	0	0	1	1	06-Oct-26	06-Oct-26	-22	-22	0	0	
4-SW-1665	Form Pour Shelter Foundations - Stewart & 7th NWC	4	4	0	0	4	4	07-Oct-26	13-Oct-26	-22	-22	0	0	
4-SW-1666	Electrical - Stewart & 7th NWC	6	6	0	0	6	6	14-Oct-26	21-Oct-26	-22	-22	0	0	
4-SW-1667	Grade Sidewalks - Stewart & 7th NWC	1	1	0	0	1	1	22-Oct-26	22-Oct-26	-22	-22	0	0	
4-SW-1668	Pour Sidewalks/Curb Ramps - Stewart & 7th NWC	5	5	0	0	5	5	23-Oct-26	29-Oct-26	-22	-22	0	0	
4-SW-1669	Slate Paving - Stewart & 7th NWC	5	5	0	0	5	5	30-Oct-26	05-Nov-26	-22	-22	0	0	
Weekend Driveways														
Virgina and Fairfiew														
4-WE-1672	Remove Driveway - Virginia & Fairview (WE)	1	1	0	0	1	1	10-Oct-26	10-Oct-26	32	32	0	0	
4-WE-1673	Pour Driveway - Virginia & Fairview (WE)	1	1	0	0	1	1	11-Oct-26	11-Oct-26	32	32	0	0	
Landscaping - Virginia & Fairview (WE)														
4-LS-1676	Trees and Shrubs - Virginia & Fairview (WE)	17	17	0	0	17	17	01-Oct-26	26-Oct-26	81	81	0	0	
SCL Services														
Yale SDOT Service														
4-SCL-1679	Install Meter Cabinet - Yale	1	1	0	0	1	1	26-Mar-26	26-Mar-26	79	79	0	0	
4-SCL-1680	SDOT Inspection - Yale	5	5	0	0	5	5	27-Mar-26	02-Apr-26	79	79	0	0	
4-SCL-1681	SDCI Inspection - Yale	5	5	0	0	5	5	03-Apr-26	09-Apr-26	79	79	0	0	
4-SCL-1682	SCL Inspection - Yale	21	21	0	0	21	21	10-Apr-26	08-May-26	79	79	0	0	
4-SCL-1683	SCL Heat Up Cabinet - Yale	21	21	0	0	21	21	11-May-26	09-Jun-26	79	79	0	0	
Ward SDOT Service														
4-SCL-1685	Install Meter Cabinet - Ward	1	1	0	0	1	1	27-Mar-26	27-Mar-26	92	92	0	0	
4-SCL-1686	SDOT Inspection - Ward	5	5	0	0	5	5	30-Mar-26	03-Apr-26	92	92	0	0	
4-SCL-1687	SDCI Inspection - Ward	5	5	0	0	5	5	06-Apr-26	10-Apr-26	92	92	0	0	
4-SCL-1688	SCL Inspection - Ward	21	21	0	0	21	21	13-Apr-26	11-May-26	92	92	0	0	
4-SCL-1689	SCL Heat Up Cabinet - Ward	21	21	0	0	21	21	12-May-26	10-Jun-26	92	92	0	0	
Aloha SDOT Service														

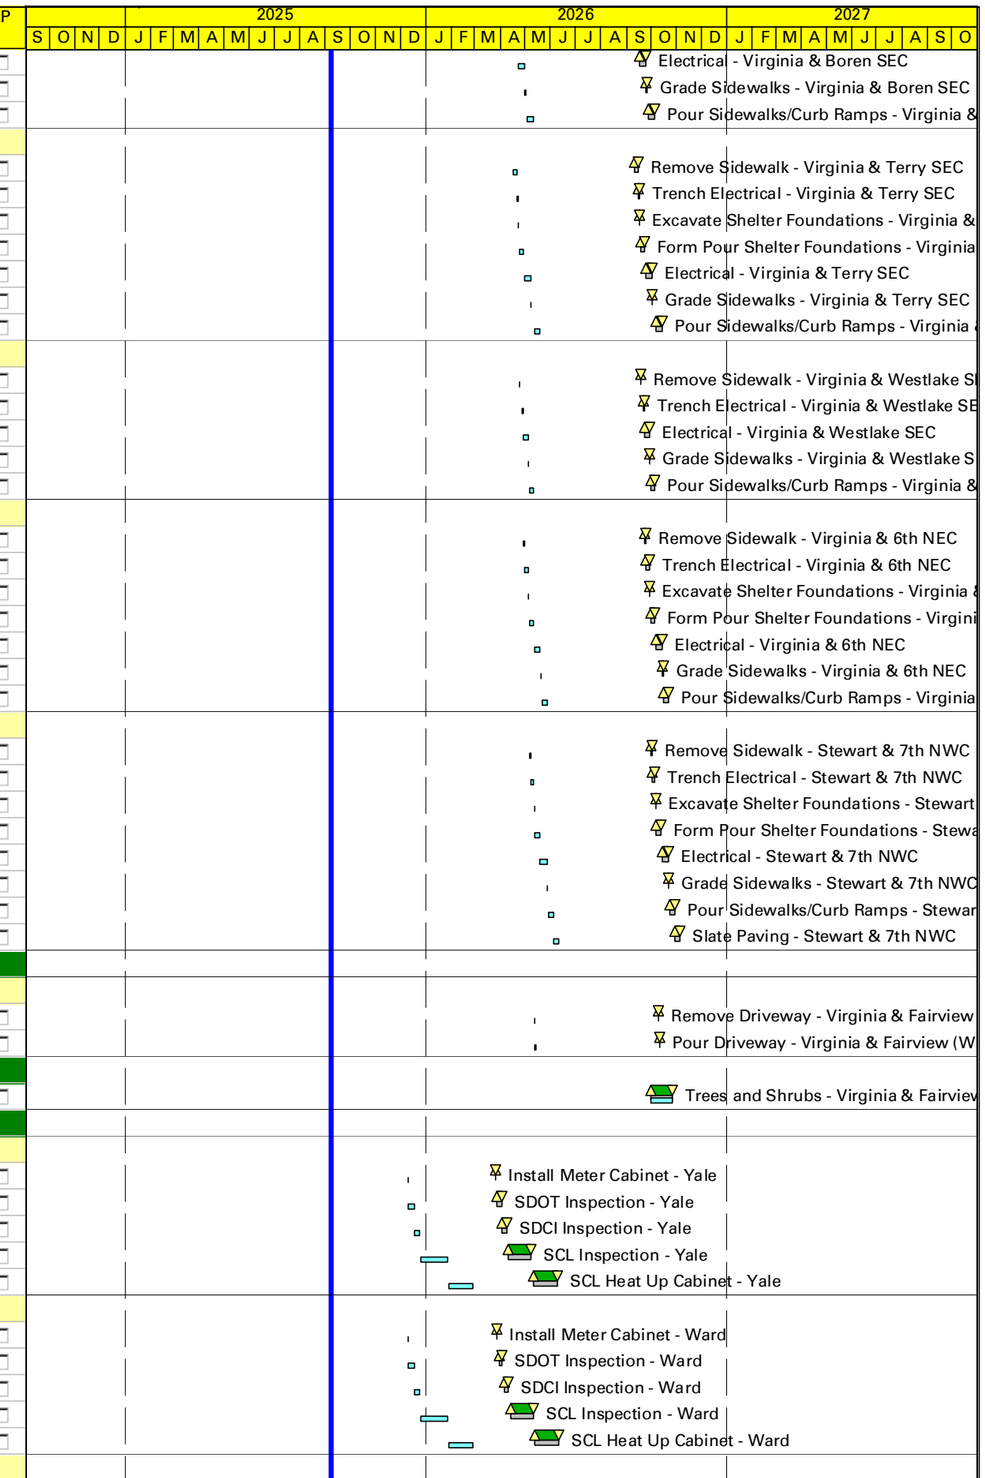

© Primavera Systems, Inc.

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
4-SCL-1691	Install Meter Cabinet - Aloha	1	1	0	0	1	1	31-Aug-26	31-Aug-26	7	7	0	0	
4-SCL-1692	SDOT Inspection - Aloha	5	5	0	0	5	5	01-Sep-26	08-Sep-26	7	7	0	0	
4-SCL-1693	SDCI Inspection - Aloha	5	5	0	0	5	5	09-Sep-26	15-Sep-26	7	7	0	0	
4-SCL-1694	SCL Inspection - Aloha	21	21	0	0	21	21	16-Sep-26	15-Oct-26	7	7	0	0	
4-SCL-1695	SCL Heat Up Cabinet - Aloha	21	21	0	0	21	21	16-Oct-26	16-Nov-26	7	7	0	0	
NB Aloha Station Service														
4-SCL-1697	Install Meter Cabinet - NB Aloha Station	1	1	0	0	1	1	31-Aug-26	31-Aug-26	18	18	0	0	
4-SCL-1698	SDOT Inspection - NB Aloha Station	5	5	0	0	5	5	01-Sep-26	08-Sep-26	18	18	0	0	
4-SCL-1699	SDCI Inspection - NB Aloha Station	5	5	0	0	5	5	09-Sep-26	15-Sep-26	18	18	0	0	
4-SCL-1700	SCL Inspection - NB Aloha Station	21	21	0	0	21	21	16-Sep-26	15-Oct-26	18	18	0	0	
4-SCL-1701	SCL Heat Up Cabinet - NB Aloha Station	21	21	0	0	21	21	16-Oct-26	16-Nov-26	18	18	0	0	
SB Aloha Station														
4-SCL-1703	Install Meter Cabinet - SB Aloha Station	1	1	0	0	1	1	31-Aug-26	31-Aug-26	19	19	0	0	
4-SCL-1704	SDOT Inspection - SB Aloha Station	5	5	0	0	5	5	01-Sep-26	08-Sep-26	19	19	0	0	
4-SCL-1705	SDCI Inspection - SB Aloha Station	5	5	0	0	5	5	09-Sep-26	15-Sep-26	19	19	0	0	
4-SCL-1706	SCL Inspection - SB Aloha Station	21	21	0	0	21	21	16-Sep-26	15-Oct-26	19	19	0	0	
4-SCL-1707	SCL Heat Up Cabinet - SB Aloha Station	21	21	0	0	21	21	16-Oct-26	16-Nov-26	19	19	0	0	
Harrison NB Station														
4-SCL-1709	Install Meter Cabinet - Harrison NB Station	1	1	0	0	1	1	30-Jan-26	30-Jan-26	150	150	0	0	
4-SCL-1710	SDOT Inspection - Harrison NB Station	5	5	0	0	5	5	02-Feb-26	06-Feb-26	150	150	0	0	
4-SCL-1711	SDCI Inspection - Harrison NB Station	5	5	0	0	5	5	09-Feb-26	13-Feb-26	150	150	0	0	
4-SCL-1712	SCL Inspection - Harrison NB Station	21	21	0	0	21	21	17-Feb-26	17-Mar-26	150	150	0	0	
4-SCL-1713	SCL Heat Up Cabinet - Harrison NB Station	21	21	0	0	21	21	18-Mar-26	15-Apr-26	150	150	0	0	
Harrison SB Station														
4-SCL-1715	Install Meter Cabinet - Harrison SB Station	1	1	0	0	1	1	25-Sep-26	25-Sep-26	3	3	0	0	
4-SCL-1716	SDOT Inspection - Harrison SB Station	5	5	0	0	5	5	28-Sep-26	02-Oct-26	3	3	0	0	
4-SCL-1717	SDCI Inspection - Harrison SB Station	5	5	0	0	5	5	05-Oct-26	09-Oct-26	3	3	0	0	
4-SCL-1718	SCL Inspection - Harrison SB Station	21	21	0	0	21	21	13-Oct-26	10-Nov-26	3	3	0	0	
4-SCL-1719	SCL Heat Up Cabinet - Harrison SB Station	21	21	0	0	21	21	12-Nov-26	14-Dec-26	3	3	0	0	
Virginia SB Station														
4-SCL-1721	Install Meter Cabinet - Virginia SB Station	1	1	0	0	1	1	23-Oct-26	23-Oct-26	-15	-15	0	0	
4-SCL-1722	SDOT Inspection - Virginia SB Station	5	5	0	0	5	5	26-Oct-26	30-Oct-26	-15	-15	0	0	
4-SCL-1723	SDCI Inspection - Virginia SB Station	5	5	0	0	5	5	02-Nov-26	06-Nov-26	-15	-15	0	0	
4-SCL-1724	SCL Inspection - Virginia SB Station	21	21	0	0	21	21	09-Nov-26	10-Dec-26	-15	-15	0	0	
4-SCL-1725	SCL Heat Up Cabinet - Virginia SB Station	21	21	0	0	21	21	11-Dec-26	12-Jan-27	-15	-15	0	0	
Terry NB Station														
4-SCL-1727	Install Meter Cabinet - Terry NB Station	1	1	0	0	1	1	15-Oct-26	15-Oct-26	-8	-8	0	0	
4-SCL-1728	SDOT Inspection - Terry NB Station	5	5	0	0	5	5	16-Oct-26	22-Oct-26	-8	-8	0	0	
4-SCL-1729	SDCI Inspection - Terry NB Station	5	5	0	0	5	5	23-Oct-26	29-Oct-26	-8	-8	0	0	
4-SCL-1730	SCL Inspection - Terry NB Station	21	21	0	0	21	21	30-Oct-26	02-Dec-26	-8	-8	0	0	
4-SCL-1731	SCL Heat Up Cabinet - Terry NB Station	21	21	0	0	21	21	03-Dec-26	04-Jan-27	-8	-8	0	0	
Westlake NB Station														
4-SCL-1733	Install Meter Cabinet - Westlake NB Station	1	1	0	0	1	1	06-Oct-26	06-Oct-26	-1	-1	0	0	
4-SCL-1734	SDOT Inspection - Westlake NB Station	5	5	0	0	5	5	07-Oct-26	14-Oct-26	-1	-1	0	0	
4-SCL-1735	SDCI Inspection - Westlake NB Station	5	5	0	0	5	5	15-Oct-26	21-Oct-26	-1	-1	0	0	
4-SCL-1736	SCL Inspection - Westlake NB Station	21	21	0	0	21	21	22-Oct-26	20-Nov-26	-1	-1	0	0	
4-SCL-1737	SCL Heat Up Cabinet - Westlake NB Station	21	21	0	0	21	21	23-Nov-26	23-Dec-26	-1	-1	0	0	
7th SB Station														
4-SCL-1739	Install Meter Cabinet - 7th SB Station	1	1	0	0	1	1	06-Nov-26	06-Nov-26	-22	-22	0	0	
4-SCL-1740	SDOT Inspection - 7th SB Station	5	5	0	0	5	5	09-Nov-26	16-Nov-26	-22	-22	0	0	
4-SCL-1741	SDCI Inspection - 7th SB Station	5	5	0	0	5	5	17-Nov-26	23-Nov-26	-22	-22	0	0	
4-SCL-1742	SCL Inspection - 7th SB Station	21	21	0	0	21	21	24-Nov-26	24-Dec-26	-22	-22	0	0	
4-SCL-1743	SCL Heat Up Cabinet - 7th SB Station	21	21	0	0	21	21	28-Dec-26	27-Jan-27	-22	-22	0	0	
Signals														

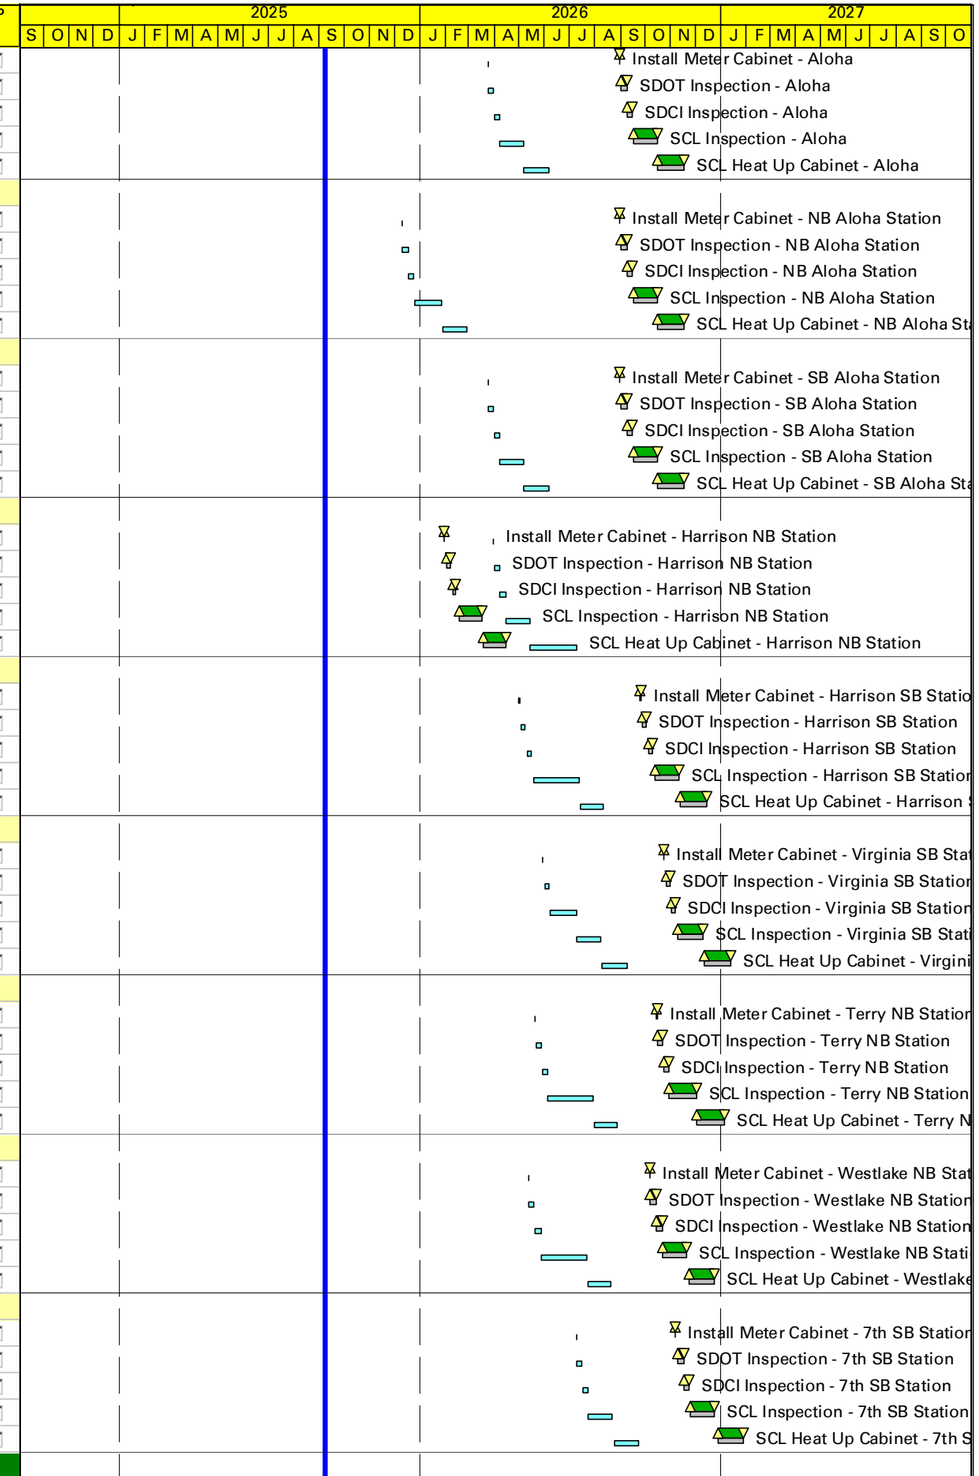

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Yale														
4-SIG-1746	Install Poles - Yale	3	3	0	0	3	3	10-Jun-26	09-Jul-26	79	79	0	0	
4-SIG-1747	Build Signal - Yale	11	11	0	0	11	11	10-Jul-26	24-Jul-26	79	79	0	0	
4-SIG-1748	SDOT Inspection - Yale	5	5	0	0	5	5	27-Jul-26	31-Jul-26	97	97	0	0	
4-SIG-1749	SDOT Commission - Yale	10	10	0	0	10	10	03-Aug-26	14-Aug-26	97	97	0	0	
4-SIG-1750	Demo Old Signal & Temp Signal - Yale	2	2	0	0	2	2	17-Aug-26	18-Aug-26	97	97	0	0	
Ward St														
4-SIG-1752	Install Poles - Ward	2	2	0	0	2	2	27-Jul-26	28-Jul-26	79	79	0	0	
4-SIG-1753	Build Signal - Ward	10	10	0	0	10	10	29-Jul-26	11-Aug-26	79	79	0	0	
4-SIG-1754	SDOT Inspection - Ward	5	5	0	0	5	5	12-Aug-26	18-Aug-26	86	86	0	0	
4-SIG-1755	SDOT Commission - Ward	10	10	0	0	10	10	19-Aug-26	01-Sep-26	86	86	0	0	
4-SIG-1756	Demo Old Signal & Temp Signal - Ward	2	2	0	0	2	2	02-Sep-26	03-Sep-26	86	86	0	0	
Aloha														
4-SIG-1758	Install Poles - Aloha	4	4	0	0	4	4	17-Nov-26	20-Nov-26	7	7	0	0	
4-SIG-1759	Build Signal - Aloha	10	10	0	0	10	10	23-Nov-26	08-Dec-26	7	7	0	0	
4-SIG-1760	SDOT Inspection - Aloha	5	5	0	0	5	5	09-Dec-26	15-Dec-26	7	7	0	0	
4-SIG-1761	SDOT Commission - Aloha	10	10	0	0	10	10	16-Dec-26	30-Dec-26	7	7	0	0	
4-SIG-1762	Demo Old Signal & Temp Signal - Aloha	2	2	0	0	2	2	31-Dec-26	04-Jan-27	7	7	0	0	
Fairview and Valley Including Mercer														
4-SIG-1764	Install Poles - Fairview & Valley (incl Mercer)	2	2	0	0	2	2	10-Aug-26	11-Aug-26	60	60	0	0	
4-SIG-1765	Build Signal - Fairview & Valley (incl Mercer)	11	11	0	0	11	11	12-Aug-26	26-Aug-26	60	60	0	0	
4-SIG-1766	SDOT Inspection - Fairview & Valley (incl Mercer)	5	5	0	0	5	5	27-Aug-26	02-Sep-26	77	77	0	0	
4-SIG-1767	SDOT Commission - Fairview & Valley (incl Mercer)	10	10	0	0	10	10	03-Sep-26	17-Sep-26	77	77	0	0	
4-SIG-1768	Demo Old Signal & Temp Signal - Fairview & Valley (incl Mercer)	2	2	0	0	2	2	18-Sep-26	21-Sep-26	77	77	0	0	
Republican St														
4-SIG-1770	Build Signal - Republican	5	5	0	0	5	5	25-Sep-26	01-Oct-26	-6	-6	0	0	
4-SIG-1771	SDOT Inspection - Republican	5	5	0	0	5	5	02-Oct-26	08-Oct-26	-6	-6	0	0	
4-SIG-1772	SDOT Commission - Republican	10	10	0	0	10	10	09-Oct-26	23-Oct-26	-6	-6	0	0	
4-SIG-1773	Demo Old Signal & Temp Signal - Republican	2	2	0	0	2	2	26-Oct-26	27-Oct-26	-6	-6	0	0	
Harrison														
4-SIG-1775	Build Signal - Harrison	5	5	0	0	5	5	28-Oct-26	03-Nov-26	-6	-6	0	0	
4-SIG-1776	SDOT Inspection - Harrison	5	5	0	0	5	5	04-Nov-26	10-Nov-26	-5	-5	0	0	
4-SIG-1777	SDOT Commission - Harrison	10	10	0	0	10	10	12-Nov-26	25-Nov-26	-5	-5	0	0	
4-SIG-1778	Demo Old Signal & Temp Signal - Harrison	2	2	0	0	2	2	30-Nov-26	01-Dec-26	-5	-5	0	0	
Thomas														
4-SIG-1780	Build Signal - Thomas	5	5	0	0	5	5	04-Nov-26	10-Nov-26	-6	-6	0	0	
4-SIG-1781	SDOT Inspection - Thomas	5	5	0	0	5	5	12-Nov-26	18-Nov-26	3	3	0	0	
4-SIG-1782	SDOT Commission - Thomas	10	10	0	0	10	10	19-Nov-26	04-Dec-26	3	3	0	0	
4-SIG-1783	Demo Old Signal & Temp Signal - Thomas	2	2	0	0	2	2	07-Dec-26	08-Dec-26	3	3	0	0	
John St														
4-SIG-1785	Build Signal - John	3	3	0	0	3	3	12-Nov-26	16-Nov-26	-6	-6	0	0	
4-SIG-1786	SDOT Inspection - John	5	5	0	0	5	5	17-Nov-26	23-Nov-26	2	2	0	0	
4-SIG-1787	SDOT Commission - John	10	10	0	0	10	10	24-Nov-26	09-Dec-26	2	2	0	0	
4-SIG-1788	Demo Old Signal & Temp Signal - John	2	2	0	0	2	2	10-Dec-26	11-Dec-26	2	2	0	0	
Boren and Fairfiew														
4-SIG-1790	Build Signal - Boren & Fairview	3	3	0	0	3	3	17-Nov-26	19-Nov-26	-6	-6	0	0	
4-SIG-1791	SDOT Inspection - Boren & Fairview	5	5	0	0	5	5	20-Nov-26	30-Nov-26	1	1	0	0	
4-SIG-1792	SDOT Commission - Boren & Fairview	10	10	0	0	10	10	01-Dec-26	14-Dec-26	1	1	0	0	
4-SIG-1793	Demo Old Signal & Temp Signal - Boren & Fairview	2	2	0	0	2	2	15-Dec-26	16-Dec-26	1	1	0	0	
Virginia and Terry														
4-SIG-1795	Build Signal - Virginia & Terry	3	3	0	0	3	3	20-Nov-26	24-Nov-26	-6	-6	0	0	
4-SIG-1796	SDOT Inspection - Virginia & Terry	5	5	0	0	5	5	25-Nov-26	03-Dec-26	0	0	0	0	
4-SIG-1797	SDOT Commission - Virginia & Terry	10	10	0	0	10	10	04-Dec-26	17-Dec-26	0	0	0	0	
4-SIG-1798	Demo Old Signal & Temp Signal - Virginia & Terry	2	2	0	0	2	2	18-Dec-26	21-Dec-26	0	0	0	0	

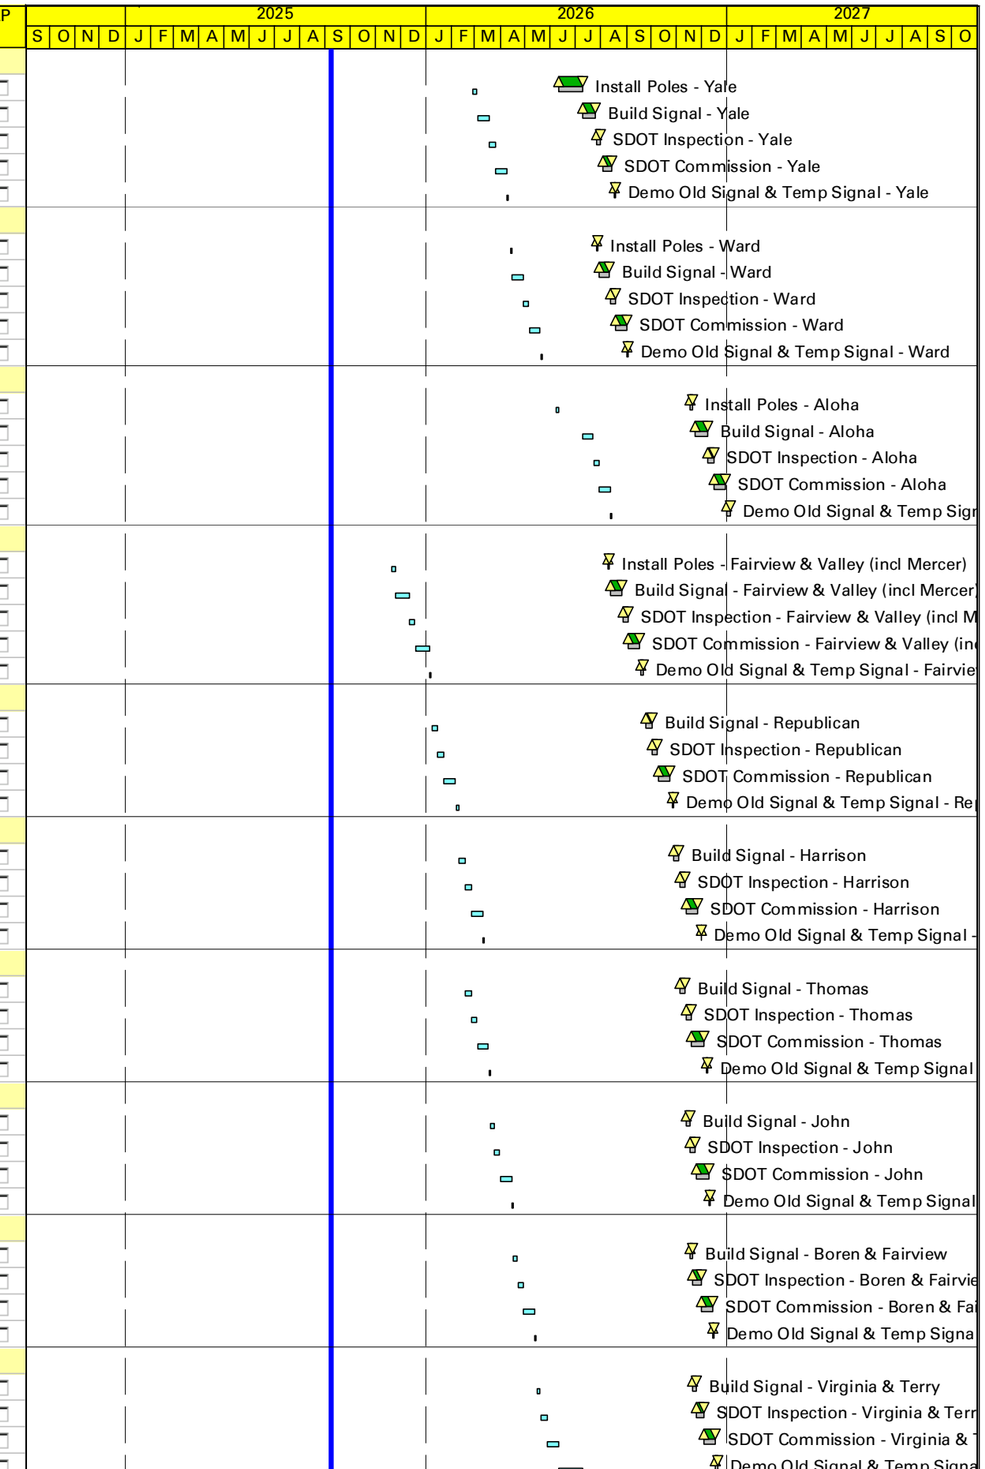

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
Virginia and 9th														
4-SIG-1800	Build Signal - Virginia & 9th	3	3	0	0	3	3	25-Nov-26	01-Dec-26	-6	-6	0	0	
4-SIG-1801	SDOT Inspection - Virginia & 9th	5	5	0	0	5	5	02-Dec-26	08-Dec-26	-1	-1	0	0	
4-SIG-1802	SDOT Commission - Virginia & 9th	10	10	0	0	10	10	09-Dec-26	22-Dec-26	-1	-1	0	0	
4-SIG-1803	Demo Old Signal & Temp Signal - Virginia & 9th	2	2	0	0	2	2	23-Dec-26	24-Dec-26	-1	-1	0	0	
Virginia and 8th														
4-SIG-1805	Build Signal - Virginia & 8th	3	3	0	0	3	3	02-Dec-26	04-Dec-26	-6	-6	0	0	
4-SIG-1806	SDOT Inspection - Virginia & 8th	5	5	0	0	5	5	07-Dec-26	11-Dec-26	-2	-2	0	0	
4-SIG-1807	SDOT Commission - Virginia & 8th	10	10	0	0	10	10	14-Dec-26	28-Dec-26	-2	-2	0	0	
4-SIG-1808	Demo Old Signal & Temp Signal - Virginia & 8th	2	2	0	0	2	2	29-Dec-26	30-Dec-26	-2	-2	0	0	
Virginia and Westlake														
4-SIG-1810	Build Signal - Virginia & Westlake SEC	3	3	0	0	3	3	07-Dec-26	09-Dec-26	-6	-6	0	0	
4-SIG-1811	SDOT Inspection - Virginia & Westlake SEC	5	5	0	0	5	5	10-Dec-26	16-Dec-26	-3	-3	0	0	
4-SIG-1812	SDOT Commission - Virginia & Westlake SEC	10	10	0	0	10	10	17-Dec-26	31-Dec-26	-3	-3	0	0	
4-SIG-1813	Demo Old Signal & Temp Signal - Virginia & Westlake SEC	2	2	0	0	2	2	04-Jan-27	05-Jan-27	-3	-3	0	0	
Stewart and 5th														
4-SIG-1815	Build Signal - Stewart & 5th	3	3	0	0	3	3	10-Dec-26	14-Dec-26	-6	-6	0	0	
4-SIG-1816	SDOT Inspection - Stewart & 5th	5	5	0	0	5	5	15-Dec-26	21-Dec-26	-4	-4	0	0	
4-SIG-1817	SDOT Commission - Stewart & 5th	10	10	0	0	10	10	22-Dec-26	06-Jan-27	-4	-4	0	0	
4-SIG-1818	Demo Old Signal & Temp Signal - Stewart & 5th	2	2	0	0	2	2	07-Jan-27	08-Jan-27	-4	-4	0	0	
Stewart and 7th														
4-SIG-1820	Build Signal - Stewart & 7th	3	3	0	0	3	3	15-Dec-26	17-Dec-26	-6	-6	0	0	
4-SIG-1821	SDOT Inspection - Stewart & 7th	5	5	0	0	5	5	18-Dec-26	24-Dec-26	-5	-5	0	0	
4-SIG-1822	SDOT Commission - Stewart & 7th	10	10	0	0	10	10	28-Dec-26	11-Jan-27	-5	-5	0	0	
4-SIG-1823	Demo Old Signal & Temp Signal - Stewart & 7th	2	2	0	0	2	2	12-Jan-27	13-Jan-27	-5	-5	0	0	
Stewart and Terry														
4-SIG-1825	Build Signal - Stewart & Terry	3	3	0	0	3	3	18-Dec-26	22-Dec-26	-6	-6	0	0	
4-SIG-1826	SDOT Inspection - Stewart & Terry	5	5	0	0	5	5	23-Dec-26	30-Dec-26	-6	-6	0	0	
4-SIG-1827	SDOT Commission - Stewart & Terry	10	10	0	0	10	10	31-Dec-26	14-Jan-27	-6	-6	0	0	
4-SIG-1828	Demo Old Signal & Temp Signal - Stewart & Terry	2	2	0	0	2	2	15-Jan-27	19-Jan-27	-6	-6	0	0	
Lighting														
N Ward Schematic														
4-EL-1831	Build Schematic, Poles, Luminaires Wiring - N Ward Schematic	2	2	0	0	2	2	12-Aug-26	13-Aug-26	79	79	0	0	
4-EL-1832	SCL Final Inspection - N Ward Schematic	10	10	0	0	10	10	14-Aug-26	27-Aug-26	79	79	0	0	
4-EL-1833	SCL Commission Lighting - N Ward Schematic	10	10	0	0	10	10	28-Aug-26	11-Sep-26	79	79	0	0	
4-EL-1834	Demo Old Lighting - N Ward Schematic	1	1	0	0	1	1	20-Jan-27	20-Jan-27	-6	-6	0	0	
Valley Schematic														
4-EL-1858	SCL Service Commissioning - Valley Schematic	21	21	0	0	21	21	31-Jul-26	28-Aug-26	79	79	0	0	
4-EL-1836	Build Schematic, Poles, Luminaires Wiring - Valley Schematic	2	2	0	0	2	2	27-Aug-26	28-Aug-26	60	60	0	0	
4-EL-1837	SCL Final Inspection - Valley Schematic	10	10	0	0	10	10	31-Aug-26	14-Sep-26	69	69	0	0	
4-EL-1838	SCL Commission Lighting - Valley Schematic	10	10	0	0	10	10	15-Sep-26	28-Sep-26	69	69	0	0	
4-EL-1839	Demo Old Lighting - Valley Schematic	1	1	0	0	1	1	21-Jan-27	21-Jan-27	-6	-6	0	0	
Aloha & Yale Schematic														
4-EL-1841	Build Schematic, Poles, Luminaires Wiring - Aloha Schematic	10	10	0	0	10	10	31-Aug-26	14-Sep-26	60	60	0	0	
4-EL-1862	SCL Service Commissioning - Aloha Schematic	21	21	0	0	21	21	31-Aug-26	29-Sep-26	59	59	0	0	
4-EL-1842	SCL Final Inspection - Aloha Schematic	10	10	0	0	10	10	15-Sep-26	28-Sep-26	60	60	0	0	
4-EL-1843	SCL Commission Lighting - Aloha Schematic	10	10	0	0	10	10	30-Sep-26	14-Oct-26	59	59	0	0	
4-EL-1844	Demo Old Lighting - Aloha Schematic	1	1	0	0	1	1	22-Jan-27	22-Jan-27	-6	-6	0	0	
Harrison														
4-EL-1846	Build Schematic, Poles, Luminaires Wiring - Harrison Schematic	10	10	0	0	10	10	02-Dec-26	15-Dec-26	-5	-5	0	0	
4-EL-1847	SCL Final Inspection - Harrison Schematic	10	10	0	0	10	10	16-Dec-26	30-Dec-26	-5	-5	0	0	
4-EL-1848	SCL Commission Lighting - Harrison Schematic	10	10	0	0	10	10	31-Dec-26	14-Jan-27	-5	-5	0	0	
4-EL-1849	Demo Old Lighting - Harrison Schematic	1	1	0	0	1	1	15-Jan-27	15-Jan-27	-5	-5	0	0	
Virginia and Boren														

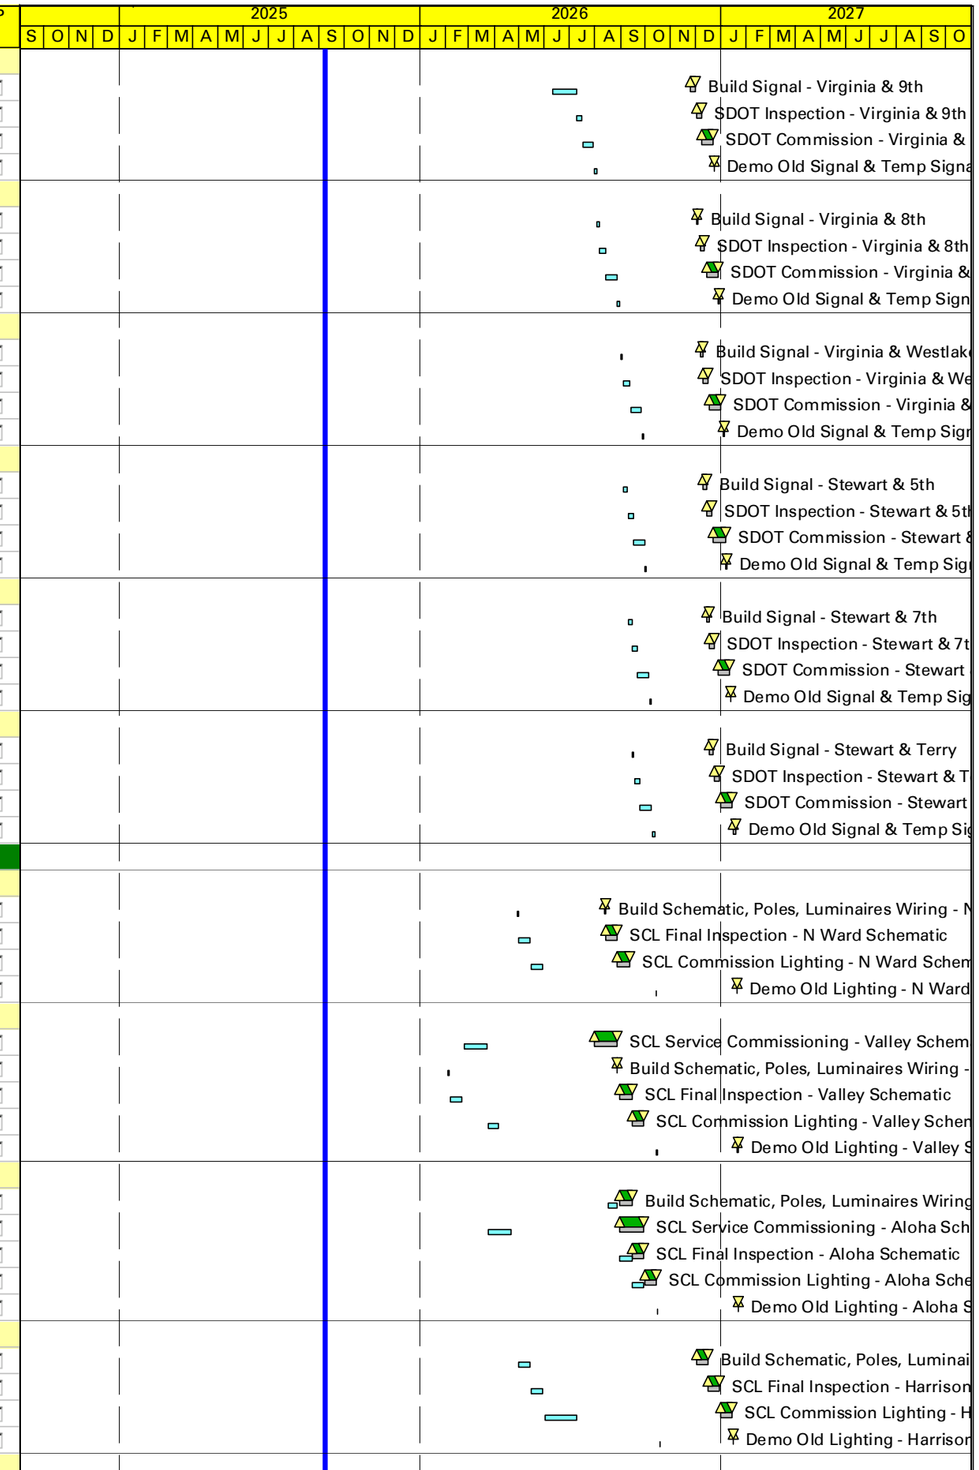

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort | Critical Remaining Work | BL1 LOE | Milestone | BL2 LOE | Previous MS | Actual Level of Effort | Previous Bar | Actual Work | Baseline MS | Remaining Work | Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
4-EL-1851	Build Schematic, Poles, Luminaires Wiring - Virginia & Boren Sch	5	5	0	0	5	5	06-Oct-26	13-Oct-26	38	38	0	0	☐
4-EL-1852	SCL Final Inspection - Virginia & Boren Schematic	10	10	0	0	10	10	14-Oct-26	27-Oct-26	38	38	0	0	☐
4-EL-1853	SCL Commission Lighting - Virginia & Boren Schematic	10	10	0	0	10	10	28-Oct-26	10-Nov-26	38	38	0	0	☐
4-EL-1854	Demo Old Lighting - Virginia & Boren Schematic	1	1	0	0	1	1	19-Jan-27	19-Jan-27	-5	-5	0	0	☐
Stations														
NB Aloha														
4-STN-1857	Install Shelters (2 Each) - NB Aloha Station	10	10	0	0	10	10	31-Aug-26	14-Sep-26	42	42	0	0	☐
4-STN-1858	Install Amenities - NB Aloha Station	1	1	0	0	1	1	15-Sep-26	15-Sep-26	42	42	0	0	☐
4-STN-1859	Install Tech Pylon - NB Aloha Station	1	1	0	0	1	1	16-Sep-26	16-Sep-26	52	52	0	0	☐
SB Aloha														
4-STN-1861	Install Shelters (2 Each) - SB Aloha Station	10	10	0	0	10	10	16-Sep-26	29-Sep-26	42	42	0	0	☐
4-STN-1862	Install Amenities - SB Aloha Station	1	1	0	0	1	1	30-Sep-26	30-Sep-26	42	42	0	0	☐
4-STN-1863	Install Tech Pylon - SB Aloha Station	1	1	0	0	1	1	01-Oct-26	01-Oct-26	42	42	0	0	☐
NB Harrison														
4-STN-1865	Install Shelters (2 Each) - NB Harrison Station	10	10	0	0	10	10	25-Sep-26	08-Oct-26	6	6	0	0	☐
4-STN-1866	Install Amenities - NB Harrison Station	1	1	0	0	1	1	09-Oct-26	09-Oct-26	6	6	0	0	☐
4-STN-1867	Install Tech Pylon - NB Harrison Station	1	1	0	0	1	1	13-Oct-26	13-Oct-26	36	36	0	0	☐
SB Harrison														
4-STN-1869	Install Shelters (2 Each) - SB Harrison Station	10	10	0	0	10	10	13-Oct-26	26-Oct-26	6	6	0	0	☐
4-STN-1870	Install Amenities - SB Harrison Station	1	1	0	0	1	1	27-Oct-26	27-Oct-26	6	6	0	0	☐
4-STN-1871	Install Tech Pylon - SB Harrison Station	1	1	0	0	1	1	28-Oct-26	28-Oct-26	26	26	0	0	☐
SB Virginia and Boren														
4-STN-1873	Install Shelters (1 Each) - SB Virginia & Boren Station	5	5	0	0	5	5	28-Oct-26	03-Nov-26	6	6	0	0	☐
4-STN-1874	Install Amenities - SB Virginia & Boren Station	1	1	0	0	1	1	04-Nov-26	04-Nov-26	6	6	0	0	☐
4-STN-1875	Install Tech Pylon - SB Virginia & Boren Station	1	1	0	0	1	1	05-Nov-26	05-Nov-26	21	21	0	0	☐
Terry NB														
4-STN-1877	Install Shelters (1 Each) - Terry NB Station	5	5	0	0	5	5	05-Nov-26	12-Nov-26	6	6	0	0	☐
4-STN-1878	Install Amenities - Terry NB Station	1	1	0	0	1	1	13-Nov-26	13-Nov-26	6	6	0	0	☐
4-STN-1879	Install Tech Pylon - Terry NB Station	1	1	0	0	1	1	16-Nov-26	16-Nov-26	16	16	0	0	☐
Westlake NB														
4-STN-1881	Install Shelters (1 Each) - Westlake NB Station	5	5	0	0	5	5	16-Nov-26	20-Nov-26	6	6	0	0	☐
4-STN-1882	Install Amenities - Westlake NB Station	1	1	0	0	1	1	23-Nov-26	23-Nov-26	6	6	0	0	☐
4-STN-1883	Install Tech Pylon - Westlake NB Station	1	1	0	0	1	1	24-Nov-26	24-Nov-26	11	11	0	0	☐
7th and Stewart SB														
4-STN-1885	Install Shelters (1 Each) - 7th & Stewart SB Station	5	5	0	0	5	5	24-Nov-26	02-Dec-26	6	6	0	0	☐
4-STN-1886	Install Amenities - 7th & Stewart SB Station	1	1	0	0	1	1	03-Dec-26	03-Dec-26	6	6	0	0	☐
4-STN-1887	Install Tech Pylon - 7th & Stewart SB Station	1	1	0	0	1	1	04-Dec-26	04-Dec-26	6	6	0	0	☐
Station Electrical														
NB Aloha														
4-SE-1890	Install Electrical - NB Aloha Station	5	5	0	0	5	5	07-Dec-26	11-Dec-26	6	6	0	0	☐
4-SE-1891	KCM Inspection - NB Aloha Station	5	5	0	0	5	5	14-Dec-26	18-Dec-26	6	6	0	0	☐
4-SE-1892	Commission Station Electrical - NB Aloha Station	1	1	0	0	1	1	21-Dec-26	21-Dec-26	6	6	0	0	☐
SB Ahoha														
4-SE-1894	Install Electrical - SB Aloha Station	5	5	0	0	5	5	17-Nov-26	23-Nov-26	19	19	0	0	☐
4-SE-1895	KCM Inspection - MSN Aloha Station	5	5	0	0	5	5	24-Nov-26	02-Dec-26	19	19	0	0	☐
4-SE-1896	Commission Station Electrical - MSN Aloha Station	1	1	0	0	1	1	22-Dec-26	22-Dec-26	6	6	0	0	☐
NB Harrison														
4-SE-1898	Install Electrical - NB Harrison Station	5	5	0	0	5	5	16-Apr-26	22-Apr-26	150	150	0	0	☐
4-SE-1899	KCM Inspection - NB Harrison Station	5	5	0	0	5	5	23-Apr-26	29-Apr-26	150	150	0	0	☐
4-SE-1900	Commission Station Electrical - NB Harrison Station	1	1	0	0	1	1	23-Dec-26	23-Dec-26	6	6	0	0	☐
SB Harrison														
4-SE-1902	Install Electrical - SB Harrison Station	5	5	0	0	5	5	15-Dec-26	21-Dec-26	3	3	0	0	☐
4-SE-1903	KCM Inspection - SB Harrison Station	5	5	0	0	5	5	22-Dec-26	29-Dec-26	3	3	0	0	☐
4-SE-1904	Commission Station Electrical - SB Harrison Station	1	1	0	0	1	1	30-Dec-26	30-Dec-26	3	3	0	0	☐

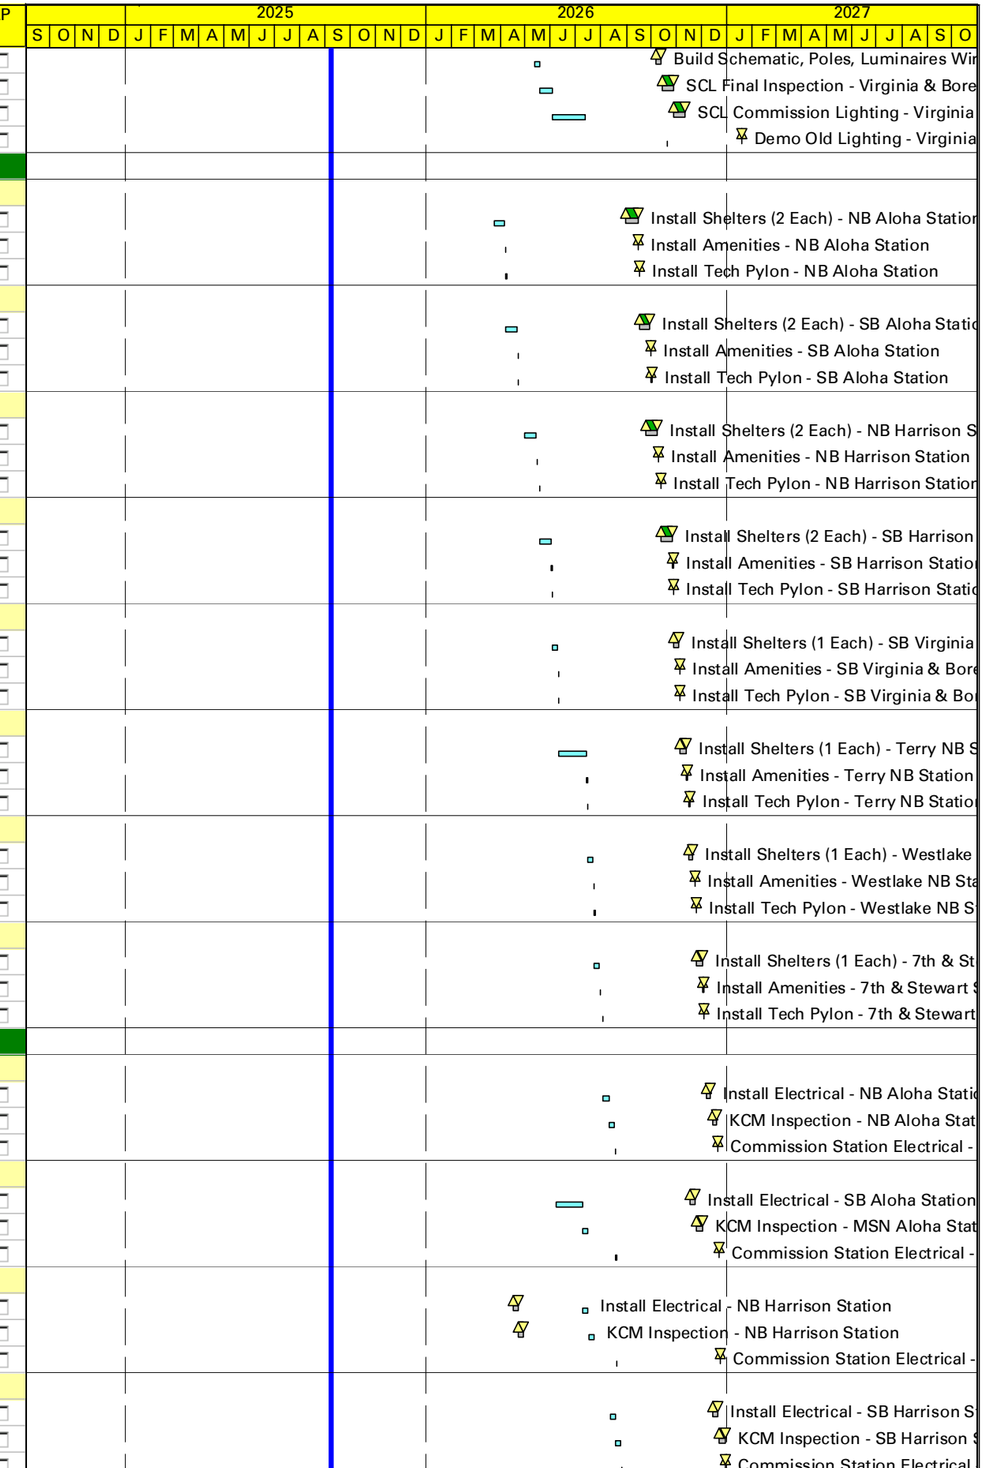

Start Date 11-Sep-24
Finish Date 06-May-27
Data Date 08-Sep-25
Run Date 16-Sep-25

Remaining Level of Effort
BL1 LOE
BL2 LOE
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Previous MS
Previous Bar
Baseline MS
Baseline Bar

J-LINE MONTHLY Update - AUGUST 2025 (v.041 / 08-SEP-25)
Jansen
P6 PID = JL-041M
DD = 08-Sep-25

TASK filter: All Activities
Layout: J-LINE-WBS-STD
© *Primavera Systems, Inc.*

JANSEN

Activity ID	Activity Name	OD	BL1 Dur	Var BL1 Dur	AD	RD	ACD	Start	Finish	TF	BL1 TF	Var BL1 ES	Var BL1 EF	LP
SB Virginia and Boren														
4-SE-1906	Install Electrical - SB Virginia & Boren Station	5	5	0	0	5	5	13-Jan-27	20-Jan-27	-15	-15	0	0	
4-SE-1907	KCM Inspection - SB Virginia & Boren Station	5	5	0	0	5	5	21-Jan-27	27-Jan-27	-15	-15	0	0	
4-SE-1908	Commission Station Electrical - SB Virginia & Boren Station	1	1	0	0	1	1	28-Jan-27	28-Jan-27	-15	-15	0	0	
Terry NB														
4-SE-1910	Install Electrical - Terry NB Station	5	5	0	0	5	5	05-Jan-27	11-Jan-27	-8	-8	0	0	
4-SE-1911	KCM Inspection - Terry NB Station	5	5	0	0	5	5	12-Jan-27	19-Jan-27	-8	-8	0	0	
4-SE-1912	Commission Station Electrical - Terry NB Station	1	1	0	0	1	1	29-Jan-27	29-Jan-27	-15	-15	0	0	
Westlake NB														
4-SE-1914	Install Electrical - Westlake NB Station	5	5	0	0	5	5	24-Dec-26	31-Dec-26	-1	-1	0	0	
4-SE-1915	KCM Inspection - Westlake NB Station	5	5	0	0	5	5	04-Jan-27	08-Jan-27	-1	-1	0	0	
4-SE-1916	Commission Station Electrical - Westlake NB Station	1	1	0	0	1	1	01-Feb-27	01-Feb-27	-15	-15	0	0	
7th and Stewart SB														
4-SE-1918	Install Electrical - 7th & Stewart SB Station	5	5	0	0	5	5	28-Jan-27	03-Feb-27	-22	-22	0	0	
4-SE-1919	KCM Inspection - 7th & Stewart SB Station	5	5	0	0	5	5	04-Feb-27	10-Feb-27	-22	-22	0	0	
4-SE-1920	Commission Station Electrical - 7th & Stewart SB Station	1	1	0	0	1	1	11-Feb-27	11-Feb-27	-22	-22	0	0	
Hardscapes After Electrical Demo														
Yale														
4-HS-1923	Remove Foundations - Yale	1	1	0	0	1	1	12-Feb-27	12-Feb-27	-22	-22	0	0	
4-HS-1924	Prep Sidewalks - Yale	1	1	0	0	1	1	16-Feb-27	16-Feb-27	-22	-22	0	0	
4-HS-1925	Pour Sidewalks - Yale	1	1	0	0	1	1	17-Feb-27	17-Feb-27	-22	-22	0	0	
Ward														
4-HS-1927	Remove Foundations - Ward	1	1	0	0	1	1	16-Feb-27	16-Feb-27	-22	-22	0	0	
4-HS-1928	Prep Sidewalks - Ward	1	1	0	0	1	1	17-Feb-27	17-Feb-27	-22	-22	0	0	
4-HS-1929	Pour Sidewalks - Ward	1	1	0	0	1	1	18-Feb-27	18-Feb-27	-22	-22	0	0	
Aloha														
4-HS-1931	Remove Foundations - Aloha	1	1	0	0	1	1	17-Feb-27	17-Feb-27	-22	-22	0	0	
4-HS-1932	Prep Sidewalks - Aloha	1	1	0	0	1	1	18-Feb-27	18-Feb-27	-22	-22	0	0	
4-HS-1933	Pour Sidewalks - Aloha	1	1	0	0	1	1	19-Feb-27	19-Feb-27	-22	-22	0	0	
Valley														
4-HS-1935	Remove Foundations - Valley	1	1	0	0	1	1	18-Feb-27	18-Feb-27	-22	-22	0	0	
4-HS-1936	Prep Sidewalks - Valley	1	1	0	0	1	1	19-Feb-27	19-Feb-27	-22	-22	0	0	
4-HS-1937	Pour Sidewalks - Valley	1	1	0	0	1	1	22-Feb-27	22-Feb-27	-22	-22	0	0	
PBL Buffers														
4-PBL-1939	Pour PBL Buffers - Zone 4	10	10	0	0	10	10	23-Feb-27	08-Mar-27	-22	-22	0	0	
Chanalization														
4-PM-1941	Channelization - Zone 4	15	15	0	0	15	15	09-Mar-27	29-Mar-27	-22	-22	0	0	
OCS														
4-OCS-1943	OCS - Material Handover - Zone 4	1	1	0	0	1	1	25-Sep-26	25-Sep-26	101	101	0	0	

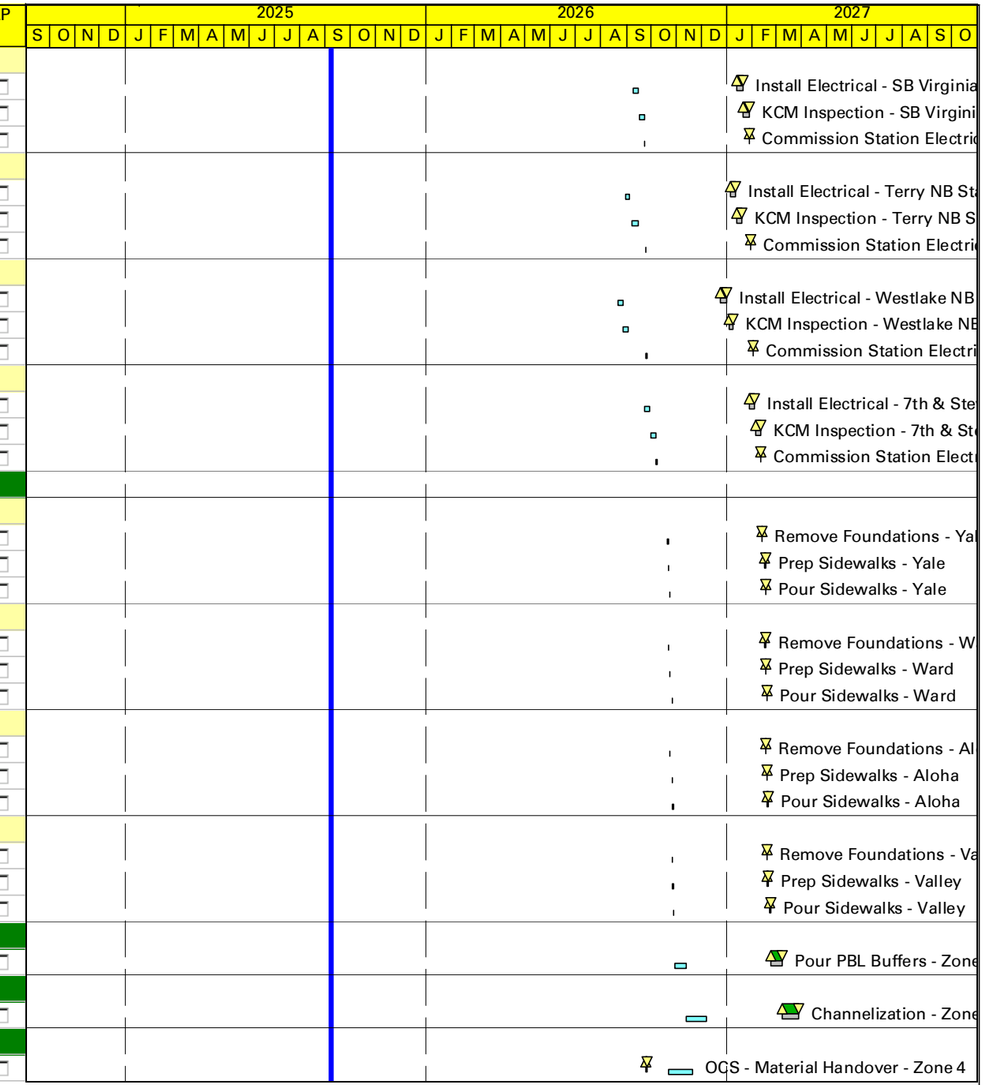

© Primavera Systems, Inc.
